


COFFS HARBOUR CULTURAL & CIVIC CENTRE "ALL WELCOME"
GORDON STREET COFFS HARBOUR, NSW
CONTRACT PROGRAMME







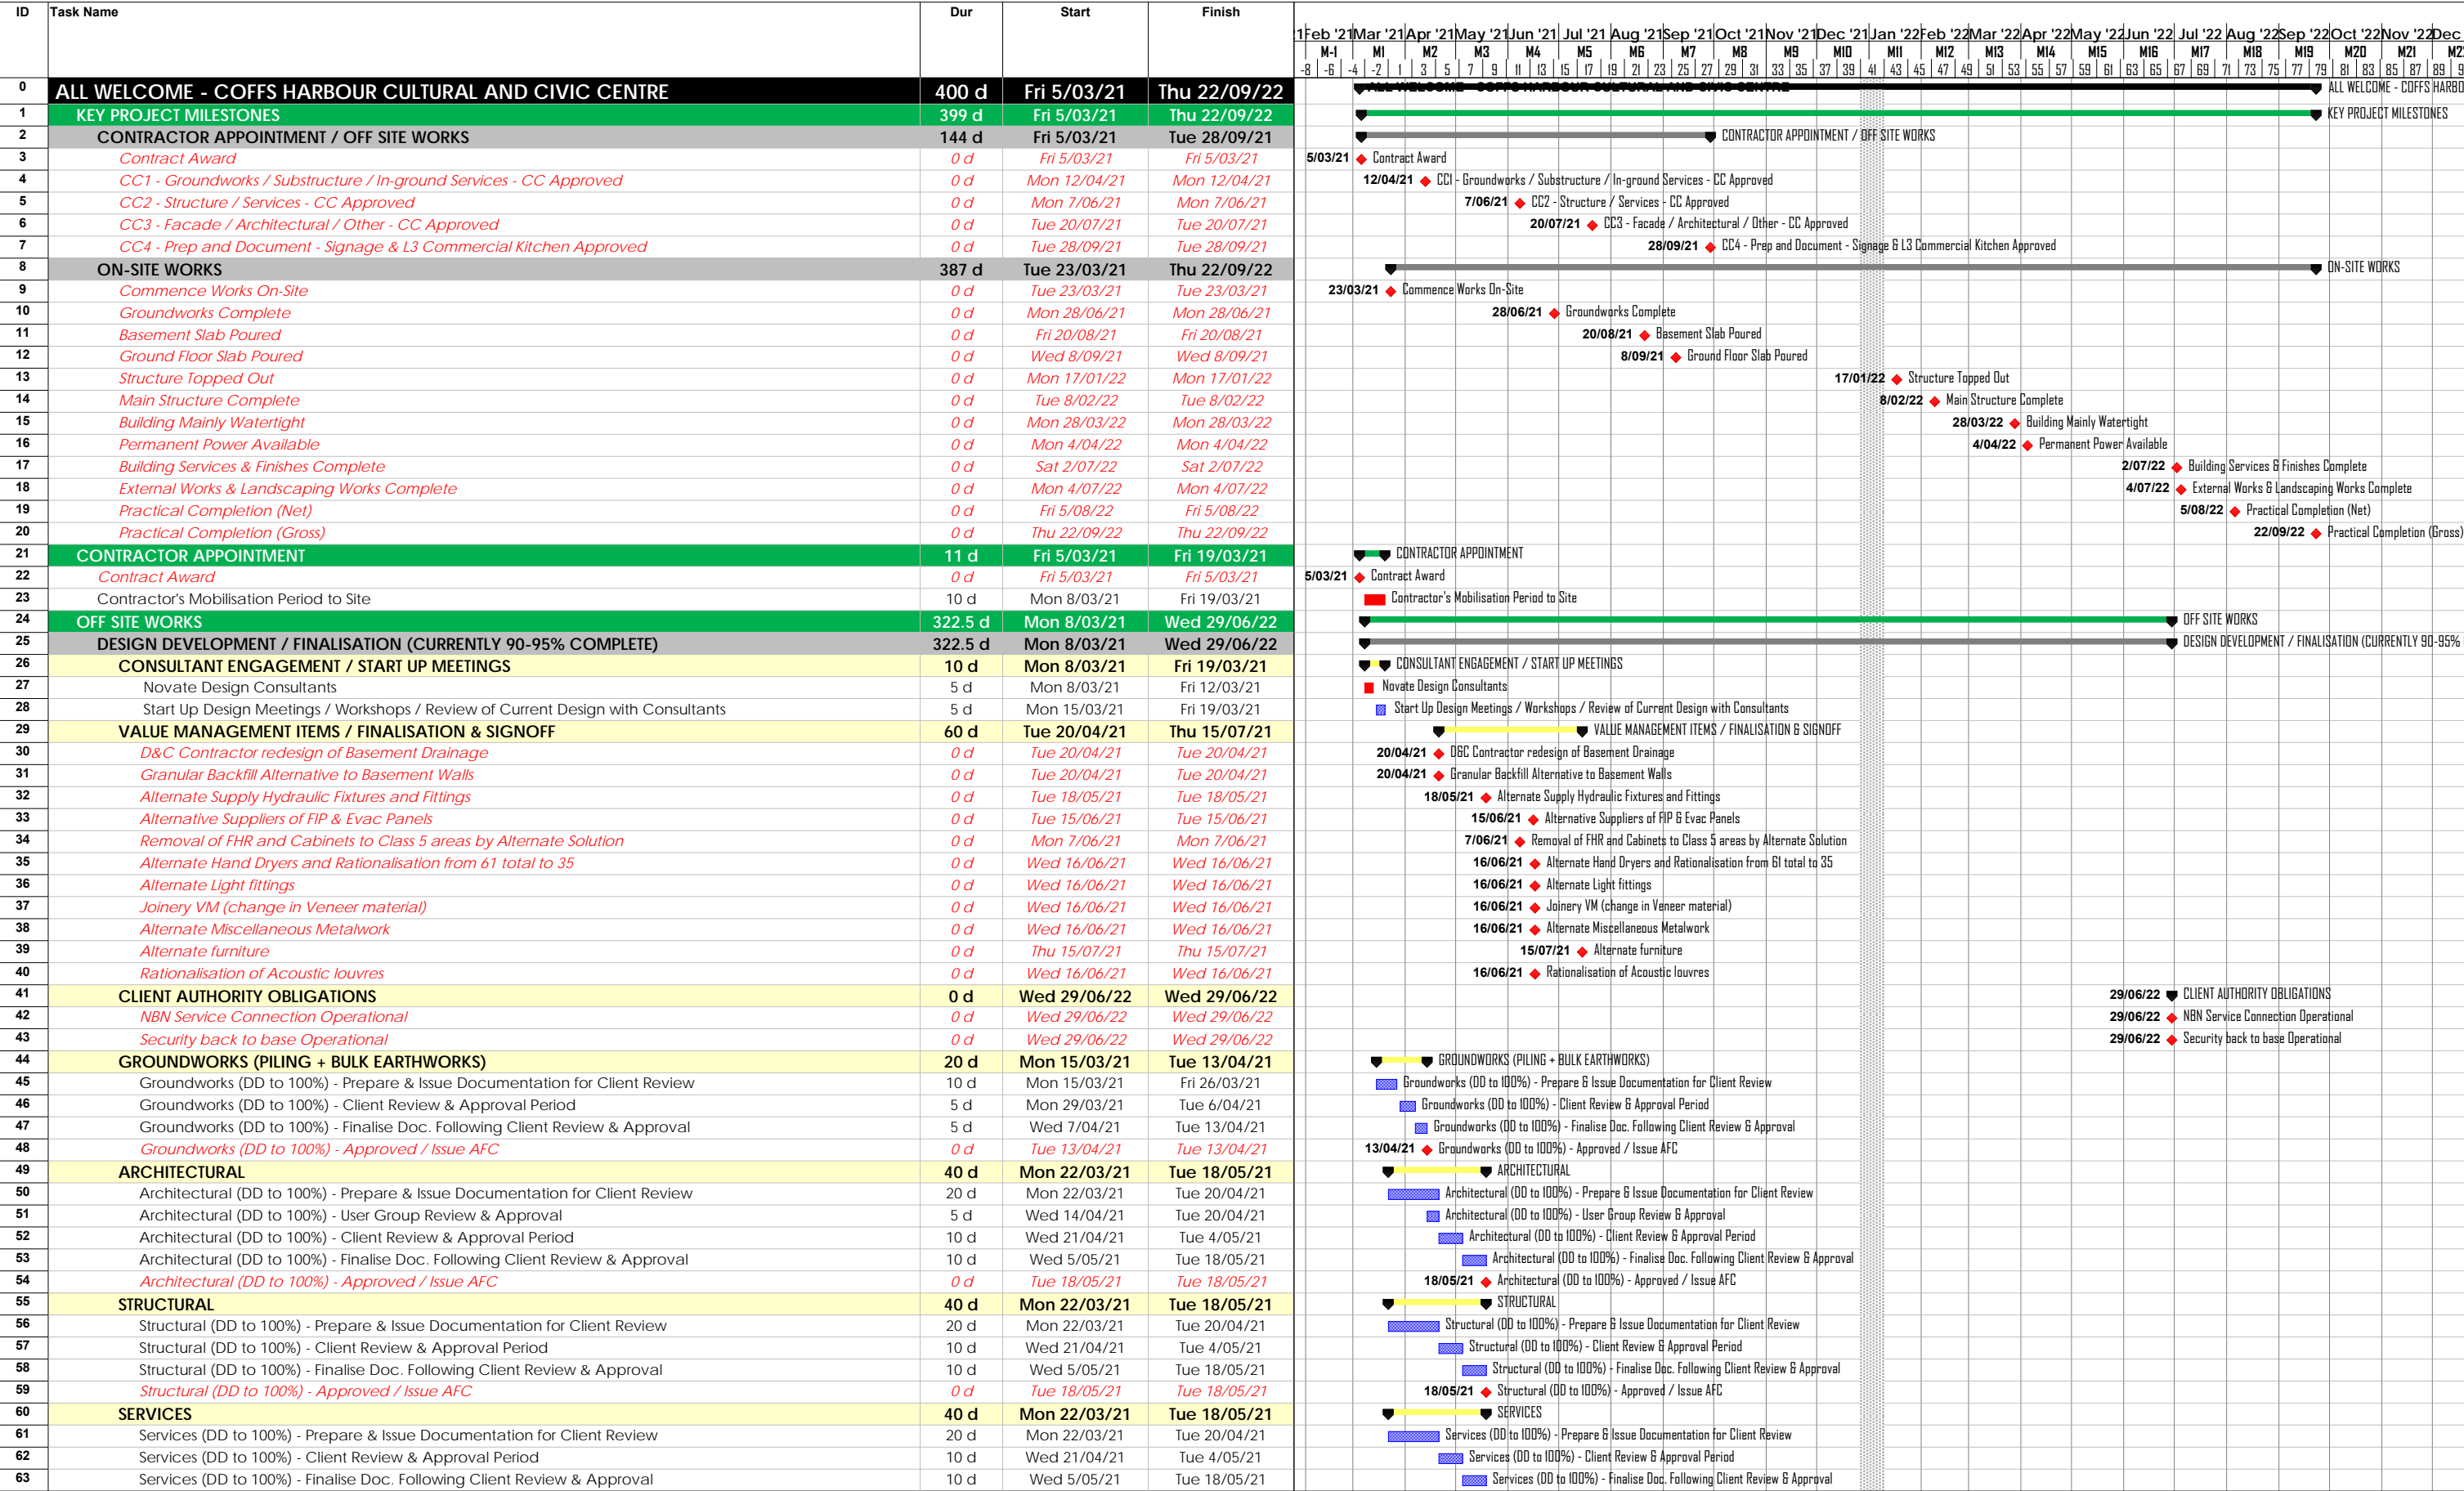

Date : 10/03/21
Planner : MF Checked: BG
Revision : A

COFFS HARBOUR CULTURAL & CIVIC CENTRE "ALL WELCOME"
GORDON STREET COFFS HARBOUR, NSW
CONTRACT PROGRAMME



ID	Task Name	Dur	Start	Finish	1Feb '21	Mar '21	Apr '21	May '21	Jun '21	Jul '21	Aug '21	Sep '21	Oct '21	Nov '21	Dec '21	Jan '22	Feb '22	Mar '22	Apr '22	May '22	Jun '22	Jul '22	Aug '22	Sep '22	Oct '22	Nov '22	Dec '22																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																						
					-8	M-1 -6	M1 -4	1	M2 3	M3 5	M4 7	M5 9	M6 11	M7 13	M8 15	M9 17	M10 19	M11 21	M12 23	M13 25	M14 27	M15 29	M16 31	M17 33	M18 35	M19 37	M20 39	M21 41	M22 43	M23 45	M24 47	M25 49	M26 51	M27 53	M28 55	M29 57	M30 59	M31 61	M32 63	M33 65	M34 67	M35 69	M36 71	M37 73	M38 75	M39 77	M40 79	M41 81	M42 83	M43 85	M44 87	M45 89	M46 91																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																												
64	Services (DD to 100%) - Approved / Issue AFC	0 d	Tue 18/05/21	Tue 18/05/21																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																													

Critical Task  Non-critical  Milestone  Project Summary  Summary  Split  Complete Milestone Progress

Date : 10/03/21
Planner : MF Checked: BG
Revision : A

COFFS HARBOUR CULTURAL & CIVIC CENTRE "ALL WELCOME"
GORDON STREET COFFS HARBOUR, NSW
CONTRACT PROGRAMME



ID	Task Name	Dur	Start	Finish	1Feb '21	Mar '21	Apr '21	May '21	Jun '21	Jul '21	Aug '21	Sep '21	Oct '21	Nov '21	Dec '21	Jan '22	Feb '22	Mar '22	Apr '22	May '22	Jun '22	Jul '22	Aug '22	Sep '22	Oct '22	Nov '22	Dec '22																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																													
					-8	-6	-4	-2	1	3	5	7	9	11	13	15	17	19	21	23	25	27	29	31	33	35	37	39	41	43	45	47	49	51	53	55	57	59	61	63	65	67	69	71	73	75	77	79	81	83	85	87	89	91																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																		
128	Structure (Concrete) - Tender, Evaluate & Award	20 d	Mon 8/03/21	Tue 6/04/21																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																				</

Critical Task Non-critical Milestone Project Summary Summary Split Complete Milestone Progress

Date : 10/03/21
Planner : MF Checked: BG
Revision : A

COFFS HARBOUR CULTURAL & CIVIC CENTRE "ALL WELCOME"
GORDON STREET COFFS HARBOUR, NSW
CONTRACT PROGRAMME

[illegible]

Critical Task Non-critical Milestone Project Summary Summary Split Complete Milestone Progress

Date : 10/03/21
Planner : MF Checked: BG
Revision : A

COFFS HARBOUR CULTURAL & CIVIC CENTRE "ALL WELCOME"
GORDON STREET COFFS HARBOUR, NSW
CONTRACT PROGRAMME



ID	Task Name	Dur	Start	Finish	1 Feb '21	2 Mar '21	3 Apr '21	4 May '21	5 Jun '21	6 Jul '21	7 Aug '21	8 Sep '21	9 Oct '21	10 Nov '21	11 Dec '21	12 Jan '22	13 Feb '22	14 Mar '22	15 Apr '22	16 May '22	17 Jun '22	18 Jul '22	19 Aug '22	20 Sep '22	21 Oct '22	22 Nov '22	23 Dec '22																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																													
					M-1 -8	M1 -6	M1 -4	M2 -2	M2 1	M3 3	M3 5	M3 7	M3 9	M4 11	M4 13	M5 15	M5 17	M5 19	M6 21	M7 23	M7 25	M8 27	M8 29	M9 31	M9 33	M10 35	M10 37	M11 39	M11 41	M12 43	M12 45	M13 47	M13 49	M14 51	M14 53	M15 55	M15 57	M16 59	M16 61	M17 63	M17 65	M18 67	M18 69	M19 71	M19 73	M20 75	M20 77	M21 79	M21 81	M22 83	M22 85	M22 87	M22 89	M22 91																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																		
256	POUR 3	13 d	Wed 18/08/21	Thu 2/09/21																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																				

Critical Task Non-critical Milestone Project Summary Summary Split Complete Milestone Progress

COFFS HARBOUR CULTURAL & CIVIC CENTRE "ALL WELCOME"
GORDON STREET COFFS HARBOUR, NSW
CONTRACT PROGRAMME



ID	Task Name	Dur	Start	Finish	1Feb '21	M-1	Mar '21	M1	M2	M3	M4	M5	M6	M7	M8	M9	M10	Nov '21	Dec '21	Jan '22	Feb '22	Mar '22	Apr '22	May '22	Jun '22	Jul '22	Aug '22	Sep '22	Oct '22	Nov '22	Dec '22																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																			
					-8	-6	-4	-2	1	3	5	7	9	11	13	15	17	19	21	23	25	27	29	31	33	35	37	39	41	43	45	47	49	51	53	55	57	59	61	63	65	67	69	71	73	75	77	79	81	83	85	87	89	91																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																												
320	Level 6 (Pour 1) - Install Reo / Services / Edge Boards	4 d	Tue 11/01/22	Fri 14/01/22																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																														

Date : 10/03/21
Planner : MF Checked: BG
Revision : A

COFFS HARBOUR CULTURAL & CIVIC CENTRE "ALL WELCOME"
GORDON STREET COFFS HARBOUR, NSW
CONTRACT PROGRAMME



ID	Task Name	Dur	Start	Finish	1 Feb '21	2 Mar '21	3 Apr '21	4 May '21	5 Jun '21	6 Jul '21	7 Aug '21	8 Sep '21	9 Oct '21	10 Nov '21	11 Dec '21	12 Jan '22	13 Feb '22	14 Mar '22	15 Apr '22	16 May '22	17 Jun '22	18 Jul '22	19 Aug '22	20 Sep '22	21 Oct '22	22 Nov '22	23 Dec '22																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																												
					M-1 -8	M1 -6	M1 -4	M2 -2	M2 1	M3 3	M3 5	M3 7	M3 9	M4 11	M4 13	M5 15	M5 17	M6 19	M6 21	M7 23	M7 25	M8 27	M8 29	M9 31	M9 33	M10 35	M10 37	M11 39	M11 41	M12 43	M12 45	M13 47	M13 49	M14 51	M14 53	M15 55	M15 57	M16 59	M16 61	M17 63	M17 65	M18 67	M18 69	M19 71	M19 73	M20 75	M20 77	M21 79	M21 81	M22 83	M22 85	M22 87	M22 89	M22 91																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																	
384	External Applied Finishes / Louvres / Seal	21 d	Tue 8/03/22	Mon 4/04/22																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																			

Critical Task Non-critical Milestone Project Summary Summary Split Complete Milestone Progress

Date : 10/03/21
Planner : MF Checked: BG
Revision : A

COFFS HARBOUR CULTURAL & CIVIC CENTRE "ALL WELCOME"
GORDON STREET COFFS HARBOUR, NSW
CONTRACT PROGRAMME

[illegible]

Critical Task Non-critical Milestone Project Summary Summary Split Complete Milestone Progress

Date : 10/03/21
Planner : MF Checked: BG
Revision : A

COFFS HARBOUR CULTURAL & CIVIC CENTRE "ALL WELCOME"
GORDON STREET COFFS HARBOUR, NSW
CONTRACT PROGRAMME



ID	Task Name	Dur	Start	Finish	1 Feb '21	Mar '21	Apr '21	May '21	Jun '21	Jul '21	Aug '21	Sep '21	Oct '21	Nov '21	Dec '21	Jan '22	Feb '22	Mar '22	Apr '22	May '22	Jun '22	Jul '22	Aug '22	Sep '22	Oct '22	Nov '22	Dec '22																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																														
					M-1	M1	M2	M3	M4	M5	M6	M7	M8	M9	M10	M11	M12	M13	M14	M15	M16	M17	M18	M19	M20	M21	M22																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																														
					-8	-6	-4	-2	1	3	5	7	9	11	13	15	17	19	21	23	25	27	29	31	33	35	37	39	41	43	45	47	49	51	53	55	57	59	61	63	65	67	69	71	73	75	77	79	81	83	85	87	89	91																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																			
512	Wet Areas - Wall & Floor Tiling	9 d	Mon 28/02/22	Thu 10/03/22																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																					

Critical Task Non-critical Milestone Project Summary Summary Split Complete Milestone Progress

Date : 10/03/21
Planner : MF Checked: BG
Revision : A

COFFS HARBOUR CULTURAL & CIVIC CENTRE "ALL WELCOME"
GORDON STREET COFFS HARBOUR, NSW
CONTRACT PROGRAMME



ID	Task Name	Dur	Start	Finish	1 Feb '21	2 Mar '21	3 Apr '21	4 May '21	5 Jun '21	6 Jul '21	7 Aug '21	8 Sep '21	9 Oct '21	10 Nov '21	11 Dec '21	12 Jan '22	13 Feb '22	14 Mar '22	15 Apr '22	16 May '22	17 Jun '22	18 Jul '22	19 Aug '22	20 Sep '22	21 Oct '22	22 Nov '22	23 Dec '22																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																					
					M-1	M	M+1	M+2	M+3	M+4	M+5	M+6	M+7	M+8	M+9	M+10	M+11	M+12	M+13	M+14	M+15	M+16	M+17	M+18	M+19	M+20	M+21	M+22																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																				
					-8	-6	-4	-2	1	3	5	7	9	11	13	15	17	19	21	23	25	27	29	31	33	35	37	39	41	43	45	47	49	51	53	55	57	59	61	63	65	67	69	71	73	75	77	79	81	83	85	87	89	91																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																										
576	Lay Floor Finishes	9 d	Wed 4/05/22	Sat 14/05/22																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																												

Critical Task Non-critical Milestone Project Summary Summary Split Complete Milestone Progress

Date : 10/03/21
Planner : MF Checked: BG
Revision : A

COFFS HARBOUR CULTURAL & CIVIC CENTRE "ALL WELCOME"
GORDON STREET COFFS HARBOUR, NSW
CONTRACT PROGRAMME

[illegible]

Critical Task Non-critical Milestone Project Summary Summary Split Complete Milestone Progress
