

Construction Parking and Access Strategy

M4-M5 Link Mainline Tunnels

March 2021



THIS PAGE LEFT INTENTIONALLY BLANK

Document control

Title	WestConnex M4-M5 Link Mainline Tunnels – Construction Parking and Access Strategy
Document No/Ref	M4M5-LSBJ-PRW-EN-MP01-PLN-0015-17
Document Path	

Version Control

Revision	Date	Description
Rev A	10/07/18	For internal review
Rev B	17/07/18	For SMC/Roads and Maritime review
Rev C	5/8/18	Updated in response to comments, for SMC/Roads and Maritime review
Rev01	15/8/2018	Updated in response to comments
Rev02	20/08/18	Updated in response to additional SMC/Roads and Maritime comments, for submission to DPE
Rev03	18/10/18	Internal Update
Rev04	09/11/18	Internal Update
Rev 05	12/11/18	LSBJV update, lodged with DPE for review
Rev 06	22/11/18	Updated to address DPE comments
Rev 07	13/12/18	Updated to address DPE comments
Rev 08	8/01/19	Updated to address DPE comments
Rev 09	16/01/19	Internal Update; for DPE approval
Rev 10	2/08/19	Updates following project changes – WestConnex Transurban review
Rev 11	12/08/19	Further update following WestConnex Transurban review
Rev 12	16/08/19	For DPIE approval
Rev 13	13/11/19	Updated to address DPIE comments – for DPIE approval
Rev 14	11/02/2020	Updated to incorporate Hawthorne Canal Grouting
Rev 15	20/02/2020	Updated following DPIE comment
Rev 16	28/02/2020	Updated following DPIE comment
Rev 17	5/11/2020	Updated following DPIE comment

Revision	Date	Description
Rev 18	22/01/2021	Internal Update
Rev 19	03/03/2021	Updated following DPIE comment

Internal Review

Role	Name	Position	Date	Signed/Authorised
Originator(s)	Denis Fung	Traffic Manager		
Authorised	Andrew Marsonet	Project Director		

Glossary

Acronym	Definition
AS	Australian Standard
CCS	Community Communication Strategy
CEMP	Construction Environmental Management Plan
CIC	Community Information Centre
CSSI	Critical State Significant Infrastructure
CTAMP	Construction Traffic and Access Management Plan (addressed as the Project Traffic and Transport and Access Management Plan)
DPE	Department of Planning and Environment
DPIE	Department of Planning, Industry and Environment
EIS	Environmental Impact Statement
IC	Independent Certifier
LSBJV	Lend Lease Bouygues Samsung Joint Venture
MUTCD	Manual of Uniform Traffic Control Devices
PBR	Pymont Bridge Road Tunnel Compound
PRVF	Haberfield Civil Site aka Parramatta Road Ventilation Facility
QA	Quality Assurance
REMM	Revised Environmental Mitigation Measure
RTA	Roads and Traffic Authority
SMC	Sydney Motorway Corporation
SPI	St Peters Interchange, Campbell Road Tunnel Compound
SPIR	Submission and Preferred Infrastructure Report
SWTC	Scope of Works and Technical Criteria

Acronym	Definition
TMSP	Traffic Management and Safety Plan (Same as TTAMP)
TTAMP	Traffic and Transport and Access Management Plan

Contents

Document control.....	3
1. Introduction.....	9
1.1 Project Background.....	9
1.2 Purpose.....	9
1.3 Objectives.....	9
2. Management Requirements.....	9
2.1 Ministers Conditions of Approval.....	9
2.2 Revised Environmental Management Measures.....	13
2.3 Relevant Legislation and Guidelines.....	13
3. Surface Sites & Parking Facilities.....	14
3.1 Surface sites.....	14
3.2 Worker Parking Availability and Demand.....	14
3.3 Northcote Street Civil Site.....	17
3.4 Parramatta Road East and Parramatta Road West.....	18
3.5 Parramatta Road Ventilation Facility.....	18
3.6 Wattle Street Tunnel Compound.....	18
3.7 Pyrmont Bridge Road Tunnel Compound.....	19
3.8 St Peters (Campbell Road) Tunnel Compound.....	19
3.9 Main Project Office.....	19
3.10 Royal Prince Alfred Hospital Carpark & RPA Medical Centre Carpark.....	20
3.11 Canal Road & Hawthorne Parade Surface Grout area.....	20
4. Shuttle Service & Worker Transport.....	20
4.1 Routes.....	20
4.2 Timing.....	22
4.3 Monitoring.....	22
5. On-street Parking Removal.....	23
5.1 Pyrmont Bridge Road.....	24
5.2 Parramatta Road East and Parramatta Road West.....	25
5.3 Canal Road & Hawthorne Parade Surface Grout area.....	26
5.4 Parking Availability.....	27
5.5 Parking demand.....	29
5.6 Conclusion of the Parking Demand Survey.....	32
5.7 Mitigation Measures.....	33
6. Access Control and Safety.....	34
6.1 Pedestrian Interface with Driveways.....	34
6.2 Visitors.....	34
7. Consultation.....	34
8. Training, Monitoring & Reporting.....	35
8.1 Training.....	35
8.2 Workforce Code of Conduct.....	36
8.3 Monitoring.....	36

8.4	Reporting.....	37
9.	Contingency.....	37
9.1	Modification to Bus Services	37
9.2	Repurpose Existing Parking Arrangements	37
9.3	Additional Overflow Parking	37
9.4	Public Transport Encouragement	37
9.5	Active Transport Encouragement	38
9.6	Re-education and Correction	38
9.7	Shift Structures	38
APPENDIX A – Other Conditions of Approval and Revised Environmental Management Measures relevant to this Plan.....		39
APPENDIX B – Parking Survey Summary		41
APPENDIX C – Inner West Council Meeting Minutes.....		42
APPENDIX D – City of Sydney Meeting Minutes		43
APPENDIX E –Transport for NSW Consultation Record		44
APPENDIX F – Community Consultation Summary.....		45
APPENDIX G – Surface grouting Consultation Summary		46

1. Introduction

1.1 Project Background

The M4-M5 Link Environmental Impact Statement (EIS) (AECOM 2017) assessed the impacts of construction and operation of the Project on traffic and transport, within Chapter 08 and Appendix H (Technical working paper: Traffic and transport). Traffic and transport considerations were further developed in the Submissions and Preferred Infrastructure Report (SPIR) and the WestConnex M4-M5 Link Mainline Tunnel Modification report (September 2018).

These documents identified the potential for impacts on traffic during construction typically associated with parking and access. However, it concluded any potential impacts could be managed by the standard mitigation and management measures that are described in this Construction Parking and Access Strategy (the Strategy).

The WestConnex M4-M5 Link project is being constructed in two stages:

- Stage 1 (the Project and subject of this document): M4-M5 Link Mainline tunnels
- Stage 2: Rozelle interchange.

WestConnex Transurban has engaged Lendlease Samsung Bouygues Joint Venture (LSBJV) to design and construct Stage 1 of the project.

The key features of the Mainline tunnels project are described in Section 1.3 of the Construction Environmental Management Plan (CEMP).

1.2 Purpose

This Strategy will outline potential parking impacts related to construction of the Project, and the proposed mitigation measures to minimise parking and access impacts. In addition, the strategy sets out mechanisms to monitor the effectiveness of mitigation measures and provides contingency options if measures are found to be unsuccessful.

This Strategy has been prepared to address the requirements of the Minister's Conditions of Approval (CoA), EIS and the Revised Environmental Management Measures (REMM) listed in the SPIR.

This Strategy was submitted to the Secretary for approval at least one (1) month prior to the commencement of any works that impact parking.

1.3 Objectives

LSBJV is committed to delivering the Project in a way that minimises impacts on parking and access through the implementation of reasonable and feasible mitigation measures.

To achieve the above objectives this Strategy will outline:

- The proposed methodology for transporting site staff and workforce between Project sites
- Available parking at each of the sites
- The proposed impacts to existing parking
- Limitations and restrictions to be placed on site staff and workforce
- Monitoring effectiveness
- Reporting of effectiveness of parking management strategy

2. Management Requirements

2.1 Ministers Conditions of Approval

The CoAs relevant to this Strategy are listed in Table 1 below. Note that some traffic related CoAs will be managed through the Traffic and Transport and Access Management Plan (TTAMP) sub plan of the CEMP,

which will be approved by the Department of Planning, Industry and Environment (DPIE) in accordance with CoA C4-C6. A cross reference is also included to indicate where the condition is addressed in this Strategy or other project management documents as appropriate.

Table 1 – CoA Compliance Table

Reference	Requirement	Section	How addressed
CoA E54	The Strategy must include, but not necessarily be limited to:		
(a)	Confirmation and timing of the removal of on- and off-street parking associated with construction of the CSSI;	Section 5 On-street Parking Removal	Section 5 of this Strategy includes details about the removal of on- and off-street parking associated with the relevant ancillary construction facilities.
(b)	Parking surveys of all parking spaces to be removed to determine current demand during peak, off-peak, school drop off and pickup, and weekend periods;	Section 5.3 Parking	Section 5.3 provide details about the parking surveys which have been completed at the Paramatta Road East & West civil sites (PRE&W) and Pyrmont Bridge Road tunnel site (PBR) sites during October 2018.
(c)	Consultation with affected stakeholders utilising existing on- and off-street parking stock which will be impacted as a result of construction;	Section 7 Consultation	Details about the consultation to be undertaken with stakeholders impacted as a result of construction are provided in Section 7. Mitigation measures will be determined as a result of consultation with local businesses and residents to bet manage the impacts of proposed on-street parking removals.
(d)	Assessment of the impacts of changes to on- and off-street parking stock taking into consideration outcomes of consultation with affected stakeholders;	Section 5.3 Parking Section 7 Consultation	The impacts are addressed in Section 5.3 and Section 7. Parking surveys and consultation will be used to assess the impacts and determine the most feasible mitigation measures.
(e)	Identification of mitigation measures to manage impacts to stakeholders as a result of on- and off-street parking changes including, but not necessarily limited to, staged removal and replacement of parking, provision of alternative parking arrangements, managed staff parking arrangement and working with relevant council(s) to introduce parking restrictions adjacent to work sites and compounds;	Section 7 Consultation	Refer to response for CoA E54(d).
(f)	Provision of a shuttle bus service(s) to transport workers to site(s) and details of the shuttle bus service(s), including service timing and frequency;	Section 3.1 Section 4 Shuttle Service & Worker Transport	Section 3 and 4 of this Strategy discusses the shuttle bus services that will be provided for the Project, as well as the planned shuttle bus routes.
(g)	Mechanisms for monitoring, over appropriate intervals, to determine the effectiveness of implemented mitigation measures;	Section 8.3 Monitoring	There will be an ongoing monitoring process for the Project, which will include the monitoring of effectiveness of mitigation measures. Further details are provided in Section 8.3.
(h)	Provision of contingency measures should the results of mitigation monitoring indicate implemented measure are ineffective; and	Section 9 Contingency	If monitoring, surveys, consultation or complaints prompt intervention by the Project to improve or otherwise modify services, one or more of the options discussed in Section 9 may be enacted to ensure impacts to public are reduced and public relations and reputation is protected.

Reference	Requirement	Section	How addressed
(i)	Provision of reporting of monitoring results to the Secretary and relevant council(s) at three (3) monthly intervals.	Section 8.4 Reporting	Monthly and quarterly reporting commitments are detailed in Section 8.4.

Please refer to Appendix A for all other CoA relevant to the development of this Plan.

2.2 Revised Environmental Management Measures

The REMMs applicable to construction parking and access are listed in Appendix A. Note that other traffic related REMMs will be managed through the TTAMP sub plan of the CEMP which will be approved by the DPIE in accordance with CoA C4-C6.

2.3 Relevant Legislation and Guidelines

2.3.1 National Guides & Specifications

- Austroads “Guide to Road Design Part 6A: Pedestrian & Cyclist Paths”
- Austroads Guide to Traffic Management -Part 3 - Traffic Studies Analysis
- Austroads “Cycling Aspects of Austroads Guides”
- Austroads “Guide to Road Design Part 3: Geometric Design (2nd Edition)”
- Austroads “*Guide to Road Design Part 4: Intersections and Crossings – General*”
- Austroads “Guide to Road Design Part 4A: Un-signalised and Signalised Intersections”
- Austroads “Guide to Road Design Part 4C: Interchanges”
- Austroads “Guide to Road Design Part 6: Roadside Design, Safety & Barriers”
- Austroads “Guide to Traffic Management Part 6: Intersections, Interchanges & Crossings”
- Austroads Paper – G34_13 “Design Vehicles & Turning Path Templates”
- Austroads Paper – R211_2 “Geometric Design for Trucks”
- Austroads Paper – R337_09 “National Approach to Traffic Control at Work Sites”
- AS 1742.1 “MUTCD, Part 1: General introduction and index of signs”
- AS1742.2 “MUTCD, Part 2: Traffic Control devices for general use”
- AS 1742.3 “MUTCD, Part 3: Traffic control for works on roads”
- AS1742.15 “MUTCD, Part 15: Direction signs, information signs and route numbering”

2.3.2 Jurisdictional Requirements

- Roads and Maritime Supplements to Austroads
- RTA Road Design Guide
- Roads and Maritime “QA Specification G10: Traffic Management”
- RTA “Accident Reduction Guide – Part 2: Road Safety Audits”
- RTA “Delineation Guidelines: Parts 1 to 19
- RTA “Guidelines for Road Safety Audit Practices:”
- Roads and Maritime “Traffic Control at Worksites Manual”

2.3.3 Client Specifications

- SWTC Appendix C.1
- SWTC Appendix C.4
- SWTC Appendix C.6
- *Ministers Conditions of Approval*

2.3.4 Lendlease Procedures

- LLE1107 – Traffic Management Procedure
- LLE Global Minimum Requirements
- Project TMSP (M4M5-MT-3D-TrafficMgmt & Safety) document

3. Surface Sites & Parking Facilities

3.1 Surface sites

LSBJV will endeavour to maximise car parking facilities within its compound and work areas in order to minimise parking on local roads and streets in accordance with CoA E54.

This will be achieved through the implementation of 'satellite parking facilities', which refers to the nominated parking areas at Parramatta Road East civils site (C3b) and the Parramatta Road West civil site (C1b) (PRE&W). These sites have been specifically prepared to provide parking for Wattle Street civil and tunnel site (C1a) (Wattle Street ramps), Northcote Street civil site (C3a) (Northcote Site), as well as the Haberfield civil site (C2b) (Parramatta Road Ventilation Facility (PVRF)). Site staff and workforce located at the Haberfield sites (Wattle Street ramps, Northcote Site, and the PRVF) will park at PRE&W site and walk to the various work locations due to their close proximity to the parking location.

The main parking for the Pyrmont Bridge Road tunnel site (C9) (PBR) will be at the private parking station at the Royal Prince Alfred Hospital (RPA). The main parking for the Campbell Road civil and tunnel site (C10), St Peters will be on site in line with an increased workforce from January 2020 when additional land is available to the Project Team.

In terms of on-street parking impacts (the removal of formal parking locations), the Project will have limited impacts on existing street parking allowances, as many of the parking spaces that are proposed to be removed are associated with adjacent buildings that are now being used by the Project.

3.2 Worker Parking Availability and Demand

Worker parking demand will vary throughout delivery of the project, from early works through to major construction and finally tunnel fit-out. Table 2 outlines the indicative peak worker numbers and parking capacity at parking areas throughout the construction period.

This table does not account for workers travelling via alternate means of transport including public transport, by foot or by bicycle or carpooling of workers, which would reduce staff and workforce parking demand at each location.

Where parking demand exceeds on site capacity, on-street parking will be utilised in combination with implementing contingency measures detailed in Section 9.

LSBJV's approach to parking and access is compliant with the requirements of CoA E52 (a) that is, to minimise on street parking by the workforce.

Table 2 – Indicative Parking Availability vs Worker Demand

Timing	Haberfield Sites (combined)		Pymont Bridge Road			Campbell Road, St Peters		Hawthorne Canal Grouting	
	Indicative Total Workforce ¹	Indicative On-site Carparks ²	Indicative Total Workforce ¹	Indicative On-site Parking	Indicative Carparks (RPA)	Indicative Total Workforce ¹	Indicative On-site Parking	Indicative Total Workforce ¹	Indicative On-site Parking
2018 (2nd half)	50	46	25	20 (During demolition)	0	50	30	0	0
2019 (1st half)	150	235	100	10	0	80	30	0	0
2019 (2nd half)	200	235	260	10	150	80	30	0	0
2020 (1st half)	260	235	260	10	210	260	270	10	10
2020 (2nd half)	260	235	260	10	210	225	176	10	10
2021 (1st half)	260	235	260	10	210	225	176	0	0
2021 (2nd half)	260	235	260	10	210	225	176	0	0
2022 (1st Half)	260	235	260	10	210	225	176	0	0
2022 (2nd Half)	260	235	260	10	210	225	176	0	0
2023 (1st Half)	150	235	150	10	50	150	176	0	0

¹ The total indicative workforce is spread over about four separate shifts. It is therefore highly unlikely that this number of workers would be on-site at any one time.

² This excludes four spaces (including one DDA compliant spaces) to be kept available for public use for the Community Information Centre.

Table 3 – SPI Local Roads Parking Demand

	Parking Occupancy						
Road	Total Capacity	21/12/2020	22/12/2020	4/01/2021	5/01/2021		11/01/2021
Burrows Road	205		134	134			191
Barwon Park Road	98		91	95			98
Crown Street	32		24	26			28
Campbell St (Between Princess Hwy and May St)	33		29		32		31
Euston Rd Southbound (clearway)	70	20		17	19		31
Euston Rd Northbound (clearway)	80	0		0	14		0
SPI Carpark	140		130	136			144

3.3 Northcote Street Civil Site

3.3.1 Site Information

The Northcote site is located between Wattle Street and Wolseley Street at Haberfield. This facility is positioned on land that is previously used as a construction ancillary facility for the M4 East project and was identified in the Project planning phase as a civil ancillary facility.

Due to spatial constraints, this site will have very limited parking and no designated light vehicle parking within the compound.

3.3.2 Parking Demand

Staff and workforce parking will be limited on site, workers will need to park at PRE&W and walk (preferred route identified in Figure 1) to the Northcote site and Wattle Street ramps.

Note, the walking route shown in Figure 1 passes around four residential properties, three of which are used for non-residential purposes otherwise the walking route is behind the new noise walls constructed as part of the M4 East Project.

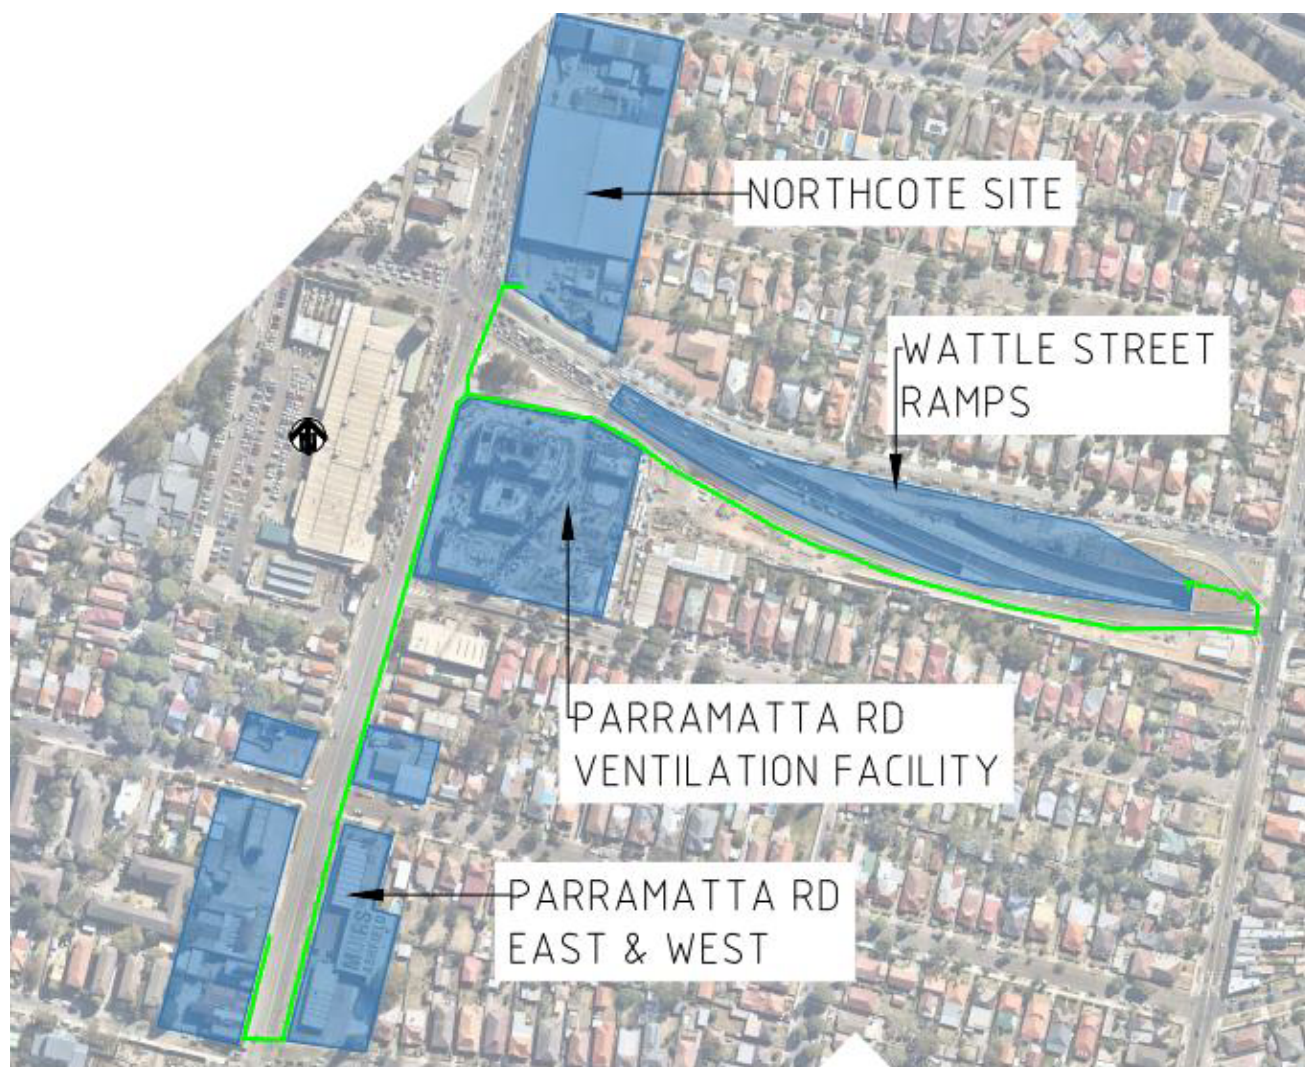


Figure 1 – Walking access route (Green line) to the Northcote Site, Wattle St Ramps and Parramatta Rd Vent Facility

3.4 Parramatta Road East and Parramatta Road West

3.4.1 Site Information

The PRE&W site will have a combined parking area for around 235 light vehicles in addition to a material laydown area for trucks. The parking spaces in this location will primarily service this facility, the Wattle Street ramps, the PRVF and the Northcote site. Workforce, staff and visitors will access the work locations via pedestrian access to minimise the need for parking at each of the other sites.

It is proposed that the Community Information Centre (CIC) will be located at this location and accessed by the public. There will be designated parking spaces for CIC visitors and clearly delineated pedestrian route from the street.

3.4.2 Parking Demand

During establishment of PRE&W, parking will be available on site for the workforce and staff. There may however be some limited times when parking is not permitted due to safety requirements during demolition and other works. During these periods, on street parking will be utilised.

During the peak tunnelling and construction phases, workforce and staff numbers around the Haberfield area are expected to grow to around 260 workers. It is proposed that the vast majority of the Haberfield workforce and staff will be parking at the PRE&W site daily, prior to attending works. An electronic tag system will be located at PRE&W for all Haberfield sites for the staff and workforce.

3.5 Parramatta Road Ventilation Facility

3.5.1 Site Information

The activities required in this location include the fit out (mechanical and electrical) of the ventilation fan shaft constructed by the M4 East project.

3.5.2 Parking Demand

Works are proposed to commence in this location in 2019 and are not planned for completion until the latter stages of the project. Worker parking is not proposed at this location. Only construction vehicles and deliveries will be permitted at the site.

The ventilation facility will have a limited demand for worker parking during site establishment, as the site will be already established (as part of M4 East project works). There will be no parking possible on site during the works with parking to be provided at the PRE&W parking facilities.

Parking for the site will be provided by the PRE&W facility, with pedestrian access to this site.

3.6 Wattle Street Tunnel Compound

3.6.1 Site Information

Due to spatial constraints, no parking will be provided at the Wattle Street ramps site other than for project vehicles and deliveries. Workforce, staff and visitors will park at and walk between the PRE&W site and Wattle Street using existing footpaths. A shuttle service will also be provided for the workforce to travel between Wattle St and Northcote site.

3.6.2 Parking Demand

During site establishment, parking will be available at the PRE&W site. Similarly; during construction, no parking will be provided on site for light vehicles, only access and egress arrangements for material deliveries and spoil movements.

Parking for the site will be provided by the PRE&W facility.

3.7 Pyrmont Bridge Road Tunnel Compound

3.7.1 Site Information

The Pyrmont Bridge Road facility is a key construction compound for the Project due to its location approximately half way between the Haberfield sites and the Campbell Road St Peters facility. Demolition is required prior to its use as a tunnelling compound to remove commercial buildings for the installation of acoustic shed, site offices and other site components.

3.7.2 Parking Demand

A limited workforce is required during site establishment and demolition. Around 20 car parking locations will be available on site during this phase, with some demolition phases requiring that no parking is available on the site for safety and special constraint reasons. Excess parking during these phases will utilise existing on street parking locations.

Part of the site establishment process following demolition will be the creation of an onsite car park with a capacity of around 10 spaces. This parking facility will be used by the workforce with excess parking utilising on street parking locations. Once the overall facility is operational and supporting tunnelling, this car park will be used by senior staff, visitors and deliveries. The bulk of the workforce and staff will be parking at the RPA carpark.

3.8 St Peters (Campbell Road) Tunnel Compound

3.8.1 Site Information

Tunnelling operations from the southern part of the Project will be launched from this site. In addition, this site will hold the operational ventilation facility. Initially this site will have a limited workforce of around 80 which grows over time in line with the construction activities located at this site.

3.8.2 Parking Demand

A limited workforce was in place during the initial phases of construction as the facility was built and road headers became operational. Until 2020, around 30 light vehicle parking spaces were available inside the facility to provide parking for workforce, staff and visitors.

From early 2020 LSBJV were provided with additional land from the adjacent contractor which has largely been converted into an onsite car parking facility. Following establishment of this additional car park area in early 2020, around 151 LV vehicles and 10 motorcycles are able to park on site. From staff survey, excess parking demand during this peak parking period (approximately 85 vehicles) has been shown to be managed via staggered shift commencement and finishing times, utilisation of the shuttle bus service, carpooling, cycling, and a very small number of on street parking along Burrows Rd and Euston Rd.

A parking survey was completed on the 22nd of December 2020 and the 4th of January 2021 when the majority of local business were closed for the holidays while the project was operational. A subsequent survey undertaken on the 11th of January 2021, when the majority of local businesses were fully operational, shows that Burrows Road can accommodate both local parking and the project while maintaining spare parking capacity.

3.9 Main Project Office

The main Project Office will be located at Mascot on O'Riordan Street and is well connected to public transport via Sydney Buses and the train network at Mascot and Green Square Stations. The office will have parking for visitors and senior staff; around 80 spaces will be made available for the Project, with half of these spaces allocated to WestConnex Transurban / Roads and Maritime Services (Roads and Maritime) and Independent Certifier staff.

Additional nearby commercial parking space may be utilised pending agreement with relevant owner/occupier and will be investigated should proposed supply be insufficient.

3.10 Royal Prince Alfred Hospital Carpark & RPA Medical Centre Carpark

3.10.1 Site Information

The Royal Prince Alfred Hospital and the TPA Medical Centre parking facility will provide around 210 parking spaces, supporting the workforce at the PBR site. The carpark is located within a 10 minute walk to the PBR site. Workforce will walk along the existing footpath on Church Street or Missenden Road to Parramatta Road.

Consultation has been undertaken with Secure carparks for the use of the Royal Prince Alfred Medical Centre and Prince Alfred Hospital carparks to ensure the use of these car parks will not take away from parking for hospital and medical centre patrons.

3.11 Canal Road & Hawthorne Parade Surface Grout area

3.11.1 Site Information

The Canal Road and Hawthorne Parade area is a surface grouting area for the Project due to its location above the tunnel corridor near the Hawthorne Canal. Approximately five untimed carparking spaces along Hawthorne Parade will be required for the duration of the works in order to provide access to the working area on the western side of the canal. A further twenty informal and untimed car parking spots along Canal Road will be required by the proposal from time to time to allow works to progress safely on the eastern side of the canal.

3.11.2 Parking Demand

A limited workforce is expected during the setup and operation of the grouting works. Until September 2020, around 10 light vehicle parking spaces will be available inside the work areas for the workforce.

4. Shuttle Service & Worker Transport

A shuttle service will be provided, with mini-buses to transport site staff and workforce. Bus numbers, frequencies and sizes will be determined by demand.

Promotion of the shuttle bus services will be undertaken during the Project induction, regular toolbox training sessions and through posters and project newsletters.

As presented in Section 3 car parking at the PRE&W facility will service the Haberfield sites via existing pedestrian access. Those working at PBR site will primarily park at the RPA parking facility and walk to the compound.

Those working at the Campbell Road site are expected to park on site where possible or utilise public transport.

The electronic tag system will also allow those who choose to walk, bicycle or catch public transport to gain access directly to their worksite.

The effectiveness of the shuttle bus service will be reported on in the quarterly CPAS report.

4.1 Routes

The bus route proposed relates to the Wattle St site, Northcote site, and M&E Transfer Facility for light vehicles only (Figure 2 and 3). The Indicative route is shown below and may be adjusted depending on demand.

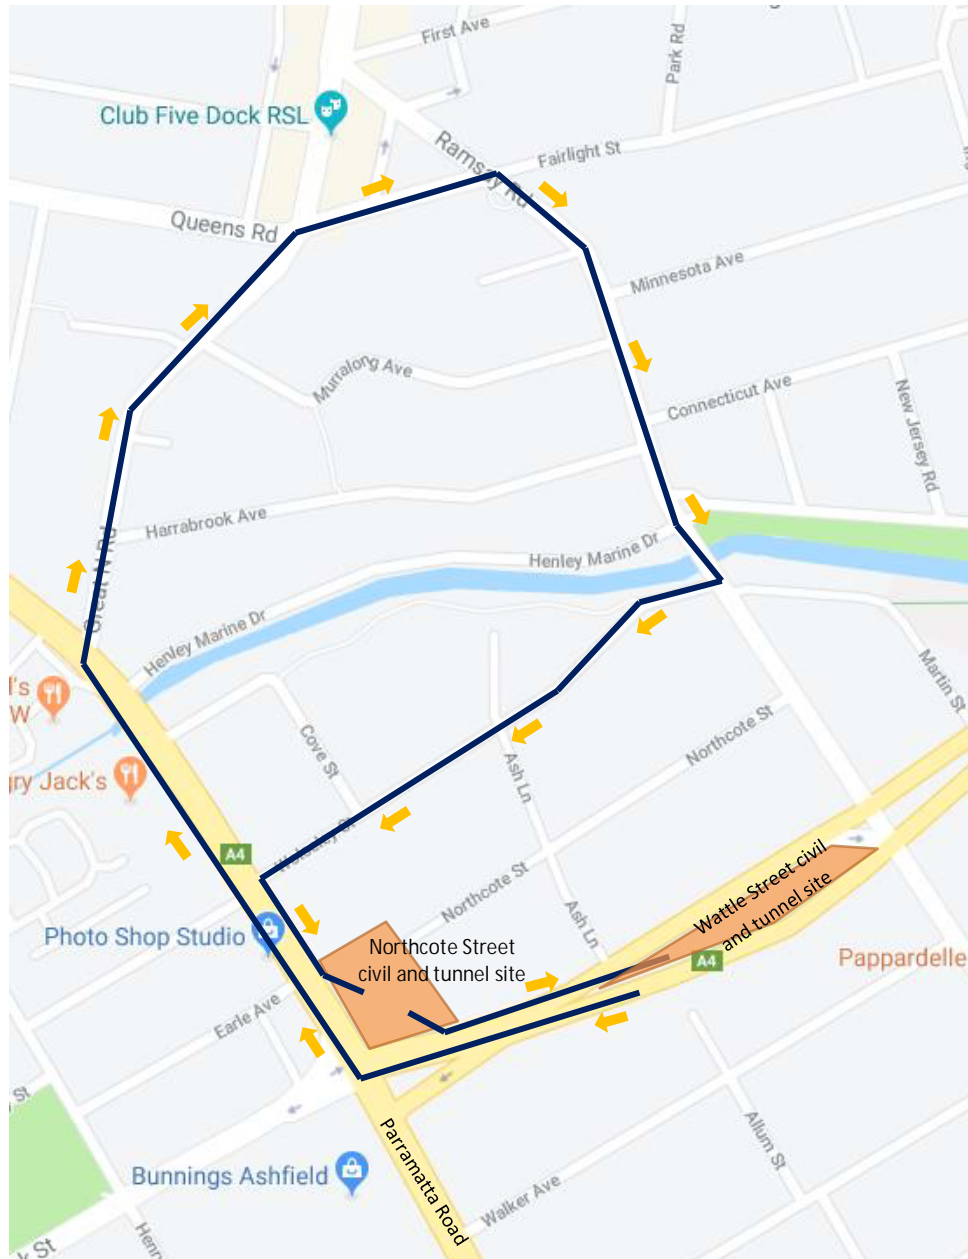


Figure 2 - Shuttle Bus Route – Wattle St to Northcote.



Figure 3 - Shuttle Bus Route –M&E Transfer Facility to Northcote.

4.2 Timing

Shuttle services will be provided on an as needs basis in line with shift patterns and times on a week to week basis during tunnelling works. During demand periods, this should see a bus reaching each site approximately every 15 to 20 minutes, or less when traffic congestion is low.

The proposed bus routes have travel times of between 7 and 15 minutes (depending on time of day). During peak traffic periods and worker shift changes additional services may be provided to try to limit waiting times to 15 minutes for any worker or staff member waiting for a shuttle. Inter-peak periods will have fewer services, due to the reduced delay due to traffic on the roads.

Worker shift times are expected to vary throughout the delivery of the project, typically however tunnel shifts are likely to commence at 6am and 6pm and run for between 10 and 12 hours. Efficiency or construction program (among other things) may be reasons for adjusting these shift times during delivery.

Additional bus services may be commissioned during peak periods to best cater for workforce volumes. The additional services will be arranged on an as needs basis.

4.3 Monitoring

The project conducts weekly parking inspections and quarterly parking surveys to evaluate the effectiveness of the mitigation measures. The effectiveness of the mitigation measures will be reported on in the quarterly CPAS report.

5. On-street Parking Removal

Some public on-street parking at the PRE&W, PBR, and Canal Road & Hawthorne Parade surface grout area locations will require temporary removal during establishment and construction of the Project to:

- Cater for relocated bus stops
- Improve public safety for the community and workforce
- Better cater for the expected vehicle turning points and movements of trucks and other large vehicles entering and exiting the facilities
- Reduce traffic congestion behind large vehicles accessing sites.

Currently no on-street parking removal is proposed at Northcote Street, Wattle Street ramps, PRVF or Campbell Road.

The temporary removal of the existing on-street parking has been discussed through targeted stakeholder consultation in advance with:

- Inner West Council (relevant officers)
- City of Sydney Council (relevant officers)
- Roads and Maritime (relevant Project officers)
- Local businesses (as identified during local on-street parking and door-knock survey to establish special circumstances e.g. loading zones, regular delivery times/days) within 50m area from the identified parking spaces
- Local residents including sensitive receivers (as identified during local on-street parking and door-knock survey to establish any special circumstances e.g. meals on wheels delivery) within 50m area from the identified parking spaces.

More detail regarding consultation process is outlined in Section 7 below.

Road safety audits will be conducted on changed parking as outlined in section 6.4 of the TTAMP and CoA E56.

Table 4 provides the number of parking spaces and their type (e.g. timed, unmetered, etc) and the approximate period for their removal, as based on the Project program for different phases of works.

Table 4 Indicative Parking Removal Totals

Site Reference	Parking Spaces Type	Removal Qty Proposed	Removal Period (approx.)	
			From	To
PBR – Parramatta Road (In front of site, Eastbound)	Clearway - 6-10am, 3-7pm 1P - 10am-3pm Mon-Fri 1P – 8:30am-12:30pm Sat Untimed at other times	18	January, 2019	December, 2022
PBR – Parramatta Road (Bus Relocation, Eastbound)	Clearway - 6-10am, 3-7pm 1P – 10am-3pm Mon-Fri 1P – 8:30am-12:30pm Sat Untimed at other times	5	January, 2019	December, 2022
PBR – Mallett Street (Northbound)	1P – 8:30am-4pm Mon-Fri 1P – 8:30am-12:30pm Sat Untimed at other times	7	January, 2019	December, 2022

Site Reference	Parking Spaces Type	Removal Qty Proposed	Removal Period (approx.)	
			From	To
PBR – Pyrmont Bridge Road (Westbound)	Clearway - 6-10am, 3-7pm Untimed at other times	7	January, 2019	December, 2022
PBR – Bignell Lane	No Parking - 8:30am-6pm Mon-Fri, 8:30am-12:30pm Sat	5	January, 2019	December, 2022
PRE&W – Alt Street (East – both sides of street)	Untimed	7	January, 2019	December, 2022
PRE&W – Parramatta Road (both sides of street)	Clearway - 6-10am, 3-7pm Untimed at other times	17	January, 2019	December, 2022
Hawthorne Parade	Non marked Untimed	5	March, 2020	July, 2020
Canal Road	Non marked Untimed	20	June, 2020	September, 2020
Coroners Court	Private Parking	32	June, 2020	September, 2022

5.1 Pyrmont Bridge Road

Parking will be required to be removed or adjusted around the PBR site, as shown in Figure 3, due to site constraints, truck turning requirements, to minimise potential pedestrian/truck interface, and for commissioning of new driveway access or egress points or the proposed future tie-in of Bignell Lane with Pyrmont Bridge Road. Proposed temporary on-street parking removal includes:

- The existing 1-hour on-street parking from the western side of Mallett Street, between Parramatta Road and the existing Bignell Lane. This section of available parking is approximately 43.5m in length, allowing 6m per vehicle would allow parking for 7 vehicles in this section.
- Approximately 18 vehicles from the existing 10am to 3pm on-street parking on Parramatta Road adjacent to the site. Removal of these spaces is particularly important during demolition, as a type B hoarding structure will need to be erected, limiting access onto the footpath, thereby forcing drivers to walk adjacent to live traffic after exiting their vehicles.

Note, thoroughfare of pedestrians in front of the facility adjacent to Parramatta Road will be maintained unless specific activities require diversions for safety purposes (e.g., demolition of buildings adjacent to the footpath). Should this occur site specific pedestrian management plans will be developed and consulted as required in accordance with the Community Communication Strategy (CCS).

- The length of Bignell Lane will become a 'No Parking' zone to maintain clear access for the local residents. Note, this section of road is already subject to limited parking opportunities under the existing pre-construction conditions, due to the limited width. The entirety of the southern side of Bignell Lane is already 'No Parking' with the northern side of the lane permits parking only between 6:00pm and 8:30am Monday to Saturday and from 12:30pm Saturday, to 8:30am Monday. The number of actual spaces on Bignell Lane is limited due to existing property accesses and is estimated to be around 5.
- Approximately seven spaces, (based on 6m per vehicle), to be removed as 'no stopping' to allow clear line of site and appropriate turning for site access and egress along Pyrmont Bridge Road.

- Provision for the relocation of the public transport bus stop to the East of Mallett Street, from the Western Side of Mallett Street (in front of the compound). The bus stop relocation will be less than 400m and will meet the criteria of CoA E43 and E44. It will require 30m of space to meet the requirements of a single bus stops
- Approximately thirty two spaces from the Coroners Court is not be available for project parking as the lease to this parking facility terminates in late June 2020. The additional parking demand created by the removal of the Coroner Court carpark has been offset within the RPA and PAH parking facilities.

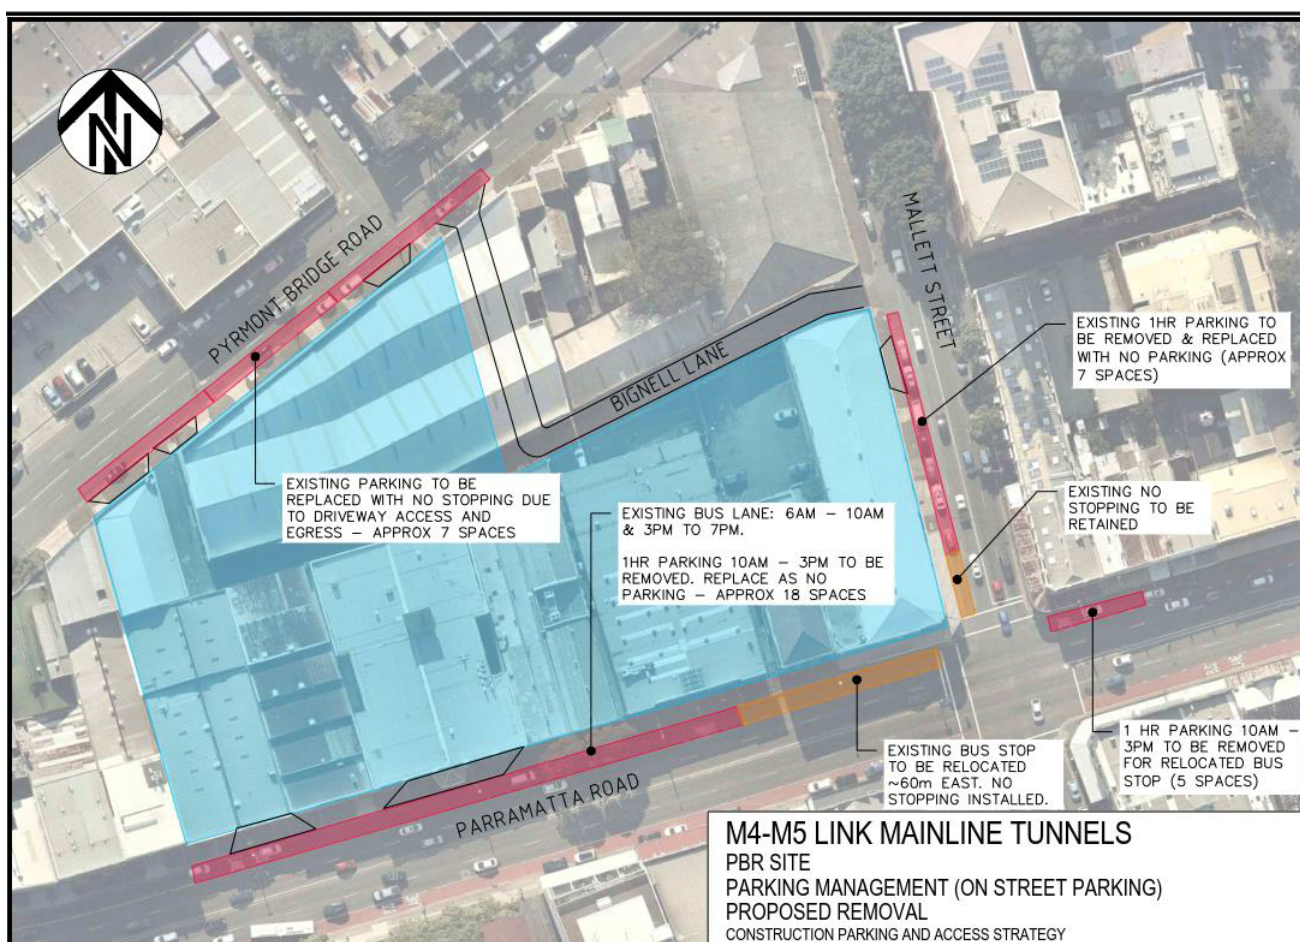


Figure 3 - PBR On-street Parking Removal Areas - Pyrmont Bridge Road

5.2 Parramatta Road East and Parramatta Road West

Parking will be required to be removed or adjusted around the PRE&W site, as shown in Figure 4, due to site constraints, truck turning requirements, to minimise potential pedestrian/truck interface, and for commissioning of new driveway access or egress points. All proposed parking removal will be undertaken in consultation with RMS and Inner West Council. Proposed temporary on-street parking removal includes:

- On-street parking along both sides of Parramatta Road adjacent to the PRE&W site, will be prevented with 'No Parking' signage. The current parking arrangement is:
 - An existing 'No Stopping' on the southbound side which will be retained (therefore no reduction in parking)
 - An a.m. and p.m. clearway on the northbound side, allowing parking between 10am to 3pm, consisting of around 14 spaces between Alt Street and the bus stop adjacent Bland Street
 - A total of 3 spaces to be relocated either north or south of the existing stop (currently shown as being relocated to the north of Alt Street in Figure 4) as determined following an assessment of nearby bus facilities, and in consultation with Inner West Council. This relocation will be within

400m of the existing stop and will only be conducted to meet the requirements of CoA E43 and 44

- A total of 7 spaces are proposed to be removed on Alt Street, to the east of Parramatta Road.

Alt Street west of Parramatta Road shall retain the current parking arrangements to allow 'time limited' visitor parking at this location.

The proposed changes are partially offset as a result of the relocation of the Muirs car sales yard and other businesses (confirmed through parking surveys, as outlined in Section 5.3) removing the previous parking demand in this area. The adjacent area to the PRE&W site is residential properties each which has driveway parking.

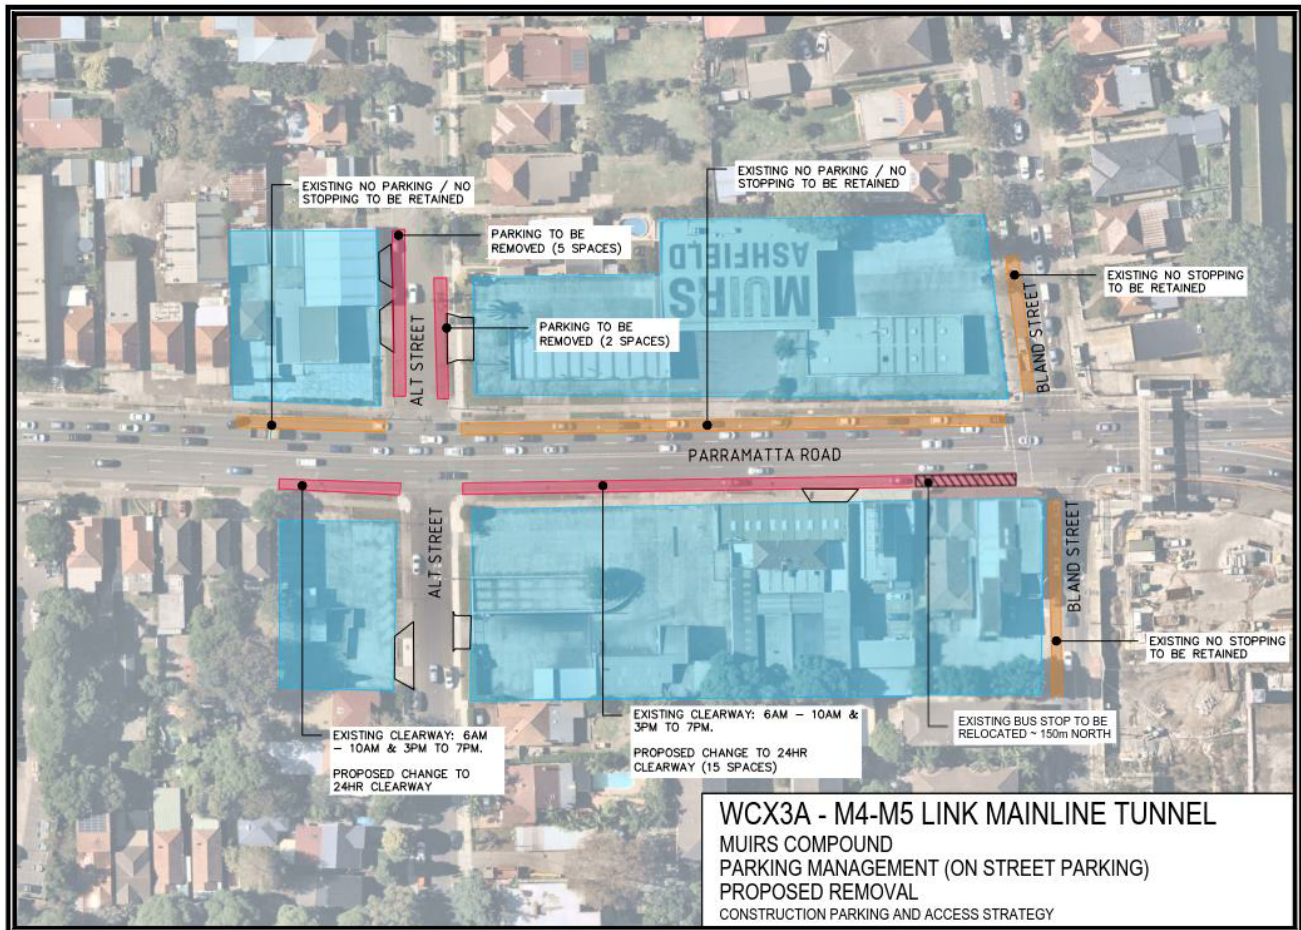


Figure 4 - PRE&W site - On-street Parking Changes

In order to optimise safety at the PRE&W site, a pedestrian fence is proposed to be installed along the median island of Parramatta Road, stretching from approximately 15m north of Alt Street, through to Bland Street intersection (subject to Roads and Maritime approval) to prevent pedestrians crossing Parramatta Road (Shown above in red). While an existing at-grade signalised pedestrian crossing and public pedestrian over bridge exist at Bland Street, this would require a diversion of some 200m by the workforce to cross onto the opposite side of the site compound at PRE&W. These initiatives should provide a suitable environment to reduce impacts on the local community, road users and increase safety of the workforce.

5.3 Canal Road & Hawthorne Parade Surface Grout area

Parking will be required to be removed around the Canal Road and Hawthorne Parade Surface Grout area, as shown in Figure 5, due to site setup, truck turning requirements, to minimise potential pedestrian/truck interface, and for surface grouting works. All proposed parking removal will be undertaken in consultation with RMS and Inner West Council. Proposed temporary on-street parking removal includes

- 5 untimed on-street parking spaces along Hawthorne Parade (shown in yellow with dark blue boundary in the Figure below). This is required in order to maintain an access to the work area on the western

side of the canal and would be required until the grouting works are complete and the netball court restoration has been completed. This area is a prioritised work location, as such these parking impacts will finish earlier than the impacts on the eastern side of the canal.

Note, thoroughfare for pedestrians will be maintained.

- 20 untimed on-street parking spaces on Canal Road will be occupied from time to time during the grouting works along Canal Road. The 20 impacted unlimited on-street parking spaces will change as the surface grouting works move around within the yellow highlighted area on the eastern side of the canal, shown in the Figure below.

Note, thoroughfare for pedestrians will be maintained.

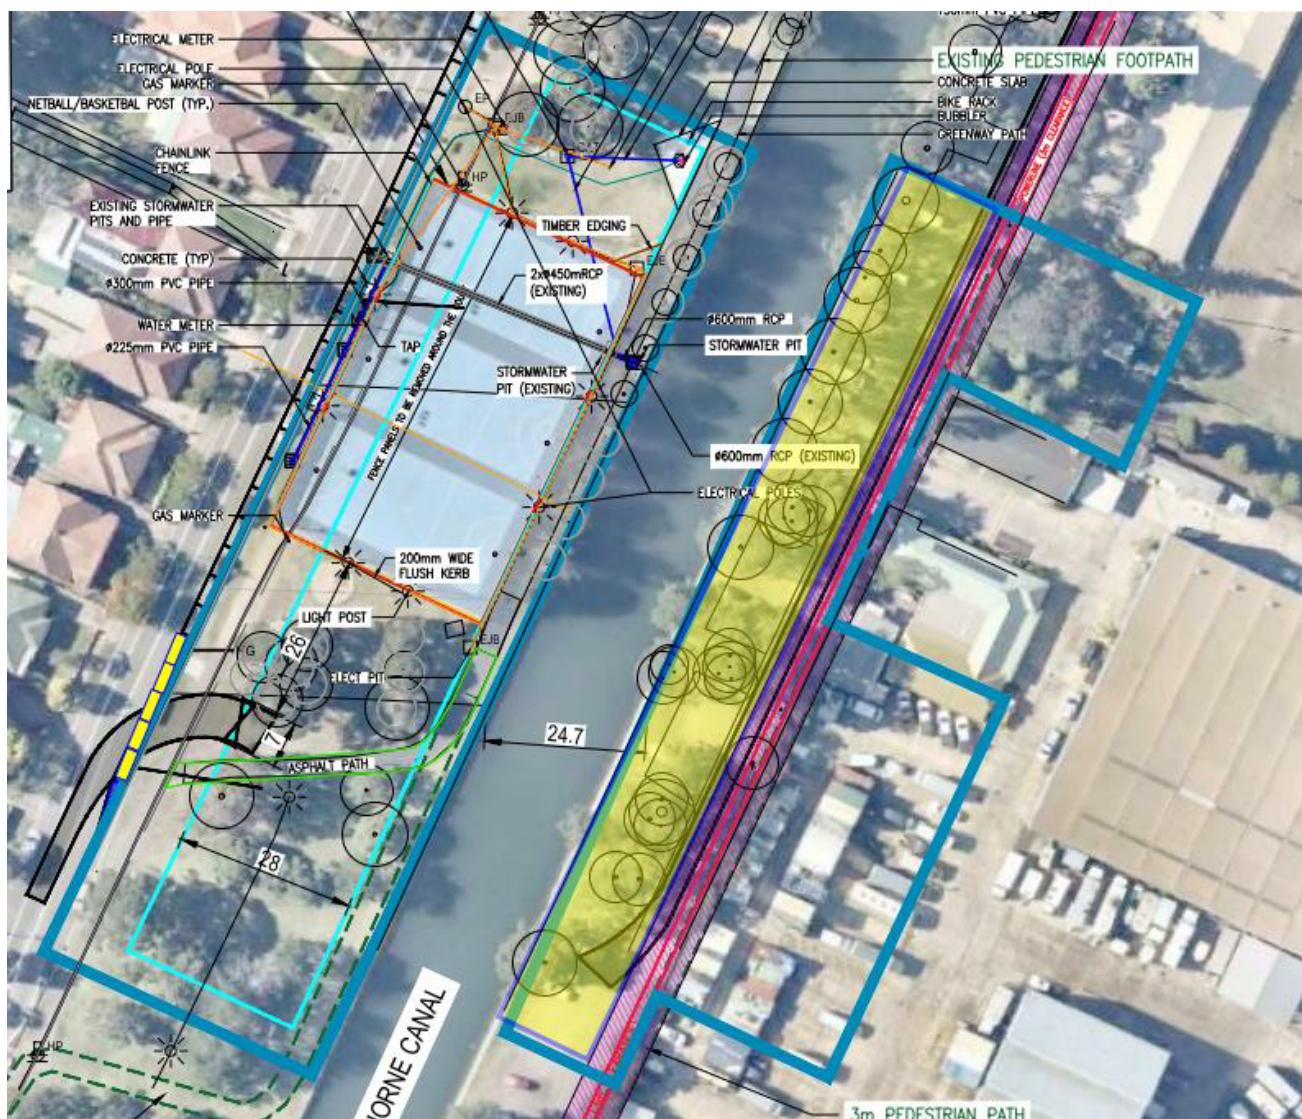


Figure 5 - Canal Road and Hawthorne Parade Surface Grouting area - On-street Parking Changes (in Yellow)

5.4 Parking Availability

Parking surveys have been conducted now that some of the businesses have been vacated. The parking surveys were conducted in accordance with CoA E54 b) and in line with the 'Patrol Survey' methodology outlined in the Austroads Guide to Traffic Management Part 3, Section H.3.3. This includes an observer patrolling along a predetermined route at fixed intervals, recording the location of parked vehicles to provide information on total parking demand, arrival and departure rates, parking duration and spatial distribution.

CoA E54 b) requires the parking surveys be conducted to cover peak and off-peak periods, school pick-up and drop-off periods and weekend periods. The times informing the assessment have been adopted are detailed in Table 5 below.

Table 5 Parking assessment times

Period	Times assessed	
Peak	Weekdays 6am to 10am	Weekdays 3pm to 7pm
Off-peak	Weekdays 10am to 3pm	
School pick-up	Weekday 2:30pm to 3:30pm	
School drop-off	Weekday 8:30am to 9:30am	
Weekend	Saturday 9am to 4pm	Sunday 9am to 4pm

It is noted that during school periods and peak periods some areas are clearways, and therefore the spaces are required to be vacated during these times.

5.4.1 Parking Supply

Table 6, Table 7, and Table 8 provides a summary of the parking supply at the surveyed roads. Refer to Table 6 and Table 7 for the total parking supply immediately adjacent to the Pyrmont Bridge Road site and the Parramatta Road East and West site. Table 8 refers to the parking supply immediately adjacent to the Canal Road and Hawthorne Parade Surface Grout area.

Table 6 Parking Supply Adjacent to the PBR site

Site Reference	Parking Space Type	Spaces
PBR – Parramatta Road (In front of site)	Clearway - 6-10am, 3-7pm 1P - 10am-3pm Mon-Fri 1P – 8:30am-12:30pm Sat Untimed at other times	18
PBR – Parramatta Road (Bus Relocation)	Clearway - 6-10am, 3-7pm 1P – 10am-3pm Mon-Fri 1P – 8:30am-12:30pm Sat Untimed at other times	5
PBR – Mallett Street (In front of site)	1P – 8:30am-4pm Mon-Fri 1P – 8:30am-12:30pm Sat Untimed at other times	7
PBR – Pyrmont Bridge Road (In front of site)	Clearway - 6-10am, 3-7pm Untimed at other times	7
PBR – Bignell Lane	No Parking - 8:30am-6pm Mon-Fri, 8:30am-12:30pm Sat	5
	Total	42

Table 7 Parking Supply adjacent to PRE&W sites

Site Reference	Parking Space Type	Spaces
PRE&W – Alt Street (East)	Untimed	7
PRE&W – Parramatta Road	Clearway - 6-10am, 3-7pm Untimed at other times	17
	Total	24

Table 8 Parking Supply adjacent to Canal Road and Hawthorne Parade Surface Grout area

Site Reference	Parking Space Type	Total Spaces Available
Canal Road (East)	Untimed	16
Canal Road (West)	Untimed	68
Hawthorne Parade – north of Learmonth Street (East)	Untimed	43
Hawthorne Parade – north of Learmonth Street (West)	Untimed	30
Hawthorne Parade – south of Learmonth Street (East)	Untimed	50
Hawthorne Parade – south of Learmonth Street (West)	Untimed	33
Darley Road – Charles St to Falls Street (North)	Untimed	19
Darley Road – Charles St to Falls Street (South)	Untimed	5

5.5 Parking demand

5.5.1 Pyrmont Bridge Rd

The parking survey results for the Pyrmont Bridge Road site are outlined in Table 9 and 10, below, and reflect the time periods outlined in Section 5.4. Further details of the surveys are presented in Appendix B.

Table 9 PBR average weekday peak parking demand

Site Reference	Total Spaces Available	Average peak parking demand (During permitted parking times where limited)				
		Weekday (6-10am)	School Drop Off (8:30-9:30am)	Off Peak (10am-3pm)	School Pick Up (2:30-3:30pm)	Weekday (3-7pm)
PBR – Parramatta Road (In front of site)	18	N/A	N/A	4	N/A	N/A
PBR – Parramatta Road (Bus Relocation)	5	N/A	N/A	1	N/A	N/A
PBR – Mallett Street (In front of site)	7	7	7	7	7	7
PBR – Pyrmont Bridge Road (In front of site)	7	N/A	N/A	7	N/A	N/A
PBR – Bignell Lane	5	0	N/A	N/A	N/A	0

The parking demands records shows a high weekday parking demand along Mallet St throughout the day and on Pyrmont Bridge Road between 10am-3pm. Parking demand along Parramatta Road is low during the weekdays. There is low parking demand observed on Bignell lane during the weekday, as a result of the restricted parking times.

Table 10 PBR weekend peak parking demand

Site Reference	Total Spaces Available	Peak parking demand (During permitted parking times where limited)	
		Saturday (9am-4pm)	Sunday (9am-4pm)
PBR – Parramatta Road (In front of site)	18	13	4
PBR – Parramatta Road (Bus Relocation)	5	1	2
PBR – Mallett Street (In front of site)	7	6	6
PBR – Pyrmont Bridge Road (In front of site)	7	7	7
PBR – Bignell Lane	5	0	0

The results indicate a high parking occupancy around the PBR site during Saturday, with Mallet Street and Pyrmont Bridge Road maintaining a high parking occupancy during Sunday. Bignell Lane parking demand remains low due to parking restrictions.

5.5.2 Parramatta Road East & West

The parking survey results for the Parramatta Road East & West site are outlined in Table 11 and 12 below, and reflect the time periods outlined in Section 5.4.

Table 11 PRE&W average weekday peak parking demand

Site Reference	Total Spaces Available	Average peak parking demand (During permitted parking times where limited)				
		Weekday (6-10am)	School Drop Off (8:30-9:30am)	Off Peak (10am-3pm)	School Pick Up (2:30-3:30pm)	Weekday (3-7pm)
PRE&W – Alt Street (East)	7	6	6	6	6	5
PRE&W – Parramatta Road	17	N/A	N/A	1	N/A	N/A

The parking demands records shows a high weekday parking demand along Alt Street (east of Parramatta Rd) and minimal demand on Parramatta Road between 10am-3pm.

Table 12 PRE&W weekend peak parking demand

Site Reference	Total Spaces Available	Peak parking demand (During permitted parking times where limited)	
		Saturday (9am-4pm)	Sunday (9am-4pm)
PRE&W – Alt Street (East)	7	7	2
PRE&W – Parramatta Road	17	4	3

The weekend parking occupancy on Alt Street remains high during Saturday while reducing on Sunday. The parking occupancy on Parramatta Road remains low during the weekend.

5.5.3 Canal Road and Hawthorne Parade Surface Grout area

The parking survey results for the Canal Road & Hawthorne Parade Surface Grout area are outlined in Table 13 and Table 14 below, and reflect the time periods outlined in Section 5.4.

Table 13 Canal Road and Hawthorne Parade parking demand

Site Reference	Total Spaces Available	Surplus Spaces available	Average peak parking demand (During permitted parking times where limited)				
			Weekday (6-10am)	School Drop Off (8:30-9:30am)	Off Peak (10am-3pm)	School Pick Up (2:30-3:30pm)	Weekday (3-7pm)
Hawthorne Parade – north of	73	49 to 36	34	37	31	31	24

Site Reference	Total Spaces Available	Surplus Spaces available	Average peak parking demand (During permitted parking times where limited)				
			Weekday (6-10am)	School Drop Off (8:30-9:30am)	Off Peak (10am-3pm)	School Pick Up (2:30-3:30pm)	Weekday (3-7pm)
Learmonth Street							
Hawthorne Parade – south of Learmonth Street	83	56 to 46	28	29	28	27	37
Canal Road	84	55 to 5	57	76	79	69	30
Darley Road – Charles Street to Falls Street	24	18 to 13	11	10	11	10	6

Table 14 Canal Road & Hawthorne Parade weekend parking demand

Site Reference	Total Spaces Available	Surplus Spaces Available	Peak parking demand	
			Saturday (9am-4pm)	Sunday (9am-4pm)
Hawthorne Parade – north of Learmonth Street	73	34 to 31	39	42
Hawthorne Parade – south of Learmonth Street	83	42 to 38	41	45
Canal Road	84	50 to 48	36	34
Darley Road – Charles Street to Falls Street	24	17	7	7

The results indicate a high parking occupancy on Canal Road during weekday office hours (08:30 – 17:00), with moderate to low level of parking occupancy during Saturday and Sunday.

On Hawthorne Parade, moderate level of parking occupancy was observed during Saturday and Sunday morning (08:00 – 10:00), and low occupancy during weekdays.

5.6 Conclusion of the Parking Demand Survey

5.6.1 Pyrmont Bridge Road

Pyrmont Bridge Road has low parking occupancy during weekdays along Parramatta Road in front of the PBR site and east of Mallett Street. Parking occupancy is high during Saturday while occupancy remains low during Sunday. The removal of parking along Parramatta Road should have minimal impact during the weekday period, and moderate impact during the weekend.

Along Mallett Street, there is high parking occupancy during weekdays and weekends, therefore, the removal of parking in this section would have moderate to high impact to road users.

There is high parking occupancy along Pyrmont Bridge Road outside of the am and pm clearway due to no timed parking restrictions. The removal of parking along Pyrmont Bridge Road would likely have a moderate impact to overnight parking.

5.6.2 Parramatta Road East & West

Parramatta Road along the PRE&W site was observed to have low parking occupancy during the weekday and weekend. The removal of parking on Parramatta Road should have minimal impact local parking. There should be minimal parking impact with the relocation of the bus stop (ID: 213131) outside 246 Parramatta Road to the north of Alt St (296 Parramatta Road).

Alt road has high parking occupancy east of Parramatta Road during weekdays and Saturday. Properties along Alt St were observed to all have off street parking and long driveways, which can occupy two to three vehicles. Even through the seven proposed parking spots on Alt St is highly utilised, it should have minimal impact to residents on Alt Street due to existing off-street parking.

There are approximately 15 residential properties on each side of Alt St between Parramatta Road and Allum Street (210m length). This equates to approximately 15 vehicle spots on each side of Alt Street for an average of 3 vehicles per household along Alt St (2 vehicles within premise and 1 on street). Therefore, the reduction of 7 parking spots on Alt Street is expected to have minimal impact to residents.

5.6.3 Canal Road and Hawthorne Parade Surface Grout area

Canal Road in the vicinity of the eastern surface grouting area was observed to have high parking occupancy during the weekday period, with these parking spaces servicing local business and office along Canal Road. Although the temporary removal of parking on Canal Road will impact local parking, there are sufficient parking capacity along Hawthorne Parade which is within 5 minutes walking distance to the local businesses and offices. Parking survey has identified over 30 spaces available on Hawthorne Parade north of Learmonth Street (within 5 minutes walking distance) and over 45 spaces available south of Learmonth Street (within 10 minutes walking distance) that will absorb light vehicle parking displaced from Canal Road. Delivery vehicles for the Film centre will continue to load/unload within the property on Canal Road.

Canal Road along the Surface Grout area was observed to have low parking occupancy during the weekend with less than 50% of occupancy.

Hawthorne Parade was observed to have low parking occupancy during the weekday with less than 50% of occupancy. During the weekend, a moderate level of parking occupancy was observed (50-60%).

Darley Road was observed to have moderate to low parking occupancy during weekday and weekend.

The removal of parking spaces on Hawthorn Parade and Canal Road can be easily absorbed along Hawthorne Parade with over 30 spaces available north of Learmonth Street (within 5 minutes walking distance) and over 45 spaces available south of Learmonth Street (within 10 minutes walking distance) after 5 are taken by the proposal. There are also over 10 spaces available on Darley Road (within 10 minutes walking distance) for parking displaced from Canal Road.

Given the availability of alternate parking opportunities in the close vicinity, further mitigation measures and not considered necessary.

5.7 Mitigation Measures

Consultation (refer to Section 7) and the parking surveys (refer to Section 5.3) have identified limited areas where mitigation will be warranted, which includes the spaces on Parramatta Road for the bus stop relocation, and the spaces in Mallett Street; being the most utilised, and in highest demand of all areas surveyed. However, possible contingencies have been provided in Section 9 should future surveys identify such need.

In addition, reintroduction of on-street parking on parts of Parramatta Road prior to project completion will be investigated where possible, and where there is opportunity to reintroduce the parking on the western side of Mallett Street.

There is limited alternative parking options in the area, or land that can be re-purposed to offset the impacts of the removal completely so generally alternate parking options are going to be limited, however investigation into potential opportunities will continue during the construction phase.

The consultation with impacted residents and stakeholders suggested that most believed the parking removal would have little consequence on them. In consideration of the feedback provided, the project team will:

- Monitoring of worker on-street parking (in relation to Gordon St Annandale). Please refer to inspections proposed in Section 8.3.1.
- Work with Council to put in place special parking arrangements outside of 137 Alt Street. If Council cannot install formal arrangements, a Project based no parking rule will be put in place.
- Investigate with Council the change of loading zones to timed parking on Mallet St to provide an additional parking option for local businesses

6. Access Control and Safety

6.1 Pedestrian Interface with Driveways

Each of the sites will be assessed as to the demand for pedestrian movements past the access and egress points, especially those which carry heavy vehicles, spoil movements and delivery trucks. Potential mitigation measures include a warning control implemented to alert pedestrians as to the potential for heavy (and some light) vehicles crossing their paths ahead.

It is acknowledged that the frequency and duration of truck movements for the life of the Project may increase the relative risk in those locations. For sites where greater volumes of pedestrians and increased risk profiles are apparent, additional engineered controls based on risk assessments will be implemented to better control interactions between vehicle and pedestrian movements around and past the access and egress points, to ensure safety is maintained for the duration of the Project. Additional information is provided in the Traffic and Transport and Access Management Sub-Plan (TTAMP).

6.2 Visitors

As described within this document, limited (approximately 2) visitor parking is available at most sites, and, unless otherwise organised, all visitors will initially report to the main Project office to attend the mandatory visitor's induction, which will provide detail on the Project parking strategy (i.e. locations of available visitors parking and shuttle bus options).

Where a visitor has been instructed by their Project contact to go directly to site, this contact will be required to inform them of the Project parking strategy and locations of available visitor parking, prior to conducting the visitor's induction on site.

Repeat visitors will subsequently know of the satellite parking facilities and will utilise these as appropriate.

7. Consultation

Consultation with community, relevant government departments, local businesses and identified stakeholders including Inner West Council (refer to Appendix C for Meeting Minutes), City of Sydney Council (refer to Appendix D for Meeting Minutes) has been conducted via meetings to discuss the proposed parking removal and the general parking management strategies. Transport for New South Wales has been consulted (refer to Appendix E for consultation records) on the position of relocated bus stops and they have advised that they have no objections.

Generally positive feedback was received with no concerns raised regarding the spaces identified for removal. The councils requested LSBJV maintain on going engagement regarding public transport options and shuttle services as they may be able to assist, and suggestions were proposed regarding bus stop relocation based on local feedback that bus stop spacing needs improving.

Businesses and residents were consulted to outline the need for the removal of on-street parking, subsequent impacts of any of the proposed changes and outline potential mitigation measures for the management of on-street parking removal to support the proposed site access and egress arrangements. Two rounds of community consultation were undertaken at Parramatta Road E/W, and three rounds of consultation were undertaken at Pyrmont Bridge Road tunnelling site between 4pm-6pm on weekdays. An additional round of consultation was conducted for the Pyrmont Bridge Road tunnelling site as removal of parking potentially impacts a larger number

of stakeholders. The local community and local businesses within a 50m notification zone were included in consultation through a door-knock or contact cards where no response occurred.

In general, comments from stakeholders indicated that removal of on-street parking would have a low to medium impact. Some specific concerns were raised in relation to worker parking and the need to maintain disabled parking. Additional consultation with the impacted stakeholder requiring disabled parking was undertaken on Thursday 4 October via doorknock. The Project team reiterated they were investigating options such as line-marking and working with Council to get a designated disabled parking spot, to further deter worker's parking at the property and to facilitate easy access for emergency vehicles.

Ongoing consultation with stakeholder's is occurring on a regular basis via email and phone calls.

Based on the outcomes of consultation and parking strategies above, no need was identified for additional mitigation measures such as staged removal. Refer to Appendix F for a summary of the outcomes of the community consultation.

Ongoing consultation with relevant councils and other stakeholders, including any unique local receivers, may be undertaken throughout construction of the Project. Community feedback and complaints relating to traffic and parking will be dealt with in accordance with the Community Communication Strategy and Complaints Management System.

Local residents, local businesses and stakeholders have been consulted on the proposal and will again be notified of the final changes to on-street parking in accordance with the project's CCS (i.e. outline use of communication tools including email, letter and door-knock). The results of the door-knock and subsequent consultation will be documented within the Consultation Manager database (in accordance with the CCS).

Prior to undertaking consultation with Secure carparks for the use of the Royal Prince Alfred Medical Centre and Prince Alfred Hospital carparks the use of other car parks was considered. These included the Wilson Parking Lifehouse (subsidised for patients of the Chris O'Brien Lifehouse Centre), King George V Parking (for RPA patients, visitors and carers), RPA Staff Car Park (for RPA staff only). All of these car parks are located closer to the Royal Prince Alfred Hospital than the Secure carparks. As such they are heavily used by hospital patients, visitors, carers and staff. They were therefore not considered any further. During consultation with Secure, Secure undertook traffic counts to determine the level of parking they could provide to LSBJV, whilst ensuring the use of these car parks would not take away from parking for hospital and medical centre patrons. Based on this, Secure agreed to provide the number of parking spaces outlined in Table 2 on the basis that their traffic counts identified that this number of spaces would not impact on their ability to serve the RPA medical facilities.

In January and February 2020, LSBJV consulted with a number of stakeholders along Canal Road as well as local residents about the planned surface grouting work either side of Hawthorne Canal and associated parking and access impacts. Summary of feedback received is listed below while details of the consultation undertaken are included in Appendix G.

- Owners and tenants of Canal Road Film Centre raised concerns about potential impact on the centre's day to day operations including removal of unmarked parking along Canal Road. In response to this, LSBJV has agreed to liaise daily with the Film Centre manager to plan work and access to accommodate reasonable requirements they may have with.
- Local Café at the end of Canal Road uses Canal Road for intermittent access for deliveries and LSBJV will work with them on an as-needs basis to ensure deliveries are accommodated.
- Inner West Council's main concern is about impact to the three recently opened netball/basketball courts within Richard Murden Reserve.
- Out of the 26 properties doorknocked along Hawthorne Parade, direct contact has been made with eighteen (18) or 69% of the properties. 3 of the 18 properties contacted directly expressed some concern about potential impact on parking however given the availability of alternate parking opportunities close by, further mitigation measures are not considered necessary.

8. Training, Monitoring & Reporting

8.1 Training

All staff will receive LSBJV site induction training, which will outline this Project parking strategy, the preferred parking arrangements, details on the satellite parking facilities, use of shuttle buses, public transport that is

available and carpooling and active transport opportunities. In addition, further promotion will be undertaken during the regular toolbox training sessions and through posters and project newsletters.

Site parking areas and nearby public transport services will be highlighted for each of the sites to outline the wider Project transport options, parking options for their specific sites and alternative access arrangements opportunities.

The site induction training will be reviewed and updated following any changes to the management of workforce and staff parking.

8.2 Workforce Code of Conduct

A workforce Code of Conduct will be provided as part of the onboarding and induction process. All workforce and staff will be required to acknowledge and formally accept the Code of Conduct. The Code of Conduct will outline the key protocols for workers travelling to and from work, be it by foot, public transport or personal vehicle (among other things).

The primary goal will be to eliminate potential issues that may come from the following

- Excess noise during shift change and travel to and from sites by foot
- Getting changed into and out of work clothes beside the road / in public
- Parking vehicles illegally
- Outline the goals of this parking strategy, and intent for the workers to park in the parking facilities provided where possible
- Engaging with members of public in a way which may reflect poorly on the Project
- Poor worker behaviour
- Littering and general site cleanliness.

The acceptance of the worker code of conduct during onboarding will assist in the implementation of disciplinary action or dismissal of workers where disregard of the expectations of management is evidenced during the inspections detailed in Section 8.3.1.

8.3 Monitoring

8.3.1 Inspections

As part of the ongoing monitoring processes on the Project, parking assessment and monitoring will play a vital role of the surveillance team's responsibility. Monitoring will include attending tunnel sites around the times of shift changes to identify entering and exiting staff, and their origin. This will provide indication of the effectiveness of alternative arrangements, and mechanisms of encouraging workers to park at the satellite parking facilities and catch public transport or the Project shuttle service.

One inspection will be conducted per week as a minimum, at each of the primary tunnel sites (including Wattle Street ramps, PBR, PRE&W and St Peters Interchange) from the commencement of tunnelling. The inspections will assess the on-street parking utilisation in adjacent areas to the compounds, assessment of occupancy / utilisation of the off street parking and shuttle buses and to capture an indication of worker numbers using public transport. Utilisation of the RPA car parks will be monitored by assessing the number of tickets issued by LSBJV to workers. The results will be reported to the project Traffic Manager for reporting and disseminated to the relevant site Project Managers for intervention for those not following the site transport and parking protocol.

Informal feedback will be sought from the workforce if it is identified that the proposed measures are not working satisfactory. Measures will then be identified and implemented as needed to promote the use of the on street parking minimisation measures detailed within this Strategy.

In response to the community feedback the inspections will also be carried out along Gordon Street Annandale and Alt Street Haberfield to ensure that parking is being undertaken in accordance with this CPAS and the applicable CoA.

The Project Managers at each of the sites with the support from the Traffic Manager will be responsible for the parking strategy implementation. The findings of the inspections completed by the Traffic Team will determine the need for implementing additional mitigation measures (refer to Section 9) accordingly. Where regular performance of the shuttle and parking management is poor the Traffic Manager and the respective Project Managers will discuss and agree the most appropriate course of action, out of the mitigation measures available or through new innovative ideas.

In addition, audits and inspections will be conducted following the process outlined in Section 6.3 of the TTAMP.

8.4 Reporting

Monthly updates on compliance will be reported internally and determine any additional requirements, or controls to be implemented.

Quarterly reports of compliance, monitoring results, and effectiveness of the controls and parking strategies will be provided to the Secretary and local councils in accordance with E54(i). The report will be provided as a standalone report.

Ongoing regular consultation with stakeholders, businesses and residents, to ensure early identification of issues will be maintained for the duration of works. LSBJV will report back to WestConnex Transurban as described in Section 6.6 of the TTAMP.

9. Contingency

If monitoring, surveys, consultation or complaints prompt intervention by the Project to improve or otherwise modify services, one or more of the options discussed in the sections below may be enacted to ensure impacts to public are reduced and public relations and reputation is protected.

9.1 Modification to Bus Services

9.1.1 Additional Services

If the services are inadequate, additional services will be added to try to improve travel times between parking and tunnel sites.

9.1.2 Modification to Routes

Where travel between sites and the satellite parking facilities is causing significant delay to workers alternate routes will be investigated, with the potential for operating a number of different scenarios or routes in lieu of those currently proposed, to try to better cater for workers from each site. This may include adding popular pick up points, such as public transport hubs, to the shuttle bus routes. Following capture of informal feedback from the workforce.

9.2 Repurpose Existing Parking Arrangements

A potential mitigation has been identified by working with the businesses and City of Sydney Council to try to re-purpose part of the loading zone on the eastern side of Mallett Street to be timed parking, if possible this can provide up to three spaces of timed parking for the businesses on this street. Any changes to parking arrangements would need to be coordinated and approved by City of Sydney Council, however this would be driven and facilitated by the Project as required.

9.3 Additional Overflow Parking

Parking utilisation will be monitored at each of the primary parking areas. Where supply is dwindling additional parking will be investigated and provided where practical solutions can be identified.

Investigations will potentially include lease options with adjacent businesses to sites, investigating layout improvements within sites where opportunities arise, or expanding existing parking facilities at other sites and modifying bus movements to provide suitable and efficient transport solutions from the additional parking.

9.4 Public Transport Encouragement

Where existing strategies are nearing capacity as determined through the inspections or the informal feedback channels as detailed in Section 8.3.1, alternate options to promote public transport use will be investigated. This will include investigating opportunities to encourage public transport use by providing additional shuttle pick up points at popular public transport hubs. Promotion of the public transport opportunities will be carried out in accordance with Section 8.1.

9.5 Active Transport Encouragement

Active transport options will also be encouraged through the provision of changing facilities and bike storage areas for cyclists. Promotion of the active transport opportunities will be carried out in accordance with Section 8.1.

9.6 Re-education and Correction

Where workers are impacting the amenity of residents, not complying with the Worker Code of Conduct, or repeatedly behaving or parking inappropriately they may be required to re-attend the Project induction which will include detail on the alternative parking options and incentives for parking at the satellite parking facilities. Stronger sanctions, up to and including dismissal, may be implemented for repeat offenders at the discretion of the Project Manager.

9.7 Shift Structures

The workforce shift times will contemplate, where possible the availability and running times of the nearest public transport options. Typically, the tunnel management teams will endeavour to structure their workers into team's that encourage carpooling. This is achieved by grouping crews based on where they reside. Similar shift patterns with a workforce that live near each other, will naturally assist in the minimisation car parking demand and increase carpooling.

APPENDIX A – Other Conditions of Approval and Revised Environmental Management Measures relevant to this Plan

Other Conditions of Approval relevant to the development of this Plan

Reference	Requirement	Section
CoA E43	During construction, where bus stops are required to be temporarily closed or relocated, such closure must not occur until relocated bus stops are functioning, have similar capacity and are relocated within a 400-metre walking distance of the existing bus stop. Closures and relocation of bus stops during construction must be undertaken in consultation with Transport for NSW and relevant council(s). Wayfinding signage must be provided directing commuters to adjacent or relocated bus stops. Footpaths must be provided to any relocated bus stops such that accessibility standards are met.	Section 5.1 Section 5.2
CoA E44	Prior to the commencement of operation of the CSSI, all bus stops temporarily closed or relocated must be reinstated in a manner that provides equal or improved capacity and accessibility (including footpaths) in consultation with Transport for NSW and relevant council(s).	Section 5.1 Section 5.2
CoA E52	Construction vehicles (including staff vehicles) associated with the CSSI must be managed to: (a) minimise parking on public roads; (b) minimise idling and queuing on public roads; and (c) ensure spoil haulage vehicles must adhere to the nominated haulage routes identified in the Traffic and Transport CEMP.	This Strategy & TTAMP
CoA E56	An independent Road Safety Audit(s) is to be undertaken by an appropriately qualified and experienced person during detailed design to assess the safety performance of new or modified local road, parking, pedestrian and cycle infrastructure provided as part of the CSSI (including ancillary facilities) to ensure that they meet the requirements of relevant design, engineering and safety guidelines, including Austroads Guide to Traffic Management. Audit findings and recommendations must be actioned prior to construction of the relevant infrastructure and must be made available to the Secretary on request.	Section 5 Section 6.4 of the TTAMP

Revised Environmental Management Measures relevant to the development of this Plan

Reference	Requirement	Section
TT04	<p>The car parking strategy described in the CTAMP will:</p> <ul style="list-style-type: none"> quantify construction workforce parking demand around project work sites and ancillary facilities during site establishment and the construction phase generally; identify public transport options and other management measures (such as carpooling and shuttle-buses) to reduce construction workforce parking demand; identify all locations that will be used for construction workforce parking (including potential use of government owned land and other potential areas near to the construction ancillary facilities); identify potential offsite areas that could be used for construction workforce parking that would be investigated and secured for use during construction where required and possible; and identify parking exclusion zones, in consultation with potentially affected stakeholders, around construction sites and facilities where construction workforce parking would be restricted. <p>The strategy will also be developed in consultation with the M4 East and New M5 contractors to identify opportunities to use existing parking arrangements associated with those projects during their respective construction periods and once those periods are completed.</p>	<p>Table 2</p> <p>Section 4 Shuttle Service & Worker Transport</p> <p>Section 3 Surface Sites & Parking Facilities</p> <p>Section 3 Surface Sites & Parking Facilities</p> <p>Section 3 Surface Sites & Parking Facilities</p>

APPENDIX B – Parking Survey Summary

APPENDIX C – Inner West Council Meeting Minutes

TTM Data

TTM Reference: 18SYD0161
Suburb: Camperdown
Survey Duration: 0800-2000
Weather: Showers on original survey dates & Thursday 29th November
Note 1: 0000-1300 Friday data acquired on Friday 19th October
Note 2: Section A closed off after 10am on Fri 19th October
Note 3: Section F, G, H weekend data collected on 12 and 13 Jan 2019

Monday, 3 December 2018										Tuesday, 4 December 2018										Wednesday, 5 December 2018										Thursday, 29 November 2018										Friday, 12 October 2018										Saturday, 13 October 2018										Sunday, 14 October 2018										
Time	Number of parked vehicles								Total	Time	Number of parked vehicles								Total	Time	Number of parked vehicles								Total	Time	Number of parked vehicles								Total	Time	Number of parked vehicles								Total																					
	A	B	C	D	E	F	G	H			A	B	C	D	E	F	G	H			A	B	C	D	E	F	G	H			A	B	C	D	E	F	G	H			A	B	C	D	E	F	G	H																						
6:00	0	3	1	0	0	0	4	5	13	6:00	0	2	2	0	0	0	3	3	10	6:00	0	4	1	0	0	0	4	4	13	6:00	0	2	3	0	0	0	3	1	9	6:00	0	6	0	0	0	0	4	7	17	6:00	0	3	0	2	3	0	5	9	22	6:00	2	2	0	0	1	0	3	7	15	
6:30	0	3	2	0	0	0	4	7	16	6:30	0	3	2	0	0	0	4	5	14	6:30	0	6	1	0	0	0	5	5	17	6:30	0	3	3	0	0	0	5	3	14	6:30	0	7	0	0	0	0	4	8	19	6:30	0	4	0	2	3	0	5	9	23	6:30	2	3	0	0	1	0	3	7	16	
7:00	0	3	2	0	0	0	3	7	15	7:00	0	3	2	0	0	0	4	5	14	7:00	0	8	1	0	0	0	5	7	21	7:00	0	4	3	0	0	0	5	4	16	7:00	0	7	0	0	0	0	5	11	23	7:00	0	4	0	6	0	0	5	9	24	7:00	2	3	0	0	1	0	3	7	16	
7:30	0	4	2	0	0	0	4	8	18	7:30	0	3	2	0	0	0	5	6	16	7:30	0	7	1	0	0	0	5	5	18	7:30	0	3	3	0	0	0	6	5	17	7:30	0	8	0	0	0	0	5	10	23	7:30	0	5	0	5	2	0	5	9	26	7:30	2	3	0	1	0	0	3	7	16	
8:00	0	4	3	0	0	0	4	10	21	8:00	0	3	3	0	0	0	5	9	20	8:00	0	8	1	0	0	0	4	6	19	8:00	0	3	3	0	0	0	6	8	20	8:00	0	8	0	0	0	0	5	10	23	8:00	0	7	0	4	10	0	5	9	35	8:00	2	3	0	0	0	0	2	3	7	17
8:30	0	4	3	0	0	0	4	7	18	8:30	0	3	3	0	0	0	5	8	19	8:30	0	8	1	0	0	0	5	5	19	8:30	0	3	3	0	0	0	6	9	21	8:30	0	8	0	0	0	0	5	11	24	8:30	0	7	0	5	10	0	5	9	36	8:30	2	3	0	0	2	2	3	7	19	
9:00	0	4	3	0	0	0	4	7	18	9:00	0	3	3	0	0	0	5	8	19	9:00	0	8	1	0	0	0	6	6	21	9:00	0	3	3	0	0	0	6	10	22	9:00	0	6	0	0	0	0	5	10	21	9:00	5	8	0	4	13	0	5	9	44	9:00	2	3	0	0	2	3	3	7	20	
9:30	0	4	3	0	0	0	4	7	18	9:30	0	3	3	0	0	0	5	8	19	9:30	0	8	2	0	0	0	6	7	23	9:30	0	3	3	0	0	0	6	9	21	9:30	0	7	0	0	0	0	5	9	21	9:30	7	9	0	6	13	1	5	9	50	9:30	3	3	0	2	2	3	3	7	23	
10:00	4	3	2	0	0	0	5	6	20	10:00	4	3	2	0	0	0	6	7	22	10:00	2	8	1	0	0	1	6	7	25	10:00	5	3	3	0	1	0	7	9	28	10:00	0	8	0	2	5	1	5	10	31	10:00	7	7	0	6	12	0	5	9	46	10:00	4	3	0	2	2	4	3	7	25	
10:30	7	3	2	0	0	0	5	7	24	10:30	7	3	2	0	0	0	6	9	27	10:30	9	8	1	0	3	0	6	9	36	10:30	7	3	3	0	1	0	7	11	32	10:30	0	8	0	2	5	0	4	10	29	10:30	7	8	0	6	11	1	5	9	47	10:30	7	3	0	2	2	4	3	8	29	
11:00	8	3	3	0	0	0	5	7	26	11:00	8	2	3	0	0	0	5	9	27	11:00	8	8	1	0	2	0	6	6	31	11:00	8	2	3	0	1	0	6	11	31	11:00	0	6	0	3	4	1	4	10	28	11:00	7	7	0	6	9	1	3	10	43	11:00	7	3	0	1	4	4	4	8	31	
11:30	7	4	3	0	0	0	5	9	28	11:30	7	3	3	0	0	0	5	9	27	11:30	9	8	1	0	2	0	6	7	33	11:30	8	2	3	0	1	0	6	9	29	11:30	0	6	0	4	3	1	4	10	28	11:30	7	8	0	7	12	1	3	10	48	11:30	7	3	0	3	3	3	4	8	31	
12:00	8	3	2	2	2	0	5	6	28	12:00	8	2	2	1	2	0	6	8	29	12:00	8	7	1	0	2	0	6	9	33	12:00	8	2	3	0	2	0	7	10	32	12:00	2	6	0	4	4	1	4	10	31	12:00	7	5	0	7	10	1	3	9	42	12:00	7	3	0	0	1	3	4	8	26	
12:30	9	3	2	1	1	0	4	6	26	12:30	8	2	2	0	1	0	5	8	26	12:30	8	9	1	0	2	0	7	10	37	12:30	8	9	1	0	2	0	7	10	30	12:30	2	7	0	4	2	1	4	10	30	12:30	7	7	0	4	13	1	3	8	43	12:30	7	4	0	0	2	2	3	8	26	
13:00	8	3	3	0	2	0	5	4	25	13:00	7	2	3	0	2	0	6	7	27	13:00	8	9	1	0	2	0	6	9	35	13:00	7	2	3	0	2	0	7	10	31	13:00	5	7	0	3	3	2	5	8	33	13:00	7	5	0	5	13	2	3	8	43	13:00	7	6	0	0	2	2	3	7	27	
13:30	8	3	3	0	1	1	4	5	25	13:30	8	2	3	0	1	0	5	7	26	13:30	7	9	1	0	2	0	6	10	35	13:30	8	2	3	0	2	0	6	9	30	13:30	7	6	0	3	4	2	5	8	35	13:30	7	5	0	2	12	2	3	8	39	13:30	7	5	0	1	2	2	3	7	27	
14:00	7	3	3	0	1	0	4	5	23	14:00	7	2	3	0	1	0	5	6	24	14:00	8	8	1	0	2	1	5	9	34	14:00	7	2	3	0	2	0	6	8	28	14:00	7	8	0	3	7	2	5	8	40	14:00	7	5	0	4	1	2	3	8	30											
14:30	6	3	3	0	1	0	4	5	22	14:30	7	2	3	0	2	0	5	6	25	14:30	6	8	1	0	1	0	5	8	29	14:30	8	2	3	0	3	0	6	8	30	14:30	5	8	0	2	3	2	5	8	33	14:30	7	7	0	4	3	2	3	7	33	14:30	7	4	0	0	1	2	3	8	25	
15:00	1	3	3	0	0	0	4	6	17	15:00	0	3	3	0	1	0	4	7	18	15:00	0	7	1	0	0	0	5	9	22	15:00	0	4	3	0	2	0	5	9	23	15:00	6	8	0	1	3	0	5	8	31	15:00	7	5	0	3	3	2	3	7	30	15:00	7	5	0	0	1	1	3	7	24	
15:30	0	3	3	0	0	0	4	6	16	15:30	0	3	3	0	0	0	4	7	17	15:30	0	7	1	0	0	0	5	6	19	15:30	0	4	4	0	0	0	5	9	22	15:30	0	7	0	0	0	0	5	7	19	15:30	7	5	0	3	6	1	3	7	32	15:30	7	1	0	3	2	1	3	7	24	
16:00	0	4	3	0	0	0	4	9	20	16:00	0	3	3	0	0	0	4	7	17	16:00	0	7	1	0	0	0	6	7	21	16:00	0	2	3	0	0	0	5	6	16	16:00	0	7	0	0	0	0	5	7	19	16:00	7	5	0	3	1	1	3	7	27	16:00	7	1	0	2	1	1	3	7	22	
16:30	0	3	3	0	0	0	4	8	18	16:30	0	2	2	0	0	0	4	7	15	16:30	0	6	1	0	0	0	2	6	15	16:30	0	2	2	0	0	0	5	6	15	16:30	0	6	0	0	0	0	5	7	18	16:30	6	4	0	0	5	1	3	8	27	16:30	7	2	0	0	2	1	3	7	22	
17:00	0	3	2	0	0	0	3	3	11	17:00	0	2	2	0	0	0	4	5	13	17:00	0	5	0	0	0	0	4	8	17	17:00	0	2	2	0	0	0	6	8	18	17:00	0	7	0	0	0	0	5	7	19	17:00	7	3	0	1	3	1	3	7	25	17:00	7	3	0	0	1	0	3	7	21	
17:30	0	2	2	0	0	0	4	2	10	17:30	0	2	2	0	0	0	5	4	13	17:30	0	5	1	0	0	0	4	8	18	17:30	0	2	3	0	0	0	6	6	17	17:30	0	6	0	0	0	0	5	8	19	17:30	0	6	0	0	0	0	3	7	23	17:30	7	2	0	0	3	0	3	7	22	
18:00	0	3	2	0	0	0	4	7	16	18:00	0	2	2	0	0	0	4	7</																																																				

TTM Data

TTM Reference: 18SYD0161
Suburb: Haberfield
Survey Duration: 0600-2000
Weather: Showers on original survey dates & Thursday 29th November
Notes: 0000-1300 Friday data acquired on Friday 19th October

Monday, 3 December 2018										Tuesday, 4 December 2018										Wednesday, 5 December 2018										Thursday, 29 November 2018										Friday, 12 October 2018										Saturday, 13 October 2018										Sunday, 14 October 2018											
Time	Number of parked vehicles								Total	Time	Number of parked vehicles								Total	Time	Number of parked vehicles								Total	Time	Number of parked vehicles								Total	Time	Number of parked vehicles								Total	Time	Number of parked vehicles								Total												
6:00	0	0	3	0	1	0	0	2	6	6:00	0	0	1	0	0	0	0	0	1	6	6:00	0	0	2	0	0	0	0	0	2	6:00	0	0	0	0	0	0	0	0	0	6:00	0	4	2	0	0	0	0	4	10	6:00	0	3	2	0	0	3	0	3	11	6:00	0	1	1	0	0	3	0	4	9	
6:30	0	1	3	0	1	0	0	2	7	6:30	0	1	2	0	0	0	0	0	3	6	6:30	0	2	2	0	0	0	0	0	4	6:30	0	2	2	0	0	0	0	0	4	6:30	0	4	2	0	0	0	0	4	10	6:30	0	3	2	0	0	3	0	3	11	6:30	0	1	1	0	0	3	0	4	9	
7:00	0	2	3	0	1	0	0	3	9	7:00	0	2	2	0	0	0	0	0	4	6	7:00	0	4	2	0	0	0	0	0	6	7:00	0	2	2	0	0	0	0	0	3	7	7:00	0	4	2	0	0	0	0	4	10	7:00	0	3	2	0	0	3	0	3	11	7:00	0	1	1	0	0	3	0	4	9
7:30	0	2	4	0	1	0	0	3	10	7:30	0	2	3	0	0	0	0	0	5	7	7:30	0	4	3	0	0	0	0	0	7	7:30	0	3	2	0	0	0	0	0	3	8	7:30	0	3	2	0	0	0	0	4	9	7:30	0	5	2	0	0	3	0	3	13	7:30	0	1	1	0	0	3	0	4	9
8:00	0	2	5	0	1	0	0	3	11	8:00	0	2	3	0	1	0	0	0	6	6	8:00	0	4	4	0	1	0	0	0	9	8:00	0	4	2	0	1	0	0	3	10	8:00	0	3	2	0	0	0	0	3	8	8:00	0	5	2	0	0	4	0	3	14	8:00	0	1	1	0	0	3	0	4	9	
8:30	0	2	5	0	1	0	0	3	11	8:30	0	2	3	0	1	0	0	0	6	6	8:30	0	4	4	0	1	0	0	0	9	8:30	0	5	2	0	2	0	0	3	12	8:30	0	3	2	0	0	0	0	3	8	8:30	0	5	2	0	0	5	0	2	14	8:30	0	1	1	0	0	3	0	4	9	
9:00	0	2	5	0	1	0	0	3	11	9:00	0	2	3	0	1	0	0	0	6	6	9:00	0	4	4	0	1	0	0	0	9	9:00	0	5	2	0	1	0	0	3	11	9:00	0	4	2	0	0	0	0	3	9	9:00	0	3	2	0	0	4	0	4	13	9:00	0	1	1	0	0	2	0	4	8	
9:30	0	2	4	0	1	0	0	2	9	9:30	0	2	3	0	1	0	0	0	6	6	9:30	0	4	3	0	1	0	0	0	8	9:30	0	5	2	0	1	0	0	3	11	9:30	0	4	2	0	0	0	0	3	9	9:30	0	3	2	0	0	4	0	4	13	9:30	0	1	1	0	0	2	0	4	8	
10:00	0	2	3	0	1	1	0	2	9	10:00	0	2	2	0	1	1	0	0	6	6	10:00	0	5	4	0	4	0	0	0	13	10:00	0	4	2	0	1	2	1	4	14	10:00	0	3	2	0	0	2	0	3	11	10:00	0	3	2	0	0	4	0	4	13	10:00	0	1	1	0	0	2	0	3	7	
10:30	0	2	3	0	2	0	0	1	8	10:30	0	2	2	0	1	1	0	0	6	6	10:30	0	5	4	0	4	0	0	0	13	10:30	0	4	2	0	1	2	1	4	14	10:30	0	4	2	0	0	3	1	3	13	10:30	0	5	2	0	0	3	0	3	13	10:30	0	1	1	0	0	2	0	3	7	
11:00	0	2	3	0	2	0	0	1	8	11:00	0	2	2	0	2	1	0	0	7	7	11:00	0	5	4	0	4	0	0	0	13	11:00	0	4	2	0	2	2	1	3	14	11:00	0	4	2	0	0	3	0	3	12	11:00	0	3	2	0	0	3	0	3	11	11:00	0	1	1	0	0	2	0	3	7	
11:30	0	2	3	0	3	0	0	1	9	11:30	0	2	2	0	2	1	0	0	7	7	11:30	0	5	4	0	4	0	0	0	13	11:30	0	4	2	0	1	2	1	3	13	11:30	0	4	2	0	0	2	0	3	11	11:30	0	2	2	0	0	3	0	4	11	11:30	0	0	0	0	0	2	0	3	5	
12:00	0	2	2	0	3	0	0	1	8	12:00	0	2	2	0	2	0	0	0	6	6	12:00	0	5	4	0	4	0	0	0	13	12:00	0	5	2	0	1	1	1	4	14	12:00	0	4	2	0	0	2	0	4	12	12:00	0	4	2	0	0	3	0	2	9	12:00	0	0	0	0	0	2	0	3	5	
12:30	0	2	2	0	3	0	0	1	8	12:30	0	2	2	0	2	0	0	0	6	6	12:30	0	5	4	0	4	0	0	0	13	12:30	0	5	2	0	1	1	1	4	14	12:30	0	4	2	0	0	2	0	4	12	12:30	0	4	2	0	1	2	0	2	11	12:30	0	0	0	0	0	1	1	0	3	5
13:00	0	2	2	0	3	0	0	1	8	13:00	0	2	2	0	2	0	0	0	6	6	13:00	0	5	4	0	4	0	0	0	13	13:00	1	3	2	0	1	1	1	3	12	13:00	0	5	2	0	0	3	0	4	16	13:00	0	1	1	0	0	1	0	2	5	13:00	0	0	0	0	0	1	0	3	4	
13:30	0	2	2	0	2	0	0	1	7	13:30	0	2	2	0	1	0	0	0	5	5	13:30	0	5	4	0	3	0	0	0	12	13:30	1	3	2	0	1	1	1	3	12	13:30	0	5	2	1	0	3	0	4	15	13:30	0	1	1	0	0	1	0	2	5	13:30	0	0	0	0	0	1	0	3	4	
14:00	0	2	3	0	2	0	0	1	8	14:00	0	2	2	0	1	0	0	0	5	5	14:00	0	5	4	0	3	0	0	0	12	14:00	1	2	2	0	1	1	1	3	11	14:00	0	5	2	0	0	3	1	4	15	14:00	0	1	2	0	0	1	0	3	7	14:00	0	1	1	0	0	1	0	3	6	
14:30	0	2	3	0	1	0	0	1	7	14:30	0	2	2	0	1	0	0	0	5	5	14:30	0	5	4	0	3	0	0	0	12	14:30	1	2	2	0	1	1	1	3	11	14:30	0	5	2	0	0	3	1	4	15	14:30	0	1	0	0	0	2	0	4	7	14:30	0	1	1	0	0	2	0	4	7	
15:00	0	2	3	0	1	0	0	2	8	15:00	0	2	2	0	1	0	0	0	5	5	15:00	0	5	4	0	3	0	0	0	12	15:00	1	2	2	0	1	1	1	3	11	15:00	0	3	2	0	0	3	0	3	11	15:00	0	3	2	0	0	3	0	3	9	15:00	0	1	0	0	0	2	0	4	7	
15:30	0	2	3	0	1	0	0	2	8	15:30	0	2	2	0	1	0	0	0	5	5	15:30	0	5	4	0	1	0	0	0	10	15:30	1	2	2	0	1	0	0	4	10	15:30	0	3	2	0	0	0	0	4	9	15:30	0	1	1	0	0	3	0	4	9	15:30	0	1	1	0	0	3	0	4	9	
16:00	0	2	3	0	1	0	0	2	8	16:00	0	2	2	0	1	0	0	0	5	5	16:00	0	5	4	0	1	0	0	0	10	16:00	0	2	2	0	1	0	0	3	8	16:00	0	1	2	0	0	0	0	4	7	16:00	0	1	2	0	0	0	0	4	7	16:00	0	1	1	0	0	2	0	4	7	
16:30	0	2	3	0	1	0	0	2	8	16:30	0	2	2	0	1	0	0	0	5	5	16:30	0	5	4	0	1	0	0	0	10	16:30	0	2	2	0	1	0	0	3	8	16:30	0	1	2	0	0	0	0	4	7	16:30	0	1	2	0	0	2	0	4	7	16:30	0	0	1	0	0	2	0	4	7	
17:00	0	2	3	0	1	0	0	2	8	17:00	0	2	2	0	1	0	0	0	5	5	17:00	0	4	2	0	0	0	0	0	6	17:00	0	2	2	0	1	0	0	3	8	17:00	0	1	1	0	0	0	0	4	6	17:00	0	1	1	0	0	2	0	4	6	17:00	0	0	2	0	0	0	0	4	6	
17:30	0	2	3	0	2	0	0	2	9	17:30	0	2	2	0	1	0	0	0	5	5	17:30	0	4	3	0	0	0	0	0	7	17:30	0	2	2	0	1	0	0	3	8	17:30	0	0	2	0	0	0	0	4	6	17:30	0	0	2	0	0	0	0	4	6	17:30	1	0	2	0	0	2	0	5	10	
18:00	0	2	2	0	2	0	0																																																																

20SYD0010 Lilyfield Parking Zones


This aerial map illustrates the proposed parking zones (A through H) for the M2 motorway in Lilyfield, NSW. The zones are highlighted in yellow along the motorway corridor, which runs diagonally from the top left towards the bottom right. Red arrows indicate the direction of traffic flow along the motorway. The map shows surrounding streets, including Kings, Tillock, Kingston, and Hawthorne Parade, as well as various landmarks and businesses such as Blackmore Oval, Leichhardt Men's Shed, and the Leichhardt North railway station. The zones are labeled A, B, C, D, E, F, G, and H, with some zones having sub-labels (e.g., A1, A2, B1, B2, C1, C2, D1, D2, E1, E2, F1, F2, G1, G2, H1, H2).

TTM Data

TTM Reference: 20SYD0010
Location: Lilyfield
Date: Wednesday, 22 January 2020
Weather: Fine
Notes:



Total Area Capacity		Capacity	0600	0630	0700	0730	0800	0830	0900	0930	1000	1030	1100	1130	1200	1230	1300	1330	1400	1430	1500	1530	1600	1630	1700	1730	1800	1830	1900
		264	105	104	125	119	127	136	141	140	139	140	137	134	132	132	129	129	126	121	119	119	126	103	104	95	92	88	87
		Unoccupied	159	160	139	145	137	128	123	124	125	124	127	130	132	132	135	135	138	143	145	145	138	161	160	169	172	176	177
		Percentage Occupied	40%	39%	47%	45%	48%	52%	53%	53%	53%	53%	52%	51%	50%	50%	49%	49%	48%	46%	45%	45%	48%	39%	39%	36%	35%	33%	



Location	Side	Zone	Between	Capacity	0600	0630	0700	0730	0800	0830	0900	0930	1000	1030	1100	1130	1200	1230	1300	1330	1400	1430	1500	1530	1600	1630	1700	1730	1800	1830	1900	
Hawthorne Pde	East	B	Dobroyde & Learmonth	43	17	16	21	14	18	18	18	19	19	16	17	17	16	15	15	14	13	13	12	13	15	13	12	11	15	14	15	
		D	Learmonth & Waratah	50	10	9	11	10	11	11	12	14	14	15	15	13	13	13	14	13	13	13	13	12	14	13	10	11	9	9	9	
	West	A	Dobroyde & Learmonth	30	15	17	15	15	15	16	17	15	15	16	13	12	13	13	12	13	10	10	12	12	15	15	19	19	18	18	18	
		C	Learmonth & Waratah	33	17	15	16	16	16	17	17	16	14	15	16	16	17	17	16	18	19	18	17	17	21	18	19	17	18	18	17	
	Total				156	59	57	63	55	60	62	64	62	62	61	58	59	59	56	58	56	54	54	55	63	60	60	58	60	59	59	59
	Unoccupied				97	99	93	101	96	94	94	92	92	94	94	95	98	97	97	100	98	100	102	102	101	93	96	96	98	96	97	97
Percentage Occupied				38%	37%	40%	35%	38%	40%	41%	41%	40%	40%	39%	37%	38%	38%	38%	36%	37%	36%	35%	35%	35%	40%	38%	38%	37%	38%	38%	38%	

Location	Side	Zone	Between	Capacity	0600	0630	0700	0730	0800	0830	0900	0930	1000	1030	1100	1130	1200	1230	1300	1330	1400	1430	1500	1530	1600	1630	1700	1730	1800	1830	1900
Canal Rd	East	F	Leichhardt Men's Shed & Southern End	16	4	5	9	10	10	11	12	11	11	12	12	13	9	10	10	8	9	9	9	9	8	4	4	2	2	1	1
	West	E	Leichhardt Men's Shed & Southern End	68	35	33	44	45	48	54	56	57	56	57	56	55	55	54	55	55	53	52	50	49	49	33	34	29	24	22	21
			Total	84	39	38	53	55	58	65	68	68	67	69	68	68	64	64	65	63	62	61	59	58	57	37	38	31	26	23	22
			Unoccupied	45	46	31	29	26	19	16	16	17	15	16	20	19	21	22	23	25	26	27	47	46	53	58	61	62			
			Percentage Occupied	46%	45%	63%	65%	69%	77%	81%	81%	80%	82%	81%	81%	76%	76%	77%	75%	74%	73%	70%	69%	68%	44%	45%	37%	31%	27%	26%	


[illegible]

TTM Data

TTM Reference: 20SYD0010
Location: Lilyfield
Date: Thursday, 23 January 2020
Weather: Fine
Notes:



Total Area Capacity		Capacity	0600	0630	0700	0730	0800	0830	0900	0930	1000	1030	1100	1130	1200	1230	1300	1330	1400	1430	1500	1530	1600	1630	1700	1730	1800	1830	1900
		264	91	97	100	104	116	137	146	144	135	134	133	129	127	125	119	119	119	126	123	125	126	118	116	112	114	94	92
		Unoccupied	173	167	164	160	148	127	118	120	129	130	131	135	137	139	145	145	145	138	141	139	138	146	148	152	150	170	172
		Percentage Occupied	34%	37%	38%	39%	44%	52%	55%	55%	51%	51%	50%	49%	48%	47%	45%	45%	45%	48%	47%	47%	48%	45%	44%	42%	43%	36%	35%



Location	Side	Zone	Between	Capacity	0600	0630	0700	0730	0800	0830	0900	0930	1000	1030	1100	1130	1200	1230	1300	1330	1400	1430	1500	1530	1600	1630	1700	1730	1800	1830	1900
Hawthorne Pde	East	B	Dobroyde & Learmonth	43	16	16	17	17	14	17	22	20	17	15	13	13	13	14	13	14	13	13	13	13	13	12	12	13	14	18	18
		D	Learmonth & Waratah	50	13	13	10	10	10	12	11	13	15	15	14	13	13	13	12	13	14	13	13	13	14	15	14	14	15	10	10
	West	A	Dobroyde & Learmonth	30	15	16	16	14	13	14	15	16	13	15	15	14	14	16	15	15	14	14	15	13	13	11	12	13	14	14	15
		C	Learmonth & Waratah	33	17	17	16	15	15	16	20	16	13	13	13	13	13	15	13	13	13	15	16	17	19	15	17	15	16	18	17
	Total			156	61	62	59	56	52	59	68	65	58	58	55	53	53	58	53	55	54	55	57	57	60	52	55	56	58	60	60
	Unoccupied			95	94	97	100	104	97	88	91	98	98	101	103	103	98	103	101	102	101	99	99	96	104	101	100	98	96	96	
Percentage Occupied			39%	40%	38%	36%	33%	38%	44%	42%	37%	37%	35%	34%	34%	37%	34%	35%	35%	35%	37%	37%	38%	33%	35%	36%	37%	38%	38%		

Location	Side	Zone	Between	Capacity	0600	0630	0700	0730	0800	0830	0900	0930	1000	1030	1100	1130	1200	1230	1300	1330	1400	1430	1500	1530	1600	1630	1700	1730	1800	1830	1900
Canal Rd	East	F	Leichhardt Men's Shed & Southern End	16	3	3	4	3	10	11	11	11	11	10	10	11	12	11	11	11	11	11	11	10	9	9	7	5	5	5	4
	West	E	Leichhardt Men's Shed & Southern End	68	21	26	31	38	47	61	61	60	58	57	58	55	54	50	49	47	48	54	49	52	51	50	48	45	45	23	22
	Total			84	24	29	35	41	57	72	72	71	68	67	69	67	65	61	60	58	59	65	60	62	60	59	55	50	50	28	26
Unoccupied				60	55	49	43	27	12	12	13	16	17	15	17	19	23	24	26	25	19	24	22	24	25	29	34	34	56	58	
Percentage Occupied				29%	35%	42%	49%	68%	86%	86%	85%	81%	80%	82%	80%	77%	73%	71%	69%	70%	77%	71%	74%	71%	70%	65%	60%	60%	33%	31%	


Location	Side	Zone	Between	Capacity	0600	0630	0700	0730	0800	0830	0900	0930	1000	1030	1100	1130	1200	1230	1300	1330	1400	1430	1500	1530	1600	1630	1700	1730	1800	1830	1900	
Darley Rd	North	G	Charles & Falls	19	3	3	3	3	3	3	3	5	6	6	6	6	6	3	3	3	3	3	3	3	4	3	3	3	3	3		
	South	H	Charles & Falls	5	3	3	3	4	4	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3		
	Total			24	6	6	6	7	7	6	6	8	9	9	9	9	9	6	6	6	6	6	6	6	6	7	6	6	6	6	6	
Unoccupied				18	18	18	17	17	18	18	16	15	15	15	15	15	18	18	18	18	18	18	18	18	17	18	18	18	18	18	18	18
Percentage Occupied				25%	25%	25%	29%	29%	25%	25%	33%	38%	38%	38%	38%	38%	38%	25%	25%	25%	25%	25%	25%	25%	25%	29%	25%	25%	25%	25%	25%	

TTM Data

TTM Reference: 20SYD0010
Location: Lilyfield
Date: Friday, 24 January 2020
Weather: Fine
Notes:



Total Area Capacity		Capacity	0600	0630	0700	0730	0800	0830	0900	0930	1000	1030	1100	1130	1200	1230	1300	1330	1400	1430	1500	1530	1600	1630	1700	1730	1800	1830	1900
		264	90	95	88	113	128	128	133	140	139	136	136	140	141	147	140	137	131	132	137	134	121	111	121	112	107	84	81
		Unoccupied	174	169	176	151	136	136	131	124	125	128	128	124	123	117	124	127	133	132	127	130	143	153	143	152	157	180	183
		Percentage Occupied	34%	36%	33%	43%	48%	48%	50%	53%	53%	52%	52%	53%	53%	56%	53%	52%	50%	50%	52%	51%	46%	42%	46%	42%	41%	32%	31%



Location	Side	Zone	Between	Capacity	0600	0630	0700	0730	0800	0830	0900	0930	1000	1030	1100	1130	1200	1230	1300	1330	1400	1430	1500	1530	1600	1630	1700	1730	1800	1830	1900
Hawthorne Pde	East	B	Dobroyde & Learmonth	43	18	18	16	14	15	14	15	15	14	14	14	14	15	15	15	15	13	13	15	15	13	11	11	13	15	16	13
		D	Learmonth & Waratah	50	9	9	9	15	14	13	13	15	14	13	12	14	14	15	15	15	15	15	15	13	15	15	12	14	12	10	9
	West	A	Dobroyde & Learmonth	30	12	12	12	12	12	12	14	14	16	14	14	18	18	17	16	16	15	15	14	15	15	15	18	18	13	13	13
		C	Learmonth & Waratah	33	13	16	17	17	16	16	15	15	13	12	14	15	17	12	12	12	12	12	19	18	17	19	21	18	17	18	18
	Total			156	52	55	54	58	58	55	58	59	59	54	52	60	62	64	58	58	55	55	61	63	60	57	64	61	57	57	53
	Unoccupied			104	101	102	98	98	101	98	97	97	102	104	96	94	92	98	98	101	101	95	93	96	99	92	95	99	99	103	
	Percentage Occupied			33%	35%	35%	37%	37%	35%	37%	38%	38%	35%	33%	38%	40%	41%	37%	37%	35%	35%	39%	40%	38%	37%	41%	39%	37%	37%	37%	34%

Location	Side	Zone	Between	Capacity	0600	0630	0700	0730	0800	0830	0900	0930	1000	1030	1100	1130	1200	1230	1300	1330	1400	1430	1500	1530	1600	1630	1700	1730	1800	1830	1900
Canal Rd	East	F	Leichhardt Men's Shed & Southern End	16	4	3	2	5	7	8	8	9	12	12	12	11	11	11	12	12	14	14	13	12	9	7	7	5	2	1	1
	West	E	Leichhardt Men's Shed & Southern End	68	27	28	25	43	55	57	59	64	60	62	64	62	61	65	62	59	55	56	56	52	45	40	42	39	41	20	21
			Total	84	31	31	27	48	62	65	67	73	72	74	76	73	72	76	74	71	69	70	69	64	54	47	49	44	43	21	22
			Unoccupied	53	53	57	36	22	19	17	11	12	10	8	11	12	8	10	13	15	14	15	20	30	37	35	40	41	63	62	
	Percentage Occupied	37%	37%	32%	57%	74%	77%	80%	87%	86%	88%	90%	87%	86%	90%	88%	85%	82%	83%	82%	76%	64%	56%	58%	52%	51%	25%	26%			


Location	Side	Zone	Between	Capacity	0600	0630	0700	0730	0800	0830	0900	0930	1000	1030	1100	1130	1200	1230	1300	1330	1400	1430	1500	1530	1600	1630	1700	1730	1800	1830	1900
Darley Rd	North	G	Charles & Falls	19	4	6	4	4	5	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	5	4	4	3	3	
	South	H	Charles & Falls	5	3	3	3	3	3	4	4	4	4	4	4	3	3	3	3	4	4	3	3	3	3	3	3	3	3	3	
		Total			24	7	9	7	7	8	8	8	8	8	8	8	7	7	7	8	8	7	7	7	7	7	8	7	7	6	6
	Unoccupied			17	15	17	17	16	16	16	16	16	16	16	16	17	17	17	16	16	17	17	17	17	17	17	16	17	17	18	18
	Percentage Occupied			29%	38%	29%	29%	33%	33%	33%	33%	33%	33%	33%	33%	29%	29%	29%	33%	33%	29%	29%	29%	29%	29%	29%	33%	29%	29%	25%	25%

TTM Data

TTM Reference: 20SYD0010
Location: Lilyfield
Date: Saturday, 25 January 2020
Weather: Fine
Notes:



Total Area Capacity		Capacity	0600	0630	0700	0730	0800	0830	0900	0930	1000	1030	1100	1130	1200	1230	1300	1330	1400	1430	1500	1530	1600	1630	1700	1730	1800	1830	1900
		264	67	79	84	82	100	104	110	109	102	106	107	120	91	105	102	97	99	93	94	91	97	91	93	105	99	92	89
		Unoccupied	197	185	180	182	164	160	154	155	162	158	157	144	173	159	162	167	165	171	170	173	167	173	171	159	165	172	175
		Percentage Occupied	25%	30%	32%	31%	38%	39%	42%	41%	39%	40%	41%	45%	34%	40%	39%	37%	38%	35%	36%	34%	37%	34%	35%	40%	38%	35%	34%



Location	Side	Zone	Between	Capacity	0600	0630	0700	0730	0800	0830	0900	0930	1000	1030	1100	1130	1200	1230	1300	1330	1400	1430	1500	1530	1600	1630	1700	1730	1800	1830	1900
Hawthorne Pde	East	B	Dobroyde & Learmonth	43	9	8	10	9	18	19	20	16	18	16	14	17	11	12	15	9	11	10	10	10	10	8	9	9	10	8	10
		D	Learmonth & Waratah	50	8	8	10	9	12	12	10	13	11	12	14	18	12	13	17	17	11	12	11	14	11	9	13	19	16	12	13
	West	A	Dobroyde & Learmonth	30	12	17	14	14	17	20	21	17	17	18	21	21	17	19	19	16	13	16	14	14	16	15	13	17	16	15	13
		C	Learmonth & Waratah	33	18	14	18	18	18	19	19	23	18	20	17	23	16	18	19	21	17	15	22	24	21	21	23	26	21	21	23
	Total			156	47	47	52	50	65	70	70	69	64	66	66	79	56	62	70	63	52	53	57	62	58	53	58	71	63	56	59
	Unoccupied			109	109	109	104	106	91	86	86	87	92	90	90	77	100	94	86	93	104	103	99	94	98	103	98	85	93	100	97
	Percentage Occupied			30%	30%	33%	32%	42%	45%	45%	44%	41%	42%	42%	51%	36%	40%	45%	40%	33%	34%	37%	40%	37%	34%	37%	46%	40%	36%	38%	

Location	Side	Zone	Between	Capacity	0600	0630	0700	0730	0800	0830	0900	0930	1000	1030	1100	1130	1200	1230	1300	1330	1400	1430	1500	1530	1600	1630	1700	1730	1800	1830	1900
Canal Rd	East	F	Leichhardt Men's Shed & Southern End	16	3	3	3	3	3	3	3	3	3	3	3	3	3	3	2	2	1	1	1	1	1	1	2	2	1	1	1
	West	E	Leichhardt Men's Shed & Southern End	68	10	22	22	22	25	24	30	30	29	31	32	32	25	33	22	25	39	32	30	22	32	30	27	26	29	29	23
	Total			84	13	25	25	25	28	27	33	33	32	34	35	35	28	36	24	27	40	33	31	23	33	31	29	28	30	30	24
	Unoccupied				71	59	59	59	56	57	51	51	52	50	49	49	56	48	60	57	44	51	53	61	51	53	55	56	54	54	60
Percentage Occupied				15%	30%	30%	30%	33%	32%	39%	39%	38%	40%	42%	42%	33%	43%	29%	32%	48%	39%	37%	27%	39%	37%	35%	33%	36%	36%	29%	


Location	Side	Zone	Between	Capacity	0600	0630	0700	0730	0800	0830	0900	0930	1000	1030	1100	1130	1200	1230	1300	1330	1400	1430	1500	1530	1600	1630	1700	1730	1800	1830	1900
Darley Rd	North	G	Charles & Falls	19	4	4	4	4	4	4	4	4	3	3	3	3	4	4	5	4	4	4	3	3	3	4	3	3	3	3	3
	South	H	Charles & Falls	5	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3
	Total			24	7	7	7	7	7	7	7	7	6	6	6	6	7	8	7	7	7	7	6	6	6	7	6	6	6	6	6
	Percentage Occupied			29%	29%	29%	29%	29%	29%	29%	29%	29%	25%	25%	25%	25%	29%	29%	33%	29%	29%	29%	25%	25%	25%	29%	25%	25%	25%	25%	25%

TTM Data

TTM Reference: 20SYD0010
Location: Lilyfield
Date: Sunday, 26 January 2020
Weather: Fine
Notes:



Total Area Capacity		Capacity	0600	0630	0700	0730	0800	0830	0900	0930	1000	1030	1100	1130	1200	1230	1300	1330	1400	1430	1500	1530	1600	1630	1700	1730	1800	1830	1900
		264	72	73	89	96	113	107	112	126	116	102	93	78	78	85	76	85	87	83	84	73	83	89	83	81	80	88	80
		Unoccupied	192	191	175	168	151	157	152	138	148	162	171	186	186	179	188	179	177	181	180	191	181	175	181	183	184	176	184
		Percentage Occupied	27%	28%	34%	36%	43%	41%	42%	48%	44%	39%	35%	30%	30%	32%	29%	32%	33%	31%	32%	28%	31%	34%	31%	31%	30%	33%	30%



Location	Side	Zone	Between	Capacity	0600	0630	0700	0730	0800	0830	0900	0930	1000	1030	1100	1130	1200	1230	1300	1330	1400	1430	1500	1530	1600	1630	1700	1730	1800	1830	1900
Hawthorne Pde	East	B	Dobroyde & Learmonth	43	9	8	13	17	15	25	20	20	17	18	11	10	11	12	7	8	10	9	7	8	8	10	11	11	14	13	
		D	Learmonth & Waratah	50	8	12	12	12	15	16	17	22	22	15	19	17	17	15	17	17	13	16	16	12	13	17	12	11	14	18	13
	West	A	Dobroyde & Learmonth	30	13	11	13	15	18	14	14	22	17	13	13	11	10	15	11	11	16	17	13	13	14	14	11	13	15	17	11
		C	Learmonth & Waratah	33	18	20	21	21	33	23	22	23	22	17	22	16	15	16	16	25	19	16	18	16	20	22	24	22	19	19	25
	Total			156	48	51	59	65	81	78	73	87	78	63	65	54	53	58	51	61	58	58	56	48	55	61	57	57	59	68	62
	Unoccupied			108	105	97	91	75	78	83	69	78	93	91	102	103	98	105	95	98	98	100	108	101	95	99	99	97	88	94	
Percentage Occupied			31%	33%	38%	42%	52%	50%	47%	56%	50%	40%	42%	35%	34%	37%	33%	39%	37%	37%	36%	31%	35%	39%	37%	37%	38%	44%	40%		

Location	Side	Zone	Between	Capacity	0600	0630	0700	0730	0800	0830	0900	0930	1000	1030	1100	1130	1200	1230	1300	1330	1400	1430	1500	1530	1600	1630	1700	1730	1800	1830	1900
Canal Rd	East	F	Leichhardt Men's Shed & Southern End	16	2	2	3	3	2	2	2	3	2	2	2	2	2	2	2	2	2	2	3	2	2	2	2	2	1	1	
	West	E	Leichhardt Men's Shed & Southern End	68	16	14	21	22	24	20	32	31	31	32	21	17	18	20	18	17	21	18	20	18	22	22	20	18	16	15	14
	Total			84	18	16	24	25	26	22	34	34	33	34	23	19	20	22	20	19	23	20	23	20	24	24	22	20	17	16	14
	Unoccupied			66	68	60	59	58	62	50	50	51	50	61	65	64	62	64	65	61	64	61	64	60	60	62	64	67	68	70	
Percentage Occupied			21%	19%	29%	30%	31%	26%	40%	40%	39%	40%	27%	23%	24%	26%	24%	23%	27%	24%	27%	24%	29%	29%	26%	24%	20%	19%	17%		


Location	Side	Zone	Between	Capacity	0600	0630	0700	0730	0800	0830	0900	0930	1000	1030	1100	1130	1200	1230	1300	1330	1400	1430	1500	1530	1600	1630	1700	1730	1800	1830	1900
Darley Rd	North	G	Charles & Falls	19	3	3	3	3	3	4	2	2	2	2	2	2	2	2	2	3	2	2	2	1	1	1	1	1	1	1	
	South	H	Charles & Falls	5	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3
	Total			24	6	6	6	6	6	7	5	5	5	5	5	5	5	5	5	6	5	5	5	4	4	4	4	4	4	4	4
	Percentage Occupied			25%	25%	25%	25%	25%	25%	29%	21%	21%	21%	21%	21%	21%	21%	21%	21%	21%	25%	21%	21%	21%	17%	17%	17%	17%	17%	17%	17%

TTM Data

TTM Reference: 20SYD0010
Location: Lilyfield
Date: Tuesday, 28 January 2020
Weather: Fine
Notes:



Total Area Capacity		Capacity	0600	0630	0700	0730	0800	0830	0900	0930	1000	1030	1100	1130	1200	1230	1300	1330	1400	1430	1500	1530	1600	1630	1700	1730	1800	1830	1900
		264	89	93	90	122	128	145	143	148	148	154	148	142	141	143	135	150	153	142	145	140	137	142	134	128	126	124	114
		Unoccupied	175	171	174	142	136	119	121	116	116	110	116	122	123	121	129	114	111	122	119	124	127	122	130	136	138	140	150
		Percentage Occupied	34%	35%	34%	46%	48%	55%	54%	56%	56%	58%	56%	54%	53%	54%	51%	57%	58%	54%	55%	53%	52%	54%	51%	48%	48%	47%	43%



Location	Side	Zone	Between	Capacity	0600	0630	0700	0730	0800	0830	0900	0930	1000	1030	1100	1130	1200	1230	1300	1330	1400	1430	1500	1530	1600	1630	1700	1730	1800	1830	1900
Hawthorne Pde	East	B	Dobroyde & Learmonth	43	14	16	18	22	22	25	23	22	22	24	22	21	20	15	15	18	17	14	15	16	16	16	16	16	16	16	22
		D	Learmonth & Waratah	50	12	13	10	12	12	11	13	12	10	9	11	10	10	11	11	15	15	13	14	16	16	17	17	16	16	16	15
	West	A	Dobroyde & Learmonth	30	20	20	17	17	16	18	18	21	20	18	17	17	17	20	20	20	20	19	19	16	15	15	16	16	18	18	19
		C	Learmonth & Waratah	33	18	17	14	15	14	13	13	14	15	17	15	16	16	17	15	18	19	15	15	15	14	17	16	18	19	19	21
	Total			156	64	66	59	66	64	67	67	69	67	68	65	64	63	63	61	71	71	61	63	63	61	65	65	66	69	69	77
	Unoccupied			92	90	97	90	92	89	89	87	89	88	91	92	93	93	95	85	85	95	93	93	95	91	91	90	87	87	79	
	Percentage Occupied			41%	42%	38%	42%	41%	43%	43%	44%	43%	44%	42%	41%	40%	40%	39%	46%	46%	39%	40%	40%	39%	42%	42%	42%	44%	44%	49%	

Location	Side	Zone	Between	Capacity	0600	0630	0700	0730	0800	0830	0900	0930	1000	1030	1100	1130	1200	1230	1300	1330	1400	1430	1500	1530	1600	1630	1700	1730	1800	1830	1900
Canal Rd	East	F	Leichhardt Men's Shed & Southern End	16	3	3	4	5	11	11	12	12	12	13	14	12	12	12	11	11	13	12	12	11	12	12	12	8	6	6	2
	West	E	Leichhardt Men's Shed & Southern End	68	14	16	21	45	47	61	58	59	58	61	59	58	58	60	55	57	61	61	61	60	58	58	51	48	46	44	30
Total				84	17	19	25	50	58	72	70	71	70	74	73	70	70	72	66	68	74	73	73	71	70	70	63	56	52	50	32
Unoccupied				67	65	59	34	26	12	14	13	14	10	11	14	14	12	18	16	10	11	11	13	14	14	21	28	32	34	52	
Percentage Occupied				20%	23%	30%	60%	69%	86%	83%	85%	83%	88%	87%	83%	83%	86%	79%	81%	88%	87%	87%	87%	85%	83%	83%	75%	67%	62%	60%	38%


Location	Side	Zone	Between	Capacity	0600	0630	0700	0730	0800	0830	0900	0930	1000	1030	1100	1130	1200	1230	1300	1330	1400	1430	1500	1530	1600	1630	1700	1730	1800	1830	1900	
Darley Rd	North	G	Charles & Falls	19	5	5	3	3	3	3	3	3	4	5	3	3	3	3	4	3	3	4	4	3	3	4	3	3	2	2	2	
	South	H	Charles & Falls	5	3	3	3	3	3	3	3	5	7	7	7	5	5	5	5	7	5	5	5	3	3	3	3	3	3	3	3	
	Total			24	8	8	6	6	6	6	6	8	11	12	10	8	8	8	8	11	8	8	9	6	6	7	6	6	5	5	5	
	Unoccupied				16	16	18	18	18	18	18	16	13	12	14	16	16	16	16	13	16	16	15	18	18	17	18	18	19	19	19	19
	Percentage Occupied				33%	33%	25%	25%	25%	25%	25%	33%	46%	50%	42%	33%	33%	33%	33%	46%	33%	33%	38%	25%	25%	29%	25%	25%	21%	21%	21%	21%

TTM Data

TTM Reference: 20SYD0010
Location: Lilyfield
Date: Wednesday, 29 January 2020
Weather: Fine
Notes:



Total Area Capacity		Capacity	0600	0630	0700	0730	0800	0830	0900	0930	1000	1030	1100	1130	1200	1230	1300	1330	1400	1430	1500	1530	1600	1630	1700	1730	1800	1830	1900
		264	96	102	104	116	133	146	151	150	156	156	154	154	156	150	143	145	146	136	134	135	144	141	147	155	157	126	127
		Unoccupied	168	162	160	148	131	118	113	114	108	108	110	110	108	114	121	119	118	128	130	129	120	123	117	109	107	138	137
		Percentage Occupied	36%	39%	39%	44%	50%	55%	57%	57%	59%	59%	58%	58%	59%	57%	54%	55%	55%	52%	51%	51%	55%	53%	56%	59%	59%	48%	48%



Location	Side	Zone	Between	Capacity	0600	0630	0700	0730	0800	0830	0900	0930	1000	1030	1100	1130	1200	1230	1300	1330	1400	1430	1500	1530	1600	1630	1700	1730	1800	1830	1900
Hawthorne Pde	East	B	Dobroyde & Learmonth	43	16	18	18	17	18	19	19	19	18	17	16	17	19	19	18	18	16	16	18	18	22	22	18	17	20	18	18
		D	Learmonth & Waratah	50	12	12	14	14	13	15	13	13	14	15	15	15	18	16	13	13	11	11	12	13	12	15	19	19	16	16	
	West	A	Dobroyde & Learmonth	30	16	16	16	13	12	19	18	15	18	16	17	15	13	13	13	13	13	13	14	14	17	18	18	20	19	20	19
		C	Learmonth & Waratah	33	16	15	14	13	14	15	15	13	14	13	12	12	13	12	13	13	15	15	14	14	19	16	22	25	23	15	17
	Total			156	60	61	62	57	57	68	65	60	64	61	60	59	63	60	57	57	55	55	58	59	70	68	73	81	81	69	70
	Unoccupied				96	95	94	99	99	88	91	96	92	95	96	97	93	96	99	99	101	101	98	97	86	88	83	75	75	87	86
	Percentage Occupied				38%	39%	40%	37%	37%	44%	42%	38%	41%	39%	38%	38%	40%	38%	37%	37%	35%	35%	37%	38%	45%	44%	47%	52%	52%	44%	45%

Location	Side	Zone	Between	Capacity	0600	0630	0700	0730	0800	0830	0900	0930	1000	1030	1100	1130	1200	1230	1300	1330	1400	1430	1500	1530	1600	1630	1700	1730	1800	1830	1900
Canal Rd	East	F	Leichhardt Men's Shed & Southern End	16	4	4	3	6	8	10	14	15	14	16	16	16	15	12	11	12	13	12	11	11	10	10	9	8	9	3	3
	West	E	Leichhardt Men's Shed & Southern End	68	22	26	27	42	57	57	62	65	68	69	68	68	67	67	62	65	67	58	56	56	55	53	55	56	58	46	46
Total				84	26	30	30	48	65	67	76	80	82	85	84	84	82	79	73	77	80	70	67	67	65	63	64	64	67	49	49
Unoccupied				58	54	54	36	19	17	8	4	2	-1	0	0	2	5	11	7	4	14	17	17	19	21	20	20	17	35	35	35
Percentage Occupied				31%	36%	36%	57%	77%	80%	90%	95%	98%	101%	100%	100%	98%	94%	87%	92%	95%	83%	80%	80%	77%	75%	76%	76%	80%	58%	58%	58%

Location	Side	Zone	Between	Capacity	0600	0630	0700	0730	0800	0830	0900	0930	1000	1030	1100	1130	1200	1230	1300	1330	1400	1430	1500	1530	1600	1630	1700	1730	1800	1830	1900
Darley Rd	North	G	Charles & Falls	19	7	8	9	7	8	8	7	7	7	7	7	7	7	7	7	6	7	8	6	6	6	7	6	6	6	5	5
	South	H	Charles & Falls	5	3	3	3	4	3	3	3	3	3	3	3	4	4	4	6	5	4	3	3	3	3	3	4	4	3	3	3
	Total			24	10	11	12	11	11	11	10	10	10	10	10	11	11	11	13	11	11	11	9	9	9	10	10	10	9	8	8
	Percentage Occupied			42%	46%	50%	46%	46%	46%	46%	42%	42%	42%	42%	42%	46%	46%	46%	54%	46%	46%	46%	38%	38%	38%	42%	42%	42%	38%	33%	33%

APPENDIX C – Inner West Council Meeting Minutes

Minutes

Meeting:	M4-M5 Link Project – Introduction and Construction Parking and Access Strategy
Meeting Date:	Wednesday, 8 August 2018, 10am
Meeting Location:	Inner West Council, St Peters Depot – 15 Unwins Bridge Road, St Peters
Attendees:	<div>Candice Camacho (CC) Interface Mgr – WestConnex M4-M5 Link</div> <div>Erran Woodward (EW) Environmental Approvals Mgr – WestConnex M4-M5 Link</div> <div>Alex Gosper (AG) Traffic Mgr – WestConnex M4-M5 Link</div> <div>Louisa Bertino-Clarke (LB) Community Engagement Manager Sydney Motorway Corporation</div> <div>Jade McManus (JM) Env. Manager – Sydney Motorway Corporation</div> <div>Ken Welsh (KW) Transport Planner – Inner West Council</div> <div>Felix Liu (FL) Engineer WestConnex Unit – Inner West Council</div> <div>Bruce Muha (BH) Engineer Traffic & Projects – Inner West Council</div>
Distribution:	As above
Attachments	Presentation: Construction Parking and Access Strategy
Next Meeting:	As required

Agenda:

1. General overview of the Construction Parking and Access Strategy
2. Strategy for Parramatta Road East and West (PREW) (also known as Muirs Site at Haberfield/Ashfield)
3. Strategy for Pyrmont Bridge Road site (Annandale/Camperdown)
4. Strategy for other sites (St Peters, Northcote Street, Parramatta Road Ventilation Facility and Wattle Street ramps)
5. Shuttle service routes
6. Bignell Lane (Camperdown) closures
7. Worker Code of Conduct
8. Inner West Council lessons learnt

Discussion:

Construction parking and access strategy:

1. General

- a. The M4-M5 Link Mainline Tunnels design and construction partner Lend Lease Samsung Bouygues Joint Venture (LSBJV) have developed a strategy which aims to accommodate the majority of worker parking on site as a way of reducing the impact to on-street parking.
- b. The project looks to achieve this through satellite parking sites with shuttle bus services to key construction sites.
- c. The parking strategy has been based on conservative workforce numbers (and does not account for potential carpooling and public transport uses by workers)
- d. The project will encourage carpooling and public transport through the onboarding and induction process. The project will also look to incentivise shuttle bus use.
- e. A parking patrol survey for kerbside occupancy at PREW site has started
- f. A parking patrol survey for Pyrmont Bridge Road will occur once all premises have been vacated.
- g. All parking areas which will be established will be sealed and line-marked.

2. PREW (Muir's Site):

- a. Provides prioritised parking for Wattle Street and Northcote Street sites

- b. Estimated workforce utilising this site = 260 - 220 car spaces available
- c. Existing no parking/ no stopping zones to be retained on Bland Street, Parramatta Road (southbound)
- d. Parking removal to facilitate site distance, heavy vehicle deceleration and access to driveways.
 - i. Removal of 15 parking spaces on Parramatta Road (northbound) – 24 hour clearway
 - ii. Removal of 7 parking spaces on Alt Street (east of Parramatta Road) – No stopping zone to be installed
- e. Initially designed with bus stop relocation 150m north of existing corner Parramatta Road/Bland Street – reduces interface between trucks and buses at access points; note bus stop distances will be investigated by LSBJV with the intention of minimising distances between stops. This may result in a relocation to the south, due to residents south of this location already having impacts due to existing M4 East worksites and changes.
- f. Change clearway south of Alt Street from peak periods to 24hrs.

3. Pyrmont Bridge Road

- a. Parking removal to facilitate site distance, heavy vehicle deceleration, worker transport shuttle stop, demolition, hoarding and access to driveways.
 - i. Removal of 7 parking spaces on Pyrmont Bridge Road (westbound)
 - ii. Removal of 18 off-peak timed parking spaces on Parramatta Road (westbound)
 - iii. Removal of 8 timed parking spaces on Mallet Street (Northbound)
- b. Parking removals proposed to be partially offset by the relocation of the businesses within this block.
- c. The Strategy initially proposed:
 - i. No stopping on Mallet Street (just north of Parramatta Rd), however this will be updated to no-parking to allow short-term holding in the case of backlog at the site access driveway (prevents truck circling – reduces congestion).
 - ii. No stopping on Parramatta Road adjacent to site, however this will be updated to no-parking to allow short-term holding in the case of backlog at the site access driveway.
 - iii. Existing bus stop on Parramatta Road (westbound) corner Mallet Street to be relocated 60Mm east
 - iv. Some parking available onsite (about 30 spaces) for senior project staff, visitors and deliveries.

4. Other sites

- a. White Bay Site
 - i. Prioritised worker parking for Pyrmont Bridge Road site
 - ii. Truck marshalling area– project team confirmed that the truck marshalling area would have capacity for about 10 truck and dogs available in addition to light vehicle parking, however the team are still working on layout
 - iii. Proposed car parking availability of about 200 spaces
- b. Campbell Road primary parking for St Peters site – reduced parking initially, supported by parking at the Main Site Office (Mascot) and coincides with reduced scope of works during this period. Then following an expanded parking area when the remaining site area is taken over from New M5 project team providing an excess of 300 spaces.

5. Shuttle service routes

- a. Route 1 - PREW to Northcote Street and Wattle Street
- b. Route 2 - White Bay to PBR
- c. Route 3 - Mascot to St Peters

6. Bignell Lane (Camperdown) closures proposed to Inner West Council for consideration

- a. In accordance with the EIS the team will realign Bignell Lane to establish the PBR site and demolish existing buildings along the existing Bignell Lane alignment.
- b. The M4-M5 Link project team propose to close the part of Bignell Lane which will eventually be diverted, to facilitate demolition of buildings and better manage safety during this activity. The following will be ensured as part of this process:
 - i. Resident access to Bignell Lane will be maintained. Access controls will be determined depending on the resident / occupier's needs and access requirements.

- ii. M4-M5 Link would consult with residents and businesses to understand concerns and/or access requirements prior to further development and a decision being made.

7. Worker Code of Conduct

- a. M4-M5 Link Project is currently developing a worker code of conduct to address impacts of worker behaviour, a known issue on previous projects in this location.
- b. There is a potential for the code of conduct to be included in the EBA.
- c. Council requests possible inclusion of the code of conduct in WCX Community Liaison Forum. Project Comms team will work on a strategy with Council to facilitate this.

8. Inner West Council lessons learnt

- a. Light vehicle use of local roads
 - i. Encourage workforce light vehicles in and out of the sites using main roads - possible inclusion in Code of Conduct and a 'right turn only' sign at the exit of the site on Alt Street (directing light vehicles to Parramatta Road)
- b. Worker behaviour to be managed closely.
- c. Messaging about site activities in the past has been muddled/unclear and does not inspire confidence in local residents. Resident feedback is that when passed on to a Community Information line they are given the run around.
 - i. Messaging and communication from ground staff or workers onsite could improve this process. For example Messaging from parking survey/investigations on when, why, how and how long could be made available to residents via site staff conducting work. This could include short information sheets, training for work force.
- d. Clearly communicate management strategies to community.

Item No.	Outcomes/ Action	Resp	Date
1.0	Inner West Council to provide cumulative total of HVs in the Glebe Island and White Bay area	KW	Completed
	M4-M5 Link to provide updated numbers for HV usage.	AG	17/08/18
	KW advised SPI site will become increasingly congested as Boral would be tripling the size of their facility which would mean the performance of the intersection of Princes Highway and Canal Road would perform at LoS F at all times (not just during peak periods. The intersection and its operation are being reviewed as part of this work.	All	Noted
	IWC noted improvement in the approach to off-street parking management	All	Noted
	IWC noted a preference for SPECT vehicles if HV haulage was to occur on local roads. IWC to provide presentation on SPECT vehicles	KW	Completed
2.0	IWC advised the Approval process for local road use will be through CTMP.	All	Noted
	Inner West Council asked M4-M5 Link to consider relocating the bus stop further to the south to improve spacing of bus stops based on local resident feedback.	All	Noted
	M4-M5 Link agreed to review the relocation of this bus stop to the south of Alt Street at the Muirs Site	AG	17/08/2018
3.0	Inner West Council advised there were limitations at the PBR strategy in relation to HV movement if site access can't be achieved.	All	Noted
	M4-M5 Link advised real time monitoring of congestion and truck movements to manage this proactively.		

	Inner West Council suggested proposed "No stopping" on Parramatta Road be changed to "No Parking" to utilise this area for Heavy Vehicle storage		
	M4-M5 Link to consider contingency routes /go around strategy for Heavy Vehicles at the PBR site and review "No Stopping" arrangement in line with IWC's suggested solution	AG	17/08/2018
	IWC advised Northeast Chester Street - two major DAs - which will see an increase in construction traffic increase on Chester St.	All	Noted
	IWC advised M4-M5 Link on Collaboration Precinct - Eveleigh to Sydney Uni/Hospital precinct to Camperdown. – Working on a Master plan and coordination due to the many DA's through the area. Potential for M4-M5 Link involvement in working toward a combined construction management plan for the area	All	Noted
4.0	M4-M5 Link project to provide clarity on Haulage strategy in the vicinity of Wattle Street	AG	31/08/2018
	<ul style="list-style-type: none"> Access via new tunnel - Wattle Street TTAMP - clarity on haulage routes 		
5.0	Inner West Council encouraged M4-M5 Link to continue engaging them re: public transport options and shuttle services as Council may be able to assist	KW	Noted
6.0	Inner West Council believes approach to closing Bignell Lane is logical but will depend on engineering and community engagement outcomes including: <ul style="list-style-type: none"> U-turn facilities for light-rigid vehicles, and provide a hammerhead u-turn facility (cul-de-sac not expected to be feasible due to swept path requirements of light-rigid trucks etc.) Close Communication and engagement regarding access requirements Precise timeline required. 	All	Noted
	M4-M5 Link to further develop proposal in consultation with IWC and impacted community/businesses	AG/EW/CC	31/08/2018
7.0	Consultation with IWC – Westconnex Community Consultative Committee re: Worker Code of Conduct	EW	31/08/2018
8.0	M4-M5 Link to carry out survey of increased of LV numbers on side streets - provide numbers pre and post to IWC	AG	31/08/2018
	Right turn only signage at site egress to improve compliance and improve visibility of LV management to surrounding community	AG	31/08/2018

APPENDIX D – City of Sydney Meeting Minutes

Minutes

Meeting:	M4-M5 Link Project – Introduction and Construction Parking and Access Strategy	
Meeting Date:	Thursday 16 August 2018, 1.30pm	
Meeting Location:	City Of Sydney offices – Town Hall	
Attendees:	Candice Camacho (CC) Interface Mgr – WestConnex M4-M5 Link Erran Woodward (EW) Environmental Approvals Mgr – WestConnex M4-M5 Link Alex Gosper (AG) Traffic Mgr – WestConnex M4-M5 Link Louisa Bertino-Clarke (LB) Community Engagement Manager Sydney Motorway Corporation Verity Turner (VT) Env. Manager – Sydney Motorway Corporation Asad Rajbhoy (AR) Traffic and Transport Planner Major Projects – CoS Joshua Faull (JF) Construction Liaison Coordinator - CoS Manbir Singh (MS) Senior Traffic Engineer – CoS Van Le (VL) Traffic Manager North – CoS	
Distribution:	As above	
Attachments	Presentation: Construction Parking and Access Strategy	
Next Meeting:	Ongoing meeting requirements – to be confirmed.	

Agenda:

1. General overview of the Construction Parking and Access Strategy
2. Parking strategy for St Peters Interchange Site and Pyrmont Bridge road
3. Use of local roads and shuttle bus service routes
4. Worker Code of Conduct
5. City of Sydney Council Lessons Learnt
6. Other business

Discussion:

Construction parking and access strategy:

1. General

- a. The M4-M5 Link Mainline Tunnels design and construction partner Lendlease Samsung Bouygues Joint Venture (LSBJV) have developed a strategy which aims to accommodate the majority of worker parking on site as a way of reducing the impact to on-street parking.
- b. The project looks to achieve this through satellite parking sites with shuttle bus services to key construction sites.
- c. The parking strategy has been based on conservative workforce numbers (and does not account for potential carpooling and public transport use by workers)
- d. The project will encourage carpooling and public transport through the onboarding and induction process. The project will also look to incentivise shuttle bus use.
- e. Clarification of Cos and Inner West Council boundaries – CoS/RMS shared owners of Pyrmont Bridge Road and Parramatta Road

2. St Peters Interchange and Pyrmont Bridge Road

- a. Parking removal to facilitate site distance, heavy vehicle deceleration, worker transport shuttle stop, demolition, hoarding and access to driveways.
 - i. Proposed removal of approximately 7 parking spaces on Pyrmont Bridge Road (westbound)
 - ii. Proposed removal of approximately 18 off-peak timed parking spaces on Parramatta Road (westbound)

- iii. Proposed removal of approximately 8 timed parking spaces on Mallet Street (Northbound)
- b. Parking removal proposed to be partially offset by the relocation of the businesses within this block.
- c. The Strategy initially proposed:
 - i. No parking on Mallet Street (just north of Parramatta Rd) to allow left turn for heavy vehicles into site.
 - ii. No parking on Parramatta Road adjacent to site, to allow left turn for heavy vehicles into Mallet Street.
 - iii. Existing bus stop on Parramatta Road (westbound) corner Mallet Street to be relocated 60m east for a minimum 6 month period up to duration of the project– further consultation required if final position for the bus stop sites within Cos Council area.
 - iv. In relation to bus movements through the area it was confirmed that no buses turned left from Mallet Street on to Parramatta Road – all bus movements through the area move east-west along Parramatta Road.
- d. White Bay Site
 - i. Prioritised worker parking for Pymont Bridge Road site – however in early stages the indicative workforce will be 25 people who will be able to use onsite parking.
 - ii. Truck marshalling area– project team confirmed that the truck marshalling area would have capacity for about 10 truck and dogs available in addition to light vehicle parking, however the team are still working on layout
 - iii. Proposed car parking availability of about 200 spaces
- e. Campbell Road primary parking for St Peters site – reduced parking initially, supported by parking at the Main Site Office (Mascot) for staff, and coincides with reduced scope of works during this period. Then following an expanded parking area when the remaining site area is taken over from New M5 project team providing an excess of around 300 spaces.
- f. CoS raised concern relating to increased traffic on local roads in the vicinity of focused parking sites

3. Local road use and shuttle service routes (see attached presentation)

- a. Light vehicle use of local roads
 - i. Encourage workforce light vehicles in and out of the sites using main roads - possible inclusion in Code of Conduct
- b. Route 2 - White Bay to PBR – shuttle service runs along borders of CoS Council area.
- c. Route 3 - Mascot to St Peters – No local road use.
- d. LSBJV advised frequency of shuttle services during peak periods would be a service every 15-20 minutes – a fleet of 16-20 buses across sites

4. Worker Code of Conduct

- a. M4-M5 Link Project is currently developing a worker code of conduct to address impacts of worker behaviour, a known issue on previous projects in this location.
- b. There is a potential for the code of conduct to be included in the EBA.

5. City of Sydney lessons learnt

- a. CoS advised that the Council is strongly opposed to the WestConnex Project so any negative feedback from community will escalate to media and a political level.
- b. Where possible, try not to be seen – don't display negative behaviours that will draw community attention.
- c. Worker behaviour to be managed closely.
- d. Clearly communicate management strategies to community.
- e. Loading and unloading of passengers using shuttle services to be undertaken within site boundaries to reduce perception of workforce loitering

6. Other business

- a. CoS advised that other areas of interest included impacts to assets, pedestrian detours and road detours using local roads.

Item No.	Outcomes/ Action	Resp	Date
1.0	City of Sydney to provide map of CoS boundaries	AR	ASAP
	City of Sydney asked LSBJV to put a strong focus on the use of public transport ie. Use of St Peters Station for the SPI site and suggested site based signage indicating the closest public transport with direction	All	Noted
	LSBJV to consider use of site based signage and internal posters to direct workforce to public transport as part of the workforce communications strategy	All	Noted
	LSBJV confirmed that they would be encouraging alternative transport through Induction and Onboarding, Incentivising workforce provision of bike racks – LSBJV also advised they would be conducting worker surveys to identify which public transport hubs to introduce shuttle services and would also consider shift staggering.	All	Noted
2.0	CoS asked that after LSBJV's use for the Campbell Street site for parking, would the area be converted to green/recreational space – SMC confirmed that it would be converted.	All	Noted
	LSBJV to report quarterly on effectiveness of the Construction Parking and Access Strategy – to be provided to CoS. This will provide CoS the opportunity to comment and provide feedback	All	Noted
	LSBJV to consider CoS request on how demonstrate evidence of management strategies in quarterly reporting.	All	Noted
	LSBJV advised CoS that they were open to ongoing feedback from CoS regarding concerns and issues.	All	Noted
3.0	Although LSBJV have developed the Construction Parking and Access Strategy it can not guarantee that there will be no overflow of worker parking on local roads.	All	Noted
	VL advised that there was a potential for traffic congestion, particularly during peak periods, could impact on travel times for shuttles.	All	Noted
4.0	Nil	N/A	N/A
5.0	LSBJV note and will consider all lessons learnt provided by CoS in development of the Construction Parking and Access Strategy and management of community.	All	Noted
	LSBJV advised that they could not brand all site vehicles (ie trucks and project vehicles) due to risk of vandalism but would consider the branding of shuttle buses.	All	Noted

APPENDIX E –Transport for NSW Consultation Record

Date	Contact	From	Notes
2.10.18	Peter Keyes	Transport for NSW – Sydney Coordination Office	Consulted as part of Traffic Coordination Group meeting (TCG) in relation to proposed bus stop relocations. Peter Keyes requested drawing / diagram to commence consultation with Bus representatives from TfNSW within his office.
30.10.18	Peter Keyes	Transport for NSW – Sydney Coordination Office	Peter Keyes confirmed at TCG meeting that bus department of TfNSW had been consulted, and had no objection to the proposed relocations.

APPENDIX F – Community Consultation Summary

Parramatta Road E/W on-street parking removal consultation												
Address	Contact Name	Phone Number	Email Address	Doorknock #1 10-Sept-18	Doorknock #2 26-Sept-18	Will parking removal affect you? If yes how?	Which streets do you park on?	Low impact Medium impact High Impact	Is there an alternative area for you to park?	Do you have any special requirements for parking? Ie, access, deliveries etc	Additional comments	Additional information to be provided
119 Alt Street	N/A	N/A	N/A	No response	No response	N/A	N/A	N/A	N/A	N/A	N/A	N/A
117 Alt Street	N/A	N/A	N/A	No response	No response	N/A	N/A	N/A	N/A	N/A	N/A	N/A
115 Alt Street	N/A	N/A	N/A	No response	No response	N/A	N/A	N/A	N/A	N/A	N/A	N/A
113 Alt Street	Vacant property (under construction)	N/A	N/A	No response	No response	N/A	N/A	N/A	N/A	N/A	Property is currently under construction	N/A
122 Alt Street	N/A	N/A		No response	No response	N/A	N/A	N/A	N/A	N/A	N/A	N/A
124 Alt Street	Withheld	Withheld	Withheld	N/A	Spoke directly with stakeholder	No, sufficient parking at property and no current issues with workers on streets	N/A	N/A	N/A	N/A	N/A	N/A
126 Alt Street	N/A	N/A	N/A	No response	No response	N/A	N/A	N/A	N/A	N/A	N/A	N/A
128 Alt Street	N/A	N/A	N/A	No response	No response	N/A	N/A	N/A	N/A	N/A	N/A	N/A
142 Alt Street	N/A	N/A	N/A	No response	No response	N/A	N/A	N/A	N/A	N/A	N/A	N/A
144 Alt Street	N/A	N/A	N/A	No response	No response	N/A	N/A	N/A	N/A	N/A	N/A	N/A
146 Alt Street	N/A	N/A	N/A	No response	No response	N/A	N/A	N/A	N/A	N/A	N/A	N/A
146a Alt Street	No contact details provided	N/A	N/A	N/A	Spoke directly with stakeholder	N/A	N/A	N/A	N/A	N/A	Unhappy with current worker parking	N/A
143 Alt Street	No contact details provided	N/A	N/A	Spoke directly with stakeholder	N/A	No, sufficient parking at property and no current issues with workers on streets	N/A	N/A	N/A	N/A	N/A	N/A
141 Alt Street	N/A	N/A	N/A	No response	No response	N/A	N/A	N/A	N/A	N/A	N/A	N/A
139 Alt Street	N/A	N/A	N/A	No response	No response	N/A	N/A	N/A	N/A	N/A	N/A	N/A
137 Alt Street	Withheld	Withheld	Withheld	Spoke directly with stakeholder	N/A	Yes, need access to be maintained at all times for her disabled daughter who has a van that picks and drops her off daily. They have applied for a disabled parking space outside of their property but have been rejected by council. Parking is currently very limited due to current working parking.	Alt Street	High impact	No	Access to be maintained at all times for disabled daughter	Workers at the Parramatta Rd E/W site will use on-site parking. Staff will be toolboxed on permitted areas to park. Meeting arranged with stakeholder to discuss project and use of the Parramatta Road E/W site	N/A

Property	Address	Contact Name	Phone Number	Doorknock #1 30-Aug-18	Doorknock #2 19-Sept-18	Doorknock #3 12- October-18	Email Address	Will parking removal affect you? If yes how?	Which streets do you park on?	Impact level	Is there an alternative area for you to park?	Do you have any special requirements for parking? I.e. access, deliveries etc	Additional comments	Mitigation Measure
Camperdown Fitness	166 Parramatta Road	Withheld	Withheld	Meeting held on 17/09/18	N/A		N/A	Yes, customers park on the street	Mallett Street and Parramatta Road (currently). Customers will park on Pymont Bridge Road when we move.	Medium	Yes, parking spaces are included on the property	N/A	Removal of street parking will be an annoyance but is not a critical impact	Some on-street parking will be available on Mallett Street and Pymont Bridge Road outside the Project boundary
Motor Motive	196 Parramatta Road	Withheld	Withheld	Spoke directly with stakeholder	N/A		Withheld	No, as long as the spaces out front of the business remain available. Customers park on the street and the business uses the vergeside lane to store cars before entering the workshop	Parramatta Road	Low	7 Eleven/ Gordon Street	Request for access and parking spaces out front to be maintained at all times	Do not require many on-street parking spaces	Confirmed with stakeholder that parking spaces on Parramatta Road outside Motor Motive, will not be removed as part of the Project Project offered to frequently monitor Gordon Street to ensure workers are not parking there
Mansours	190-192 Parramatta Road	Withheld	Withheld	Spoke directly with stakeholder	N/A		Withheld	No, as long as the spaces out front of the business remain available. All customers park on the street. Some parking is available on site for workers. Business does not have a high volume of customers at one time	Parramatta Road	Low	Other local streets	N/A	N/A	Confirmed with stakeholder that parking spaces on Parramatta Road outside Mansours will not be removed as part of the Project Project offered to frequently monitor Gordon Street to ensure workers are not parking there
Chim Cham Cafe	1/156-158 Parramatta Road	Withheld	Withheld	Spoke directly with stakeholder	N/A		Withheld	No	Mallett Street	Low	Business has on-site parking for workers. Customers generally walk to café of park on Parramatta Road (east of Mallett Street)	N/A	N/A	N/A
Sax and Woodwind and Brass	2-5/156-158 Parramatta Road	Withheld	Withheld	Spoke directly with stakeholder	N/A		Withheld	Yes, customers use on-street parking adjacent to the business	Mallett Street	Medium	Customers can use other street parking	N/A	Requested that Council remove the 'Loading Zone' signs adjacent to the business into timed parking spaces. They are never used for unloading.	The Project offered to create a map for customers showing available parking spaces around the business. To be sent to business prior to parking removal occurring The Project offered to investigate possibility of changing the "Loading Zone" signs on Mallett Street. Request has been raised with Project Traffic Manager.
Dental Imaging	6/ 156-158 Parramatta Road			N/A	Spoke directly with stakeholder		N/A	No, no customers parkign requirments. Staff parking is accommodated on site	Mallett Street	Low	No customers to store	N/A	N/A	N/A
Withheld	7/ 156-158 Parramatta Road			No response	No response	Spoke directly with stakeholder	N/A	No, the business has an on-site parking space at back of property	Mallett Street (to unload if required)	Low	No customers to store	N/A	N/A	N/A
Vacant property	8/ 156-158 Parramatta Road	Vacant		No response	No response	No response	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A
Value Network	9/ 156-158 Parramatta Road	Withheld	Withheld	No response	No response	Spoke directly with stakeholder		No, the business has an on-site parking space at back of property	N/A	Low	N/A	N/A	No real impact	
Vacant property	10/ 156-158 Parramatta Road	Vacant		No response	No response	No response	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A
Withheld	11/156-158 Parramatta Road	Withheld	Withheld	No response	Spoke directly with stakeholder		Withheld	Yes, customers park in front of the shop. Minimal staff parking is available in the area	Mallett Street	Medium	Remaining parking on Mallet Street	N/A	Supported request for Council change the 'Loading Zone' signs adjacent to the business into timed parking spaces. They are never used for unloading.	The Project offered to investigate possibility of changing the "Loading Zone" signs on Mallett Street. Request has been raised with Project Traffic Manager. Stakeholder was interested in also receiving a map to place online for customers
	12/156-158 Parramatta Road			No response	No response	No response	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A
	13/156-158 Parramatta Road			No response	No response	No response	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A
	14/156-158 Parramatta Road			No response	No response	No response	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A
	15/156-158 Parramatta Road			No response	No response	No response	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A
	16/156-158 Parramatta Road			No response	No response	No response	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A
	17/156-158 Parramatta Road			No response	No response	No response	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A
PFS Accountants	10 D/Mallett Street	Withheld	Withheld	Spoke directly with stakeholder	N/A		Withheld	No, as long as the spaces out front of the business remain available	Mallett Street	Medium	N/A	N/A	N/A	Confirmed with stakeholder that parking spaces on Mallett Street outside PFS Accounting will not be removed as part of the Project
Buildcorp	Level 4/10 Mallett Street	Withheld	Withheld	Spoke directly with stakeholder	N/A		Withheld	No, current on-street parking is timed and therefore not useful for staff. Business has leased parking spaces off-site for workers	Mallett Street	Low	Other local streets Additional leased parking spaces	N/A	Parking has been a long-term issue for the company	N/A
James Squire Brewery	99 Pymont Bridge Road	Withheld	Withheld	Spoke directly with stakeholder	N/A		Withheld	No	N/A	Low	Company has parking off-site for employees. No customers to the property	Deliveries occur via Pymont Bridge Road. No special requirements other than access required to driveway	Removal of on-street parking may actually help with some of their deliveries that reverse into the premises	N/A
Terraces	54 Pymont Bridge Road			No response	No response	No response	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A
Terraces	56 Pymont Bridge Road			No response	No response	No response	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A
Terraces	56A Pymont Bridge Road	Withheld	Withheld	No response	No response	Phonecall with stakeholder	N/A	No, as long as parking remains on their side of the road. Residents also have a parking space around the back.	Pymont Bridge Road and inside garage	Low	N/A	N/A	No real impact	N/A
Terraces	58 Pymont Bridge Road	Withheld	Withheld	No response	No response	Phonecall with stakeholder	N/A	Moving out shortly so not concerned, opposed to project. There is one parking space at back of property and parking hasn't been an issue.	N/A	N/A	N/A	N/A	No real impact	N/A
Terraces	60 Pymont Bridge Road	Withheld	Withheld	Spoke directly with stakeholder	N/A	N/A	N/A	No, on-street parking will remain on their side of the road	Pymont Bridge Road	N/A	N/A	N/A	N/A	N/A
Terraces	62 Pymont Bridge Road			No response	No response	No response	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A
Terraces	64 Pymont Bridge Road	Withheld		Spoke directly with stakeholder	N/A	N/A	N/A	No, was not concerned at all	Pymont Bridge Road	N/A	N/A	N/A	N/A	N/A
Terraces	66 Pymont Bridge Road			No response	No response	No response	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A
Terraces	67 Pymont Bridge Road			No response	No response	Phone call also attempted	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A
Terraces	68 Pymont Bridge Road			No response	No response	No response	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A
Terraces	69 Pymont Bridge Road			No response	No response	No response	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A
Terraces	71 Pymont Bridge Road	Withheld		Discussed on phonecall	N/A	N/A	Withheld	Maybe	Pymont Bridge Road	Low	Some of the tenants use on-street parking on Pymont Bridge Road. Shouldn't be a major issue but some people may have to park elsewhere	N/A	N/A	N/A
Terraces	73 Pymont Bridge Road	Withheld		Discussed on phonecall	N/A	N/A	Withheld	Maybe	Pymont Bridge Road	Low	Some of the tenants use on-street parking on Pymont Bridge Road. Shouldn't be a major issue but some people may have to park elsewhere	N/A	N/A	N/A
Terraces	73 Pymont Bridge Road	Withheld		No response	N/A	Phonecall with stakeholder	N/A	No, uses public transport	Pymont Bridge Road	Low	N/A	N/A	Parking spaces out front of properties must remain available for emergency vehciles. They have a number of elderly tenants who may require emergency assistance	Parking spaces out front of property are not proposed to be removed.

Terraces	75 Pymont Bridge Road	Withheld		Discussed on phonecall	N/A		Withheld	Maybe	Pymont Bridge Road	Low	Some of the tenants use on-street parking on Pymont Bridge Road. Shouldn't be a major issue but some people may have to park elsewhere	N/A	N/A	N/A
Terraces	77 Pymont Bridge Road	Withheld		Meeting held on 26/09/18	N/A		Withheld	No, parking out front of the terraces will remain available	Pymont Bridge Road	Low	Parking out front of terraces will remain. The on-street parking is currently a clearway so not very useful during the day-time anyway	N/A	N/A	N/A
Grumpy Donuts	70 -72 Pymont Bridge Road	Withheld		Spoke directly with stakeholder	N/A		N/A	No, as long as parking on their side of the road remains available	Pymont Bridge Road	Low	N/A	N/A	N/A	N/A
Baby Bunting	1-4/78-96 Pymont Bridge Road	Withheld	Withheld	Spoke directly with stakeholder	N/A		N/A	No, business has its own dedicated parking spaces	Pymont Bridge Road	Low	N/A	N/A	N/A	N/A
Repco	74/96 Pymont Bridge Road	Withheld	Withheld	Spoke directly with stakeholder	N/A		N/A	No, business has its own dedicated parking spaces	Pymont Bridge Road	Low	N/A	N/A	N/A	N/A

APPENDIX G – Surface grouting Consultation Summary

Stakeholder	Date	Consultation	Comments
Inner west council	5/12/2019 – Meeting	<p>LSBJV explained the surface grout operation including the following:</p> <ul style="list-style-type: none"> • The work must be undertaken to improve ground conditions in the area prior to tunnelling later in the year. • Work will be undertaken on both sides of the canal and is expected to take between 3 and 6 months to complete. • Work will involve a large section of the park, including the new netball courts being fenced off, up to around 150 holes being drilled and grout being pumped into each hole. • The work area will be accessed under the NSW Roads Act • There will be some impact on parking in the area • The new netball courts are likely to be damaged during the work. • After the works are complete the park and netball courts will be restored to the condition they are prior to the work. 	<p>Concerned about impact on the new netball courts. Advised there are daily weekday bookings for the courts from March to September.</p> <p>Follow up meeting scheduled for Feb 2020</p> <p>Consultation with Netball court and park users to occur once Council confirm who the users are at the IWC meeting in February 2020.</p>
Canal Road Film Centre	12/12/2019 - Meeting	<p>LSBJV explained the surface grout operation including the following:</p> <ul style="list-style-type: none"> • The work must be undertaken to improve ground conditions in the area prior to tunnelling later in the year. • Work will be undertaken on both sides of the canal and is expected to take between 3 and 6 months to complete. • Work will involve an area being fenced off while a large number of holes are drilled and grout is pumped into each hole. • Several of the holes are within the boundary of the 1 Canal Road property. • There will be some impact on parking in the area • After the works are complete the area will be restored to the condition it was prior to the work. 	<p>No issue with the work being carried out.</p> <p>Concerned about interruption to business. Wants to be included in daily planning while working inside the property to manage potential interruptions.</p> <p>Concerned about loss of parking on Canal Road.</p>
Owner – 1 Canal Road Leichhardt	Several emails between 13/12/2019 and 31/01/2020	<p>LSBJV explained the surface grout operation including the following:</p> <ul style="list-style-type: none"> • The work must be undertaken to improve ground conditions in the area prior to tunnelling later in the year. • Work must be undertaken inside the boundary of 1 Canal Road Leichhardt. • Work is expected to take between 3 and 6 months to complete. • Work will involve an area being fenced off while a large number of holes are drilled and grout is pumped into each hole. 	<p>No issues as long as the tenant (Canal Road Film Centre) is consulted throughout and access maintained for their tenant at all times.</p>

		<ul style="list-style-type: none"> • There will be some impact on parking in the area • After the works are complete the area will be restored to the condition it was prior to the work. • The project has met with the tenant and will work with them throughout the operation. 	Access agreement form has been signed.
Blackmore Oval and Leichhardt Mens Shed	Phone calls between 3 and 6 February 2020	LSBJV has left voice messages requesting a call back from the Blackmore Oval Manager and the Leichhardt Mens Shed to discuss planned work in the area that requires access to the oval and to outline potential impacts and mitigation measures. LSBJV will continue to try reaching the manager	No feedback provided as of 6 February 2020
Café Bones	5/02/2020 6/02/2020	<p>LSBJV explained the surface grout operation including the following:</p> <ul style="list-style-type: none"> • The work must be undertaken to improve ground conditions in the area prior to tunnelling later in the year. • Work will be undertaken on both sides of the canal and is expected to take between 3 and 6 months to complete. • Work will involve an area being fenced off while a large number of holes are drilled and grout is pumped into each hole. • There will be some impact on parking in the area • A compound will be established at the end of Canal Road. • After the works are complete the area will be restored to the condition it was prior to the work <p>LSBJV asked about the businesses access requirements and requested the contact details of the business owner to discuss the work.</p> <p>LSBJV called business owner and left a voice message requesting a call back to discuss upcoming work on Canal Road and mitigation measures</p>	<p>Staff member provided contact details for the business owner.</p> <p>Staff member working at the café advised the business intermittently uses Canal Road for access.</p> <p>Staff member said he will advise the owner of the visit and planned work but also provided LSBJV contact details of the owner.</p>

Resident doorknock

Residential Address	Contact date	Consultation	Comments received
216 Hawthorne Parade	3/02/2020	<p>Doorknock 1. LSBJV spoke to the stakeholder regarding upcoming surface grouting work to be undertaken on either side of Hawthorne Canal including in Richard Murden Reserve. LSBJV explained the following;</p> <ul style="list-style-type: none"> • The work must be undertaken to improve ground conditions in the area prior to tunnelling later in the year, • Work will involve a large section of the park, including the new netball courts being fenced off, up to around 150 holes being drilled and grout being pumped into each hole. 	No issues raised about the work. Stakeholder advised he previously worked on tunnel project and asked general questions about the LSBJV parent companies and

		<ul style="list-style-type: none"> • Mitigation to manage noise impacts including noise blankets and not starting high impact work until 8am. • Parking impacts • The work is expected to take between 3 and 6 months to complete. • After the works are complete the park and netball courts will be restored to the condition they are prior to the work. 	subcontractors on the project.
218 Hawthorne Parade	3/02/2020 5/02/2020	<p>Doorknock 1. Left a sorry we missed you card advising that the project team visited the property to discuss upcoming work in Richard Murden Reserve. The sorry we missed you card stated work is planned to start in March 2020 to improve the ground conditions in the area prior to tunnelling later in the year.</p> <p>Doorknock 2. LSBJV spoke to the stakeholder regarding upcoming surface grouting work to be undertaken on either side of Hawthorne Canal including in Richard Murden Reserve. LSBJV explained the following;</p> <ul style="list-style-type: none"> • The work must be undertaken to improve ground conditions in the area prior to tunnelling later in the year, • Work will involve a large section of the park, including the new netball courts being fenced off, up to around 150 holes being drilled and grout being pumped into each hole. • Mitigation to manage noise impacts including noise blankets and not starting high impact work until 8am. • Parking impacts • The work is expected to take between 3 and 6 months to complete. <p>After the works are complete the park and netball courts will be restored to the condition they are prior to the work.</p>	Stakeholder commented that he did not care and would not complain about the work
220 Hawthorne Parade	3/02/2020	<p>Doorknock 1. LSBJV spoke to the stakeholder regarding upcoming surface grouting work to be undertaken on either side of Hawthorne Canal including in Richard Murden Reserve. LSBJV explained the following;</p> <ul style="list-style-type: none"> • The work must be undertaken to improve ground conditions in the area prior to tunnelling later in the year, • Work will involve a large section of the park, including the new netball courts being fenced off, up to around 150 holes being drilled and grout being pumped into each hole. • Mitigation to manage noise impacts including noise blankets and not starting high impact work until 8am. • Parking impacts • The work is expected to take between 3 and 6 months to complete. • After the works are complete the park and netball courts will be restored to the condition they are prior to the work. 	Stakeholder thanked LSBJV for letting them know about the work and advised they have no further questions at this point.

222 Hawthorne Parade	3/02/2020	<p>Doorknock 1. LSBJV spoke to the stakeholder regarding upcoming surface grouting work to be undertaken on either side of Hawthorne Canal including in Richard Murden Reserve. LSBJV explained the following;</p> <ul style="list-style-type: none"> • The work must be undertaken to improve ground conditions in the area prior to tunnelling later in the year, • Work will involve a large section of the park, including the new netball courts being fenced off, up to around 150 holes being drilled and grout being pumped into each hole. • Mitigation to manage noise impacts including noise blankets and not starting high impact work until 8am. • Parking impacts • The work is expected to take between 3 and 6 months to complete. • After the works are complete the park and netball courts will be restored to the condition they are prior to the work. 	Stakeholder understood the reason for the work and had no additional questions at this point
224 Hawthorne Parade	3/02/2020	<p>Doorknock 1. LSBJV spoke to the stakeholder regarding upcoming surface grouting work to be undertaken on either side of Hawthorne Canal including in Richard Murden Reserve. LSBJV explained the following;</p> <ul style="list-style-type: none"> • The work must be undertaken to improve ground conditions in the area prior to tunnelling later in the year, • Work will involve a large section of the park, including the new netball courts being fenced off, up to around 150 holes being drilled and grout being pumped into each hole. • Mitigation to manage noise impacts including noise blankets and not starting high impact work until 8am. • Parking impacts • The work is expected to take between 3 and 6 months to complete. • After the works are complete the park and netball courts will be restored to the condition they are prior to the work. 	Stakeholder had no questions about the work.
226 Hawthorne Parade	3/02/2020 5/02/2020	<p>Doorknock 1. Left a sorry we missed you card advising that the project team visited the property to discuss upcoming work in Richard Murden Reserve. The sorry we missed you card stated work is planned to start in March 2020 to improve the ground conditions in the area prior to tunnelling later in the year. Follow up doorknock will be attempted during the week.</p> <p>Doorknock 2. Left a sorry we missed you card advising that the project team visited the property to discuss upcoming work in Richard Murden Reserve. The sorry we missed you card requested the resident call the project to discuss potential impacts from the upcoming work.</p>	

228 Hawthorne Parade	3/02/2020	<p>Doorknock 1. LSBJV spoke to the stakeholder regarding upcoming surface grouting work to be undertaken on either side of Hawthorne Canal including in Richard Murden Reserve. LSBJV explained the following;</p> <ul style="list-style-type: none"> • The work must be undertaken to improve ground conditions in the area prior to tunnelling later in the year, • Work will involve a large section of the park, including the new netball courts being fenced off, up to around 150 holes being drilled and grout being pumped into each hole. • Mitigation to manage noise impacts including noise blankets and not starting high impact work until 8am. • Parking impacts • The work is expected to take between 3 and 6 months to complete. • After the works are complete the park and netball courts will be restored to the condition they are prior to the work. 	Stakeholder did not have any questions about the work proposed across the road.
232 Hawthorne Parade	3/02/2020 5/02/2020	<p>Doorknock 1. Left a sorry we missed you card advising that the project team visited the property to discuss upcoming work in Richard Murden Reserve. The sorry we missed you card stated work is planned to start in March 2020 to improve the ground conditions in the area prior to tunnelling later in the year. Follow up doorknock will be attempted during the week.</p> <p>Doorknock 2. Left a sorry we missed you card advising that the project team visited the property to discuss upcoming work in Richard Murden Reserve. The sorry we missed you card requested the resident call the project to discuss potential impacts from the upcoming work.</p>	
234 Hawthorne Parade	3/02/2020 5/02/2020	<p>Doorknock 1. Left a sorry we missed you card advising that the project team visited the property to discuss upcoming work in Richard Murden Reserve. The sorry we missed you card stated work is planned to start in March 2020 to improve the ground conditions in the area prior to tunnelling later in the year. Follow up doorknock will be attempted during the week.</p> <p>Doorknock 2. LSBJV spoke to the stakeholder regarding upcoming surface grouting work to be undertaken on either side of Hawthorne Canal including in Richard Murden Reserve. LSBJV explained the following;</p> <ul style="list-style-type: none"> • The work must be undertaken to improve ground conditions in the area prior to tunnelling later in the year, • Work will involve a large section of the park, including the new netball courts being fenced off, up to around 150 holes being drilled and grout being pumped into each hole. • Mitigation to manage noise impacts including noise blankets and not starting high impact work until 8am. 	Stakeholder commented it was funny the netball courts would be closed so soon after opening. Stakeholder advised that majority of her neighbours had signed a petition to have courts removed as they are disruptive. No issue raised about the work going ahead.

		<ul style="list-style-type: none"> • Parking impacts • The work is expected to take between 3 and 6 months to complete. <p>After the works are complete the park and netball courts will be restored to the condition they are prior to the work.</p>	
236 Hawthorne Parade	3/02/2020 5/02/2020	<p>Doorknock 1. Left a sorry we missed you card advising that the project team visited the property to discuss upcoming work in Richard Murden Reserve. The sorry we missed you card stated work is planned to start in March 2020 to improve the ground conditions in the area prior to tunnelling later in the year. Follow up doorknock will be attempted during the week.</p> <p>Doorknock 2 – Not undertaken as neighbour in 234 advised they are away until 14/02/2020. Neighbour will advise them on return and have them call the project.</p>	Neighbour advised they are away until 14/02/2020
238 Hawthorne Parade	3/02/2020 5/02/2020	<p>Doorknock 1. Left a sorry we missed you card advising that the project team visited the property to discuss upcoming work in Richard Murden Reserve. The sorry we missed you card stated work is planned to start in March 2020 to improve the ground conditions in the area prior to tunnelling later in the year. Follow up doorknock will be attempted during the week.</p> <p>Doorknock 2. Left a sorry we missed you card advising that the project team visited the property to discuss upcoming work in Richard Murden Reserve. The sorry we missed you card requested the resident call the project to discuss potential impacts from the upcoming work.</p>	
246 Hawthorne Parade	3/02/2020 5/02/2020	<p>Doorknock 1. Left a sorry we missed you card advising that the project team visited the property to discuss upcoming work in Richard Murden Reserve. The sorry we missed you card stated work is planned to start in March 2020 to improve the ground conditions in the area prior to tunnelling later in the year.</p> <p>Doorknock 2. Left a sorry we missed you card advising that the project team visited the property to discuss upcoming work in Richard Murden Reserve. The sorry we missed you card requested the resident call the project to discuss potential impacts from the upcoming work.</p>	
248 Hawthorne Parade	3/02/2020 5/02/2020	<p>Doorknock 1. Left a sorry we missed you card advising that the project team visited the property to discuss upcoming work in Richard Murden Reserve. The sorry we missed you card stated work is planned to start in March 2020 to improve the ground conditions in the area prior to tunnelling later in the year. Follow up doorknock will be attempted during the week.</p> <p>Doorknock 2. LSBJV spoke to the stakeholder regarding upcoming surface grouting work to be undertaken on either side of Hawthorne Canal including in Richard Murden Reserve. LSBJV explained the following;</p> <ul style="list-style-type: none"> • The work must be undertaken to improve ground conditions in the area prior to tunnelling later in the year, 	Stakeholder advised they do not have any issues with the work but was interested in parking impacts on Hawthorne Parade. Also advised that some people apparently often sleep overnight in

		<ul style="list-style-type: none"> • Work will involve a large section of the park, including the new netball courts being fenced off, up to around 150 holes being drilled and grout being pumped into each hole. • Mitigation to manage noise impacts including noise blankets and not starting high impact work until 8am. • Parking impacts • The work is expected to take between 3 and 6 months to complete. • After the works are complete the park and netball courts will be restored to the condition they are prior to the work. 	campervans along Canal Road
250 Hawthorne Parade	3/02/2020	<p>Doorknock 1. LSBJV spoke to the stakeholder regarding upcoming surface grouting work to be undertaken on either side of Hawthorne Canal including in Richard Murden Reserve. LSBJV explained the following;</p> <ul style="list-style-type: none"> • The work must be undertaken to improve ground conditions in the area prior to tunnelling later in the year, • Work will involve a large section of the park, including the new netball courts being fenced off, up to around 150 holes being drilled and grout being pumped into each hole. • Mitigation to manage noise impacts including noise blankets and not starting high impact work until 8am. • Parking impacts • The work is expected to take between 3 and 6 months to complete. • After the works are complete the park and netball courts will be restored to the condition they are prior to the work. 	Stakeholder commented that they found it amusing the netball courts would be closed so soon after opening. Residents indicated they understood the need for the work and had no further questions.
252 Hawthorne Parade	3/02/2020 5/02/2020	<p>Doorknock 1. Left a sorry we missed you card advising that the project team visited the property to discuss upcoming work in Richard Murden Reserve. The sorry we missed you card stated work is planned to start in March 2020 to improve the ground conditions in the area prior to tunnelling later in the year.</p> <p>Doorknock 2. Door was answered by the owner's teenage son. Requested the parents call the project to discuss impacts from upcoming work. Provided a sorry we missed you card with the projects contact details and reason for the visit.</p>	Door answered by the owner's teenage son who advised he would pass the message onto his parents and request they call the project.
254 Hawthorne Parade	3/02/2020 5/02/2020	<p>Doorknock 1. Left a sorry we missed you card advising that the project team visited the property to discuss upcoming work in Richard Murden Reserve. The sorry we missed you card stated work is planned to start in March 2020 to improve the ground conditions in the area prior to tunnelling later in the year.</p> <p>Doorknock 2. LSBJV spoke to the stakeholder regarding upcoming surface grouting work to be undertaken on either side of Hawthorne Canal including in Richard Murden Reserve. LSBJV explained the following;</p>	Owner was very pleased to hear the netball courts would be closed and asked they be closed for a long as possible. Stakeholder said she understood the reason

		<ul style="list-style-type: none"> • The work must be undertaken to improve ground conditions in the area prior to tunnelling later in the year, • Work will involve a large section of the park, including the new netball courts being fenced off, up to around 150 holes being drilled and grout being pumped into each hole. • Mitigation to manage noise impacts including noise blankets and not starting high impact work until 8am. • Parking impacts • The work is expected to take between 3 and 6 months to complete. • After the works are complete the park and netball courts will be restored to the condition they are prior to the work 	for the work and advised she is nervous about damage to the home from tunnelling. Potential noise and vibration impacts during tunnelling as well as mitigation measures were discussed.
254a Hawthorne Parade	3/02/2020 5/02/2020	<p>Doorknock 1. Left a sorry we missed you card advising that the project team visited the property to discuss upcoming work in Richard Murden Reserve. The sorry we missed you card stated work is planned to start in March 2020 to improve the ground conditions in the area prior to tunnelling later in the year.</p> <p>Doorknock 2. LSBJV spoke to the stakeholder regarding upcoming surface grouting work to be undertaken on either side of Hawthorne Canal including in Richard Murden Reserve. LSBJV explained the following;</p> <ul style="list-style-type: none"> • The work must be undertaken to improve ground conditions in the area prior to tunnelling later in the year, • Work will involve a large section of the park, including the new netball courts being fenced off, up to around 150 holes being drilled and grout being pumped into each hole. • Mitigation to manage noise impacts including noise blankets and not starting high impact work until 8am. • Parking impacts • The work is expected to take between 3 and 6 months to complete. • After the works are complete the park and netball courts will be restored to the condition they are prior to the work. 	Stakeholder advised he did not have concerns with the planned work but asked if the project had been undertaking nightwork recently on the other side of the canal. LSBJV has not carried out nightwork in the area.
256 Hawthorne Parade	3/02/2020	<p>Doorknock 1. LSBJV spoke to the stakeholder regarding upcoming surface grouting work to be undertaken on either side of Hawthorne Canal including in Richard Murden Reserve. LSBJV explained the following;</p> <ul style="list-style-type: none"> • The work must be undertaken to improve ground conditions in the area prior to tunnelling later in the year, • Work will involve a large section of the park, including the new netball courts being fenced off, up to around 150 holes being drilled and grout being pumped into each hole. • Mitigation to manage noise impacts. 	Stakeholder understood the reason for the work and did not raise any issues with it going ahead.

		<ul style="list-style-type: none"> • Parking impacts • The work is expected to take between 3 and 6 months to complete. • After the works are complete the park and netball courts will be restored to the condition they are prior to the work. 	
258 Hawthorne Parade	3/02/2020 5/02/2020	<p>Doorknock 1. Left a sorry we missed you card advising that the project team visited the property to discuss upcoming work in Richard Murden Reserve. The sorry we missed you card stated work is planned to start in March 2020 to improve the ground conditions in the area prior to tunnelling later in the year.</p> <p>Doorknock 2. Left a sorry we missed you card advising that the project team visited the property to discuss upcoming work in Richard Murden Reserve. The sorry we missed you card requested the resident call the project to discuss potential impacts from the upcoming work.</p>	
260 Hawthorne Parade	3/02/2020 5/02/2020	<p>Doorknock 1. Left a sorry we missed you card advising that the project team visited the property to discuss upcoming work in Richard Murden Reserve. The sorry we missed you card stated work is planned to start in March 2020 to improve the ground conditions in the area prior to tunnelling later in the year.</p> <p>Doorknock 2. LSBJV spoke to the stakeholder regarding upcoming surface grouting work to be undertaken on either side of Hawthorne Canal including in Richard Murden Reserve. LSBJV explained the following;</p> <ul style="list-style-type: none"> • The work must be undertaken to improve ground conditions in the area prior to tunnelling later in the year, • Work will involve a large section of the park, including the new netball courts being fenced off, up to around 150 holes being drilled and grout being pumped into each hole. • Mitigation to manage noise impacts including noise blankets and not starting high impact work until 8am. • Parking impacts • The work is expected to take between 3 and 6 months to complete. • After the works are complete the park and netball courts will be restored to the condition they are prior to the work. 	Stakeholder was amused the courts would be closed so soon after opening and wondered why they were built if WestConnex was coming. Stakeholder did not raise any concerns with the proposed work but is interested in geology and asked if she could have a core sample from the area.
262 Hawthorne Parade	3/02/2020 5/02/2020	<p>Doorknock 1. Left a sorry we missed you card advising that the project team visited the property to discuss upcoming work in Richard Murden Reserve. The sorry we missed you card stated work is planned to start in March 2020 to improve the ground conditions in the area prior to tunnelling later in the year.</p> <p>Doorknock 2. Left a sorry we missed you card advising that the project team visited the property to discuss upcoming work in Richard Murden Reserve. The sorry we missed you card requested the resident call the project to discuss potential impacts from the upcoming work.</p>	

264 Hawthorne Parade	3/02/2020	<p>Doorknock 1. LSBJV spoke to the stakeholder regarding upcoming surface grouting work to be undertaken on either side of Hawthorne Canal including in Richard Murden Reserve. LSBJV explained the following;</p> <ul style="list-style-type: none"> • The work must be undertaken to improve ground conditions in the area prior to tunnelling later in the year, • Work will involve a large section of the park, including the new netball courts being fenced off, up to around 150 holes being drilled and grout being pumped into each hole. • Mitigation to manage noise impacts including noise blankets and not starting high impact work until 8am. • Parking impacts • The work is expected to take between 3 and 6 months to complete. • After the works are complete the park and netball courts will be restored to the condition they are prior to the work. 	Stakeholder concerned with potential parking impacts but not the work itself.
266 Hawthorne Parade	3/02/2020 5/02/2020	<p>Doorknock 1. Left a sorry we missed you card advising that the project team visited the property to discuss upcoming work in Richard Murden Reserve. The sorry we missed you card stated work is planned to start in March 2020 to improve the ground conditions in the area prior to tunnelling later in the year.</p> <p>Doorknock 2. Left a sorry we missed you card advising that the project team visited the property to discuss upcoming work in Richard Murden Reserve. The sorry we missed you card requested the resident call the project to discuss potential impacts from the upcoming work.</p>	
268 Hawthorne Parade	3/02/2020	<p>Doorknock 1. LSBJV spoke to the stakeholder regarding upcoming surface grouting work to be undertaken on either side of Hawthorne Canal including in Richard Murden Reserve. LSBJV explained the following;</p> <ul style="list-style-type: none"> • The work must be undertaken to improve ground conditions in the area prior to tunnelling later in the year, • Work will involve a large section of the park, including the new netball courts being fenced off, up to around 150 holes being drilled and grout being pumped into each hole. • Mitigation to manage noise impacts including noise blankets and not starting high impact work until 8am. • Parking impacts • The work is expected to take between 3 and 6 months to complete. • After the works are complete the park and netball courts will be restored to the condition they are prior to the work. 	Stakeholder did not have any questions about the planned work.
270 Hawthorne Parade	3/02/2020 5/02/2020	<p>Doorknock 1. Left a sorry we missed you card advising that the project team visited the property to discuss upcoming work in Richard Murden Reserve. The sorry we</p>	Advised no issue with the planned work but

		<p>missed you card stated work is planned to start in March 2020 to improve the ground conditions in the area prior to tunnelling later in the year.</p> <p>Doorknock 2. LSBJV spoke to the stakeholder regarding upcoming surface grouting work to be undertaken on either side of Hawthorne Canal including in Richard Murden Reserve. LSBJV explained the following;</p> <ul style="list-style-type: none"> • The work must be undertaken to improve ground conditions in the area prior to tunnelling later in the year, • Work will involve a large section of the park, including the new netball courts being fenced off, up to around 150 holes being drilled and grout being pumped into each hole. • Mitigation to manage noise impacts including noise blankets and not starting high impact work until 8am. • Parking impacts • The work is expected to take between 3 and 6 months to complete. <p>After the works are complete the park and netball courts will be restored to the condition they are prior to the work.</p>	<p>wanted to know how close the tunnel is to her property.</p> <p>LSBJV will provide a map showing the tunnel location relative to the property.</p>
276 Hawthorne Parade	3/02/2020	<p>Doorknock 1. LSBJV spoke to the stakeholder regarding upcoming surface grouting work to be undertaken on either side of Hawthorne Canal including in Richard Murden Reserve. LSBJV explained the following;</p> <ul style="list-style-type: none"> • The work must be undertaken to improve ground conditions in the area prior to tunnelling later in the year, • Work will involve a large section of the park, including the new netball courts being fenced off, up to around 150 holes being drilled and grout being pumped into each hole. • Mitigation to manage noise impacts including noise blankets and not starting high impact work until 8am. • Parking impacts • The work is expected to take between 3 and 6 months to complete. • After the works are complete the park and netball courts will be restored to the condition they are prior to the work. 	<p>No issues raised with the work but has some concern about potential parking impacts.</p>

