


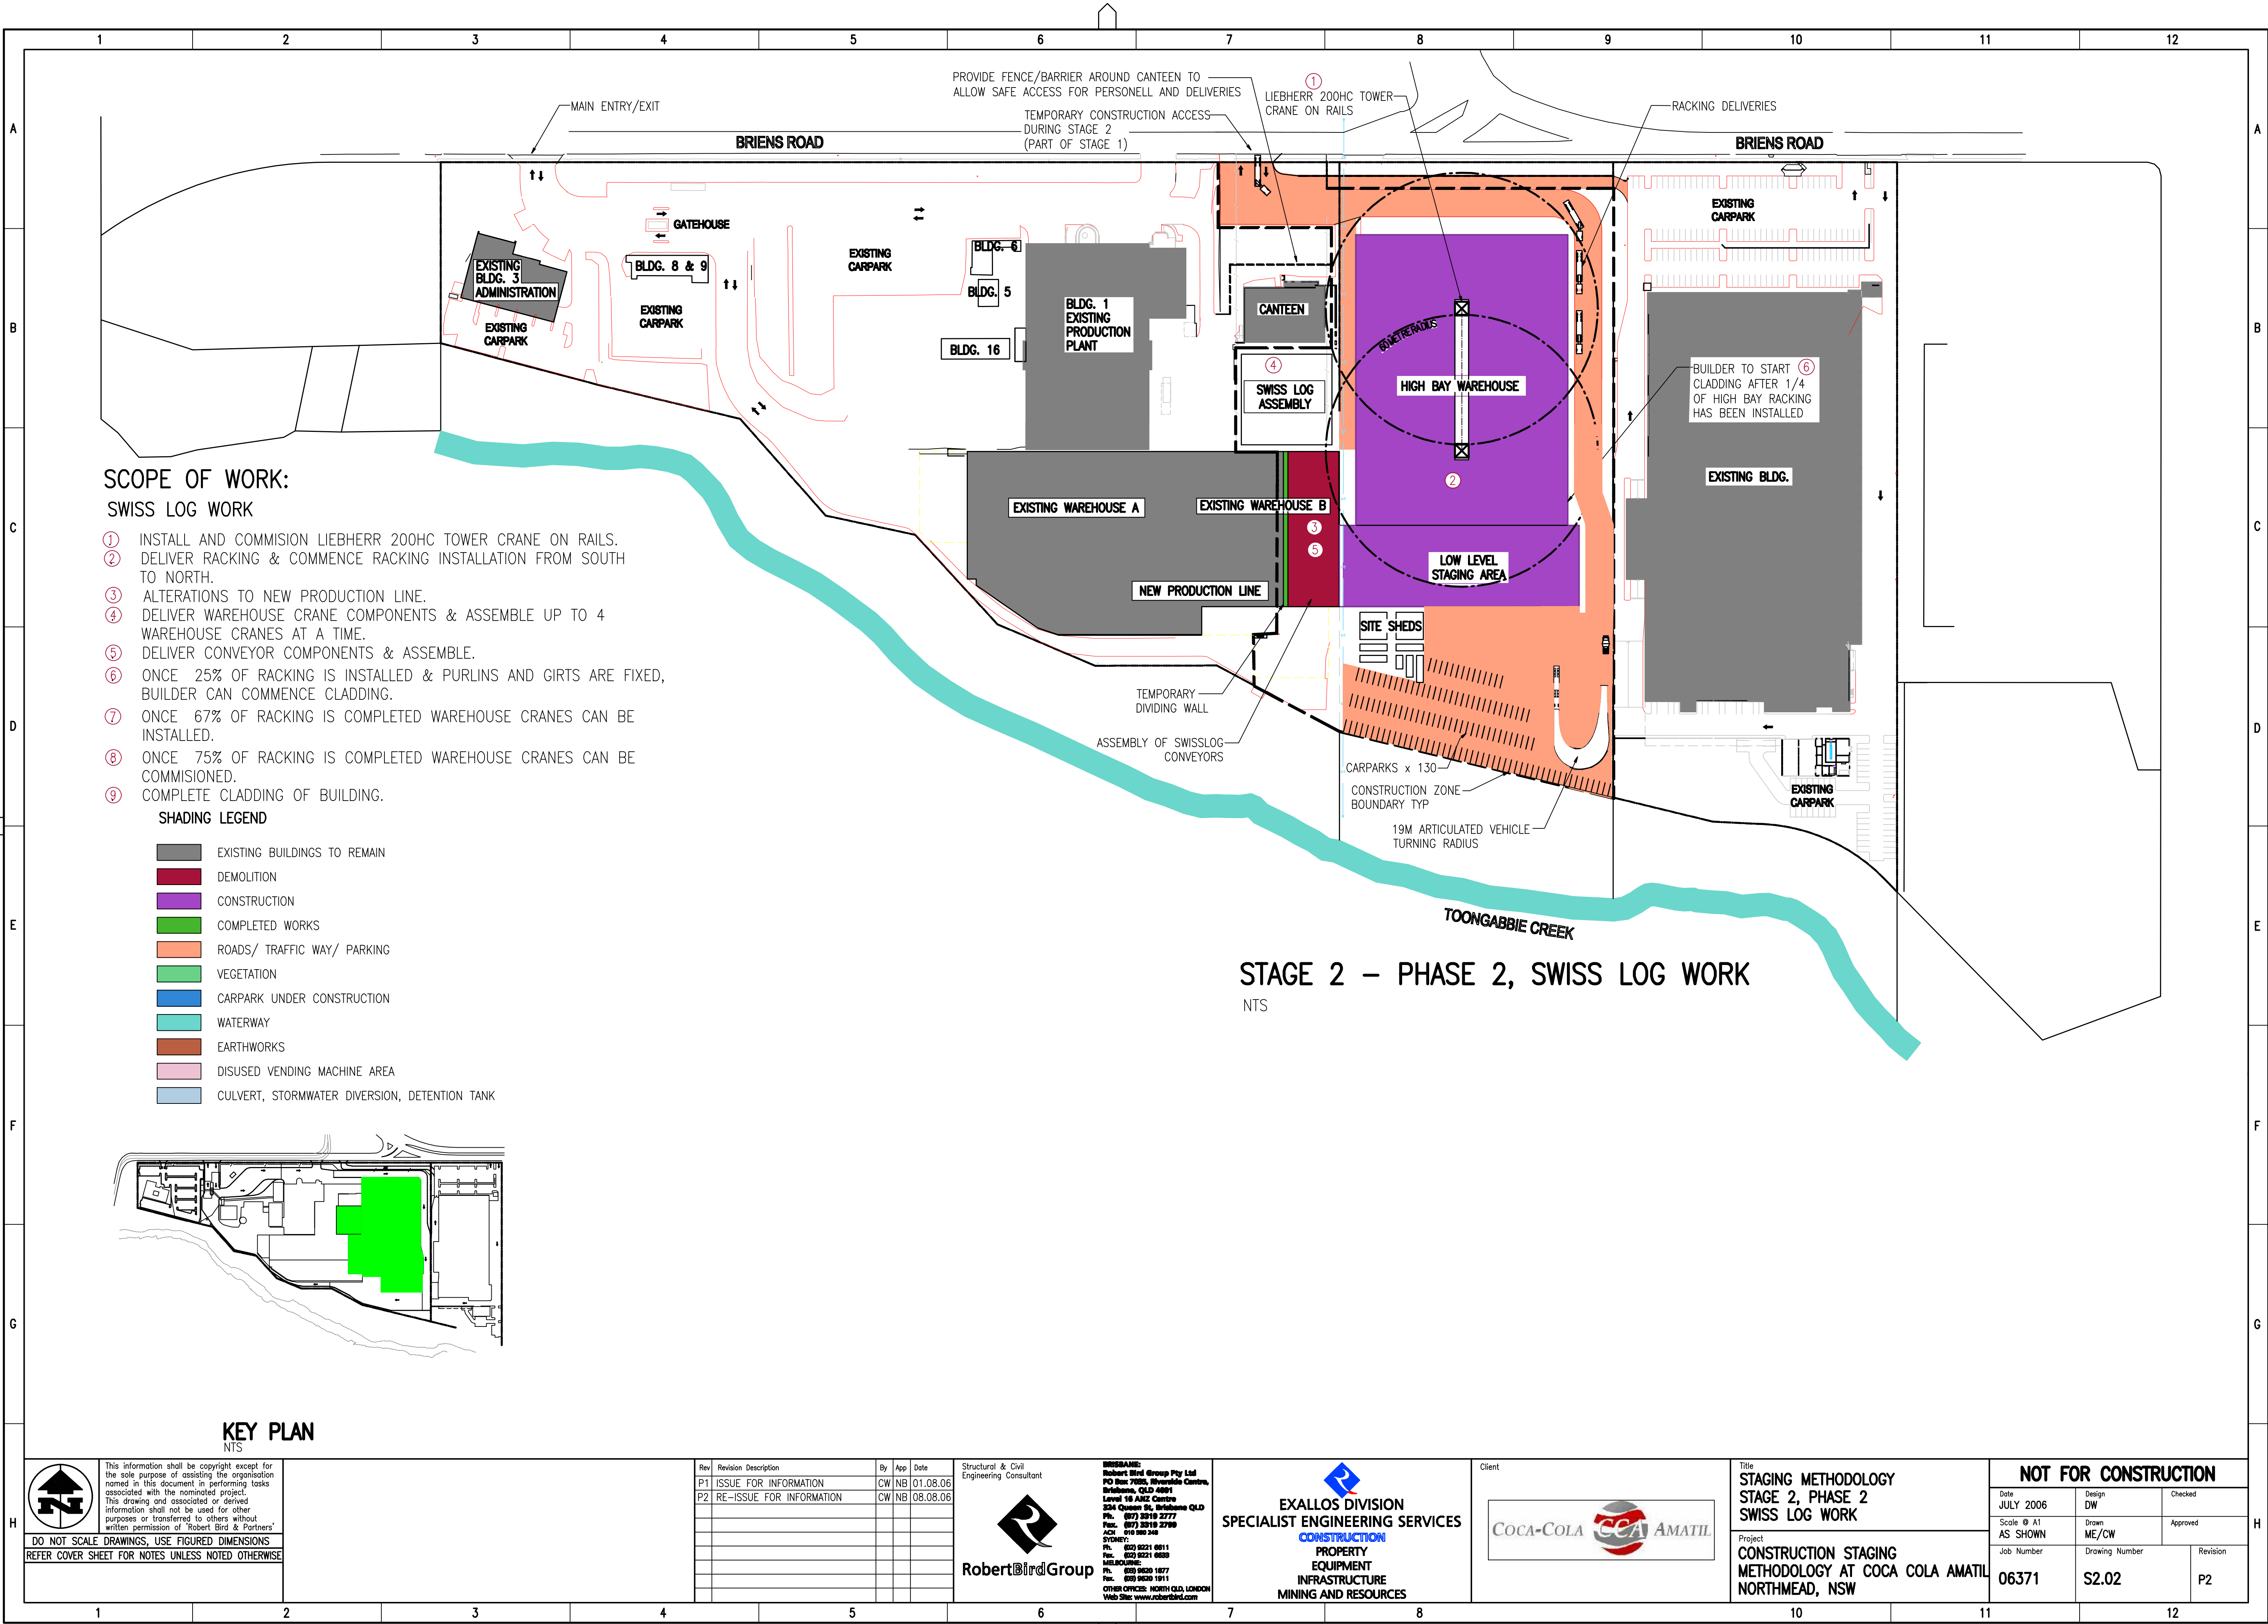


SCOPE OF WORK:
SWISS LOG WORK

- 1 INSTALL AND COMMISSION LIEBHERR 200HC TOWER CRANE ON RAILS.
- 2 DELIVER RACKING & COMMENCE RACKING INSTALLATION FROM SOUTH TO NORTH.
- 3 ALTERATIONS TO NEW PRODUCTION LINE.
- 4 DELIVER WAREHOUSE CRANE COMPONENTS & ASSEMBLE UP TO 4 WAREHOUSE CRANES AT A TIME.
- 5 DELIVER CONVEYOR COMPONENTS & ASSEMBLE.
- 6 ONCE 25% OF RACKING IS INSTALLED & PURLINS AND GIRTS ARE FIXED, BUILDER CAN COMMENCE CLADDING.
- 7 ONCE 67% OF RACKING IS COMPLETED WAREHOUSE CRANES CAN BE INSTALLED.
- 8 ONCE 75% OF RACKING IS COMPLETED WAREHOUSE CRANES CAN BE COMMISSIONED.
- 9 COMPLETE CLADDING OF BUILDING.

SHADING LEGEND

- EXISTING BUILDINGS TO REMAIN
- DEMOLITION
- CONSTRUCTION
- COMPLETED WORKS
- ROADS/ TRAFFIC WAY/ PARKING
- VEGETATION
- CARPARK UNDER CONSTRUCTION
- WATERWAY
- EARTHWORKS
- DISUSED VENDING MACHINE AREA
- CULVERT, STORMWATER DIVERSION, DETENTION TANK

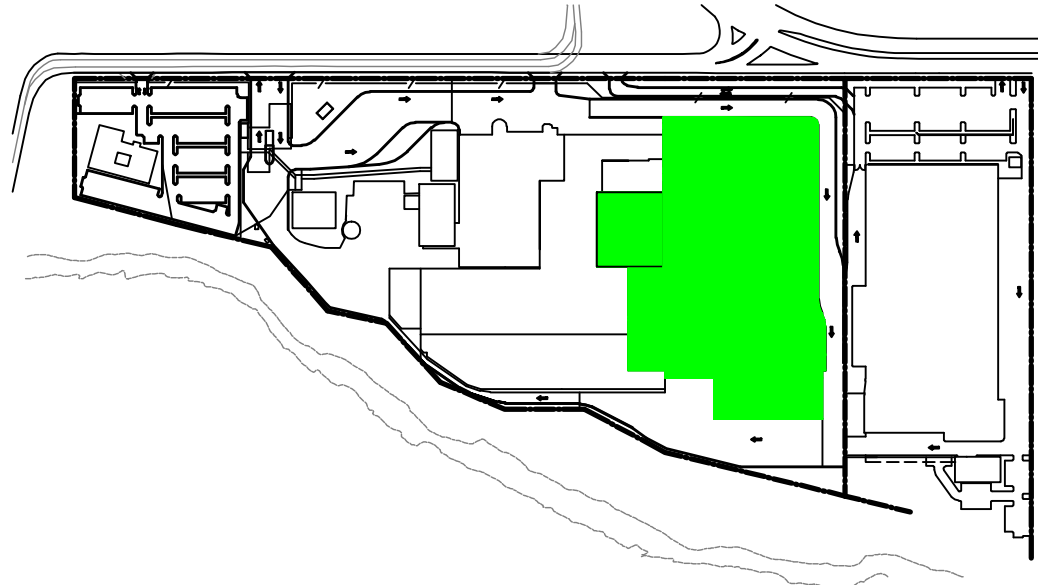

KEY PLAN
NTS

STAGE 2 – PHASE 2, SWISS LOG WORK
NTS

Information block containing copyright notice, disclaimer, and scale information.

Rev	Revision Description	By	App	Date
P1	ISSUE FOR INFORMATION	CW	NB	01.08.06
P2	RE-ISSUE FOR INFORMATION	CW	NB	08.08.06

Information block for Robert Bird Group, including contact details and other offices.

Information block for EXALLOS DIVISION, SPECIALIST ENGINEERING SERVICES.

Client logos: COCA-COLA, CCA, AMATIL.

Information block containing project title, location, and drawing details.

NOT FOR CONSTRUCTION			
Date JULY 2006	Design DW	Checked	
Scale @ A1 AS SHOWN	Drawn ME/CW	Approved	
Job Number 06371	Drawing Number S2.02	Revision P2	
