


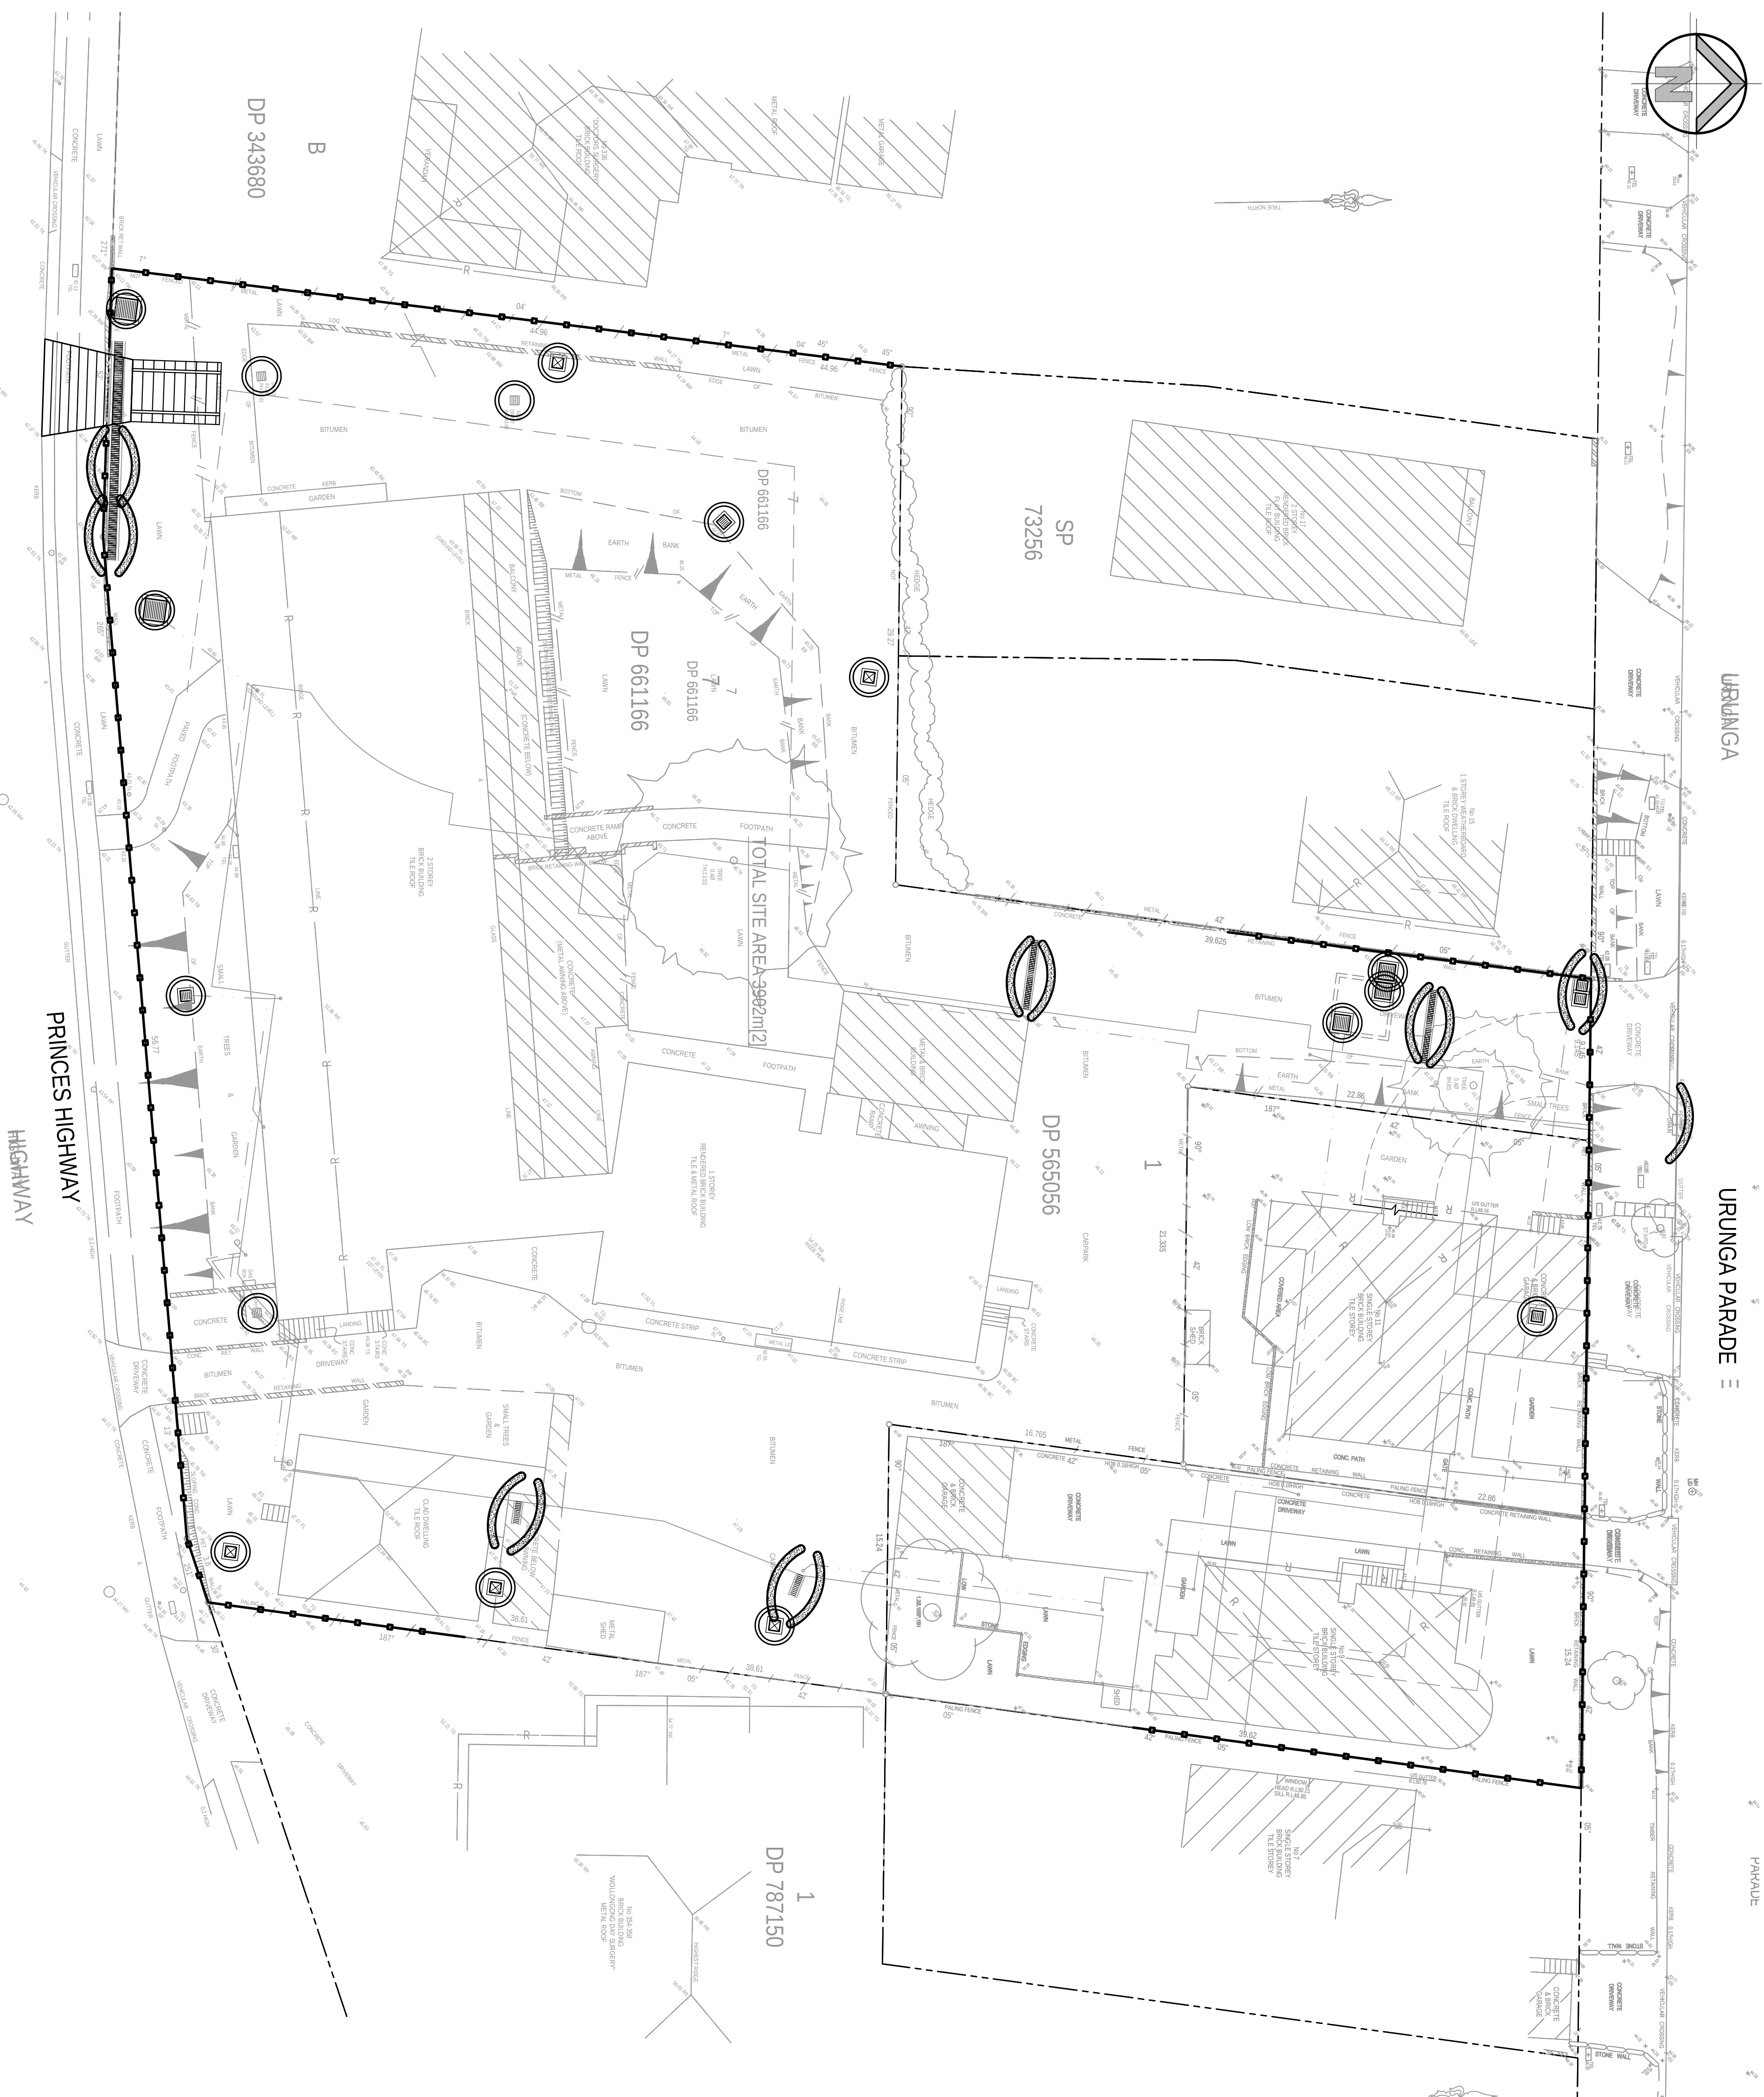

LEGEND

-
- Diagram illustrating the components of a proposed sedimentation fence layout:
- PROPOSED SEDIMENTATION FENCE (represented by a vertical line with four circular markers)
 - PROPOSED VEHICLE SHAKER GRID (represented by a grid of 4 rows and 10 columns)
 - PROPOSED STABILISED SITE ACCESS (represented by a trapezoidal shape with horizontal lines)
 - PROPOSED MESH & GRAVEL INLET FILTER (represented by a curved, textured shape)
 - GEOTEXTILE INLET FILTER (represented by a circular shape with a central hole)

SEDIMENT & EROSION CONTROL NOTES

- ALL SEMENT CONTROL DEVICES ARE TO BE CONSTRUCTED, SPECIFIED AND MAINTAINED IN ACCORDANCE WITH RESPECTIVE CONTROL, PLACEMENTS AND LAMCORN SOIL AND CONSTRUCTION MANUAL.
- ALL PERIMETER & SILTATION CONTROL MEASURES ARE TO BE PLACED PRIOR TO, OR AS THE FIRST STEP IN EARTH WORKS AND/OR CLEARING.
- THE SEMENT & EROSION CONTROL PLAN MAY REQUIRE FUTURE ADJUSTMENT TO REFLECT CONSTRUCTION STAGING. IT IS THE SOIL CONTRACTORS RESPONSIBILITY TO PREPARE THEIR OWN SEDIMENT AND EROSION CONTROL PLAN WHICH SUITS THE DESIGNED CONSTRUCTION STAGING.
- SILTATION BUFFER ZONES ARE TO BE FENCED OFF AND ACCESS PROHIBITED TO ALL PLANT AND MACHINERY.
- ALL TEMPORARY EARTH BERRIS, DIVERSIONS & SILT DRAWBACKMENTS ARE TO BE MACHINE COMPACTED, SEEDED & MULCHED FOR TEMPORARY VEGETATION COVER AS SOON AS THEY HAVE BEEN FORMED.
- ALL SEDIMENT TRAPPING STRAIGHTCUTS AND DEVICES ARE TO BE INSPECTED AFTER STORMS FOR STRUCTURAL DAMAGE OR CLOSING. TRAPPED MATERIAL IS TO BE REMOVED TO A SAFE LOCATION.
- ALL TOPSOIL IS TO BE STOCKPILED ON SITE FOR REUSE AWAY FROM TREES AND DAMAGE LINES. MEASURES SHALL BE APPLIED TO PREVENT EROSION OF THE STOCKPILES.
- ALL EARTHWORK AREAS SHALL BE ROLLED EACH EVENING TO SEAL THE BATHWORKS.
- ALL FILLS ARE TO BE LEFT WITH A LIP AT THE TOP OF THE SLOPE AT THE END, AND ALL SLOPES ARE TO BE SEED AND MULCH WITHIN 14 DAYS OF COMPLETION OF FORMATION AND BY LANDSCAPE ARCHITECTS.
- UPON COMPLETION OF ALL EARTHWORKS OR AS DIRECTED BY COUNCIL SOIL CONSERVATION TREATMENTS SHALL BE APPLIED SO AS TO REPAIR AREAS THAT HAVE BEEN DISTURBED. EROSION PROOF WITHIN 14 DAYS.
- EROSION AND SILT PROTECTION MEASURES ARE TO BE MAINTAINED AT ALL TIMES.

SEDIMENT & EROSION CONTROL PLAN

[illegible]
