

HORSLEY LOGISTICS PARK LOT 201

Waste Management Plan

Prepared for:

ESR
Level 29
20 Bond St
Sydney, 2000,
NSW Australia

SLR Ref: 610.19360-R05
Version No: -v2.0
April 2021



PREPARED BY

SLR Consulting Australia Pty Ltd
ABN 29 001 584 612
Tenancy 202 Submarine School, Sub Base Platypus, 120 High Street
North Sydney NSW 2060 Australia

T: +61 2 9427 8100
E: sydney@slrconsulting.com www.slrconsulting.com

BASIS OF REPORT

This report has been prepared by SLR Consulting Australia Pty Ltd (SLR) with all reasonable skill, care and diligence, and taking account of the timescale and resources allocated to it by agreement with ESR (the Client). Information reported herein is based on the interpretation of data collected, which has been accepted in good faith as being accurate and valid.

This report is for the exclusive use of the Client. No warranties or guarantees are expressed or should be inferred by any third parties. This report may not be relied upon by other parties without written consent from SLR.

SLR disclaims any responsibility to the Client and others in respect of any matters outside the agreed scope of the work.

DOCUMENT CONTROL

Reference	Date	Prepared	Checked	Authorised
610.19360-R05-v2.0	14 April 2021	Emerson Helmi Patch	Celine El-Khouri	Andrew Quinn

CONTENTS

1	INTRODUCTION	6
1.1	Overview	6
1.2	Objectives	6
1.3	Review of WMP	6
2	PROJECT DESCRIPTION	7
2.1	Overview of Proposed Development.....	7
2.2	Overview of Proposed Construction Work	7
2.3	Overview of Proposed Operations.....	7
3	BETTER PRACTICE WASTE MANAGEMENT AND RECYCLING.....	8
3.1	Waste Management Hierarchy.....	8
3.2	Benefits of Adopting Better Practice	8
4	WASTE LEGISLATION AND GUIDANCE	9
5	CONSTRUCTION WASTE AND RECYCLING MANAGEMENT	11
5.1	Targets for Resource Recovery	11
5.2	Waste Streams and Classifications	11
5.3	Construction Waste Types and Quantities	14
5.3.1	Construction waste quantities.....	14
5.4	Waste Avoidance	15
5.5	Reuse, Recycling and Disposal	16
5.6	Waste Storage and Servicing	17
5.6.1	Waste Segregation and Storage	17
5.6.2	Waste Storage Areas	18
5.6.3	Waste Servicing and Record Keeping	18
5.6.4	Contaminated or Hazardous Waste Management	19
5.7	Site Inductions	19
5.8	Signage	19
5.9	Monitoring and Reporting	20
5.10	Roles and Responsibilities.....	21
6	OPERATIONAL WASTE MANAGEMENT	22
6.1	Targets for Resource Recovery	22
6.2	Waste Streams and Classifications	22
6.3	Estimated Quantities of Operational Waste.....	24
6.3.1	Estimated quantities of operational waste	24

CONTENTS

6.4	Waste Storage Area Size	25
6.4.1	Waste storage area size.....	26
6.5	Bulky and Hazardous Waste Management.....	26
6.6	Waste Storage Room Location	27
6.7	Waste Storage Area Features	27
6.8	Waste Servicing.....	28
6.9	Waste Avoidance, Reuse and Recycling Measures.....	28
6.9.1	Waste Avoidance.....	28
6.9.2	Re-use.....	29
6.9.3	Recycling.....	29
6.10	Communication Strategies.....	29
6.11	Signage.....	30
6.12	Monitoring and Reporting	30
6.13	Roles and Responsibilities.....	31

DOCUMENT REFERENCES

TABLES

Table 1 Legislation and guidance.....	9
Table 2 Potential waste types and their management methods	12
Table 3 Average waste generation rates for the construction of the project	14
Table 4 Estimated types and quantities of construction waste from Project	15
Table 5 Suggested roles and responsibilities for construction waste management	21
Table 6 Potential waste types, classifications and management methods for operational waste	22
Table 7 Waste generation rates applied to the operations of Warehouses 2 and 3.....	24
Table 8 Estimated quantities of operational general waste and recycling of Warehouses 2 and 3.....	25
Table 9 Dimensions and approximate footprint of bins	25
Table 10 Collection frequency for Warehouses 2 and 3.....	26
Table 11 Recommended number of bins and storage area for weekly operations for Warehouses 2 and 3.....	26
Table 12 Operational waste management responsibility allocation	31

FIGURES

Figure 1 Lot 201 Site Plan	7
Figure 2 Waste management hierarchy	8

CONTENTS

Figure 3 Examples of NSW EPA labels for waste skips and bins	20
Figure 4 Example of bin labels for operational waste	30

APPENDICES

Appendix A Client architectural drawings	
Appendix B Fairfield Council DCP Appendix E - waste management plan	

1 Introduction

1.1 Overview

SLR Consulting Australia Pty Ltd (SLR) has been commissioned by ESR (Aust) Pty Ltd (the Client) to prepare a waste management plan (WMP) in support of State Significant Development Application (SSDA) for a proposed 20 ha industrial estate within the existing CSR quarry site located at 327-335 Burley Road, Horsley Park. This WMP is for the construction and operational activities of the development of ESR Horsley Logistics Park (the Project) and has been prepared using architectural drawings supplied by the Client and attached in **Appendix A**.

This WMP is required as a planning modification to the SSDA for Lot 201. A separate WMP applies for all other Lots.

1.2 Objectives

The principal objective of this WMP is to identify all potential wastes likely to be generated at the Project site during construction and operational phases, including a description of how waste would be handled, processed and disposed of, or re-used or recycled, in accordance with Fairfield City Council's (Council) requirements.

The objectives of this WMP are as follows:

- Identify potential waste types likely to be generated during the construction and operational phases of the Project
- Provide advice on how identified wastes should be handled, identified, processed, disposed of, reused or recycled in accordance with Council requirements, relevant Australian codes and standards and better practice waste minimisation principles
- Encourage waste avoidance and minimisation through advice on design, ordering and planning, and
- Help implement safe and practical options for waste collection from the Project by Council or private waste servicing contractors.

1.3 Review of WMP

This WMP is not a static document. It is a working document that requires review and updating to ensure ongoing suitability for the proposed on-going operations at the site.

This WMP will be reviewed and updated:

- To remain consistent with waste and landfill regulations and guidelines
- If changes are made to site waste and recycling management, or
- To take advantage of new technologies, innovations and methodologies for waste or recycling management.

Copies of the original WMP and its future versions should be retained by the building manager. Changes made to the WMP, as well as the reasons for the changes made, should be documented by the building manager as part of the review process.

2 Project Description

2.1 Overview of Proposed Development

The Client is developing an industrial estate at 327-335 Burley Road, Horsley Park as part of the ESR Horsley Logistics Park. The Client has sought approval for the proposed industrial estate via an SSDA. SLR has been advised that by the time this modification is lodged, there will be a consent to cover the entire estate. This WMP applies specifically to Lot 201.

2.2 Overview of Proposed Construction Work

The Project works will include construction activities. The site plan for development of the Lot 201 of the ESR Horsley Logistics Park is shown below in **Figure 1**. The anticipated construction works for this development include construction of:

- Three warehouse buildings
- Three two-storey ancillary office buildings
- Truck and car parking areas and associated site hardstands, and
- Minor landscaping areas, sprinkler tanks and pump rooms.

2.3 Overview of Proposed Operations

The uses for Warehouses 1, 2 and 3 are not yet finalised however, at this stage, they are expected to be warehouses and bulky goods facilities.

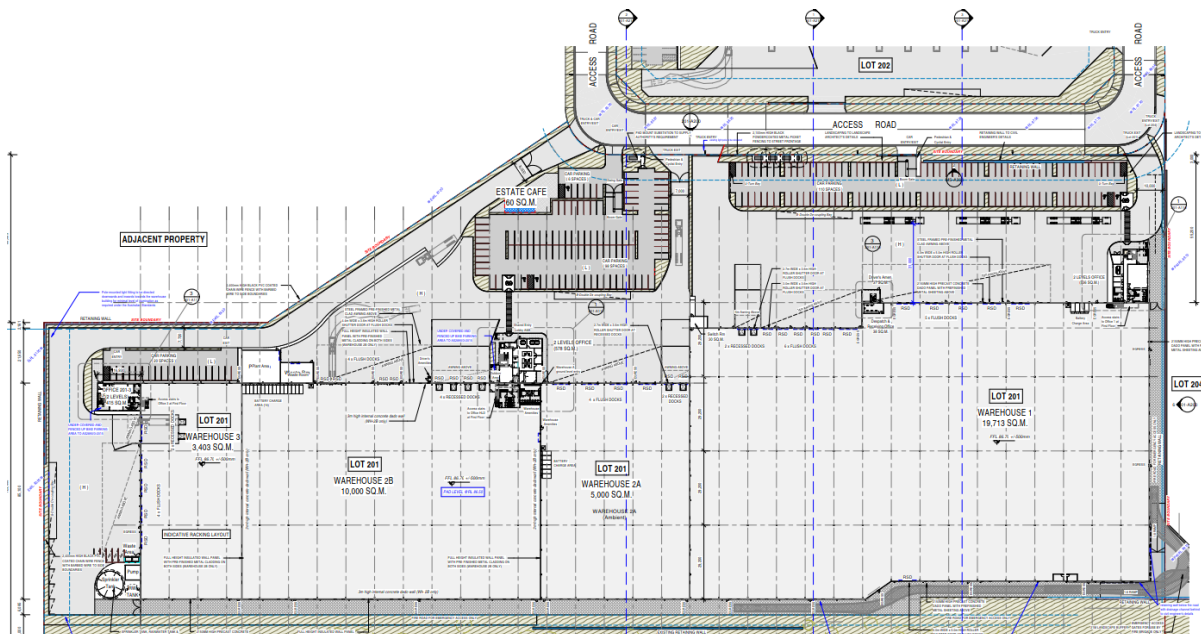


Figure 1 Lot 201 Site Plan

3 Better Practice Waste Management and Recycling

3.1 Waste Management Hierarchy

This WMP has been prepared in line with the waste management hierarchy shown in **Table 2**, which summarises the objectives of the *Waste Avoidance and Resource Recovery Act 2001*.

The waste management hierarchy comprises the following principles, from most to least preferable:

- Waste **avoidance**, prevention or reduction of waste generation. Achievable through better design and purchasing choices.
- Waste **reuse**, reuse without substantially changing the form of the waste.
- Waste **recycling**, treatment of waste that is no longer usable in its current form to produce new products.
- Energy **recovery**, processing of residual waste materials to recover energy.
- Waste **treatment**, reduce potential environmental, health and safety risks.
- Waste **disposal**, in a manner that causes the least harm to the natural environment.

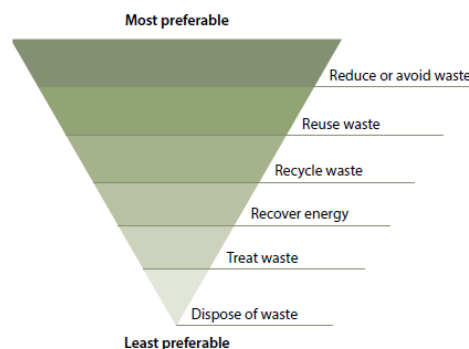


Image from NSW EPA (2014) NSW Waste Avoidance and Resource Recovery Strategy 2014-21.

Figure 2 Waste management hierarchy

3.2 Benefits of Adopting Better Practice

Adopting better practice principles in waste minimisation offers significant benefits for organisations, stakeholders and the wider community. Benefits from better practice waste minimisation include:

- Improved reputation of an organisation due to social and environmental responsibility.
- Lowered consumption of non-renewable resources.
- Reduced environmental impact, for example, pollution, from materials manufacturing and waste treatment.
- Reduced expenses from lower waste disposal.
- Providing opportunities for additional revenue streams through beneficial reuse.

4 Waste Legislation and Guidance

The legislation and guidance outlined in **Table 1** below should be referred to during the demolition, construction and operational phases of the Project.

Table 1 Legislation and guidance

Legislation and Guidance	Objectives
Council legislation and guidelines	
Secretary Environmental Assessment Requirements (SEARs)	SEARs provide the additional requirements that must be completed when a critical state significant infrastructure project is submitted in a DA in NSW. The objective of SEARs submissions is to achieve better environmental outcomes by focusing on environmentally sensitive areas and areas of the greatest community concern. The provisions of the SEARs must be met for DA approval including the provision of a construction and operational waste management plan.
Fairfield Local Environmental Plan 2013 (FLEP 2013) ¹	The Fairfield LEP came into force for the local government area in 2013 and guides land use and development by zoning land, identifying what land uses are allowed in each zone, and specifying development standards such as maximum height and minimum lot sizes. LEPs are the main planning tool to shape the future of development in Fairfield City.
Fairfield Citywide Development Control Plan 2013 ²	The Fairfield DCP came into effect in 2013 and provides greater planning detail for developments, supplementing the zoning and development standards contained within the FLEP 2013. The DCP helps promote better development throughout the city, protecting the community's lifestyle and enjoyment of town centres and neighbourhoods. One of the objectives of the DCP is to assist in reducing Fairfield's ecological footprint by encouraging the diversion of waste from landfill. This WMP specifically addresses Appendix E of the DCP for demolition and construction waste and the waste management guidelines in chapter 9 for industrial use.
State and National legislation and guidelines	
Building Code of Australia (BCA) and relevant Australian Standards	The BCA has the aim of achieving nationally consistent, minimum necessary standards of relevant health and safety, amenity and sustainability objectives efficiently.
Council of Australian Governments National Construction Code 2019	The National Construction Code 2019 sets the minimum requirements for the design, construction and performance of buildings throughout Australia.
NSW EPA's Better Practice Guidelines for Waste Management and Recycling in Commercial and Industrial Facilities 2012	These better practice guidelines present information on waste minimisation and resource recovery as well as information on commonly used waste management provisions. The guidelines also provide benchmarks for assessing waste production rates in Australia.
NSW EPA (2014) NSW Waste Avoidance and Resource Recovery Strategy 2014-21	The <i>NSW Waste Avoidance and Resource Recovery Strategy 2014-21</i> is aimed at ultimately 'improving environment and community well-being by reducing the environmental impact of waste and using resources more efficiently' by presenting a framework intended to avoid and reduce waste generation, increase recycling, divert more waste from landfill, manage problem wastes better, reduce litter and reduce illegal dumping.

¹ <https://www.legislation.nsw.gov.au/view/html/inforce/current/epi-2013-0213>

² https://www.fairfieldcity.nsw.gov.au/files/assets/public/documents/plan_build/fairfield-citywide-dcp-2013-amendment-no.22-21-september-20203.pdf

Legislation and Guidance	Objectives
NSW EPA Resource Recovery Orders and Resource Recovery Exemptions	The NSW EPA has issued a number of resource recovery orders and resource recovery exemptions under the POEO (Waste) Regulation 2014 for a range of wastes that may be recovered for beneficial re-use. These wastes typically include those from demolition and construction works, as well as operational wastes such as food waste. - Resource recovery orders present conditions which generators and processors of waste must meet to supply the waste material for beneficial re-use. - Resource recovery exemptions contain the conditions which consumers must meet to use waste for beneficial re-use.
NSW EPA's Waste Classification Guidelines 2014	The NSW EPA <i>Waste Classification Guidelines</i> assists waste generators to effectively manage, treat and dispose of waste to ensure the environmental and human health risks associated with waste are managed appropriately and in accordance with the <i>POEO Act 1997</i> and its associated regulations.
<i>Protection of the Environment Operations Act (POEO) 1997 and Amendment Act 2011</i>	The <i>POEO Act 1997</i> and <i>POEO Amendment Act 2011</i> are administered by the NSW Environment Protection Authority (NSW EPA) to enable the NSW Government to establish instruments for setting environmental standards, goals, protocols and guidelines. They outline the regulatory requirements for lawful disposal of wastes generated during the demolition, construction and operational phases of a development, as well as the system for licencing waste transport and disposal.
The Work Health and Safety Regulation 2011	The Work Health and Safety Regulation 2011 provide detailed actions and guidance associated with the topics discussed in <i>The Work Health and Safety Act 2011</i>. The primary aim of the regulation is to protect the health and safety of workers and ensure that risks are minimised in work environments. Workplaces are to ensure that they are compliant with the requirements specified in the regulations. The regulations discuss items such as actions that are prohibited or obligated in work environments, the requirements for obtaining licences and registrations, and the roles and responsibilities of staff in workplaces.
<i>Waste Avoidance and Resource Recovery Act 2001</i>	The <i>Waste Avoidance and Resource Recovery Act 2001</i> aims to promote waste avoidance and resource recovery and repeals the <i>Waste Minimisation and Management Act 1995</i>. Specific objectives of the <i>Waste Avoidance and Resource Recovery Act 2001</i> include: - Encouraging efficient use of resources - Minimising the consumption of natural resources and the final disposal of waste by encouraging the avoidance of waste and the reuse and recycling of waste - Ensuring industry and the community share responsibility in reducing/dealing with waste, and - Efficiently funding of waste/resource management planning, programs and service delivery. As of 2016, the addition to the Act of Part 5 defines the legislative framework for the 'Return and Earn Container Deposit Scheme' whereby selected beverage containers can be returned to State Government authorities for a monetary refund.

5 Construction Waste and Recycling Management

5.1 Targets for Resource Recovery

The performance of each new development should contribute to the following target from the NSW EPA (2014) *NSW Waste Avoidance and Resource Recovery Strategy 2014-21*:

- 75 % of total construction and demolition waste recycled, increasing to 80 % by 2021.

It is anticipated that the waste minimisation measures in the following sections will assist the Project to meet this target. Waste reporting and audits can be used to determine the actual percentage of wastes that have been recycled during the construction stage of the Project.

5.2 Waste Streams and Classifications

The construction stage of the Project is likely to generate the following broad waste streams:

- Construction wastes
- Plant maintenance waste
- Packaging wastes, and
- Work compound waste from on-site employees.

A summary of likely waste types generated from construction activities, along with their waste classifications and proposed management methods, is provided in **Table 2**.

For further information on how to classify a waste type refer to the NSW EPA (2014) *Waste Classification Guidelines*³. Further information on managing construction wastes is available from the NSW EPA website⁴ and Council's DCP⁵.

³ Available online from <https://www.epa.nsw.gov.au/your-environment/waste/classifying-waste/waste-classification-guidelines>

⁴ <http://www.epa.nsw.gov.au/your-environment/waste/industrial-waste/construction-demolition>

⁵ http://www.fairfieldcity.nsw.gov.au/info/20002/planning_and_building/231/dcps_and_structure_plans

Table 2 Potential waste types and their management methods

Waste Types	NSW EPA Waste Classification	Proposed Management Method
Construction		
Sediment fencing, geotextile materials	General solid waste (non-putrescible)	Reuse at other sites where possible or disposal to landfill
Concrete	General solid waste (non-putrescible)	Off-site recycling for filling, levelling or road base
Bricks and pavers	General solid waste (non-putrescible)	Cleaned for reuse as footings, broken bricks for internal walls, crushed for landscaping or driveway use, off-site recycling
Gyprock or plasterboard	General solid waste (non-putrescible)	Off-site recycling or returned to supplier
Sand or soil	General solid waste (non-putrescible)	Off-site recycling
Metals such as fittings, appliances and bulk electrical cabling, including copper and aluminium	General solid waste (non-putrescible)	Off-site recycling at metal recycling compounds and remainder to landfill
Conduits and pipes	General solid waste (non-putrescible)	Off-site recycling
Timber	General solid waste (non-putrescible)	Off-site recycling, Chip for landscaping, Sell for firewood <i>Treated</i> : reused for formwork, bridging, blocking, propping or second-hand supplier <i>Untreated</i> : reused for floorboards, fencing, furniture, mulched second hand supplier Remainder to landscape supplies.
Doors, Windows, Fittings	General solid waste (non-putrescible)	Off-site recycling at second hand building supplier
Insulation material	General solid waste (non-putrescible)	Off-site disposal
Glass	General solid waste (non-putrescible)	Off-site recycling, glazing or aggregate for concrete production
Asbestos	Hazardous waste	Off-site disposal at a licenced landfill facility.
Fluorescent light fittings and bulbs	Hazardous waste	Off-site recycling or disposal; contact <i>FluoroCycle</i> for more information ⁶
Paint	Hazardous waste	Off-site recycling, Paintback collection ⁷ or disposal
Synthetic Rubber or carpet underlay	General solid waste (non-putrescible)	Off-site recycling; reprocessed and used in safety devices and speed humps

⁶ Available online from <http://www.fluorocycle.org.au/> or <http://www.environment.gov.au/settlements/waste/lamp-mercury.html>

⁷ Available online from <https://www.paintback.com.au/>

Waste Types	NSW EPA Waste Classification	Proposed Management Method
Ceramics including tiles	General solid waste (non-putrescible)	Off-site recycling at a crushing and recycling company
Carpet	General solid waste (non-putrescible)	Off-site recycling or disposal; reused for landscaping, insulation or equestrian uses
Plant Maintenance		
Empty oil and other drums or containers, such as fuel, chemicals, paints, spill clean ups	Hazardous waste: Containers were previously used to store Dangerous Goods (Class 1, 3, 4, 5 or 8) and residues have not been removed by washing or vacuuming. General solid waste (non-putrescible): Containers have been cleaned by washing or vacuuming.	Transport to comply with the transport of Dangerous Goods Code applies in preparation for off-site recycling or disposal at licensed facility
Air filters and rags	General solid waste (non-putrescible)	Off-site disposal
Oil filters	Hazardous waste	Off-site recycling
Batteries	Hazardous waste	Off-site recycling, Contact the Australian Battery Recycling Initiative ⁸ for more information
Packaging		
Packaging materials, including wood, plastic, including stretch wrap or LLPE, cardboard and metals	General solid waste (non-putrescible)	Off-site recycling
Wooden or plastic crates and pallets	General solid waste (non-putrescible)	Reused for similar projects, returned to suppliers, or off-site recycling. Contact <i>Business Recycling</i> for more information ⁹
Work Compound and Associated Offices		
Food Waste	General solid (putrescible) waste	Dispose to landfill with general garbage
Recyclable beverage containers including glass and plastic bottles, aluminium cans and steel cans	General solid waste (non-putrescible)	Co-mingled recycling at off-site licensed facility or deliver to local NSW container deposit scheme 'Return and Earn' facility ¹⁰
Clean paper and cardboard	General solid waste (non-putrescible)	Paper and cardboard recycling at off-site licensed facility
General domestic waste generated by workers such as soiled paper and cardboard and polystyrene	General solid waste (non-putrescible) mixed with putrescible waste	Disposal at landfill

⁸ <http://www.batteryrecycling.org.au/home>

⁹ Available online from <http://businessrecycling.com.au/search/>

¹⁰ Available online from <http://returnandearn.org.au/>

5.3 Construction Waste Types and Quantities

The construction site manager will need to specify the types and quantities of wastes produced during construction and on this basis, the numbers and capacity of skip bins can be determined.

In the absence of readily available construction waste generation rates from Council, SLR has adopted the waste generation rates from Appendix A of The Hills Development Control Plan (DCP) 2012 for estimating the type and quantities of waste generated from construction of the Project. The waste generation rates listed in the Hills DCP include '2 Bedroom', '3 Bedroom', 'Block of Flats', 'Factory' and 'Office'. SLR has adopted the 'Factory' and 'Office' rates to measure waste expected from the Project, as the construction of a factory and office is the most relevant in representing the construction of the industrial warehouse and office precinct.

In the absence of readily available published information for 'Carpark', construction waste generation rates, SLR has developed 'Carpark' construction rates based on the 'Office' rates by:

- Removing timber, bricks and gyprock as these materials are unlikely to be present in significant quantities in a modern carpark structure, and
- Increasing the rates for concrete, sand or soil, metal and 'other', in proportion, to maintain the total assumed tonnage per 1000 m² of construction.

The waste generation rates are shown in **Table 3**.

Table 3 Average waste generation rates for the construction of the project

Rate Type	Floor Area (m ²)	Waste types and quantities (m ³)						
		Timber	Concrete	Bricks	Gyprock	Sand or Soil	Metal	Other
Factory	1,000	0.25	2.10	1.65	0.45	4.80	0.60	0.50
Office	1,000	5.1	18.8	8.5	8.6	8.8	2.75	5
Carpark	1,000	--	30.6	--	--	14.3	4.5	8.1

These waste generation rates are used to estimate the waste generated from the construction of the Project. The anticipated construction waste quantities for are shown in **Section 5.3.1** below.

The waste generation rates for 'Factory' are applied to calculate the waste quantities from the construction of each level of the warehouses and the mezzanines. The 'Office' waste generation rates are applied to calculate the waste quantities from all office administration areas, the guard house and dock office 1. The 'Carpark' waste generation rates are applied to calculate the waste quantities from the construction of all external hard surface areas including access roads, carparks, light duty pavement and heavy-duty pavement. The areas are based on area information provided by the Client.

Actual waste quantities and composition will vary; however, this estimate is provided so that the construction site manager can make provision for on-site or off-site re-use and recycling opportunities.

5.3.1 Construction waste quantities

The construction waste quantities anticipated from Lot 201 are provided in **Table 4**. The areas are based on area information provided by the Client's site plans in **Appendix A**.

Table 4 Estimated types and quantities of construction waste from Project

Project Component		Area (m ²)	Waste types and quantities (m ³)						
			Timber	Concrete	Brick	Gyprock	Sand and Soil	Metal	Other
Lot 201	Warehouse 1 (Jalco)	19,713	5	45	35	10	95	15	10
	Main office 1 (Jalco) (2 levels)	550	5	15	5	5	5	5	5
	Mezzanine office and lab (Jalco)	143	5	5	5	5	5	5	5
	Liquid storage shed	375	5	5	5	5	5	5	5
	Switch, pump and compressor rooms	175	5	5	5	5	5	5	5
	Driver's amen. (Jalco)	40	5	5	5	5	5	5	5
	Warehouse 2	15,000	5	35	25	10	75	10	10
	Main office 2 (2 levels)	560	5	15	5	5	5	5	5
	General waste area	100	5	5	5	5	5	5	5
	Plant room	200	5	5	5	5	5	5	5
	Warehouse 3	3,403	5	10	10	5	20	5	5
	Main office 3 (2 levels)	400	5	10	5	5	5	5	5
	Estate café	60	5	5	5	5	5	5	5
	Heavy duty pavement	17,750	-	545	-	-	255	80	145
	Light duty pavement	6,400	-	200	-	-	95	30	55
Totals		40,719	65	910	120	75	590	190	275

Waste quantity estimates have been rounded up to the nearest 5 m³

Council's DCP requires architectural drawings to show details of the location of containers, separated materials, and treatment of construction waste. Council's checklist is provided in **Appendix B**, which will aid in checking the drawings against Council's requirement. The form is also available on Council's website¹¹.

At the time of preparing this plan, architectural drawings with storage details for construction waste were not available. This is to be updated by the site manager once waste streams, estimated quantities, and final disposal locations and recycling services have been identified.

5.4 Waste Avoidance

In accordance with best practice waste management, the building contractor, building designer and/or equivalent roles should:

- Develop a purchasing policy based on the approximate volumes of materials to be used so that the correct quantities are purchased.
- Arrange for delivery of materials on an 'as needed' basis to avoid material degradation through weathering and moisture damage.

¹¹ https://www.fairfieldcity.nsw.gov.au/files/assets/public/documents/building_development/waste_management_form.pdf

- Communicate strategies to handle and store waste to minimise environmental, health and amenity impacts.
- Select materials with a low environmental impact over the lifecycle of the building.
- Choose timber from certified plantations and avoid unsustainable timber imports including western red cedar, oregon, meranti, luan or merbau.
- Use leased equipment rather than purchase and disposal.
- Minimise site disturbance and unnecessary excavation.
- Incorporate existing trees and shrubs into the landscape plan.
- Grouping wet areas together to minimise the amount of pipe work required.
- Design the Project to require standard material sizes or make arrangements with manufacturing groups for the supply of non-standard material sizes.
- Design works for de-construction.
- Reduce packaging waste by:
 - Returning packaging to suppliers where practicable to reduce waste further along the supply chain
 - Purchasing in bulk
 - Requesting cardboard or metal drums rather than plastics
 - Requesting metal straps rather than shrink wrap, and
 - Using returnable packaging such as pallets and reels.
- Use prefabricated materials.
- Select materials for Project works with low embodied energy properties or materials that have been salvaged or recycled for the construction of the Project including concrete that utilises slag and fly ash content, structural and reinforced steel that uses recycled steel content or bulk insulation products that contain recycled content, such as recycled glass in glass-wool.
- Preferentially use paints, floor coverings and adhesives with low VOC (volatile organic compound) content.
- Reduce the use of polyvinyl chloride products.
- Implement measures to prevent the occurrence of windblown litter, dust and stormwater pollution.
- Ensure subcontractors are informed of and implement site waste minimisation and management procedures.

5.5 Reuse, Recycling and Disposal

Effective management of construction materials and construction and demolition waste, including options for reuse and recycling where applicable and practicable, will be conducted. Only wastes that cannot be cost effectively reused or recycled are to be sent to landfill or appropriate disposal facilities.

Refer to **Table 2** for an outline of the proposed reuse, recycling and disposal methods for potential construction waste streams generated by the Project.

In accordance with best practice waste management, the following specific procedures should be implemented:

- Ensure the site's project management of the site includes minimising waste generation, requiring the appropriate storage and timely collection of waste materials, and maximising re-use or recycling of materials.
- Store wastes on site appropriately to prevent cross-contamination and guarantee the highest possible re-use value.
- Consider the potential of any new materials to be re-used and recycled at the end of the Project's life.
- Determine opportunities for the use of prefabricated components and recycled materials.
- Re-use formwork where appropriate.
- Retain roofing material cut-offs for re-use or recycling.
- Retain used crates for storage purposes unless damaged.
- Recycle cardboard, glass and metal wastes.
- Recycle or dispose of solid waste timber, brick, concrete, asphalt and rock, where such waste cannot be re-used on site, to an appropriately licenced construction and demolition waste recycling facility or an appropriately licenced landfill.
- Dispose of all asbestos and/or hazardous wastes in accordance with SafeWork NSW and NSW EPA requirements.
- Deliver batteries and florescent lights to drop off-site recycling facility.
- Return excess materials and packaging to the supplier or manufacturer.
- Dispose of all garbage via a council approved system.

5.6 Waste Storage and Servicing

5.6.1 Waste Segregation and Storage

As outlined in the DCP and better practice waste management, Waste materials from site preparation, demolition and construction activities are to be separated at the source and stored separately on-site. It is anticipated that the Development will provide sorting bins and areas on-site for recycling and disposal of building waste materials and indicated on the site plans or drawings. Enough space should be for separate storage, for example, separate skip bins or appropriately managed stockpiles, of the following waste types:

- Landfill waste
- Non-recyclable general waste.
- Bricks, concrete, and scrap metal
- Metal and steel, in a condition suitable for recycling at metal recycling facilities
- Timber
- Glass
- Hardstand rubble
- Paper and cardboard

- General co-mingled recycling waste, and
- Uncontaminated excavation spoil if present
- Contaminated excavation spoil if present
- Hazardous waste if present.

If there is insufficient space on-site for full segregation of waste types, the Site Manager, or equivalent role, should consult with the waste and recycling collection contractor to confirm which waste types may be co-mingled prior to removal from the site.

5.6.2 Waste Storage Areas

Waste storage areas will be accessible and allow enough space for storage and servicing requirements. The storage areas will also be flexible in order to cater for change of use throughout the Development. Where space is restricted, dedicated stockpile areas are to be delineated on the site, with regular transfers to dedicated skip bins for sorting.

All waste placed in skips or bins for disposal or recycling will be adequately contained to ensure that the waste does not fall, blow, wash or otherwise escape from the site. Waste containers and storage areas are to be kept clean and in a good state of repair.

Where a skip is required and on-site constraints do not enable it to be located on the property, a separate application for a road occupancy license is required.

In accordance with the Council DCP and better practice waste management, areas designated for waste storage should:

- Allow for appropriate vehicular access to enable the removal of waste materials for reuse, recycling and/or disposal.
- Ensure construction materials are to be stored separately from waste and recycling materials to enable easy access for waste collectors.
- Allow unimpeded access by site personnel and waste disposal contractors
- Consider environmental factors which could potentially cause an impact to the waste storage, such as slope, drainage and the location of watercourses and native vegetation
- Consider visual amenity, safety, accessibility, and convenience in their selection, and
- Not present hazards to human health or the environment.

5.6.3 Waste Servicing and Record Keeping

The site manager or equivalent role is to:

- Arrange for suitable waste collection contractors to remove any construction waste from site
- Ensure waste bins are not filled beyond recommended filling levels
- Ensure that all bins and loads of waste materials leaving site are covered
- Maintain waste disposal documentation detailing, at a minimum:
 - Descriptions and estimated amounts of all waste materials removed from site

- Details of the waste and recycling collection contractors and facilities receiving the waste and recyclables
- Records of waste and recycling collection vehicle movements, for example, date and time of loads removed, licence plate of collection vehicles, tip dockets from receiving facility, and
- Waste classification documentation for materials disposed to off-site recycling or landfill facilities.
- Remove waste during hours approved by Council.

If skips and bins are reaching capacity, removal and replacement should be organised as soon as possible. All site generated building waste collected in the skips and bins will leave the site and be deposited in the approved site lawfully able to accept them.

5.6.4 Contaminated or Hazardous Waste Management

During the site preparation and construction phases, SLR recommends that a qualified and certified contractor is engaged to remove all contaminated or hazardous materials, for example, asbestos, and dispose of all contaminated or hazardous waste at an appropriately licenced facility.

All asbestos and other hazardous waste must be handled according to appropriate legislation and regulation including the Work Health and Safety Regulation 2011. Fairfield DCP also covers handling of asbestos.

5.7 Site Inductions

All staff, including sub-contractors and labourers, employed during the construction phase of the Project must undergo induction training regarding waste management for the site.

Induction training is to cover, as a minimum, an outline of the WMP including:

- Legal obligations and targets
- Emergency response procedures on-site
- Waste priorities and opportunities for reduction, reuse and recycling
- Waste storage locations and separation of waste
- Procedures for suspected contaminated and hazardous wastes
- Waste related signage
- The implications of poor waste management practices, and
- Responsibilities and reporting, including identification of personnel responsible for waste management and individual responsibilities.

It is the responsibility of the site manager or building contractor to notify Council of the appointment of waste removal, transport or disposal contractors.

5.8 Signage

Standard signage is to be posted in all waste storage and collection areas. All waste containers should be labelled correctly and clearly to identify stored materials.

Signs approved by the NSW EPA for labelling of waste materials are available online¹² and should be used where applicable. A selection of signs prepared by NSW EPA is provided in **Figure 3**.



Figure 3 Examples of NSW EPA labels for waste skips and bins

5.9 Monitoring and Reporting

The following monitoring practices are to be undertaken to improve construction waste management and to obtain accurate waste generation figures:

- Conduct waste audits of current projects where feasible.
- Note waste generated and disposal methods.
- Look at past waste disposal receipts.
- Record this information to track waste avoidance, reuse and recycling performance and to help in waste estimations for future waste management plans.

As per Council's DCP, all demolition and construction waste dockets must be kept which show which facility received the material for recycling or disposal. Audits may be conducted by Council to verify that dockets have been kept and waste recycled and disposed of as described within the WMP. Dockets will need to show the company's Australian Business Number (ABN). This can include dockets or receipts verifying recycling and disposal in accordance with this WMP. This evidence should also be presented to regulatory bodies when required.

Daily visual inspections of waste storage areas will be undertaken by site personnel and inspection checklists and logs recorded for reporting to the site manager on a weekly basis or as required. These inspections will be used to identify and rectify any resource and waste management issues.

Waste audits are to be carried out by the building contractor to gauge the effectiveness and efficiency of waste segregation procedures and recycling and reuse initiatives. Where audits show that the above procedures are not carried out effectively, additional staff training will be undertaken and signage re-examined.

¹² NSW EPA approved waste materials signage <https://www.epa.nsw.gov.au/your-environment/recycling-and-reuse/business-government-recycling/standard-recycling-signs>

5.10 Roles and Responsibilities

All personnel have a responsibility for their own environmental performance and compliance with all legislation. It will be the responsibility of the building contractor to implement the WMP, and an employee and subcontractor responsibility to ensure that they always comply with the WMP.

Where possible, an environmental management representative should be appointed for the Project. Suggested roles and responsibilities are provided in **Table 5**.

Table 5 Suggested roles and responsibilities for construction waste management

Responsible Person	General Tasks
Construction Site Manager	Ensuring plant and equipment are well maintained.
	Ordering only the required amount of materials.
	Keeping materials segregated to maximise reuse and recycling.
	Ultimately responsible for routinely checking waste sorting and storage areas for cleanliness, hygiene and safety issues, contaminated waste materials, and also ensuring that all monitoring and audit results are well documented and carried out as specified in the WMP.
Construction Environmental Manager or equivalent	Approaching and establishing the local commercial reuse of materials where reuse on-site is not practical.
	Establishing separate skips and recycling bins for effective waste segregation and recycling purposes.
	Ensuring staff and contractors are aware of site requirements.
	Provision of training of the requirements of the WMP and specific waste management strategies adopted for the Project.
	Contaminated waste management and approval of off-site waste transport, disposal locations and checking licensing requirements.
	Approval of off-site waste disposal locations and checking licensing requirements.
	Assessment of suspicious potentially contaminated materials, hazardous materials and liquid wastes.
	Monitoring, inspection and reporting requirements.

Daily visual inspections of waste storage areas may be delegated to other on-site staff. All subcontractors will be responsible for ensuring that their work complies with the WMP through the project induction and contract engagement process.

6 Operational Waste Management

6.1 Targets for Resource Recovery

The waste management performance of each new development should contribute to the overall NSW State targets for recycling outlined in the *NSW Waste Avoidance and Resource Recovery Strategy 2014-21*. The targets include increasing waste diverted from landfill to 75% and recycling 70% of commercial, industrial and municipal solid waste¹³. Each commercial and industrial development can contribute to this NSW State target through an effective waste management plan.

It is anticipated that the waste minimisation measures in the following sections will assist the Project to meet the state's targets. Waste reporting and audits can be used to determine the actual percentage of waste that are being, or have been, recycled during operation.

6.2 Waste Streams and Classifications

The operation of the Project is anticipated to generate the following broad waste streams:

- Domestic wastes generated by employees, including food wastes
- Bulk packaging wastes, including polystyrene, plastic wrapping and cardboard boxes
- Office waste
- Garden organic waste from landscaped areas
- Bulky waste items such as furniture and e-waste, and
- Stores, plant and general maintenance wastes.

Potential ongoing waste types, their associated waste classifications, and management methods are provided in **Table 6**. For further information on how to determine a waste's classification, refer to the NSW EPA (2014) Waste Classification Guidelines. Suggestions for recycling drop off locations and contacts can be found on <https://businessrecycling.com.au/> for each waste type.

Table 6 Potential waste types, classifications and management methods for operational waste

Waste Types	NSW EPA Classification	Proposed Management Method
General Operations		
Clean office paper	General solid (non-putrescible) waste	Paper recycling at off-site licensed facility
Cardboard including bulky cardboard boxes	General solid (non-putrescible) waste	Cardboard recycling at off-site licensed facility
Recyclable beverage containers, glass and plastic bottles, aluminium cans, steel cans	General solid (non-putrescible) waste	NSW container deposit scheme 'Return and Earn', container recycling at off-site licensed facility

¹³ <https://www.epa.nsw.gov.au/-/media/epa/corporate-site/resources/wastestrategy/140876-warr-strategy-14-21.pdf?la=en&hash=EC6685E6624995242B0538B18C2E80C0CA2E51B3>

Waste Types	NSW EPA Classification	Proposed Management Method
Food waste	General solid (putrescible) waste	Compost on or off-site or dispose to landfill with general garbage
Batteries	Hazardous waste	Off-site recycling, alternatively contact the Australian Battery Recycling Initiative for more information
Mobile Phones	Hazardous waste	Off-site recycling; can be taken to the Mobile Muster program. Contact Mobile Muster for more information
Bulky polystyrene	General solid (non-putrescible) waste	Off-site recycling or disposal at landfill
Furniture	General solid (non-putrescible) waste	Off-site reuse or disposal to landfill
E-waste	Hazardous waste	Off-site recycling
Printer toners and ink cartridges	Hazardous waste	Off-site recycling, free disposal box or bags and pickup service exists for printer toners and ink cartridges
General garbage, including non-recyclable plastics	General solid (putrescible and non-putrescible) waste	Disposal at landfill
Maintenance		
Spent smoke detectors ¹⁴	General solid (non-putrescible) waste, or Hazardous waste (some commercial varieties)	Disposal to landfill, or off-site disposal at licensed facility
Glass, other than containers	General solid (non-putrescible) waste	Off-site recycling
Light bulbs and fluorescent tubes	Hazardous waste	Off-site recycling or disposal, contact FluoroCycle ¹⁵ or Lamp Recyclers ¹⁶ for more information
Cleaning chemicals, solvents, area wash downs, empty oil or paint drums, chemical containers	Hazardous waste if containers used to store Dangerous Goods (Class 1, 3, 4, 5 or 8) and residues have not been removed by washing or vacuuming. General solid (non-putrescible) waste if containers cleaned by washing or vacuuming.	Transport to comply with the transport of Dangerous Goods Code applies in preparation for off-site recycling or disposal at licensed facility.
Garden organics - lawn mowing, tree branches, hedge cuttings, leaves	General solid (non-putrescible) waste	Reuse on-site or contractor removal for recycling at licenced facility

¹⁴ The Australian Radiation Protection and Nuclear Safety Agency (ARPANSA) require that when more than 10 smoke alarms (particularly americium-241 sources) are collected for bulk disposal they must be treated as radioactive waste and the requirements of the National Health and Medical Research Council's Code of practice for the near-surface disposal of radioactive waste in Australia (1992) must be met.

¹⁵ <https://www.fluorocycle.org.au/>

¹⁶ <https://www.lamprecyclers.com.au/>

6.3 Estimated Quantities of Operational Waste

In the absence of waste generation rates from Council, SLR has adopted the waste generation rates for 'Offices' and 'Warehouse' from the Penrith City Council DCP 2014 section 3.3.4¹⁷ for estimating the type and quantities of waste generated for from the operational activities of Warehouses 2 and 3 of Lot 201. The operational waste generation rates used are shown below in **Table 7**.

Table 7 Waste generation rates applied to the operations of Warehouses 2 and 3

Type of Premises	General Waste Generation (L/100 m ² /day)	Recycling Generation (L/100 m ² /day)
Warehouse	10	10
Offices	10	10
Cafe	300	200

Using the waste generation rates in **Table 7** above, the approximate weekly waste quantities for the Project have been calculated and are presented in **Section 6.3.1**. The operational waste quantities were additionally calculated based on the below assumptions:

- GFAs as presented on the architectural drawings shown in **Appendix A**, and
- A week comprising seven days of operation.

Based on the Project's activities, SLR estimates that large quantities of the recycling stream will include pallets and plastic and cardboard packaging waste. To minimise packaging waste generated in the recyclables stream, it is recommended that packing waste is returned to the suppliers where possible. Standard pallets are recommended to be returned to their owners and non-standard and broken pallets are to be stockpiled and collected as required by a private waste contractor.

If additional collection services are required, such as secured document destruction, these can be organised with a private waste contractor who can provide additional bins and take collected waste to an off-site licenced facility.

6.3.1 Estimated quantities of operational waste

The estimated quantities of operational waste generated by Warehouses 1, 2 and 3 are shown in **Table 8**. The naming conventions used in **Table 8** are as per the plans provided by the Client.

Based on communication with the Client, the anticipated operations of Warehouses 1, 2 and 3 are primarily anticipated to be packaging waste consisting of paper and recycling. Comingled recycling is anticipated to be minimal and primarily be generated from the office areas. Hence the recycling breakdown of 60% paper and cardboard, and 40% other recycling has only been considered for the office spaces, where comingled recycling will be generated.

¹⁷ <https://www.penrithcity.nsw.gov.au/building-development/planning-zoning/planning-controls/development-control-plans>

Table 8 Estimated quantities of operational general waste and recycling of Warehouses 2 and 3

Complex	Location	Area (m ²)	General Waste (L/week)	Recycling Paper and Cardboard (L/week)	Recycling Other (L/week)
Lot 201	Warehouse 1	19,713	13,825	8,295	5,530
	Main office 1 (2 levels)	536	385	245	175
	Total – Warehouse 2	20,249	14,210	8,540	5,705
	Warehouse 2	15,000	10,500	6,300	4,200
	Main office 2 (2 levels)	560	420	245	175
	Total – Warehouse 2	15,560	10,920	6,545	4,375
	Warehouse 3	3,403	2,415	1,435	980
	Main office 3	400	280	175	140
	Total – Warehouse 3	3,803	2,695	1,610	1,120
	Estate Cafe	60	1,260	525	350

Waste quantity estimates have been rounded up to the nearest 5 L.

'Other Recycling': comingled recycling excluding paper and cardboard.

The Project is anticipated to produce minimal quantities of garden organics, less than 100 L per week. This waste will be taken by a landscaping contractor who will dispose of it at an off-site licenced facility.

6.4 Waste Storage Area Size

For each building that is a part of the Project, the waste storage area must be large enough to adequately store all quantities of operational waste and recycling between collections.

In the absence of bin dimensions from Council, SLR has adopted the bin dimensions from the Penrith City Council DCP 2014 section 3, as outlined in **Table 9**.

Table 9 Dimensions and approximate footprint of bins

Capacity	Height (mm)	Depth (mm)	Width (mm)	Footprint (m ²)
240 L	1,100	740	600	0.44
660 L	1,400	1,260	800	1.01
1,100 L	1,330	1,240	1,090	1.35
1.5 m ³	1,190	1,080	2,070	2.24
3 m ³	1,540	1,520	2,060	3.13

To allow for ready movement of bins into and out of the bin storage area, the bin storage area is to provide a floor area of at least 150% of the total minimum bin footprint. This can also act as a contingency in the event of spikes in waste generation. This has been considered in the calculation of the waste storage area for each of the buildings in the Project. The waste storage area sizes are shown in **Section 6.4.1**.

The recommended storage areas do not include consideration for the storage of bulky and hazardous waste. For the additional storage space for bulky and hazardous waste, refer to **Section 6.5**.

6.4.1 Waste storage area size

The estimated number of bins required for weekly storage of operational waste and recycling generated by the project are in **Table 11** and are based on:

- The estimated quantities of operational waste and recycling as shown in **Table 8**
- Bin dimensions from as shown in **Table 9**
- Garbage and recycling collection frequency as shown in **Table 10** below

Table 10 Collection frequency for Warehouses 2 and 3

Complex	Location	Collections Per Week		
		Garbage	Recycling Paper and Cardboard	Recycling other
Lot 201	Warehouse 1	4	4	4
	Warehouse 2	4	4	4
	Warehouse 3	3	3	3
	Cafe	3	3	3

The waste storage areas calculations in **Table 11** are only recommendations, based on preliminary master planning information, and should be updated for Warehouses 1, 2 and 3 once detailed drawings are available.

Table 11 Recommended number of bins and storage area for weekly operations for Warehouses 2 and 3

Complex	Location	Bins Required			Total Number of Bins	Recommended Storage Area (m ²)
		General Waste	Paper and Cardboard Recycling	Comingled Recycling		
Lot 201	Warehouse 1	2 x 3 m ³	1 x 3 m ³	1 x 1.5 m ³	4	20
	Warehouse 2	1 x 3 m ³	1 x 3 m ³	1 x 1.5 m ³	3	15
	Warehouse 3	1 x 1,100 L	1 x 660 L	2 x 240 L	4	5
	Cafe	1 x 660 L	1 x 240 L	1 x 240 L	3	5

In accordance with waste management best practice, SLR recommends that the architectural drawings, attached in **Appendix A**, are updated to show the anticipated specifications for a waste collection room. Following the revision of the architectural plans, SLR recommends that this WMP is updated.

6.5 Bulky and Hazardous Waste Management

Sufficient space will be provided in the Project for the storage of large and/or bulky items and hazardous wastes that cannot be disposed of in the general waste or recyclable streams. This would include broken pallets, furniture, shelving, monitors, batteries, fluorescent tubes and smoke detectors.

Building management may consider organising a separate casual collection service for as required, to remove bulky waste items, or engaging a contractor to collect and transport these items for reuse, recycling or disposal.

6.6 Waste Storage Room Location

In accordance with better practice waste management and recommendations from Council's DCP, the waste storage area should be located so that:

- It is away from adjoining residential dwellings
- It does not cause any negative impacts, in terms of visual appearance, noise or smell, to adjoining properties, or to the street
- It is near any on-site loading bays
- It is convenient, safe, functional and directly accessible to users in each tenancy and servicing collection staff, but inaccessible to the public
- It avoids pedestrian or vehicular traffic hazards likely to be caused by waste collection and storage,

SLR recommends the architectural plans for this Project are updated to show the waste storage areas recommended in **Section 6.4**. Following the revision of the architectural plans, SLR recommends that this WMP is updated.

6.7 Waste Storage Area Features

In accordance with best practice waste management and Council's DCP, the Project's waste storage areas should have the following features:

- Be designed so that the floors and walls can be washed on a regular basis
- Include separation facilities for waste to be divided into separate waste streams in order to recycle materials
- Blend into the design of the wider development and the surrounding streetscape
- Be well lit and well-ventilated
- Fully enclosed and walled
- Adequate vermin prevention measures
- Reduce potential noise and odour impacts
- Enhance safety for the public
- Be connected to a water outlet for washing purposes
- Equipped with a hot and cold tap-based water supply centralised mixing valve
- Floor graded to a central drainage point which is connected to the sewer
- Have water discharge from washing flow to a sewer approved by the relevant authority
- Waterproofed and sealed non-slip floor constructed in accordance with the Building Code of Australia.
- Waste equipment is protected from theft and vandalism
- Be fully enclosed, walled and not permit through access to other on-site waste infrastructure
- Adequate lighting and natural or mechanical ventilation in accordance with the Building Code of Australia

- Provide administrative management, including signage to ensure appropriate use
- Be screened from public areas to reduce the impacts of noise, odour and visual amenity, and
- Flexible in design to allow for future changes in operation, tenancies and uses.

6.8 Waste Servicing

The following general waste servicing access requirements should be implemented:

- Waste will be removed regularly.
- Arrangements should be in place so that the waste and recycling storage rooms are not accessible to the general public.

In accordance with best practice waste management, the following is recommended for the access provisions for of waste collection vehicles:

- Collection vehicles should be able to enter and exit the collection area in a forward direction
- Drawings should show the site's entry point, vehicle's route of travel and manoeuvring
- Swept path models should illustrate how a standard waste collection vehicle will enter, service and exit the site
- Unobstructed access, adequate driveways and ramps of sufficient strength to support waste collection

SLR recommends that the design of the Project is reviewed by a traffic specialist and that the drawings are updated accordingly. This WMP should then be updated to reflect those updates.

Hazardous waste produced at the site will be collected by appropriately licensed specialised services.

Once a private waste contractor is engaged, a valid waste and recycling collection contract is recommended to demonstrate disposal at a waste facility lawfully able to accept it. Written evidence of the valid contract should be kept on-site.

6.9 Waste Avoidance, Reuse and Recycling Measures

6.9.1 Waste Avoidance

Waste avoidance measures include:

- Participating in take-back services to suppliers to reduce waste further along the supply chain
- Avoiding printing where possible
- Review of packaging design to reduce waste but maintain 'fit for purpose'
- Providing ceramic cups, mugs, crockery and cutlery rather than disposable items
- Purchasing consumables in bulk to avoid unnecessary packaging
- Presenting all waste reduction initiatives to staff as part of their induction program, and
- Investigating leased office equipment and machinery rather than purchase and disposal.

6.9.2 Re-use

Possible re-use opportunities include establishing systems with in-house and supply chain stakeholders to transport products in re-useable packaging where possible.

6.9.3 Recycling

Recycling opportunities include:

- Collecting and recycling e-wastes
- Flatten or bale cardboard to reduce number of bins required
- Paper recycling trays provided in office areas for scrap paper collection and recycling
- Collecting printer toners and ink cartridges in allocated bins for appropriate contractor recycling, and
- Development of 'buy recycled' purchasing policy.

6.10 Communication Strategies

Waste management initiatives and management measures should be clearly communicated to building managers, owners, employees, customers and cleaners. Benefits of providing this communication include:

- Improved satisfaction with services
- Increased ability and willingness to participate in recycling
- Improved amenity and safety
- Improved knowledge and awareness through standardisation of services
- Increased awareness or achievement of environmental goals and targets
- Reduced contamination of recyclables stream
- Increased recovery of recyclables and organics material, if implemented, and
- Greater contribution to targets for waste reduction and resource recovery, the environment and heritage conservation.

To realise the above benefits, the following communication strategies should be considered:

- Use consistent signage and colour coding throughout the Project
- Ensure all staff are trained in correct waste separation and management procedures
- Provide directional signage to show location of and routes to waste storage area
- General waste and co-mingled recycling bins should be clearly labelled and colour-coded to ensure no cross contamination, where applicable
- Employees and cleaners should adhere to the WMP for compliance, in consultation with management, and
- Repair signs and labels promptly to avoid breakdown of communications.

6.11 Signage

In accordance with best practice waste management, the waste storage and collection areas should be provided with appropriate signage. These signs should clearly identify waste management procedures and provisions to contractors, tenants and visitors should be distributed around the Project.

Signs which clearly identify waste management procedures and provisions to staff and visitors should be distributed around the Project. Key signage considerations are:

- Clear and correct labelling on all waste and recycling bins, indicating the correct type or types of waste that can be placed into a given bin, as shown in **Figure 4**
- Signposts and directions to location of waste storage areas
- Clear signage in all waste storage areas to instruct users how to correctly separate waste and recycling
- Maintaining a consistent style colour scheme and system for signs throughout the Project, and
- Emergency contact information for reporting issues associated with waste or recycling management.

Colour-coded and labelled bin lids are necessary for identifying bins. All signage should conform to the relevant Australian Standard and use labels approved by the NSW EPA¹⁸. The design and use of safety signs for waste rooms and enclosures should comply with Australian Standard AS 1319 Safety Signs for the Occupational Environment and clearly describes the types of materials designated for each bin.



Figure 4 Example of bin labels for operational waste

6.12 Monitoring and Reporting

Monitoring is recommended to ensure waste and recycling management arrangements and provisions for the Project are functional, practical and are maintained to the standard outlined in this plan, at a minimum.

Visual assessments of bins and bin storage areas should be conducted by the building manager, at minimum:

- Weekly, in the first two months of operation to ensure the waste management system is sufficient for the operation, and
- Every six months, to ensure waste is being managed to the standards outlined in this document.

¹⁸ NSW EPA waste signage and label designs <http://www.epa.nsw.gov.au/wastetools/signs-posters-symbols.htm>

In addition, audits are to be conducted on a half-yearly basis to ensure WMP provisions are maintained.

Quantities of waste and recycling associated with disposal of waste and recycling, including dockets, receipts and other physical records should be recorded by the Building Manager. This is to allow reviews of the waste management arrangements and provisions at the site over time. Records of waste disposal should also be available to regulatory authorities such as the NSW Environmental Protection Authority and SafeWork NSW, upon request.

Any deficiencies identified in the waste management system, including, but not limited to, unexpected waste quantities, is to be rectified by the Building Manager as soon as it is practical. Where audits show that recycling is not carried out effectively, management should carry out additional staff training, signage re-examination and reviews of the waste management system where the audit or other reviewing body has deemed necessary. If this waste management plan no longer sufficiently meets the needs of the Project, review and updates to maintain suitability must be undertaken.

6.13 Roles and Responsibilities

It is the responsibility of the Building Manager, or equivalent role, to implement this WMP and a responsibility of all warehouse tenants and staff to follow the waste management procedures set out by the WMP. SLR recommends that all subcontractors enlisted by the Client are to have roles and responsibilities identified and the Project's waste management system clearly explained. A summary of recommended roles and responsibilities are provided in **Table 12**.

Table 12 Operational waste management responsibility allocation

Responsible Person	General Tasks
Management	Ensure the WMP is implemented throughout the life of the operation.
	Update the WMP on a regular basis (e.g. annually) to ensure the Plan remains applicable.
	Undertake liaison and management of contracted waste collections.
	Organise internal waste audits on a regular basis.
	Manage any complaints and non-compliances reported through waste audits etc.
	Perform inspections of all waste storage areas and waste management equipment on a regular basis.
	Organise cleaning and maintenance requirements for waste management equipment.
	Monitor bins to ensure no overfilling occurs.
	Ensure effective signage, communication and education is provided to alert visitors, employees and cleaners about the provisions of this WMP and waste management equipment use requirements.
	Monitor and maintain signage to ensure it remains clean, clear and applicable.
	Ensure waste and recycling storage rooms are kept tidy.
	Ensure that regular cleaning and daily transfer of bins is being undertaken by the cleaners
	Ultimately responsible for the management of all waste management equipment, cleaning requirements, waste transfer and collection arrangements.
Cleaners and Staff	Removal of general waste, recyclables, cardboard waste and hazardous waste from floor areas for transfer to centralised waste and recycling collection rooms daily or as required.
	Cleaning of all bins and waste and recycling rooms on a weekly basis or as required.

Responsible Person	General Tasks
	Compliance with the provisions of this WMP.
Gardening Contractor, as applicable	Removal of all garden organics waste generated during gardening maintenance activities for recycling at an off-site location or reuse as organic mulch on landscaped areas.

APPENDIX A

Client Architectural Drawings



DEVELOPMENT TOTAL AREA	
TOTAL SITE AREA	208,168 sqm
TOTAL BUILDING AREA	109,493 sqm
TOTAL EFFICIENCY	52.60 %

DEVELOPMENT SUMMARY (LOT 201)	
SITE 1 AREA (Warehouse 1)	96,580 sqd
SITE 2 AREA (Warehouse 2 & 3 & Cafe Site)	40,728 sqd
SITE AREA (Lot 201) Total	77,310 sqd
WAREHOUSE 1 (incl. Receiving & Dispatch Office)	51,831 sqd
WAREHOUSE 2	19,713 sqd
WAREHOUSE 3	536 sqd
WAREHOUSE 1 DRIVERS AMENITIES	38 sqd
WAREHOUSE 1 SATELLITE ROOM	30 sqd
WAREHOUSE 2	15,000 sqd
WAREHOUSE 2 OFFICE 2 (2 weeks)	578 sqd
WAREHOUSE 2 GENERAL WASTE AREA	100 sqd
WAREHOUSE 2 PLANT ROOM	100 sqd
WAREHOUSE 3	3,400 sqd
WAREHOUSE 3 OFFICE 3 (2 weeks)	415 sqd
ESTATE CAFE	60 sqd
TOTAL BUILDING AREA	40,073 sqd
CAR PARKING PROVIDED	234 spaces
CAR PARKING PROVISIONAL	10 spaces
WALKING (5M)	3,730 sqd
AWING (5M)	28 sqd
HEAVY DUTY PAVEMENT (H)	18,100 sqd
LIGHT DUTY PAVEMENT (L)	6,100 sqd

DEVELOPMENT SUMMARY (LOT 202)	
SITE AREA	50,483 sqmrs
EFFICIENCY	66.08 %
WAREHOUSE A	15,880 sqmrs
OFFICE & DOCK OFFICE A	800 sqmrs
WAREHOUSE B	15,880 sqmrs
OFFICE & DOCK OFFICE B	800 sqmrs
TOTAL BUILDING AREA	33,360 sqmrs
CAR PARKING PROVIDED	147 Spaces
HEAVY DUTY PAVEMENT (H)	11,230 sqmrs
LIGHT DUTY PAVEMENT (L)	3,900 sqmrs
SUSPENDED SLAB	2,550 sqmrs

DEVELOPMENT SUMMARY (LOT 203)	
SITE AREA (Ind: Environmental Zone - 6,464 sqm)	40,295 sqm
EFFICIENCY	48.47 %
WAREHOUSE	18,730 sqm
OFFICE & DOCK OFFICE	800 sqm
TOTAL BUILDING AREA	19,530 sqm
CAR PARKING PROVIDED	140 Spaces
HEAVY DUTY PAVEMENT (H)	6,160 sqm
LIGHT DUTY PAVEMENT (L)	4,120 sqm

DEVELOPMENT SUMMARY (LOT 204)	
SITE AREA (APZ included): 7,166 sqm	42,082 sqm
EFFICIENCY:	41.36 %
WAREHOUSE A	4,728 sqm
OFFICE A (2 LEVELS)	500 sqm
WAREHOUSE B	3,454 sqm
OFFICE B (2 LEVELS)	400 sqm
WAREHOUSE C	3,397 sqm
OFFICE C (2 LEVELS)	400 sqm
SHARED LOBBY	78 sqm
OFFICE D (2 LEVELS)	3,156 sqm
OFFICE E (2 LEVELS)	400 sqm
TOTAL BUILDING AREA	16,513 sqm
AWNING (5m)	172sqm
AWNING (15m)	2,215 sqm
AWNING (40m)	117sqm
CAR PARKING PROVIDED	134 Spaces
HEAVY DUTY PAVEMENT (H)	9,220 sqm
LIGHT DUTY PAVEMENT (L)	4,970 sqm


DEVELOPMENT SUMMARY (LOT 201)		
SITE 1 AREA (Warehouse 1)	36,582 sqm	
SITE 2 AREA (Warehouse 2 & 3 & Cafe Site)	40,728 sqm	
SITE AREA (Lot 201 Total)	77,310 sqm	
EFFICIENCY	51.83%	
WAREHOUSE 1 (incl. Receiving & Dispatch Office)	19,713 sqm	
MAIN OFFICE 1 (2 Levels)	536 sqm	
WAREHOUSE 1 DRIVERS AMENITIES	38 sqm	
WAREHOUSE 1 Switch Room	30 sqm	
WAREHOUSE 2	15,000 sqm	
MAIN OFFICE 2 (2 Levels)	578 sqm	
WAREHOUSE 2 GENERAL WASTE AREA	100 sqm	
WAREHOUSE 2 PLANT ROOM	200 sqm	
WAREHOUSE 3	3,403 sqm	
MAIN OFFICE 3 (2 Levels)	415 sqm	
ESTATE CAFE	60 sqm	
TOTAL BUILDING AREA	40,073 sqm	
CAR PARKING PROVIDED	234 spaces	
CAR PARKING PROVISIONAL	10 spaces	
AWNING (15M)	3,730 sqm	
AWNING (5M)	280 sqm	
HEAVY DUTY PAVEMENT (H)	18,100 sqm	
LIGHT DUTY PAVEMENT (L)	6,100 sqm	

Parking Schedule (Lot 201 - WH1)		
Type Mark	Type	Count
PK-CP1	PK-CP1-5500 x 2500mm - 90 deg	108
PK-CP1	PK-CP1-5500 x 2500mm - (Disable)	2
Grand total		110

Parking Schedule (Lot 201 - WH2)		
Type Mark	Type	Count
PK-CP1	PK-CP1-5500 x 2500mm - 90 deg	96
PK-CP1	PK-CP1-5500 x 2500mm - (Disable)	2
Grand total		98

Parking Schedule (Lot 201 - WH3)		
Type Mark	Type	Count
PK-CP1	PK-CP1-5500 x 2500mm - 90 deg	15
PK-CP3	PK-CP3-5500 x 2400mm - 90 deg 2	4
PK-CP1	PK-CP1-5500 x 2500mm - (Disable)	1
PK-PP1	PK-PP1-2.4w x 5.4m (Provisional Parking)	5
PK-PP2	PK-PP2-5.9 x 2.2m Parallel (Provisional Parking)	5
Grand total		30

Parking Schedule (Cafe)		
Type Mark	Type	Count
PK-CP1	PK-CP1-5500 x 2500mm - 90 deg	5
PK-CP1	PK-CP1-5500 x 2500mm - (Disable)	1
Grand total		6

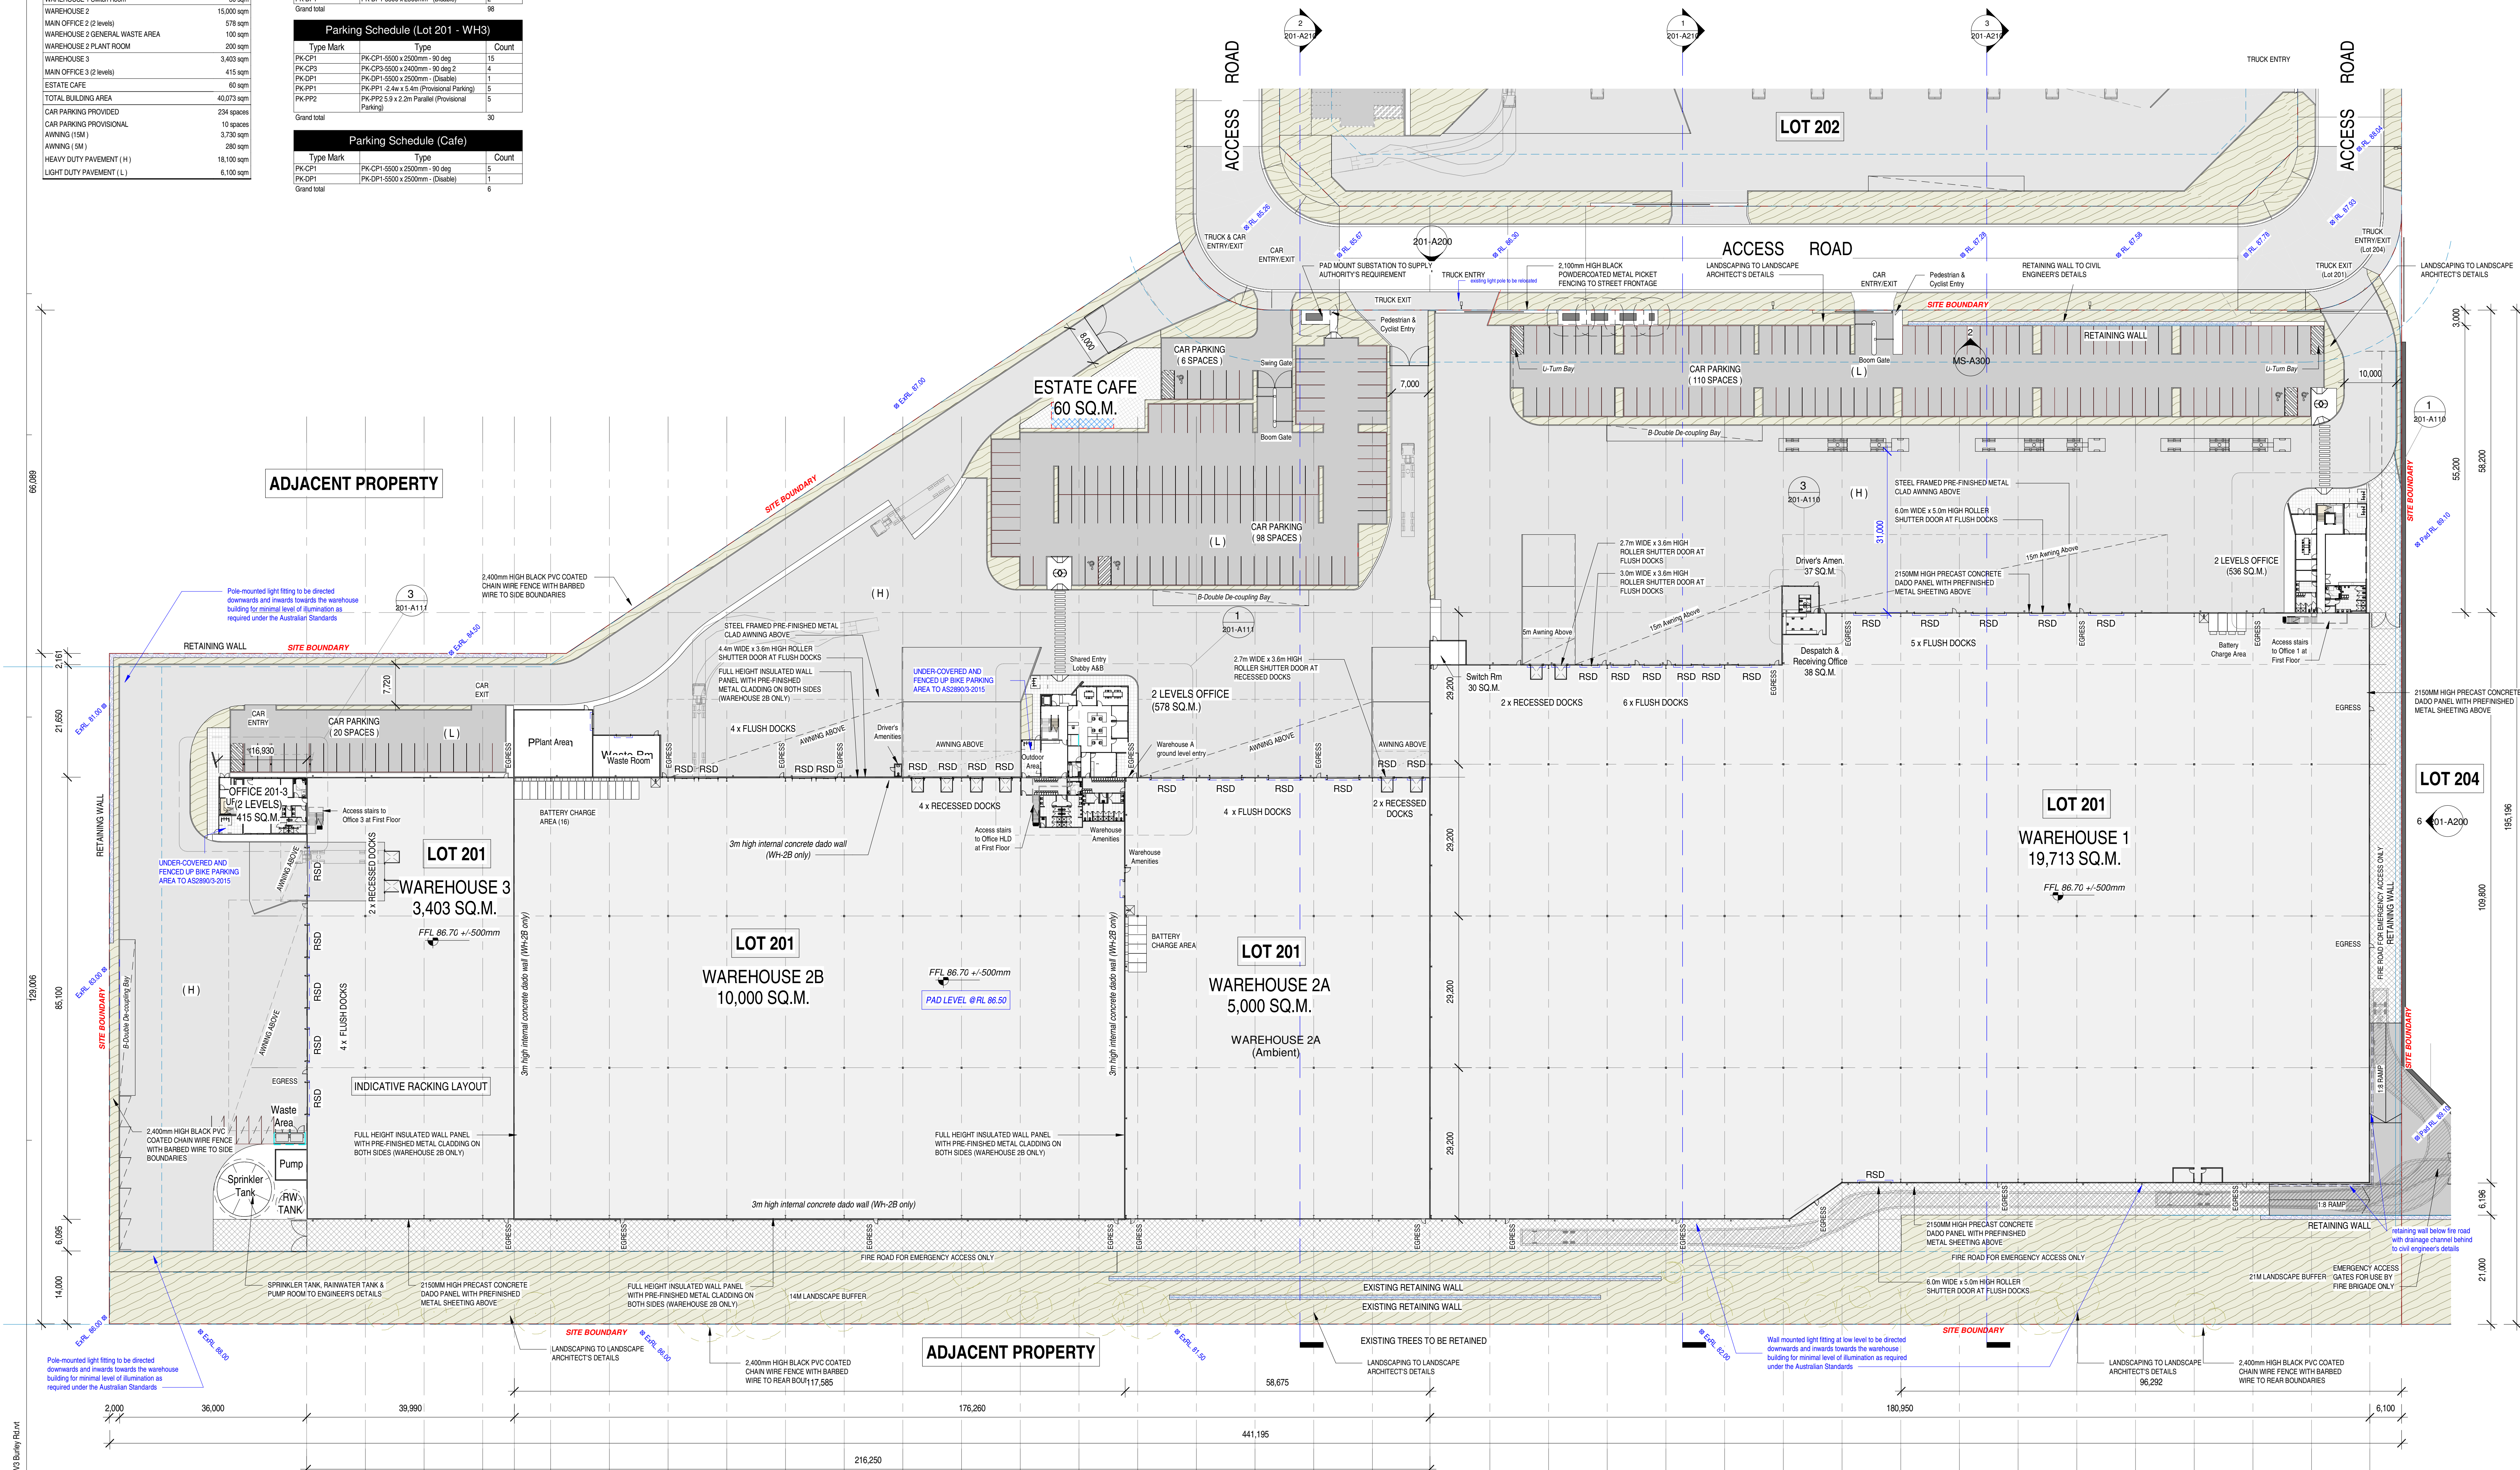

1 MS-A010 1:500 @B1 Site Facilities Plan (Lot 201)

APPENDIX B

Fairfield City Council DCP Appendix E - Waste management Plan



Waste Management Plan

Demolition and Construction

This Waste Management Plan:

- must be completed and submitted to the Principle Certifying Authority;
- details what and how much waste will be generated, avoided, reused on site, recycled and disposed of;
- shows on a site plan the location of containers, separated materials, and treatment;
- will be assessed on how it keeps disposal of waste to a minimum; and
- will be audited by Council through the checking of all demolition and construction waste dockets which show which facility received the material for recycling or disposal.

Your proposal

Site address: 327-335 Burley Road, Horsley Park

Applicant's name and address: ESR (AUST) Pty Ltd.

Level 29, 20 Bond St, Sydney 2000, Australia

Phone: +61 2 9506 1411

Mobile:

Fax:

Email

Buildings and other structures on site: *What is on the land now?*

Description of proposal: *What do you want to do on the land?*

Lots 201 of industrial estate comprised of four industrial warehouses with attached office precincts, including internal roads, car parking spaces, hardstands and a guard house

The details provided in this Waste Management Plan are how I intend to treat waste during this project.

- I have made an assessment on the material on site and considered if it contains asbestos. I know my responsibilities about asbestos removal and disposal under and that if asbestos is disturbed during renovation and demolition it can be deadly.
- **I will keep all demolition and construction waste dockets** which show which facility received the material for recycling or disposal. I understand that an audit may be conducted by Council to verify that dockets have been kept and waste recycled and disposed of as described within the Waste Management Plan.

Applicant's signature

Date

Construction

Section 2: Construction Waste Management Plan

Materials on site		Destination Reuse and recycling		
Type of material	Estimated Volume (m ² or m ³)	ON SITE Detail reuse or onsite recycling	OFF-SITE Detail contractor and recycling outlet • Company Name • Telephone number (contactable during Council office hours).	DISPOSAL Detail contractor and landfill site • Company Name • Telephone number (contactable during Council office hours).
Excavation material	sand and soil 590 m ³			
Green waste				
Bricks	120 m ³			
Concrete	910 m ³			
Timber – what kind?	65 m ³			
Plasterboard	75 m ³			
Metals – what kind?	190 m ³			
Other	275 m ³			

ASIA PACIFIC OFFICES

BRISBANE

Level 2, 15 Astor Terrace
Spring Hill QLD 4000
Australia
T: +61 7 3858 4800
F: +61 7 3858 4801

MACKAY

21 River Street
Mackay QLD 4740
Australia
T: +61 7 3181 3300

SYDNEY

Tenancy 202, Sub Base Platypus
120 High Street
North Sydney NSW 2060
Australia
T: +61 2 9427 8100
F: +61 2 9427 8200

AUCKLAND

68 Beach Road
Auckland 1010
New Zealand
T: 0800 757 695

CANBERRA

GPO 410
Canberra ACT 2600
Australia
T: +61 2 6287 0800
F: +61 2 9427 8200

MELBOURNE

Level 11, 176 Wellington Parade
East Melbourne VIC 3002
Australia
T: +61 3 9249 9400
F: +61 3 9249 9499

TOWNSVILLE

12 Cannan Street
South Townsville QLD 4810
Australia
T: +61 7 4722 8000
F: +61 7 4722 8001

NELSON

6/A Cambridge Street
Richmond, Nelson 7020
New Zealand
T: +64 274 898 628

DARWIN

Unit 5, 21 Parap Road
Parap NT 0820
Australia
T: +61 8 8998 0100
F: +61 8 9370 0101

NEWCASTLE

10 Kings Road
New Lambton NSW 2305
Australia
T: +61 2 4037 3200
F: +61 2 4037 3201

WOLLONGONG

Level 1, The Central Building
UoW Innovation Campus
North Wollongong NSW 2500
Australia
T: +61 404 939 922

GOLD COAST

Level 2, 194 Varsity Parade
Varsity Lakes QLD 4227
Australia
M: +61 438 763 516

PERTH

Ground Floor, 503 Murray Street
Perth WA 6000
Australia
T: +61 8 9422 5900
F: +61 8 9422 5901
