



Construction Traffic Management Plan (CTMP)

200 Aldington Road, Kemps Creek, NSW – Industrial Estate

Revision Record








Issue No.	Author	Reviewed/Approved	Description	Date
1.	Danny White 20 Years TCT0017873		Rev 01	31/07/22
2.	Danny White 20 Years TCT0017873		Rev 02	1/08/22
3.	Danny White 20 Years TCT0017873		Rev 03	3/08/22
4.	Christopher Joleski - Statewide Roads and Traffic Pty Ltd (SRT) TCT0013932 Experience: 9 years		Rev 04	11/5/23
5.	Christopher Joleski - Statewide Roads and Traffic Pty Ltd (SRT) TCT0013932 Experience: 9 years		Rev 05	26/04/24
6.	Danny White 20 Years TCT0017873		Rev 06	18/01/24
7.	Danny White 20 Years TCT0017873		Rev 07	21/02/24
8.	Danny White 20 Years TCT0017873		Rev 08	26/07/24
9.	Danny White 20 Years TCT0017873		Rev 09	25/03/25

TABLE OF CONTENTS

<i>Revision Record</i>	<i>1</i>
1. INTRODUCTION	4
1.1 Executive Summary	4
1.2 Background.....	4
1.3 Site Location	5
1.4 Scope	6
1.5 Objective of this Plan.....	6
1.6 Guideline & Design Standards – Reference Documents	6
2. ROLES AND RESPONSABILITIES.....	10
2.1 Roles.....	10
2.2 Responsibilities.....	11
3. EXISTING TRANSPORT INFRASTRUCTURE.....	12
3.1 The Road Network.....	12
3.2 Existing Traffic Controls.....	12
3.3 Risk Assessment.....	13
3.4 Public Transport.....	13
3.5 Pedestrian Infrastructure	13
3.6 Cyclist Infrastructure.....	13
4. CONSTRUCTION METHODOLOGY.....	13
4.1 Duration of works and Daily / Weekly schedule	13
4.2 Staging	14
4.3 Earthworks & Construction Vehicle Traffic Generation	15
4.4 Heavy Construction Vehicles.....	16
5. TRAFFIC MANAGEMENT STRATEGY.....	18
5.1 Traffic Management.....	18
5.2 Vehicle Management.....	18
5.3 Temporary Road Closure	18
5.4 Working on Footpaths	18
5.5 Pedestrian & Cyclist Management.....	18
5.6 Emergency Services.....	19

5.7 ROL's & SZA's.....	19
5.8 Road Barriers.....	19
5.9 Line Marking.....	19
5.10 Lighting	19
6. INSPECTION, AUDITING AND REPORTING.....	19
6.1 Inspections & Audits.....	19
6.2 Monitoring Effectiveness	20
6.3 Contingency Planning.....	20
6.4 TMP Up-dates & Amendments.....	21
6.5 Reporting.....	21
7. CONSULTATION AND COMMUNICATION.....	21
7.1 Site Contact Details	21
7.2 Complaints Management	22
7.3 VMS.....	22
7.4 Neighboring Construction Developments.....	22
7.5 Mamre Road Precinct Working Group.....	24
7.6 Cumulative Impact of Construction.....	25
7.7 Minimise Traffic Impacts on the surrounding Network.....	26
APPENDIX A.....	27
APPENDIX B.....	29
APPENDIX C.....	31
APPENDIX D.....	33
APPENDIX E.....	34
APPENDIX F.....	36

1. INTRODUCTION

This report has been prepared by a consultant who holds a SafeWork NSW Work Health and Safety Traffic Control Work Card, accredited for the 'prepare a Work Zone Traffic Management Plan' Details of the accredited Consultant Is Provided Below:

Danny White Ticket Number. TCT0017873 Experience: 20 Years

This Construction Traffic Management Plan has been prepared to meet the requirements outlined in Part D stage 1 development specific environmental conditions: D1,D2,D.3 & E1

1.1 Executive Summary

Construction Consent provides for the creation of the Construction Traffic Management Plan (CTMP) for the works at 200 Aldington Road, Kemps Creek.

The works will cover the construction of the proposed new industrial estate on Aldington Road. Within this Construction Traffic Management Plan (CTMP), all relevant Conditions relating to traffic management have been addressed.

1.2 Background

200 Aldington Road, Kemps Creek, Industrial Estate SSD10479 – Development was granted consent by Dept Planning & Environment on 5 May, 2023.

White Group has been engaged by Simmons Civil, to prepare a Construction Traffic Management Plan (CTMP) to be implemented during the on-site work.

1.3 Site Location

The Lot 200 DP 1285691 site is located at 200 Aldington Road, Kemp's Creek, NSW, as shown in Figure 1-1.



[Figure 1-1: Site Location: Aldington Road](#)

1.4 [Scope](#)

The works within the site will include clearing of the land, leveling, haulage of soil both to & from the site, excavation, installation of stormwater, water and utility services, roads, driveways, car parks & footpaths.

External works associated with but not part of this Development requires upgrades to the local road network. These are currently subject to design & approval by PCC & TfNSW. This CTMP will be updated when these works commence.

1.5 [Objective of this Plan](#)

The Primary objective of this Construction Traffic Management Plan (CTMP) is to ensure safe & efficient movement of vehicles & pedestrians on to, off & around the site, whilst minimising disruptions / impacts & maintaining a safe environment for both vehicular & pedestrian traffic.

This document will:

- Ensure the project establishes and maintains best practice to manage traffic & pedestrians during all stages of work.
- Ensure a safe environment for members of the public & construction personnel is maintained at all times.
- Ensure compliance with relevant specifications and the RMS's - "Traffic Control at Work Sites" (TCAWS V-6.1) Manual.
- Deliver a high standard of community engagement and awareness during the works.

1.6 [Guideline & Design Standards – Reference Documents](#)

The Construction Traffic Management Plan (CTMP) has been developed in accordance with the requirements of Transport for NSW (RMS) Traffic Control at Works Sites Manual (Version 6.1, issued February 2022) and are referenced in this report:

- NSW Roads and Maritime Services Traffic Control at Worksites Manual V6.1.
- AS1742.3 Manual of Uniform Traffic Control Devices: Works on Roads & in accordance with the relevant legislation, codes of practice or other requirements
- SSD 10479 conditions of consent D1 and E1.

The following tables cross reference where the conditions D1 and E1 are addressed within this document.

Table 1.1 Conditions of Approval D1 Requirements

Condition Reference	Consent condition	Where addressed
Construction Traffic Management Plan		
D1	Prior to the commencement of construction of the development, the Applicant must prepare a Construction Traffic Management Plan for the development to the satisfaction of the Planning Secretary. The plan must form part of the CEMP required by condition E2 and must:	This CTMP which forms Appendix A of CEMP
(a)	be prepared by a suitably qualified and experienced person(s);	Section 1
(b)	be prepared in consultation with Council and TfNSW;	Appendix F
(c)	detail the measures that are to be implemented to ensure road safety and network efficiency during construction for both on-site and external road upgrade and construction works to:	Section 4 and 5
(i)	ensure access to the site and road safety and network	Section 4 / Appendix A
(ii)	manage cumulative construction traffic from other concurrent construction works within the Mamre Road Precinct, and	Section 6.2 and 7.3
(iii)	address necessary interim traffic safety controls and management measures, including consideration of any traffic control measures required to manage traffic entering Mamre Road in the period before Mamre Road/Abbotts Road intersection construction is complete;	Appendix A1.2
(d)	detail heavy vehicle routes, access and parking arrangements;	Section 4.3
(e)	include a Driver Code of Conduct to: (i) minimise the impacts of earthworks and construction on the local and regional road network; (ii) minimise conflicts with other road users; (iii) minimise road traffic noise; and	(iv) ensure truck drivers use specified routes, including entering and exiting Mamre Road via

Abbotts Road and not Bakers Lane;

Appendix E

(f) include a program to monitor the effectiveness of these measures; and

Section 6

-
- | | | |
|-----|--|-----------------------|
| (g) | if necessary, detail procedures for notifying residents and the community (including local schools), of any potential disruptions to routes. | Section 7 / and CCCHS |
|-----|--|-----------------------|
-

Table 1.2 Conditions of Approval E1 Requirements

Condition Reference	Consent condition	Where addressed
Management Plan Requirements		
E1	Management plans required under this consent must be prepared in accordance with relevant guidelines, and include:	
(a)	detailed baseline data;	Traffic counts /speed data has been gathered. Not appropriate for inclusion in CTMP
(b)	details of: (i) the relevant statutory requirements (including any relevant approval, licence or lease conditions); (ii) any relevant limits or performance measures and criteria; and (iii) the specific performance indicators that are proposed to be used to judge the performance of, or guide the implementation of, the development or any management measures;	Section 1.6
(c)	a description of the measures to be implemented to comply with the relevant statutory requirements, limits, or performance measures and criteria;	Section 4.3 and 5
(d)	a program to monitor and report on the: (i) impacts and environmental performance of the Stage 1 development; and (ii) effectiveness of the management measures set out pursuant to paragraph (c) above;	Section 6
(e)	a contingency plan to manage any unpredicted impacts and their consequences and to ensure that ongoing impacts reduce to levels below relevant impact assessment criteria as quickly as possible;	Section 6 and 7
(f)	a program to investigate and implement ways to improve the environmental performance of the Stage 1 development over time;	Section 7.3
(g)	a protocol for managing and reporting any: (i) incident and any non-compliance (specifically including any exceedance of the impact assessment criteria and performance criteria); (ii) complaint; (iii) failure to comply with statutory requirements; and	Section 6 and 7 Refer CCCHS Appendix I of CEMP

(h) a protocol for periodic review of the plan.

As per CEMP review

2. ROLES AND RESPONSIBILITIES

2.1 Roles

2.1.1 Project Manager – Contractor

Name: Kirk Wilson

Mobile Phone: 0418 235 375

Email: kirk.wilson@simmonscivil.com.au

2.1.2 Project Engineer

Name: Corey Brandon

Mobile Phone: 0435462597

Email: corey.brandon@simmonscivil.com.au

2.1.3 Emergency Contact/Client Representative

Name: Richard Harris

Mobile Phone: 0408 865 947

Email: richard.harris@fifecapital.com.au

2.1.4 Traffic Control Contractor

Company: White Group

Name: Danny White

Mobile Phone: 0427 281 171

Email: whitegroupops@outlook.com

2.1.5 Principal Certifier (PCA)/Penrith Council Inspector

Name: John Skaf, Senior Engineer Major Developments

Mobile Phone: 0427 304 533

Email: john.skaf@penrith.city

2.1.6 Transport Management Centre

Phone: 02 8396 1513

Email: tmc_piu@tmc.transport.nsw.gov.au

2.2 Responsibilities

All site personnel have a responsibility to:

- Ensure a safe workplace and safe environment during works.
- Report any hazards to a supervisor immediately.
- Advise supervisory personnel immediately of any concerns.

2.2.1 Project Manager

The Project Manager has ultimate responsibility to:

- Promote at all times the company's policies, procedures and standards relating to health, safety and environmental management and ensure that they are complied with.
- Ensure sufficient resources are available to achieve the CTMP, objectives and targets and that those resources have sufficient skills to conduct the roles competently.
- Ensuring the Project achieves compliance with the CTMP.
- Providing leadership in the development and implementation of the CTMP.
- Ensure that all staff and contractors engaged to work on the Project are appropriately inducted and trained in all relevant CTMP issues and controls.
- Organise and coordinate construction activities in accordance with the CTMP.
- Ensure that staff have been trained appropriately for the tasks that they are undertaking prior to commencing work.

2.2.2 Site Supervisor

The Site Supervisor has the responsibility to:

- Support the Project Manager in providing leadership in the implementation of the CTMP.
- Conduct surveillance with the aim to identify unusual, non-conforming conditions.
- Perform investigations of construction sites and temporary traffic control schemes, prepare necessary reports, as well as maintain incident records and inspections logs.
- Ensures receipt of the relevant approvals for construction activities and traffic control.
- Ensures the relevant Supervisors and workforce are familiar with the approval conditions and requirements prior to implementation.
- Ensures the Supervisors and workforce are re-familiarised in the approval conditions and requirements at regular intervals during the period of the approvals.
- Liaises with the Traffic Control Company and crews in the planning and implementation of the required traffic management arrangements.
- Conducts regular inspections (including pre-starts) of traffic controls and where necessary instructs the rectification of deficiencies.
- Allocates plant, equipment and human resources for the works including the provision of the temporary traffic control arrangements.
- Conducts and keeps records of daily and weekly (day and night) inspections of the traffic control arrangements, assist audits and where necessary rectifies deficiencies.
- Inform and assist with the management of unplanned incidents, providing initial response to make the site safe.
- Assist with the implementation of mitigation measures to address unsafe or unusual conditions.
- Records unplanned incident details, and when traffic controls are in operation, including the installation and removal of regulatory signage.
- Stop work on any activity if it is considered to be necessary to prevent a traffic accident, or to comply with the direction of RMS, Council or Police.
- Ensure that the approved traffic control measures are established, implemented and maintained in accordance with the approved plan.

- Carrying out regular inspections and auditing (TCAWS V-6.1 Section 8.1.3) of the traffic control measures to ensure that they are effective and are being followed.
- Monitoring traffic conditions.
- Ensuring and monitoring conformance to time and period of operation.
- Maintaining current copies of the construction Traffic Management Plan, Traffic Guidance Schemes, approvals, and their controlled distribution.
- Facilitate traffic awareness and giving toolbox talks to the site personnel.
- Managing the dedicated Traffic Control Crew in the delivery of required maintenance activities, incident and emergency support, and providing support/resources during implementation.
- Updating the CTMP in response to any incidents arising from the Contractor's Works.
- Develop a strategy for the dissemination of changed traffic condition information to potentially affected stakeholders, including road users, local communities and residents.

3. EXISTING TRANSPORT INFRASTRUCTURE

3.1 The Road Network

The roads in the immediate vicinity of the site are administered by Penrith City Council & TfNSW. The characteristics of roads in the immediate vicinity of the site are shown below in Table 3-1.

Table 3-1: Surrounding Road Characteristics

Road	Speed limit	Traffic volumes	Road Authority
Aldington Road	60 kph		Council
Abbotts Road	60 kph		Council
Mamre Road	80 kph	18,500 (5 day AADT) 2022	TfNSW
Bakers Lane	60 kph (40kph school zones)		Council
Elizabeth Drive	Varies -40-80kph Under traffic control	ADT 26,516 veh/d (2021)	TfNSW

Notes: 1) 5-day AADT CfET surveys conducted in 2022-23 on Mamre Road south of Abbotts Road

2) Transport for NSW Traffic Volume Viewer

3.2 Existing Traffic Controls

Due to the high volume of construction associated with the wider aerotropolis precinct there are many construction activities that impact vehicle movements beyond the site including M12/ M7 interchange construction.

- Traffic from this development site must comply with all temporary traffic controls on the surrounding road network.

[3.3 Risk Assessment](#)

A risk assessment is aimed to identify the hazards and risks associated with the works. The purpose of this risk assessment is to determine the controls required for the protection of the road workers and road users. A risk assessment has been completed and is attached in Appendix B.

[3.4 Public Transport](#)

[3.4.1 Bus routes](#)

There are currently no bus stops or bus routes within the area affected by the works, no consultation with bus companies will be required at this time.

[3.5 Pedestrian Infrastructure](#)

The project site will have no impact on footpaths as there are currently no formed footpaths on Aldington Road, Abbotts Road or Mamre Road at this location, pedestrian management will be in place as required.

[3.6 Cyclist Infrastructure](#)

The project site will have no impact on cycle infrastructure as there are currently no shared paths on Aldington Road..

4. CONSTRUCTION METHODOLOGY

[4.1 Duration of works and Daily / Weekly schedule](#)

The construction site works for the proposed stage are expected to take 15 months and will be undertaken as per the following condition:

As per Consent D48 Hours of Work

- Construction works between:
Monday to Friday 7:00am to 6:00pm
Saturday 8:00am to 1:00pm
No work to be undertaken on Sunday or public Holiday's.

[4.1.1 Construction Traffic management plan compliance](#)

In compliance with TfNSW & Penrith City Council conditions, across the duration of the project the Contractor and all subcontractors and employees will obey any direction or notice from the Road Controlling Authority.

4.2 Staging

4.2.1 Stage 1: Bulk Earthworks

Description of Key Activities	Bulk Earthworks
Duration	15 months
Max. Vehicle Size	20m Articulated Vehicle
Maximum Vehicle Movement Frequency	Approximately 60 light vehicle movements / day Approximately 240 heavy vehicle movements / day
Truck Access Requirements	All heavy vehicles shall access via the Site Primary access on Aldington Road via Abbots Road
Vehicle access / egress in a forward direction	Yes
Out of Hours Deliveries	Yes if in accordance with condition D49
Contractor Parking	Yes – All parking internal
Pedestrian Control Fencing	Pedestrian Control Fencing to the perimeter of the Site with 1.8 m man proof on property boundary
Public Transport Services Affected	No
Road Occupancy Requirements	No
Lane or Footpath Closures	No
Traffic Guidance Scheme	Refer Appendix A

4.2.2 Warehouse Works - Lot F and Lot J

Description of Key Activities	Warehouse construction work (Structure, fit out, landscaping)
Max. Vehicle Size	20m Articulated Vehicle
Vehicle Movement Frequency	Approximately 140 light vehicle movements / day Approximately 360 heavy vehicle movements / day
Truck Access Requirements	All vehicles shall access via the Site

	Primary access on Aldington Road via Abbotts Road
Vehicle access / egress in a forward direction	Yes
Out of Hours Deliveries	No
Contractor Parking	Yes – All parking internal
Pedestrian Control Fencing	Pedestrian Control Fencing to the perimeter of the Site with 1.8 m man proof on property boundary
Public Transport Services Affected	No
Road Occupancy Requirements	No
Lane or Footpath Closures	No
Traffic Guidance Scheme	Refer Appendix A

4.3 Earthworks & Construction Vehicle Traffic Generation

The anticipated vehicle movements generated by the earthworks and construction work have been estimated having consideration of the likely requirements for construction staff, plant, equipment, and haulage. The anticipated earthworks and construction schedule have been provided by the contractor, with the estimated network peak traffic volumes as follows:

Table 4-1: Traffic volumes

Stage	Times per day	Traffic volumes
Earthworks	7am to 6pm Minimise heavy traffic movements during peak times of 7-9am & 4-6pm.	60 light vehicle movements per day 240 Heavy vehicle movements per day
Warehouses Lot F / Lot J	7am to 6pm Minimise heavy traffic movements during peak times of 7-9am & 4-6pm.	140 light vehicle movements per day 360 heavy vehicles movements per day
Combined Volume		200 light vehicle movements per day 600 heavy vehicle movements per day

4.4 Heavy Construction Vehicles

4.4.1 Heavy Construction Vehicle Routes

Heavy construction vehicles travelling to site will travel from the M4 Motorway or Lenore Drive, south along Mamre Road for approx. 9km left onto Abbots Road, continue along Abbots Road, turning left onto Aldington Road & continue to the work site turning right & entering the work site at the marked site entry point.

Heavy Construction vehicles leaving 200A development site will turn left onto Aldington Road & then right onto Abbots Road, continue to Mamre Road & turn left only, continue to Elizabeth Drive roundabout to either head towards the M7 Motorway or any other direction.

No heavy construction traffic is permitted to use Bakers Lane to enter or exit the site.

No u turns are permitted

A sign is to be installed at the site access to remind drivers when they exit the Site the following key rules.

- The construction access shall be restricted to left-in-left-out.
- No right turns are allowed when leaving the Site or at Mamre Road.
- No U-turns are allowed on Mamre road or side roads


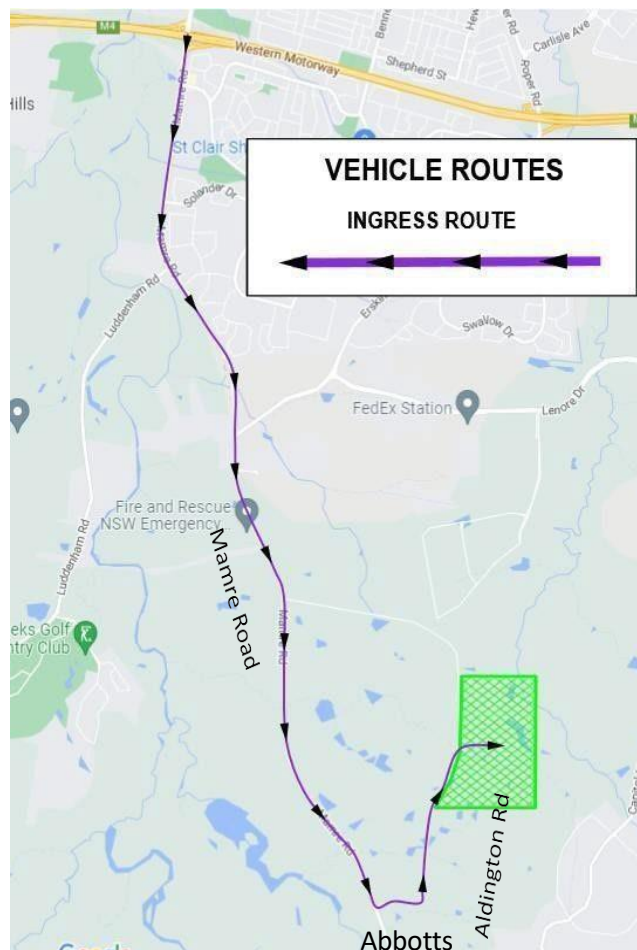


Figure 4-1: Construction Ingress

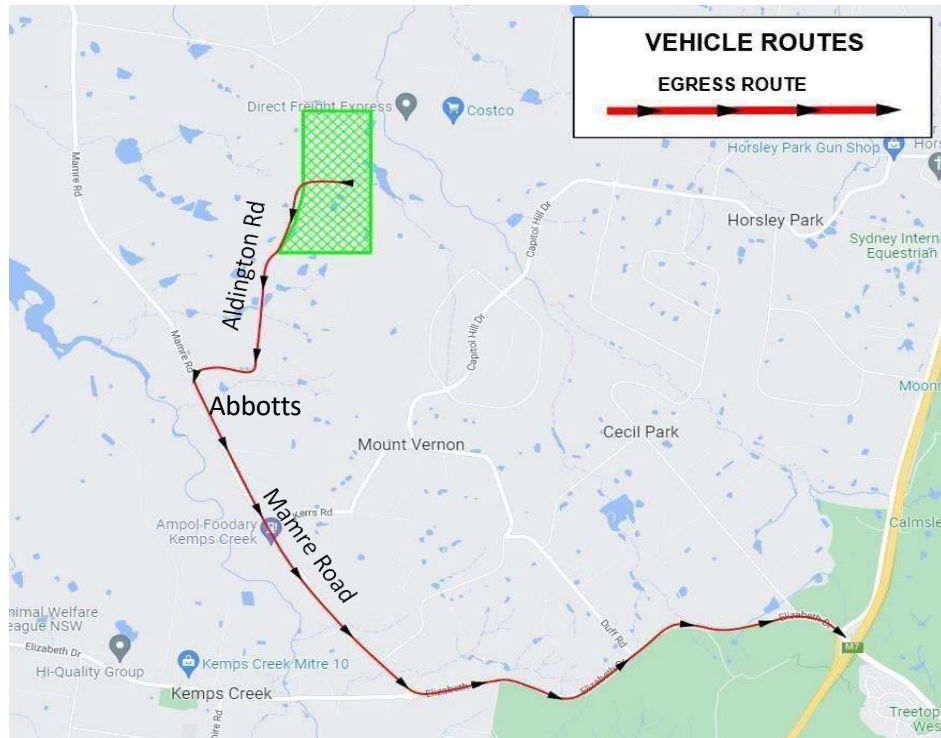

[Figure 4-2: Construction egress](#)

[4.4.2 Contractor & Heavy vehicle Parking](#)

Contractors will likely drive since there is no easily accessible public transport in close proximity to the Site. All construction work vehicles as well as staff & visitors will be parked on-site only. Suitable pedestrian connectivity shall be maintained between the work areas and this contractor parking at all times.

A dedicated area for the parking of contractors and heavy vehicles shall be developed and updated as the project progresses. The number of parking spaces provided within the Site throughout the construction will change as construction progresses, which will likely increase as construction progresses.

During each iteration of car parking location, there shall be enough parking to accommodate the expected maximum for that stage. Parking will be regularly monitored to ensure that there is no queuing on the roadway.

[4.4.3 Materials on Site](#)

All construction materials are to be stored in the designated storage areas.

[4.4.4 Materials on Road Reserve](#)

No building materials, work sheds, vehicles, machines or the like shall be allowed to remain in the road reserve area unless they are behind authorized traffic barriers.

[4.4.5 Mud & Sediment Control](#)

Two shakers and a compacted rock haul road are to be provided at the lead in to the wheel wash at site egress point to remove mud from vehicle tyres before allowing them to enter the public road, if sediment is trafficked onto the road, a street sweeper and watercart will

be used. A street sweeper is to be operating whenever heavy vehicles are leaving site. The wheel wash water is to be replaced 2-3 times per week when in use, less frequently if not in use, to ensure effective operation.

5. TRAFFIC MANAGEMENT STRATEGY

5.1 Traffic Management

The traffic management strategy prioritises :

The free flowing, unimpeded movement of vehicles past the worksite.

Safe traffic movements for heavy vehicles via Abbots Road off Mamre Road

5.1.1 Continuous Flow of Traffic

Trucks and the like will be brought onto the site at the designated entry points and routes for safety and to avoid interruptions to the traffic flow on Aldington Road, Abbots Road and Mamre Road.

5.1.2 Stop / Slow Control Measures

Stop/Slow traffic control measures will not be required.

5.2 Vehicle Management

In accordance with TfNSW requirements and the Conditions of Consent, all drivers are to be familiar with the Driver Code of Conduct before attending the Site. A copy of the Code is included in Appendix E.

All vehicles transporting loose materials will have the entire load covered and/or secured to prevent any large items, excess dust or dirt particles depositing onto the roadway during travel to and from the site. Public roads used by construction vehicles are to be kept clean at all times. All vehicles enter and exit the site in a forward direction.

All subcontractors must be inducted by the lead contractor to ensure that the procedures are met for all vehicles entering and exiting the construction site. The lead contractors will monitor the roads leading to and from the site and take all necessary steps to ensure compliance with consent conditions.

Vehicle movements to, from and within the site shall do so in a manner which does not create unreasonable or unnecessary noise or vibration. No tracked vehicles will be permitted on any paved roads. Public roads, access points and internal parking areas will not be obstructed by any materials, unapproved vehicles, refuse skips or the like, under any circumstances. At no time shall heavy vehicles and bins associated with the development park on local roads or footpaths in the vicinity of the Site.

5.3 Temporary Road Closure

There will not be a requirement for any road closures.

5.4 Working on Footpaths

There are no footpaths at this location.

5.5 Pedestrian & Cyclist Management

During the construction works there are not anticipated to be any notable movement of pedestrian and cyclists on the verge & road reserve, this is to be monitored if this changes during the course of the works, to maintain a safe area for these movements.

5.6 [Emergency Services](#)

Access must be available at all times for emergency services to adjacent properties & to the site itself. No access will be impeded by the works at this location.

5.7 [ROL's & SZA's](#)

TfNSW Road Occupancy Licences (ROL) & Speed Zones (SZA) are to be obtained prior to the commencement of any works that will affect traffic movements on TfNSW roads, they are to be activated as per TfNSW requirements & deactivated at the end of each shift.

5.8 [Road Barriers](#)

Road barriers ranging from Concrete Jersey Barriers to water filled barriers may be used on this project.

5.9 [Line Marking](#)

N/A.

5.10 [Lighting](#)

N/A.

6. INSPECTION, AUDITING AND REPORTING

6.1 [Inspections & Audits](#)

Daily site checks of signs and devices to be undertaken prior to work commencing.

The specific requirements for safety inspection and audits will meet with the requirements of the Traffic Control at Worksite Manual V6.1, Traffic audits will be undertaken after every major traffic change.

Inspection of traffic control devices for short term traffic management will be completed on weekly basis by a site supervisor with 2 years or more experience with work carried out on, in or adjacent to a road, railway, shipping lane or other traffic corridor that is used by traffic other than pedestrians.

Reporting will be in a format provided in the Traffic Control at Worksite Manual.

Site Records

Record heavy traffic entering the site including truck and trailer numberplates.

Tally daily truck numbers to site

Report monthly to ER the daily traffic numbers (for inclusion in monthly ER report)

Intersection Movement

A fixed camera and video have been located since late April at the intersection of Mamre/ Abbots recording number plates and traffic movements. This camera is used to estimate traffic volumes at the intersection and can be interrogated to determine movement patterns.

Periodic audits of vehicle movements at the Mamre/Abbots Road intersection are made to determine if truck movements are consistent with the CTMP. When inconsistent movements are identified the following checks are made:

Check vehicle company name, as indicator of site attending.

Check the daily site activities to see if the vehicle could be from SSDA site ie. if concrete truck is there any concrete works on site.

Check if plate matches site recorded plate. Take action - ban truck from site.

If not from this site refer details to other developers within precinct with SSDA traffic controls (incl. ESR Westlink or Mamre Road developers if u turns). If vehicle clearly from BAPS construction site no action taken as this DA has no conditions restricting movements.

6.2 [Monitoring Effectiveness](#)

This CTMP shall be subject to regular review and will be updated accordingly. Regular reviews will be undertaken by the on-site coordinator during implementation and execution of this CTMP. Monitoring of this CTMP shall also be picked up in the Environmental checklists, with any incidents being reported within the weekly site meeting.

All and any reviews undertaken should be documented, however key considerations regarding the review of the CTMP shall be:

To ensure the implementation of the CTMP and TGS's are consistent with the intent of this report, and that the most recent version of the CTMP and TGS (as approved by the Planning Secretary) is being implemented.

Tracking deliveries against the volumes outlined within report. Deliveries will be tracked against approved volumes and will keep a vehicle log - including Rego & time of entry - for the purpose of assessing the effectiveness of these monitoring programs.

It is expected the contractor will undertake a truck and car count/review to ensure volumes are within expected volumes, and will be undertaken once a month. In addition, the Contractor is required to retain a log of all vehicles accessing the Site on a daily basis.

To identify any shortfalls and develop an updated action plan to address issues that may arise during construction (Parking and access issues)

Regular checks to ensure all loads are entering and leaving site covered as outlined within this CTMP.

Furthermore, the monitoring and effectiveness of the Construction Traffic Management Plan (CTMP) are being implemented through a comprehensive review process that includes the following key activities:

- **Camera Reviews:** We conduct regular reviews of camera footage to monitor traffic movements and ensure compliance with the CTMP. This allows us to identify any breaches or potential issues in real-time.
- **Truck Movement Audits:** Audits of truck movements are conducted to ensure that all vehicles adhere to the designated routes and comply with site-specific requirements. These audits help in maintaining a high level of compliance and identifying any deviations from the plan.
- **Site Inspections:** Regular site inspections are carried out to verify that all aspects of the CTMP are being followed on the ground. These inspections provide an additional layer of oversight and ensure that any issues are promptly addressed.

6.3 [Contingency Planning](#)

In the event of a breach of conditions, we take the following immediate actions:

An immediate notice is issued to the driver and the company responsible for the breach. This ensures that the responsible parties are promptly informed of the violation.

As stated in the Driver's Code of Conduct (see Appendix E), the vehicle involved in the breach is banned from the site effective from the date of the notice. This measure is taken to prevent any further violations and to maintain strict adherence to the CTMP.

An updated list of banned vehicles is provided to all stakeholders and the site manager as a notice. This list ensures that all relevant parties are aware of the banned vehicles and can enforce the ban effectively.

6.4 TMP Up-dates & Amendments

Update of this plan will occur as necessary and reasons for update of the plan may include the following,

- Consideration of monitoring, inspection and audit results.
- Consideration of incidents and any lessons learnt.
- Consideration of any new regulatory issues.
 - A review of the effectiveness of traffic management controls.
 - Consideration of changes in operational needs such as resourcing.
 - Feedback from management reviews.
- At the request of the principal or their representative.
- Commencement of construction by additional developers on Aldington or Abbots Road or Mamre / Abbots Road /Aldington Road upgrade.

A copy of the updated plan and changes will be distributed to all relevant stakeholders in accordance with the approved document control procedure.

6.5 Reporting

Reporting of movements are to be undertaken to ensure that drivers are adhering to restricted times, Code of Conduct, and to ensure that the approved traffic volumes are in line with those approved.

To inspect, review and audit the traffic management plan (TMP) arrangements implemented on site, the following actions are to be undertaken during all phases of construction, being:

Activity		Frequency or Details
Shift Inspections	☐ Yes ☐ No	
Regular Inspections	☐ Yes ☐ No	
TMP Review	☐ Yes ☐ No	
Road Safety Audit	☐ Yes ☐ No	
Other	☐ Yes ☐ No	
Comments		

7. CONSULTATION AND COMMUNICATION

Consultation will be in accordance with the CCCHS

For businesses & residences impacted by the works, that may use Abbots and Aldington Road, a letterbox drop or email providing details of the works and the timing will be provided in advance of any significant changes to traffic conditions.

7.1 Site Contact Details

The site shall be clearly posted with a sign erected in a prominent position on the site perimeter, it

is to be maintained & removed at the completion of works. The sign must contain the following information,

Name, address, contractor licence number and telephone number of the *principal contractor*, including a telephone number at which the person may be contacted outside working hours, or *owner-builder* permit details.

Name, address and telephone number of the *Principal Certifying Authority*

A statement stating that ‘unauthorised entry to the work site is prohibited’.

A notice with contact names and mobile phone numbers of site supervisors be displayed at the entrance to the site for community to make contacts regarding work activities.



7.2 Complaints Management

Complaints will be managed in accordance with the Community consultation and complaints handling strategy (CCCHS) within the CEMP. Complaints are one measure to be used to determine the effectiveness of management methods.

7.3 VMS

Variable message signs may be used to notify motorists of the changed traffic conditions both prior & during works at this location.

7.4 Neighboring Construction Developments

The Site is located in the broader Mamre Road Precinct. Currently, the broader construction activities identified being undertaken within the vicinity of the Site include:

- BAPS Temple – located at 230-242 Aldington Road
- ESR Australia (ESR) – the Westlink Estate located at 290-308 Aldington Road, 59-62 and 63 Abbots Road
- Mirvac Projects Pty Ltd (Mircvac) – Aspect Industrial Estate, 788-882 Mamre Road
- Yiribana Logistic Estate (GPT) – Located at 754-786 Mamre Road
- Frasers Property Industrial (Frasers) and Altis Property Partners (Altis) – the Kemps Creek Logistics Hub at 657-769 Mamre Road

The construction activities in the vicinity of the Site are shown in Figure 7.4.

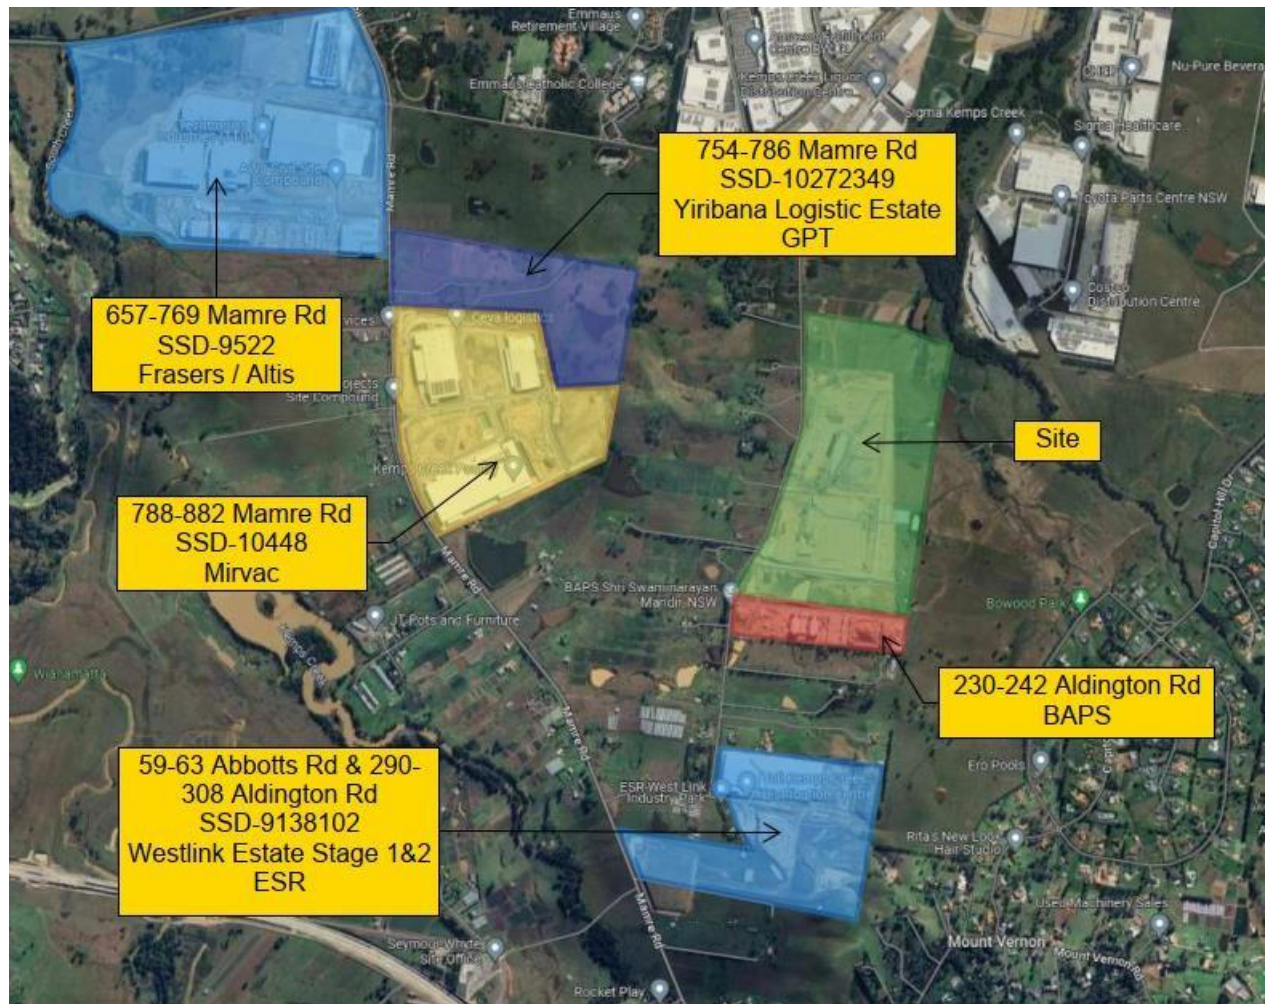


Figure 7.4: Nearby Construction Sites

7.5 Mamre Road Precinct Working Group


For the duration of construction works for each stage of development under the Concept Proposal, and until all components of the development are operational, the Applicant will participate in the Mamre Road Precinct Working Group with relevant consent holders in the MRP to the satisfaction of the Planning Secretary.

The purpose of the working group is to consult and coordinate construction works within the MRP to assist with managing and mitigating potential cumulative environmental impacts.

The details of the working group are addressed in the Community Consultation and Complaints Handling Strategy (CCCHS) in the project CEMP.

All Developers from the MRP Working group with sites accessed off Abbots Road or Aldington Road must abide by the CTMP once approved by the relevant Road Controlling Authorities (TfNSW and PCC) and the Secretary of the Department of Planning.

Heavy construction traffic must only enter from Abbots Road and exit through Abbots Road via a left in left out control until Abbots / Mamre traffic signals are operational. No construction traffic relating to any Working Group members who are associated with said location can alter or make change to the conditions within this CTMP without amendment to this CTMP.

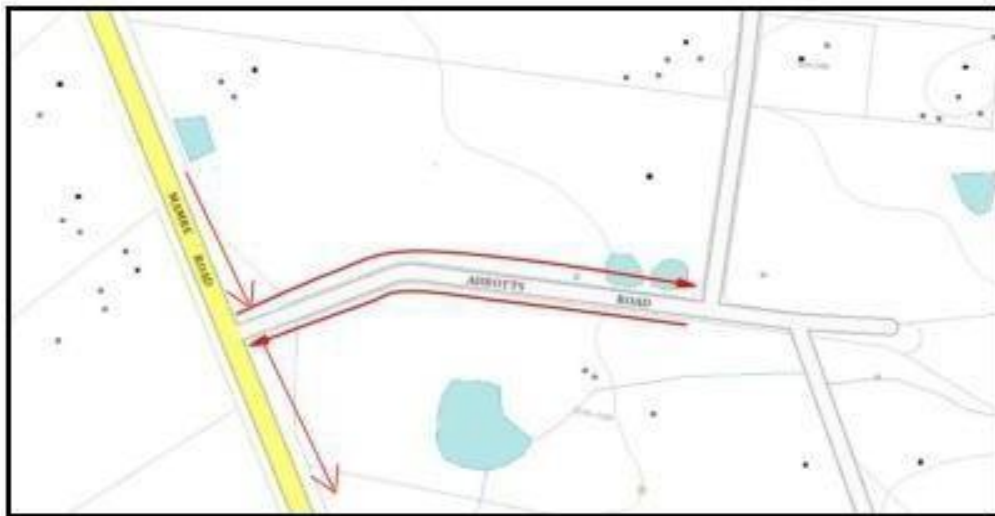

[Figure 7.5 Left in left out](#)

Any additional traffic control measures or changed to this CTMP document applicable during works will be determined and finalised based the stage of development construction traffic movements and with each group member and based on consultation with all developers involved.

7.6 Cumulative Impact of Construction

The current (July 2024) status of developments in the eastern section of the Mamre Road Precinct is shown in Table 7.6, below. With the exception of the BAPS temple site (subject to a DA and no traffic control/restrictions) these developers must abide by the CTMP control of heavy vehicles left in left out at the Mamre/Abbotts Road Intersection.

The developers subject to SSDAs are required by the SSDA conditions of consent to be part of the MRP Working Group:

Table 7.6 Current Status of Developments on Aldington Road

Developer	Development approval type	Contact	Location if not commenced	Anticipated cumulative impact / activity type / Status July – December 2024
ESR	SSDA	Grace MacDonald		Building Construction, majority of materials on site, limited heavy vehicle movements
Dexus	SSDA – not approved	Jacob Clark	West of 200 Aldington approx. 30ha	No activity
Frasers Property	SSDA – not approved	Michaela Leerdam	West of 200 Aldington (approx. 70ha)	No activity
Stockland and Fife Land 3 Pty	DA – not approved	Richard Harris	North of 200 Aldington (13 ha)	Bulk earthworks – import related heavy vehicle movements
BAPS temple (DA) PM Vertex Group	DA	David Ashcroft	Immediately south of 200 Aldington Road	Expect to complete construction Oct 2024, activity includes import of materials, concrete plus internal road construction
LOG-E	SSDA	Via PM AT&L Peter Wark	Aldington & Abbotts Road corridor	Aldington/Abbotts Road Upgrade - Commencement of this project will result in a revision to the CTMP

7.7 Minimise Traffic Impacts on the surrounding Network


To effectively minimise traffic impacts on the surrounding network, each contractor is tasked with monitoring construction vehicle volumes through manual methods or CCTV at site entrances. The principal contractor reviews these volumes regularly and alerts regulatory authorities if limits are exceeded. Construction traffic is routed through designated primary access points to manage impacts on the surrounding area, ensuring vehicles stay within approved limits. Deliveries are managed to prevent exceeding approved vehicle limits, and safety for motorists and pedestrians is ensured through Traffic Guidance Schemes (TGSs) that are updated throughout the project. Reporting and monitoring during peak periods help maintain adherence to restricted times and approved traffic generation. Coordination with stakeholders is maintained through regular working group meetings, ensuring all parties are informed and that any issues are addressed collaboratively.

- Each contractor uses manual methods or CCTV to monitor vehicle volumes at site entrances; the principal contractor reviews these volumes and notifies authorities if limits are exceeded.
- Traffic uses designated primary access points and is kept within prescribed volumes to minimise impacts on motorists.
- The contractor ensures that construction vehicles, particularly heavy ones, do not exceed approved limits.
- Traffic Guidance Schemes (TGSs) are prepared and updated to identify and manage hazards, ensuring safety for motorists and pedestrians.
- Movements during peak periods are monitored to ensure compliance with restricted times and approved traffic generation limits.
- Regular working group meetings and ongoing communication ensure effective traffic impact mitigation and collaborative problem-solving.


APPENDIX A

Traffic Control Plans

A 1.1 – Long Term Signage & Vehicle Movements on Adlington Road

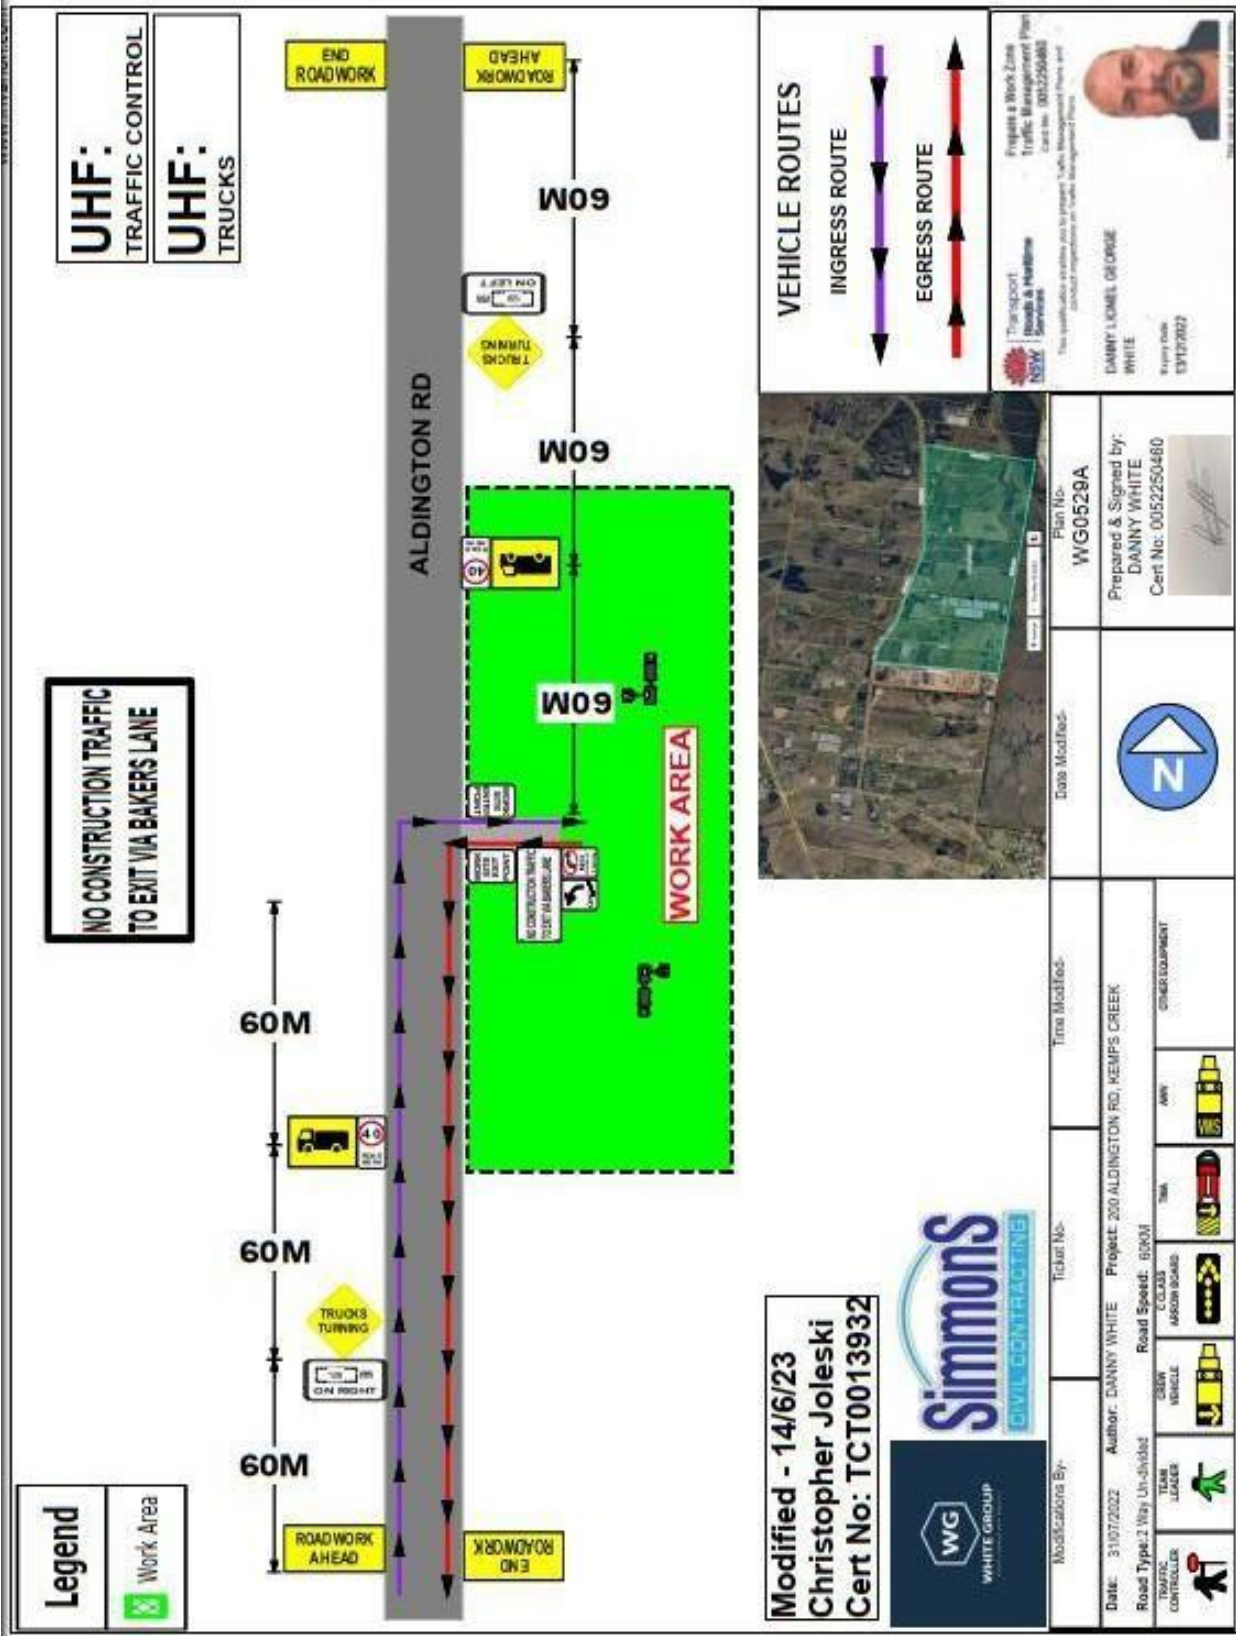

A 1.2 – Mamre Road

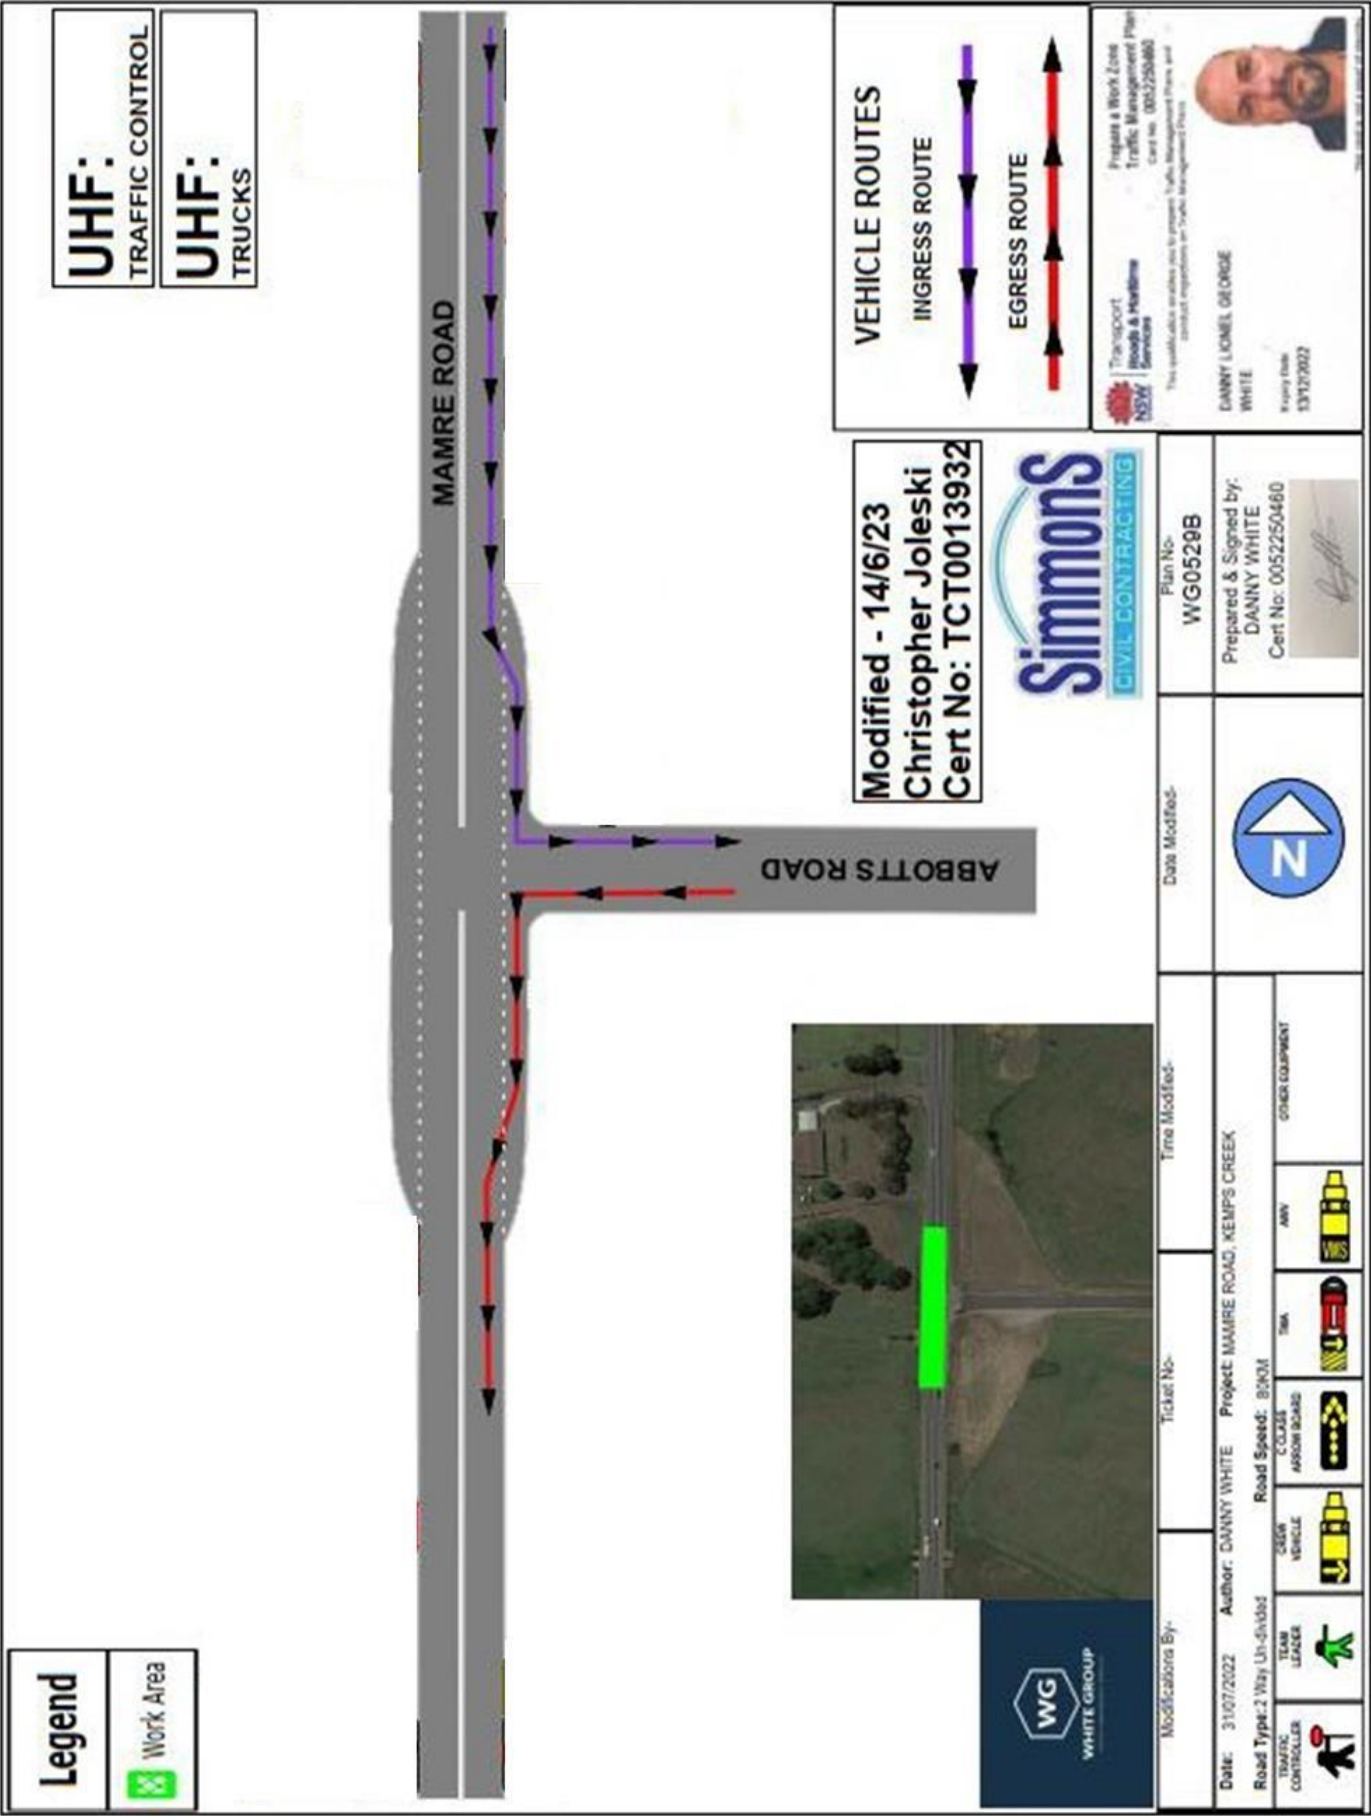

APPENDIX B

B 1.1 – RISK ASSESSMENT

No	Risks	Rate	Potential consequences	Evaluate	Proposed risk treatment
1	Work vehicles, truck & dog, moving in & out of site	3 H	Traffic accidents, unfamiliarity with area	1 L	• Provide Driver Code of Conduct • Site will require appropriate signs, all drivers to be given written directions on entry & exit procedures. • UHF communication with traffic marshal on approach to site
2	Access to site for receiving deliveries	2 M	Traffic disruption or interference, Incidents due to unfamiliarity within site	1 L	• Provide Driver Code of Conduct • Regular check of Traffic Management Plan implementation. • Limit deliveries during peak times. • Have a procedure in place for rapid recovery.
3	Working in close proximity to Intersections	2 M	Traffic delays, work vehicles pulling out of site, queuing.	1 L	• Vehicles leaving site to be aware of traffic flow & conditions. • Limit vehicle movements at peak times.
4	Pedestrian access	2 M	Potential disruption to progress causing pedestrians to not comply with pedestrian provisions.	1 L	• Ensure pedestrian access provisions are adequately addressed, well established and maintained.
5	Cyclist access	2 M	Potential disruption to progress causing cyclists to not comply with cyclist provisions.	1 L	• Ensure cyclist access provisions are adequately addressed, well established and maintained.
6	Noise pollution	1 L	Noise affecting residents & community.	1 L	• Limit noise near residential areas where possible. • Vehicles are not to use compression braking when entering site.
7	Access for emergency services restricted	2 M	Emergency vehicles & personnel unable to attend to an emergency situation.	1 L	• Make emergency services in the local area aware of the works & provide them with a copy of the Construction Traffic Management Plan (CTMP)
8	Air Quality		Dust affecting Residents		• Wheel wash • Water cart and street sweeping as necessary
9	Poor condition of Road		Generate dust and traffic hazards		• Repair and maintain potholes

B 1.2 – RISK ASSESSMENT MATRIX

Step 1: Determine Likelihood What is the possibility that the effect will occur?		Step 2: Determine Consequence What will be the expected effect?	
	Criteria	Level of Effect:	Example of each level:
Almost certain	Expected in most circumstances.	Insignificant/Acceptable	No effect – or so minor that effect is acceptable
Likely	Will probably occur in most circumstances	Minor	First Aid treatment only; no lost time injury
Possible	Might occur at some time	Moderate	Medical treatment; serious injuries, temporary partial disability; lost time injury < 7 days
Unlikely	Could occur at some time	Major	Hospital admittance; extensive injuries; lost time injury > 7 days; Permanent Total Disability injury; death
Rare	May occur only in exceptional circumstances	Catastrophic	Permanent Total Disability, Loss of life

Step 3 Determine the risk score		Step 4 Record risk score on worksheet (Note – Risk scores have no absolute value and should only be used for comparison and to engender discussion.)	
Consequence Likelihood		Score	Action
Almost certain	3 High	4 A: Acute	DO NOT PROCEED. Requires immediate attention. Introduce further high level controls to lower the risk level. Re-assess before proceeding.
Likely	2 Moderate	3 H: High	Review before commencing work. Introduce new controls and/or maintain high level controls to lower the risk level. Monitor frequently to ensure control measures are working.
Possible	1 Low	2 M: Moderate	Maintain control measures. Proceed with work. Monitor and review regularly, and if any equipment/people/materials/work processes or procedures change.
Unlikely	1 Low	1 L: Low	Record and monitor. Proceed with work. Review regularly, and if any equipment/people/materials/work processes or procedures change.

APPENDIX C

C 1.1 – SITE PHOTOS

Aldington Road – Northbound



Aldington Road – Southbound



Mamre Road & Abbotts Road – Intersection



Site Access Locations



APPENDIX E

Drivers Code of Conduct

Safe Driving Policy for the construction site of 200 Aldington Road, Kemps Creek.

Objectives of the Drivers Code of conduct

- Minimise the impact of earthworks and construction on the local and regional road network.
- Minimise conflict with other road users.
- Minimise road traffic noise; and
- Ensure truck drivers use specified routes.

Code of Conduct

The code of conduct applies to any heavy vehicle related to activities on this site.

Drivers are to be issued with a copy of this Drivers Code of Conduct and must comply with the following:

- Not queue or park on public roads
- Follow the approved site access / departure routes
- All road rules
- Speed limits as imposed within the estate
- NOT carry out U turns on Mamre Road or any side roads off Mamre Road.

All heavy vehicles must ONLY enter and exit via Abbots Road off Mamre Road using a left in left out turn on/off Mamre Road.

Arrival Trips

If arriving from the north of the site travel southbound on Mamre Road, turn left into Abbots Road, then left onto Aldington Road then turn right into site access.

Departure trips

Turn left from site onto Aldington Road, turn right onto Abbots Road, then left onto Mamre Road.


All vehicle operators accessing the site must:

- Be aware of noise impacts to residents near site, on Mamre Road and not honk, or rev excessively.
- Obey all applicable road rules and laws at all times.
- Obey all on-site signposted speed limits and comply with any temporary traffic control measures.

Environmental Procedures

- Use wheel wash located at the site exit to remove any debris attached to vehicle wheels.
- Take precautions to ensure no dirt or debris from vehicles is tracked on to the public road network.
- Should silt observed to be tracked onto the road, advise site supervisor so remedial action can be taken

As shown Approved site access & departure routes (green access route, red departure route) below -

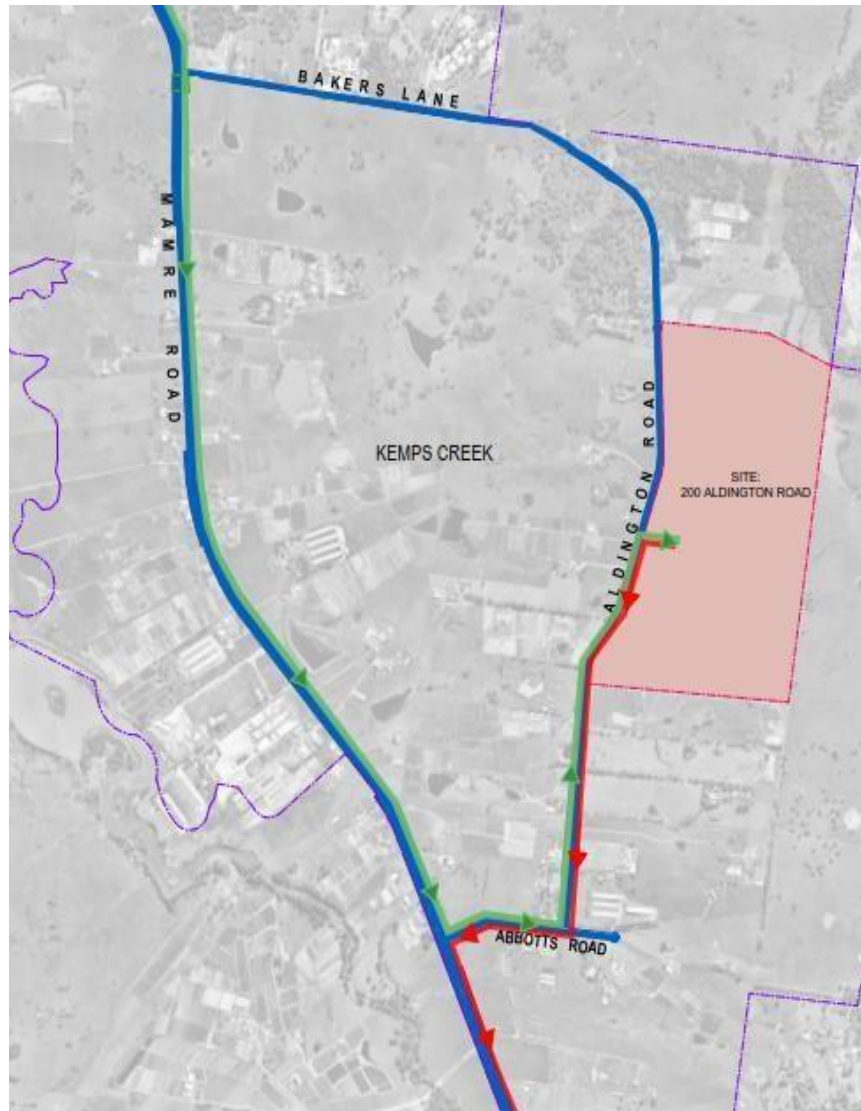

Note:

Heavy Vehicles are NOT permitted to use Bakers Lane to access or depart from the site
Heavy Vehicles are NOT permitted to turn right from Abbots Road onto Mamre Road
Heavy Vehicles are NOT permitted to turn right from Mamre Road onto Abbots Road
Heavy Vehicles are NOT permitted to complete U turns on roads off Mamre Road

Consequences of Non-Compliance with this Code of Conduct

Non compliance will result in the vehicle and driver being banned from site for the duration of the project.

Any breaches of the CTMP and Driver Code of Conduct may be considered a breach of development consent SSD-10479 and penalties such as fines and or prosecution may apply.

Enforcement action for breaching the Code of Conduct or this CTMP could include penalty notice for \$15,000 (company) and / or \$8,000 (individual). This includes haulage contractors and other subcontractors.

APPENDIX F

[Evidence of consultation](#)

Record of Consultation SSD 10479 200 Aldington Road Estate
Condition A21 Evidence of Consultation

Condition A21 Evidence of Consultation								Condition										
Date	Timing	Time	Location	Developer (initials)	Name	Details	Outcome	C13 Protect	D50 Noise	A9 Staging	D64 Dust	B1 Traffic	D89 Waste storage	D29 Trunk drainage	D27/D31 SW Mgmt	B9 Street Trees	Action	Resolution
22/05/2023	prior to commencement of construction	10:50am	53 Aldington Rd, (Lot 38) Kemps Creek (north west of site)	RH, DM	Ted and partner	Met with the Owner&occupant of 53 Ald to notify them we are starting works in the next month. Provided them with RH contact details for any enquiries.	No concerns/ No unresolved issues. Will notify if issues arise during construction		✓	✓		✓					n/a	Will notify if issues arise during construction
22/05/2023	prior to commencement of construction	11:00am	129 Aldington Road, Kemps Creek (west of site)	RH, DM	Sam J	Met with occupant and notified we will be commencing earthworks on site in the following weeks.	No concerns/ No unresolved issues. Will notify if issues arise during construction		✓	✓		✓					n/a	Will notify if issues arise during construction
22/05/2023	prior to commencement of construction	11:15am	141 Aldington Road, Kemps Creek (west of site)	RH, DM	Mr Orlovic	Met with owner, notified them of commencement of works on 200A and provided contact details.	No concerns/ No unresolved issues. Will notify if issues arise during construction		✓	✓		✓					n/a	Will notify if issues arise during construction
22/05/2023	prior to commencement of construction	11:35am	Oakdale East (to north east of site) – freight company	RH, DM	Representative	Notified representative of owner on commencement of earthworks in following weeks. RH provided contact details to man occupying front desk.	No concerns/ No unresolved issues. Will notify if issues arise during construction		✓	✓		✓					n/a	Will notify if issues arise during construction
23/05/2023 and prior	prior to commencement of construction		Lot 18 BAPS Temple (southern boundary)	RH, DM	David Ashcroft PM, Samir Patel (Owners Rep)	Met with occupant and notified we will be commencing earthworks on site in the following weeks.	No concerns/ No unresolved issues. Will notify if issues arise during construction		✓	✓		✓					n/a	Will notify if issues arise during construction
12/05/2023	In consultation with		PCC	BH	John Skaf of PCC	provided CTMP for review by email	Satisfied, provide copy on approval by TNSW and DPE					✓					Submit on approval	Satisfied, provide copy on approval by TNSW and DPE
15/05/2023 and 6/7/2023	In consultation with		TNSW	RH	TNSW	provided CTMP for review by email	Satisfied, conditions are able to be met					✓					follow conditions	satisfied
31/5/23 and prior	prior to commencement of construction		Capital Hill Estate (farmland to east of site)	RH	Capital Hill estate/WJP (engr)	Discussed by phone with David Johnstone (consultant) and Dino Selagrio (owner)	No concerns, but if any issues with dust or otherwise will advise.		✓	✓		✓					n/a	Will notify if issues arise during construction
3/01/2024	During construction		N/A	SCC	BAPS Temple (southern boundary)	Ongoing consultation with adjacent BAPS site in relation to noise, dust, traffic and erosion and sediment controls.	No concerns, but if any issues or otherwise will advise.		✓			✓			✓		submit on approval	Will notify if issues arise during construction
23/02/2024	In consultation with		TNSW	BH	TNSW	provided CTMP for review by email	Satisfied, lodge with DPE for approval.					✓					Submit on approval	satisfied
28/02/2024	In consultation with		PCC	RH	John Skaf of PCC	provided CTMP for review by email	Satisfied, lodge with DPE for approval.					✓					Submit on approval	satisfied
26/03/2024	In consultation with		TNSW	SI	TNSW	provided CTMP seeking increase in movements via email	satisfied as long as no queuing occurs					✓					Submit on approval	satisfied
2/04/2024	In consultation with		DPHI	BH	DPHI	provided CTMP for review by email	TBC					✓						
23/05/2024	In consultation with		TNSW	SI	TNSW	provided CTMP for review by email	Satisfied, lodge with ER for approval.					✓						satisfied
17/05/2024	In consultation with		PCC	SI	John Skaf of PCC	provided CTMP for review by email	Satisfied, lodge with ER for approval.					✓						satisfied
27/05/2024	In consultation with		ER	DF	Richard Peterson	provided CTMP for review by email	Satisfied, lodge with DPHI for approval.					✓						satisfied
29/05/2024	In consultation with		DPHI	DF	DPHI	provided CTMP for review by submission on portal	Under Review by DPHI					✓						satisfied
25/03/2025	In consultation with		TNSW	SI	Kylie Dasey	provided CTMP for review by email	satisfied as long as no queuing occurs					✓						satisfied
1/05/2025	In consultation with		PCC	SI	John Skaf of PCC	provided CTMP for review by email	satisfied as long as CTMP for adjacent site- 90 Aldington reduces traffic from 340 to 140. This change has been made.					✓						satisfied

From: John Skaf <John.Skaf@penrith.city>
Sent: Wednesday, 14 May 2025 2:01 PM
To: Sam Islam
Cc: richard.harris@fifecapital.com.au; Debbie Fransen
Subject: RE: 200 Aldington Road Industrial Development CTMP R9
Attachments: CTMP_R9_Updated_25_03_25.pdf; 30.04.25 CTMP - Lot 90 Aldington Rd Kemps Creek Industrial Estate (Ver 2).pdf

Hi Sam,

I reviewed the proposed changes to the CTMPs for 90 Aldington Road and 200 Aldington Road and raise no objections as there is no increase in traffic volume than what's currently approved for the two sites.

Please let me know if you have any questions.

Kind Regards,

John Skaf
Senior Engineer - Major Developments
Engineering Services

E John.Skaf@penrith.city
T +61247328085 | F | M +61427304533
PO Box 60, PENRITH NSW 2751
www.visitpenrith.com.au
www.penrithcity.nsw.gov.au



From: Sam Islam <sam.i@atl.net.au>
Sent: Thursday, 1 May 2025 11:21 AM
To: John Skaf <John.Skaf@penrith.city>
Cc: richard.harris@fifecapital.com.au; Hamish Dodson <hamish.dodson@penrith.city>; Debbie Fransen <debbie.f@atl.net.au>
Subject: RE: 200 Aldington Road Industrial Development CTMP R9

Hi John,

Please refer to the attached for approval:
200A CTMP R9 (600 Heavy Vehicle movements per day) – endorsed by TfNSW 25/03/25 (correspondence attached with CTMP). This CTMP was submitted to PCC on 25/03/25, no further changes made in the attached CTMP.
90A CPTMP R2 (decrease from 340 to 140 Heavy Vehicle movements per day). Please note CPTMP R1 has been approved by TfNSW, PCC and DPHI. We will lodge CPTMP R2 with DPHI so they're aware of the changes made.

Kind regards,

Sam Islam
Civil Engineer | Superintendent



Sydney | Melbourne | Brisbane
www.atl.net.au

Level 4 17-21 Macquarie Street
Parramatta NSW 2150

02 9068 8517
0438 657 901



Sydney Harbour, Sydney
Photo by our Civil Engineer - Ida Samadian

CIVIL ENGINEERS | PROJECT MANAGERS | WATER SERVICING COORDINATORS
INFRASTRUCTURE PLANNERS AND ADVISERS | CONSTRUCTION PHASE SERVICES

AT&L accepts no liability for the content of this email, or for the consequences of any actions taken based on the information provided unless that information is subsequently confirmed in writing. Any views or opinions presented in this email are solely those of the author and do not necessarily represent those of the company.

From: John Skaf <John.Skaf@penrith.city>
Sent: Tuesday, 29 April 2025 10:23 AM
To: Sam Islam <sam.i@atl.net.au>
Cc: richard.harris@fifecapital.com.au; Hamish Dodson <hamish.dodson@penrith.city>; Debbie Fransen <debbie.f@atl.net.au>
Subject: RE: 200 Aldington Road Industrial Development CTMP R9

Hi Sam,

Thank for the chat the other day and confirming below that Fife is happy to reduce the 90A CPTMP by 200 per day (140 per day) to allow increasing for 200A

CPTM to 600 per day. In principal Council has no objections to the proposed changes as there will be no further increase of vehicles driving along Aldington Road. Once the CTMPs are adjusted accordingly, please forward to me for review and acceptance.

Regarding the sharing of access for 200A & 90A sites, I appreciate your clarification of non-compliance with DPHI requirements. As such, please continue to comply with DPHI requirements.

Kind Regards,

John Skaf
Senior Engineer - Major Developments
Engineering Services

E John.Skaf@penrith.city
T +61247328085 | F | M +61427304533
PO Box 60, PENRITH NSW 2751
www.visitpenrith.com.au
www.penrithcity.nsw.gov.au



Follow us



From: Sam Islam <sam.i@atl.net.au>
Sent: Thursday, 24 April 2025 12:21 PM
To: John Skaf <John.Skaf@penrith.city>
Cc: richard.harris@fifecapital.com.au; Hamish Dodson <hamish.dodson@penrith.city>; Debbie Fransen <debbie.f@atl.net.au>
Subject: RE: 200 Aldington Road Industrial Development CTMP R9

Hi John,

I understand from our discussion the PCC asset management team will likely reject the revised 200A CTMP increase from 400 to 600 heavy vehicle movements per day due to the current condition of Aldington Road.

The 90A CPTMP approved by PCC allows for 340 heavy vehicle movements per day.

Fife are happy to reduce the 90A CPTMP by 200 per day (140 per day) to allow increasing 200A CPTM to 600 per day. Can you confirm with your asset team they're happy with this change? We will then issue a revised CPTMP for 90A for 140 per day for approval.

As you have proposed for 200A & 90A sites to share the total 740 heavy vehicles movements per day going into either entrance, this would be non-compliant with DPHI as 200A site cannot accept more than 400 per day as per current approved CTMP.

Thanks

Kind regards,

Sam Islam
Civil Engineer | Superintendent



Sydney | Melbourne | Brisbane
www.atl.net.au

Level 4 17-21 Macquarie Street
Parramatta NSW 2150

02 9068 8517
0438 657 901



Sydney Harbour, Sydney
Photo by our Civil Engineer - Ida Samadian

CIVIL ENGINEERS | PROJECT MANAGERS | WATER SERVICING COORDINATORS
INFRASTRUCTURE PLANNERS AND ADVISERS | CONSTRUCTION PHASE SERVICES

AT&L accepts no liability for the content of this email, or for the consequences of any actions taken based on the information provided unless that information is subsequently confirmed in writing. Any views or opinions presented in this email are solely those of the author and do not necessarily represent those of the company.

From: Sam Islam
Sent: Thursday, 24 April 2025 9:24 AM
To: john.skaf@penrith.city
Cc: richard.harris@fifecapital.com.au; Hamish Dodson <hamish.dodson@penrith.city>; Debbie Fransen <debbie.f@atl.net.au>
Subject: RE: 200 Aldington Road Industrial Development CTMP R9

Hi John,

Thanks for the discussion last week on the CTMP. Can you please confirm if you're happy with the revised CTMP R9?

We have received approval from TfNSW, and waiting for PCC before lodging the revised CTMP with DPHI for final approval.

Kind regards,

Sam Islam
Civil Engineer | Superintendent



Sydney | Melbourne | Brisbane
www.atl.net.au

Level 4 17-21 Macquarie Street
Parramatta NSW 2150

02 9068 8517
0438 657 901



Sydney Harbour, Sydney
Photo by our Civil Engineer - Ida Samadian

CIVIL ENGINEERS | PROJECT MANAGERS | WATER SERVICING COORDINATORS
INFRASTRUCTURE PLANNERS AND ADVISERS | CONSTRUCTION PHASE SERVICES

AT&L accepts no liability for the content of this email, or for the consequences of any actions taken based on the information provided unless that information is subsequently confirmed in writing. Any views or opinions presented in this email are solely those of the author and do not necessarily represent those of the company.

From: Sam Islam
Sent: Thursday, 3 April 2025 12:50 PM
To: john.skaf@penrith.city
Cc: richard.harris@fifecapital.com.au
Subject: FW: 200 Aldington Road Industrial Development CTMP R9

Hi John,

Can you please confirm acceptance of this revised CTMP for 200 Aldington Road?

The CTMP proposes to increase the heavy vehicle movements from 400 to 600 per day to cater for builder's traffic.

Thanks

Kind regards,

Sam Islam
Civil Engineer | Superintendent



Sydney | Melbourne | Brisbane
www.atl.net.au

Level 4 17-21 Macquarie Street
Parramatta NSW 2150

02 9068 8517
0438 657 901



Sydney Harbour, Sydney
Photo by our Civil Engineer - Ida Samadian

CIVIL ENGINEERS | PROJECT MANAGERS | WATER SERVICING COORDINATORS
INFRASTRUCTURE PLANNERS AND ADVISERS | CONSTRUCTION PHASE SERVICES

AT&L accepts no liability for the content of this email, or for the consequences of any actions taken based on the information provided unless that information is subsequently confirmed in writing. Any views or opinions presented in this email are solely those of the author and do not necessarily represent those of the company.

From: Sam Islam
Sent: Tuesday, 25 March 2025 11:46 AM
To: Hamish Dodson <hamish.dodson@penrith.city>
Cc: Josh Creamer <Josh.Creamer@penrith.city>; richard.harris@fifecapital.com.au; Brendan Carroll <brendan.carroll@simmonscivil.com.au>; Corey Brandon <corey.brandon@simmonscivil.com.au>; Debbie Fransen <debbie.f@atl.net.au>
Subject: 200 Aldington Road Industrial Development CTMP R9

Hi Hamish,

Fife Capital have proposed to increase the heavy vehicle movements from 400 to 600 per day in the CTMP for the 200 Aldington Road industrial development site.

Please refer to the attached revised CTMP R9 for review and endorsement by PCC in accordance with Conditions of Consent D1.

This is the change made in the CTMP from the previous revision:

Table 4-1: Traffic volumes

Stage 1	Times per day	Traffic volumes
Earthworks	7am to 6pm Minimise heavy traffic movements during peak times of 7-9am & 4-6pm.	80 light vehicle movements per day 340 Heavy vehicle movements per day
Warehouse Lot F	7am to 6pm Minimise heavy traffic movements during peak times of 7-9am & 4-6pm.	120 light vehicle movements per day 260 heavy vehicles movements per day
Combined Volume		200 light vehicle movements per day 600 heavy vehicle movements per day

Please note CTMP R8 was previously approved by TfNSW, PCC and DPHI; refer attached approval letter from DPHI.

The Contractor will ensure no queuing occurs on Addington Road due to the increase in truck movements.

Kind regards,

Sam Islam
Civil Engineer | Superintendent



Sydney | Melbourne | Brisbane
www.atl.net.au

Level 4 17-21 Macquarie Street
Parramatta NSW 2150

02 9068 8517
0438 657 901



Sydney Harbour, Sydney
Photo by our Civil Engineer - Ida Samadian

CIVIL ENGINEERS | PROJECT MANAGERS | WATER SERVICING COORDINATORS
INFRASTRUCTURE PLANNERS AND ADVISERS | CONSTRUCTION PHASE SERVICES

AT&L accepts no liability for the content of this email, or for the consequences of any actions taken based on the information provided unless that information is subsequently confirmed in writing. Any views or opinions presented in this email are solely those of the author and do not necessarily represent those of the company.

From: Kylie Dasey <Kylie.Dasey@transport.nsw.gov.au>
Sent: Tuesday, 25 March 2025 11:46 AM
To: Sam Islam
Subject: Re: 200 Aldington Road Industrial Development CPTMP R9

Hi Sam,

We have no issue with the increase of vehicle movements. Can you please ensure no queuing occurs on Addington Road due to the increase of vehicle movements.

Regards

Kylie Dasey
Network Access Interface Officer
Operations Management
Coordinator-General Division
Transport for NSW

M 0484 328 071 E kylie.dasey@transport.nsw.gov.au

Level 1
25 Garden St
Eveleigh NSW 2015

Working days Monday to Friday, 08:30am - 04:30pm



I acknowledge the Aboriginal people of the country on which I work, their traditions, culture and a shared history and identity. I also pay my respects to Elders past and present and recognise the continued connection to country.

Please consider the environment before printing this email.

OFFICIAL

OFFICIAL

From: Sam Islam <sam.i@atl.net.au>
Sent: Tuesday, 25 March 2025 11:40 AM
To: Development CTMP CJP <development.CTMP.CJP@transport.nsw.gov.au>
Cc: Development Sydney <Development.Sydney@transport.nsw.gov.au>; Development CTMP CJP <development.CTMP.CJP@transport.nsw.gov.au>; Kylie Dasey <Kylie.Dasey@transport.nsw.gov.au>
Subject: FW: 200 Aldington Road Industrial Development CPTMP R9

CAUTION: This email is sent from an external source. Do not click any links or open attachments unless you recognise the sender and know the content is safe.

Hi Development CTMP,

FYI - please refer to email below regarding the revised CTMP R9 for review and endorsement by TfNSW in accordance with Conditions of Consent D1 for 200 Aldington Road Industrial Development.

Kind regards,

Sam Islam
Civil Engineer | Superintendent

at&I

Sydney | Melbourne | Brisbane
www.atl.net.au

Level 4 17-21 Macquarie Street
Parramatta NSW 2150

02 9068 8517
0438 657 901



Sydney Harbour, Sydney
Photo by our Civil Engineer - Ida Samadian

CIVIL ENGINEERS | PROJECT MANAGERS | WATER SERVICING COORDINATORS
INFRASTRUCTURE PLANNERS AND ADVISERS | CONSTRUCTION PHASE SERVICES

AT&I accepts no liability for the content of this email, or for the consequences of any actions taken based on the information provided unless that information is subsequently confirmed in writing. Any views or opinions presented in this email are solely those of the author and do not necessarily represent those of the company.

OFFICIAL

From: Sam Islam
Sent: Tuesday, 25 March 2025 11:34 AM
To: Kylie Dasey <Kylie.Dasey@transport.nsw.gov.au>
Cc: Richard Harris <richard.harris@fifecapital.com.au>; Corey Brandon <corey.brandon@simmonscivil.com.au>; Brendan Carroll <brendan.carroll@simmonscivil.com.au>; Debbie Fransen <debbie.f@atl.net.au>; Josie Kydd <josie.kydd@simmonscivil.com.au>
Subject: RE: Road Occupancy Licence Application 2161744 - Awaiting Further Information

Hi Kylie,

I hope you're well.

Fife Capital have proposed to increase the heavy vehicle movements from 400 to 600 per day in the CTMP for the 200 Aldington Road industrial development site.

Please refer to the attached revised CTMP R9 for review and endorsement by TfNSW in accordance with Conditions of Consent D1.

This is the change made in the CTMP from the previous revision:

Table 4-1: Traffic volumes

Stage 1	Times per day	Traffic volumes
Earthworks	7am to 6pm Minimise heavy traffic movements during peak times of 7-9am & 4-6pm.	80 light vehicle movements per day 340 Heavy vehicle movements per day
Warehouse Lot F	7am to 6pm Minimise heavy traffic movements during peak times of 7-9am & 4-6pm.	120 light vehicle movements per day 260 heavy vehicles movements per day
Combined Volume		200 light vehicle movements per day 600 heavy vehicle movements per day

Please note CTMP R8 was previously approved by TfNSW, PCC and DPHI; refer attached approval letter from DPHI.

We will ensure no queuing occurs on Addington Road due to the increase in truck movements. No traffic controls are proposed on Mamre Road.

Kind regards,


Sam Islam
Civil Engineer | Superintendent



Sydney | Melbourne | Brisbane
www.atl.net.au

Level 4 17-21 Macquarie Street
Parramatta NSW 2150

02 9068 8517
0438 657 901



Sydney Harbour, Sydney
Photo by our Civil Engineer - Ida Samadian

CIVIL ENGINEERS | PROJECT MANAGERS | WATER SERVICING COORDINATORS
INFRASTRUCTURE PLANNERS AND ADVISERS | CONSTRUCTION PHASE SERVICES

AT&L accepts no liability for the content of this email, or for the consequences of any actions taken based on the information provided unless that information is subsequently confirmed in writing. Any views or opinions presented in this email are solely those of the author and do not necessarily represent those of the company.

From: Kylie Dasey <Kylie.Dasey@transport.nsw.gov.au>
Sent: Tuesday, 26 March 2024 12:42 PM
To: Sam Islam <sam.i@atl.net.au>
Cc: Richard Harris <richard.harris@fifecapital.com.au>; Corey Brandon <corey.brandon@simmonscivil.com.au>; Brendan Carroll <brendan.carroll@simmonscivil.com.au>; Debbie Fransen <debbie.f@atl.net.au>; Ignacio Vazquez Hume <ignacio@simmonscivil.com.au>
Subject: RE: Road Occupancy Licence Application 2161744 - Awaiting Further Information

Hi Sam,

We have no issue with the increase of vehicle movements. Can you please ensure no queuing occurs on Addington Road due to the increase of vehicle movements.

Regards

Kylie Dasey
Network Access Interface Officer
Network Access Coordination
Customer Journey Management
Transport for NSW

M 0484 328 071 T (02) 8396 1517 E kylie.dasey@transport.nsw.gov.au

Level 1
25 Garden St
Eveleigh NSW 2015

Working days Monday to Friday, 08:30am - 04:30pm



I acknowledge the Aboriginal people of the country on which I work, their traditions, culture and a shared history and identity. I also pay my respects to Elders past and present and recognise the continued connection to country.
Please consider the environment before printing this email.

OFFICIAL

OFFICIAL

From: Sam Islam <sam.i@atl.net.au>
Sent: Tuesday, March 26, 2024 12:11 PM

to: Kylie Dasey <Kylie.Dasey@transport.nsw.gov.au>
Cc: Richard Harris <richard.harris@fifecapital.com.au>; Corey Brandon <corey.brandon@simmonscivil.com.au>; Brendan Carroll <brendan.carroll@simmonscivil.com.au>; Debbie Fransen <debbie.f@atl.net.au>; Ignacio Vazquez Hume <ignacio@simmonscivil.com.au>
Subject: RE: Road Occupancy Licence Application 2161744 - Awaiting Further Information

You don't often get email from sam.i@atl.net.au. [Learn why this is important](#)
CAUTION: This email is sent from an external source. Do not click any links or open attachments unless you recognise the sender and know the content is safe.

Hi Kylie,

Fife Capital would like to request approval to increase the truck movements to 400 per day now for the 200 Aldington Road industrial development site.

Please refer attached revised CTMP for review and approval by TfNSW.

4.2.1 Type and Number of Construction Vehicles

The construction works for the Initial site infrastructure will be over a 15-month construction period. Throughout the main stages, the maximum number of trucks accessing the site on any given day will be 400 truck & dogs.

Table 4-1

Stage	Times per day	Movements numbers	Largest vehicles
Haulage	7am to 6pm Minimise heavy traffic movements during peak times of 7-9am & 4-6pm.	400 movements	Semi/Truck & Dog

We will ensure no queuing occurs on Addington Road due to the increase in truck movements.

Kind regards,
Sam Islam
Civil Engineer | Superintendent

at&l

Sydney | Melbourne | Brisbane
www.atl.net.au

Level 4 17-21 Macquarie Street
Parramatta NSW 2150

02 9068 8517
[0438 657 901](tel:0438657901)





Blackheath - NSW
Photo by our Associate | Civil Engineer - Tim Michel
CIVIL ENGINEERS | PROJECT MANAGERS | WATER SERVICING COORDINATORS
INFRASTRUCTURE PLANNERS AND ADVISERS | CONSTRUCTION PHASE SERVICES

AT&L accepts no liability for the content of this email, or for the consequences of any actions taken based on the information provided unless that information is subsequently confirmed in writing. Any views or opinions presented in this email are solely those of the author and do not necessarily represent those of the company.

OFFICIAL

From: Kylie Dasey <Kylie.Dasey@transport.nsw.gov.au>
Sent: Monday, February 26, 2024 11:45 AM
To: Sam Islam <sam.i@atl.net.au>
Cc: Richard Harris <richard.harris@fifecapital.com.au>; Corey Brandon <corey.brandon@simmonscivil.com.au>; Brendan Carroll <brendan.carroll@simmonscivil.com.au>; Debbie Fransen <debbie.f@atl.net.au>; Ignacio Vazquez Hume <ignacio@simmonscivil.com.au>
Subject: RE: Road Occupancy Licence Application 2161744 - Awaiting Further Information

You don't often get email from kylie.dasey@transport.nsw.gov.au. [Learn why this is important](#)
Hi Sam,

We have no issue with the increase of vehicle movements. Can you please ensure no queuing occurs on Addington Road due to the increase of vehicle movements.


Regards,

Kylie Dasey
Network Access Interface Officer
Network Access Coordination
Customer Journey Management
Transport for NSW

M 0484 328 071 T (02) 8396 1517 E kylie.dasey@transport.nsw.gov.au

Level 1
25 Garden St
Eveleigh NSW 2015

Working days Monday to Friday, 08:30am - 04:30pm



OFFICIAL

OFFICIAL

From: Sam Islam <sam.i@atl.net.au>
Sent: Friday, February 23, 2024 10:26 AM
To: Kylie Dasey <Kylie.Dasey@transport.nsw.gov.au>
Cc: Richard Harris <richard.harris@fifecapital.com.au>; Corey Brandon <corey.brandon@simmonscivil.com.au>; Brendan Carroll <brendan.carroll@simmonscivil.com.au>; Debbie Fransen <debbie.f@atl.net.au>; Ignacio Vazquez Hume <ignacio@simmonscivil.com.au>
Subject: RE: Road Occupancy Licence Application 2161744 - Awaiting Further Information

You don't often get email from sam.i@atl.net.au. [Learn why this is important](#)
CAUTION: This email is sent from an external source. Do not click any links or open attachments unless you recognise the sender and know the content is safe.

Hi Kylie,
I hope you're well.

Fife Capital would like to request approval to increase the truck movements to 300 per day for the 200 Aldington Road industrial development site. This is for catering builders' traffic in the future.

Please refer attached revised CTMP for review and approval by TfNSW.

Stage	Times per day	Movements numbers	Largest vehicles
Haulage	7am to 6pm Minimise heavy traffic movements during peak times of 7-9am & 4-6pm.	300 movements	Semi/Truck & Dog

We will continue to ensure no queuing occurs on Addington Road due to the increase of vehicle movements.

Please let me know if you have any questions.

Kind regards,
Sam Islam
Civil Engineer | Superintendent



Sydney | Melbourne | Brisbane
www.atl.net.au
Level 4 17-21 Macquarie Street
Parramatta NSW 2150

02 9068 8517
[0438 657 901](tel:0438657901)





Forster - NSW
Photo by our Civil Drafter- Jeff Suarez

CIVIL ENGINEERS | PROJECT MANAGERS | WATER SERVICING COORDINATORS
INFRASTRUCTURE PLANNERS AND ADVISERS | CONSTRUCTION PHASE SERVICES

[Click here](#) Client Choice Awards Survey

AT&I accepts no liability for the content of this email, or for the consequences of any actions taken based on the information provided unless that information is subsequently confirmed in writing. Any views or opinions presented in this email are solely those of the author and do not necessarily represent those of the company.

OFFICIAL

From: Kylie Dasey <Kylie.Dasey@transport.nsw.gov.au>
Sent: Thursday, January 11, 2024 1:55 PM
To: Sam Islam <sam.i@atl.net.au>
Cc: Richard Harris <richard.harris@fifecapital.com.au>; Corey Brandon <corey.brandon@simmonscivil.com.au>; Brendan Carroll <brendan.carroll@simmonscivil.com.au>; Debbie Fransen <debbie.f@atl.net.au>; Ignacio Vazquez Hume <ignacio@simmonscivil.com.au>
Subject: RE: Road Occupancy Licence Application 2161744 - Awaiting Further Information

Hi Sam,
We have no issue with the increase of vehicle movements. Can you please ensure no queuing occurs on Addington Road due to the increase of vehicle movements.
Regards,

Kylie Dasey
Network Access Interface Officer
Network Access Coordination
Customer Journey Management
Transport for NSW

M 0484 328 071 **T** (02) 8396 1517 **E** kylie.dasey@transport.nsw.gov.au

Level 1
25 Garden St
Eveleigh NSW 2015

Working days Monday to Friday, 08:30am - 04:30pm



I acknowledge the Aboriginal people of the country on which I work, their traditions, culture and a shared history and identity. I also pay my respects to Elders past and present and recognise the continued connection to country.

Please consider the environment before printing this email.

OFFICIAL

OFFICIAL

From: Sam Islam <sam.i@atl.net.au>
Sent: Wednesday, 10 January 2024 4:13 PM
To: Kylie Dasey <Kylie.Dasey@transport.nsw.gov.au>
Cc: Richard Harris <richard.harris@fifecapital.com.au>; Corey Brandon <corey.brandon@simmonscivil.com.au>; Brendan Carroll <brendan.carroll@simmonscivil.com.au>; Debbie Fransen <debbie.f@atl.net.au>; Ignacio Vazquez Hume <ignacio@simmonscivil.com.au>
Subject: RE: Road Occupancy Licence Application 2161744 - Awaiting Further Information

You don't often get email from sam.i@atl.net.au. [Learn why this is important](#)

CAUTION: This email is sent from an external source. Do not click any links or open attachments unless you recognise the sender and know the content is safe.

Hi Kylie,

In regard to the approved CTMP, Fife Capital would like to request approval to increase the truck movements to 200 per day for the 200 Aldington Road industrial development site.

Please refer attached revised CTMP for review and approval by TfNSW.

Stage	Times per day	Movement numbers	Largest vehicles
Haulage	7am to 6pm Minimise heavy traffic movements during peak times of 7-9am & 4-6pm.	200 movements	Semi / Truck & dog

Please let us know if you have any questions.

Regards,
Sam Islam
Civil Engineer | Superintendent



[Click here](#) [Client Choice Awards Survey](#)

Sydney | Melbourne | Brisbane
www.atl.net.au

Level 4 17-21 Macquarie Street
Parramatta NSW 2150

02 9068 8517
0438 657 901



AT&L CHRISTMAS CLOSURE

23rd December 2023 - 7th January 2024

CIVIL ENGINEERS | PROJECT MANAGERS | WATER SERVICING COORDINATORS
INFRASTRUCTURE PLANNERS AND ADVISERS | CONSTRUCTION PHASE SERVICES

AT&L accepts no liability for the content of this email, or for the consequences of any actions taken based on the information provided unless that information is subsequently confirmed in writing. Any views or opinions presented in this email are solely those of the author and do not necessarily represent those of the company.

OFFICIAL

From: Kylie Dasey <Kylie.Dasey@transport.nsw.gov.au>
Sent: Wednesday, November 15, 2023 10:57:29 AM
To: 'whitegroupops@outlook.com' <whitegroupops@outlook.com>
Subject: RE: Road Occupancy Licence Application 2161744 - Awaiting Further Information

Hi,

As per the approved TMP no ROL is required for stop/slow as all vehicles are left in left out.

Please ensure no speed reduction is implemented on Mamre Road without an approved ROL.

Kylie Dasey
Network Access Interface Officer
Network Access Coordination
Customer Journey Management
Transport for NSW

M 0484 328 071 T (02) 8396 1517 E kylie.dasey@transport.nsw.gov.au

Level 1
25 Garden St
Eveleigh NSW 2015

Working days Monday to Friday, 08:30am - 04:30pm





I acknowledge the Aboriginal people of the country on which I work, their traditions, culture and a shared history and identity. I also pay my respects to Elders past and present and recognise the continued connection to country.
Please consider the environment before printing this email.

OFFICIAL

OFFICIAL

OFFICIAL

From: White Group <whitegroupops@outlook.com>
Sent: Tuesday, 14 November 2023 12:08 PM
To: TMC Planned Incident Unit <TMC_PIU@transport.nsw.gov.au>
Subject: FW: Road Occupancy Licence Application 2161744 - Awaiting Further Information

CAUTION: This email is sent from an external source. Do not click any links or open attachments unless you recognise the sender and know the content is safe.

From: Brendan Carroll <brendan.carroll@simmonscivil.com.au>
Sent: Tuesday, November 14, 2023 12:05 PM
To: White Group <whitegroupops@outlook.com>
Subject: RE: Road Occupancy Licence Application 2161744 - Awaiting Further Information

Sorry for the slow reply.

What works will be carried out under this ROL
Entry and Exit of Trucks from Abbots RD for subdivision works. As required by our transport approved TMP.
Exact dates of works

Works commencing immediately. Works expected to be completed End of 2024.

Kind Regards,

BRENDAN CARROLL
PROJECT ENGINEER



5 St James Place, Seven Hills NSW 2147
T 02 9620 6100
M 0401 941 276
brendan.carroll@simmonscivil.com.au
www.simmonscivil.com.au



This email is confidential. If you are not the intended recipient, please notify us immediately and delete all copies of this message. The views and opinions expressed in this email are those of the sender and do not necessarily reflect the views of Simmons Civil Contracting Pty Ltd, except when the sender expressly and with authority states them to be so. Whilst all care is taken, it is the responsibility of the recipient to ensure that any attachments are scanned for viruses prior to use.

From: White Group <whitegroupops@outlook.com>
Sent: Wednesday, November 8, 2023 9:18 AM
To: Brendan Carroll <brendan.carroll@simmonscivil.com.au>
Subject: Fwd: Road Occupancy Licence Application 2161744 - Awaiting Further Information

Regards,

Operations
White Group Management Pty Ltd

From: Kylie Dasey <tmc_piu@tmc.transport.nsw.gov.au>
Sent: Wednesday, November 8, 2023 09:17
To: Whitegroupops@outlook.com <Whitegroupops@outlook.com>
Subject: Road Occupancy Licence Application 2161744 - Awaiting Further Information

Dear Valued Customer,

With regard to your Road Occupancy Licence (ROL) application -

Application No: 2161744
Road: MAMRE RD
Suburb: KEMPS CREEK
Application Status: Awaiting Further Information

The following item(s) require your action to enable us to continue to assess your application.
Pleased provide the below:
What works will be carried out under this ROL
Exact dates of works

If you have any queries please do not hesitate to contact the Road Occupancy Unit.

Kind Regards,
Road Occupancy Unit, Sydney



This email (including any attachments) may contain confidential and/or legally privileged information and is intended only to be read or used by the addressee(s). If you have received this email in error, please notify the sender by return email, delete this email and destroy any copy. Any use, distribution, disclosure or copying of this email by a person who is not the intended recipient is not authorised.

Views expressed in this email are those of the individual sender, and are not necessarily the views of Transport for New South Wales, Department of Transport or any other NSW government agency. Transport for NSW and the Department of Transport assume no liability for any loss, damage or other consequence which may arise from opening or using an email or attachment.

Please visit us at <http://www.transport.nsw.gov.au> or <http://www.transportnsw.info>
This email is intended only for the addressee and may contain confidential information. If you receive this email in error please delete it and any attachments and notify the sender immediately by reply email. Transport for NSW takes all care to ensure that attachments are free from viruses or other defects. Transport for NSW assume no liability for any loss, damage or other consequences which may arise from opening or using an attachment.

 **Consider the environment. Please don't print this e-mail unless really necessary.**
This email is intended only for the addressee and may contain confidential information. If you receive this email in error please delete it and any attachments and notify the sender immediately by reply email. Transport for NSW takes all care to ensure that attachments are free from viruses or other defects. Transport for NSW assume no liability for any loss, damage or other consequences which may arise from opening or using an attachment.

 **Consider the environment. Please don't print this e-mail unless really necessary.**
This email is intended only for the addressee and may contain confidential information. If you receive this email in error please delete it and any attachments and notify the sender immediately by reply email. Transport for NSW takes all care to ensure that attachments are free from viruses or other defects. Transport for NSW assume no liability for any loss, damage or other consequences which may arise from opening or using an attachment.

 **Consider the environment. Please don't print this e-mail unless really necessary.**
This email is intended only for the addressee and may contain confidential information. If you receive this email in error please delete it and any attachments and notify the sender immediately by reply email. Transport for NSW takes all care to ensure that attachments are free from viruses or other defects. Transport for NSW assume no liability for any loss, damage or other consequences which may arise from opening or using an attachment.

 **Consider the environment. Please don't print this e-mail unless really necessary.**
This email is intended only for the addressee and may contain confidential information. If you receive this email in error please delete it and any attachments and notify the sender immediately by reply email. Transport for NSW takes all care to ensure that attachments are free from viruses or other defects. Transport for NSW assume no liability for any loss, damage or other consequences which may arise from opening or using an attachment.

 **Consider the environment. Please don't print this e-mail unless really necessary.**
