



Altis Frasers

Waste Management Plan

Manufacturing / Warehouse Facility

Lot 12 (SSD-9522)

657-769 Mamre Road
Kemps Creek, NSW

5 November 2021



Altis Frasers
Waste Management Plan
Manufacturing / Warehouse Facility
Lot 12 (SSD-9522)

657-769 Mamre Road
Kemps Creek, NSW

5 November 2021

Contents

1. Introduction	5
1.1 Background	5
1.2 Objectives	6
2. Project Summary	7
2.1 Proposed Works	7
2.2 Development Areas	8
2.3 Project Schedule	9
3. Waste Regulatory Framework	10
3.1 Protection of the Environment Operations Act 1997	10
3.2 Waste Avoidance and Resource Recovery Act 2001	10
3.3 Protection of the Environment Operations (Waste) Regulation 2014	11
3.4 Better Practice Guidelines 2012	11
3.5 Waste Avoidance and Resource Recovery Strategy 2014 - 2021	12
3.6 Waste Classification Guidelines 2014	13
3.7 Mamre Road Precinct Development Control Plan 2020	13
4. Estimated Waste	14
4.1 Demolition Waste	14
4.2 Construction Waste	16
4.3 Operational Waste	17
5. Demolition and Construction Waste Reduction Plan	18
5.1 Waste Reduction Measures	18
5.2 Beneficial Reuses	18
5.3 Waste Storage Locations	19
6. Operational Waste Reduction Plan	20
6.1 Waste Reduction Measures	20
6.2 Beneficial Reuses	20
6.3 Waste Storage Locations	21
7. Waste Classification and Removal	22
7.1 Waste Classification	22
7.2 Waste Transporting	24

8. Limitation Statement	25
Figures	26
Attached	
Figure 1 – Site Location Plan	27
Figure 2 – Proposed Development Layout	28
Figure 3 – Demolition Waste Bin Plan	29
Figure 4 – Construction Waste Bin Plan	30
Figure 5 – Operational Waste Bin Plan	31
 Tables	
Main Text	
Table 1 – Summary of SEARs	5
Table 2 – Estimated Demolition Waste	14
Table 3 – Estimated Monthly Construction Waste	16
Table 4 – Estimated Yearly Operational Waste	17
Table 5 – Summary of Waste Classification Criteria	23

Distribution of Copies

Revision	Copy no	Quantity	Issued to
1	1	1 PDF Copy	Paul Solomon: Altis Frasers

Printed:	5 November 2021
Last saved:	5 November 2021 12:46 pm
File name:	LG2123.01 WMP 05-11-21.docx
Author:	Gonzalo Parra
Name of organisation:	Altis Frasers
Name of project:	657-769 Mamre Road, Kemps Creek, NSW
Name of document:	Waste Management Plan Manufacturing / Warehouse Facility Lot 12 (SSD-9522)
Document version:	Final
Project number:	LG2123.01

1. Introduction

1.1 Background

Land & Groundwater Consulting Pty Ltd (LG) has been commissioned by Altis Frasers JV Pty Ltd (Altis Frasers) to prepare this Waste Management Plan (WMP) in accordance with the technical requirements of the Secretary's Environmental Assessment Requirements (SEARs), and in support of the proposed design, construction, fit out and operation of a manufacturing and warehouse facility at 657-769 Mamre Road, Kemps Creek, NSW (the site).

The site is currently legally described as Lot 12 approved under State Significant Development (SSD) 9522 with a total area of approximately 43,682 m². The site location and proposed development layout are shown in **Figures 1** and **2**, respectively.

Specifically, this WMP addresses the following SEARs:

Table 1 – Summary of SEARs

SEARs	Report Reference
Details of the quantities and classification of all waste streams to be generated on site during construction and operation.	Sections 4.1, 4.2 and 4.3.
Details of waste storage, handling and disposal during the construction and operation of the development, including plans of waste storage and collection areas.	Sections 5.3, 6.3, 7.1 and 7.2.
Details of the measures that would be implemented to ensure that the development is consistent with the aims, objectives and guidance in the NSW Waste Avoidance and Resource Recovery Strategy 2014-2021.	Sections 5.1, 5.2, 6.1 and 6.2.

1.2 Objectives

The objectives of the WMP are:

- To document the procedures that will be undertaken to manage the wastes generated as part of the development works;
- To provide details of the quantities and classification of waste and wastewater (if any) to be generated onsite;
- To provide details on waste storage, handling and disposal (including the location of waste storage and management facilities); and
- To provide details of the measures that would be implemented to ensure that the development is consistent with the aims, objectives and guidance in the *NSW Waste Avoidance and Resource Recovery Strategy 2014-2021*

2. Project Summary

2.1 Proposed Works

The proposed works for the Development Application comprise the following:

- Minor earthworks involving cut and fill works, site preparation works and the establishment of a building pad;
- Infrastructure comprising civil works and augmentation of utilities servicing;
- Construction, internal fit out and operation of a manufacturing facility and warehouse (27,470 m²), comprising:
 - Manufacturing areas and associated warehouse (24,970 m²).
 - Ancillary office areas (2,500 m²).
 - 163 car parking spaces and 12 bicycle spaces.
 - Powder silo tower.
 - Liquid silo tower.
 - Associated business identification signage.
 - Site Landscaping (4,348 m²).
 - 13 loading docks.
 - Three (3) vehicle crossovers.
- Production capacity up to approximately 48,000 tonnes per annum (tpa) of powder products, resulting in an indicative weekly maximum of 932.0 tonnes and daily maximum of 131.5 tonnes;
- Production capacity up to approximately 25,000 KL per annum of liquid products, resulting in an indicative weekly maximum of 480.7 KL and daily maximum of 68.5 KL;
- Storage of dangerous goods, comprising:
 - Class 2.1 – LPG.

- Class 3 – Flammable Liquid.
- Clause 4.1 – Flammable Solids.
- Clause 5.1 – Oxidising Substances.
- Clause 6.1 – Sub-risk Toxic Substances.
- Class 8 – Corrosive Substances.
- Hours of operation being on a 24 hours per day, 7 days per week, basis; and
- Torrens Title subdivision to create the subject allotment (proposed Lot 12) measuring approximately 43,682 m² (4.3 ha).

2.2 Development Areas

The proposed development areas and GFA are as follows (refer **Figure 4**):

- Proposed Area Lot 12: 158,550 m².
- Total Utilised Site Area: 43,682 m².
- Total Building Area of 27,470 m² including the following:
 - Warehouse: 15,390 m².
 - Dock Office and Amenities: 80 m².
 - Liquids Manufacturing: 3,824 m².
 - Powder Manufacturing: 2,625 m².
 - Power Silo Tower: 600 m².
 - Receiving and Packaging Store: 1,971 m².
 - Compressor Room (2 Storey): 270 m².
 - DG Store: 56 m².
 - Waste Water Treatment: 43 m².
 - Liquid Silo Tower: 111 m².
 - Main Office (2 Storey): 2,000 m².
 - Manufacturing Office (2 Storey): 500 m².

- Awning: 1,836 m².
- Total Car Parking: 163 spots.

2.3 Project Schedule

The only significant waste to be generated by the development is anticipated to be demolition and construction waste, which will be stored in allocated areas of the site (refer **Figures 3** and **4**) and generated during the following development construction stages:

- Tree clearing and construction of building facility pads, structures and related amenities; and
- Installation of lead-in services including electricity, sewer and potable water.

All operational waste producing activities such as packaging material, servicing of equipment and employee amenities will be located outside the warehouse. Waste containers will comprise colour coded recycling bins, which will be utilised to dispose off any packaging waste. The recycling bins will be located within a designated waste storage area located within the northern corner of the site (refer **Figure 5**), and collected by a regulated waste contractor.

3. Waste Regulatory Framework

3.1 Protection of the Environment Operations Act 1997

Wastes in NSW are classified for disposal or transport into categories. It is the responsibility of those who generate the waste to classify it into groups that pose risks to the environment and human health facilitates their management and appropriate disposal.

All material to be removed from the site (including associated activities such as classification) will be undertaken in strict accordance with the requirements of the POEO Act 1997. Such requirements include:

- Ensuring waste is classified appropriately and in accordance with relevant guidelines;
- Waste materials are disposed of to appropriately licensed facilities; and
- Other materials are removed to facilities lawfully able to accept such materials.

3.2 Waste Avoidance and Resource Recovery Act 2001

The Waste Avoidance and Resource Recovery (WARR) Act 2001 establishes the waste hierarchy to ensure that resource management options are considered against the following priorities:

1. Avoidance – actions to reduce the amount of waste generated and undertaking activities;
2. Resource Recovery – which includes reuse, reprocessing, recycling and energy recovery, consistent with the most efficient use of the recovered resources; and
3. Disposal – an “end-of-pipe” option that must be carefully undertaken to minimise any negative environmental outcomes.

The objectives of the WARR Act 2001 include:

- To encourage the most efficient use of resources;
- To minimise the consumption of natural resources and the final disposal of waste by encouraging the avoidance of waste and the reuse and recycling of waste;

- To ensure that industry shares with the community the responsibility for reducing; and
- To ensure the efficient funding of waste and resource management planning, programs and service delivery.

3.3 Protection of the Environment Operations (Waste) Regulation 2014

The Regulation encourages the recovery of resources from waste by issuing both general and specific resource recovery exemptions. Where no general exemption is available for the intended use, a specific exemption may be issued after an application is made to the NSW EPA. Specific exemptions are not publicly available.

The Regulation makes requirements relating to non-licensed waste activities and waste transporting. The proposed works on the site will not require to be licensed. Section 48 of the Regulation requires that wastes are stored in an environmentally safe manner. It also stipulates that vehicles used to transport waste must be covered when loaded.

The Regulation exempts certain waste streams from the full waste tracking and record keeping requirements. Waste tracking is required only for industrial and hazardous wastes.

3.4 Better Practice Guidelines 2012

The NSW EPA (2012) *Better Practice Guidelines for Waste Management and Recycling in Commercial and Industrial Facilities 2012* promotes efficient waste minimisation and resource recovery for commercial and industrial facilities and is used as a benchmark document when assessing waste production rates within Australia.

Better practice waste management systems in commercial buildings may incorporate any, or all, of the following:

- Garbage services to manage residual wastes (those not collected by a dedicated recycling or organics collection service).
- Recycling services to manage dry recyclable materials. These materials may vary from building to building, but generally cover recyclable materials generated in a typical business, including office paper, cardboard, plastic film, metals and

LAND & GROUNDWATER CONSULTING PTY LTD

LG2123.01 WMP 05-11-21.docx

recyclable containers.

- Organics services to manage garden and food organics, which may include a bin-based collection system or onsite composting.
- Bulky waste services to manage bulky items, such as furniture and fit-out materials.
- Special waste services for items such as toner cartridges, batteries, fluorescent lights, mobile phones and chemicals.

3.5 Waste Avoidance and Resource Recovery Strategy 2014 - 2021

The NSW Government's priority areas and actions for waste avoidance and resource recovery is outlined in the Waste Strategy 2014-2021.

The six identified "key result areas" in the Strategy are:

- Key Result Area 1: Avoid and reduce waste generation (for assessment of proposed measures refer Sections 5.1 and 6.1 of this report).
- Key Result Area 2: Increase recycling (for assessment of proposed measures refer Sections 5.2 and 6.2 of this report).
- Key Result Area 3: Divert more waste from landfill (for assessment of proposed measures refer Sections 5.2 and 6.2 of this report).
- Key Result Area 4: Manage problem wastes better (for assessment of proposed measures refer Sections 5.1 and 6.1 of this report).
- Key Result Area 5: Reduce litter (for assessment of proposed measures refer Sections 5.1 and 6.1 of this report).
- Key Result Area 6: Reduce illegal dumping (for assessment of proposed measures refer Sections 5.2 and 6.2 of this report).

The Strategy also includes the following recycling targets (as relevant to the proposed works at the site)¹:

¹ *NSW Waste Avoidance and Resource Recovery Strategy 2014-21*, NSW EPA, December 2014.

- Increased recycling of commercial and industrial waste from 57% (in 2010-11) to 70% by 2021-21; and
- Increased recycling of construction and demolition waste from 75% (in 2010-11) to 80% by 2021-21.

3.6 Waste Classification Guidelines 2014

Soil materials proposed to be disposed offsite (if any) shall be assessed, classified and managed in accordance with the NSW EPA (2014) *Waste Classification Guidelines, Part 1: Classifying Waste*.

3.7 Mamre Road Precinct Development Control Plan 2020

In accordance with Section 4.6 (Waste Minimisation and Management) of the Mamre Road Precinct Development Control Plan (DCP) 2020, one of the objectives of the Draft DCP is to assist in reducing Penrith's ecological footprint by encouraging the diversion of waste from landfill.

The Mamre Road Precinct Draft DCP has been prepared in accordance with the Waste Avoidance and Resource Recovery Act 2001 and came into effect in November 2020.

4. Estimated Waste

4.1 Demolition Waste

The estimated demolition waste quantities are summarised in **Table 2**.

Table 2 – Estimated Demolition Waste

Type of Waste Generated	Reuse	Recycling	Disposal	Method of on-site reuse, contractor and recycling outlet and /or waste depot to be used
	Estimate Volume (m ³) or Weight (t)	Estimate Volume (m ³) or Weight (t)	Estimate Volume (m ³) or Weight (t)	
Excavation Material	0 m ³	0 m ³	0 m ³	N/A
Timber	0 m ³	0 m ³	0 m ³	Waste Management Centre
Concrete	0 m ³	0 m ³	0 m ³	Recycling Management Centre
Bricks/pavers	0 m ³	0 m ³	0 m ³	Recycling Management Centre
Tiles	0 m ³	0 m ³	0 m ³	Waste Management Centre
Metal	0 m ³	0 m ³	0 m ³	Recycling Management Centre
Glass	0 m ³	0 m ³	0 m ³	Waste Management Centre
Furniture	0 m ³	0 m ³	0 m ³	Waste Management Centre
Fixtures and fittings	0 m ³	0 m ³	0 m ³	Waste Management Centre
Floor coverings	0 m ³	0 m ³	0 m ³	Waste Management Centre
Packaging (used pallets, pallet wrap)	0 m ³	0 m ³	0 m ³	N/A
Garden organics	0 m ³	965 m ³	0 m ³	Recycling Management Centre
Containers (cans, plastic, glass)	0 m ³	0 m ³	0 m ³	N/A
Paper/cardboard	0 m ³	0 m ³	0 m ³	N/A
Residual waste	0 m ³	0 m ³	<5 m ³	Waste Management Centre

LAND & GROUNDWATER CONSULTING PTY LTD

LG2123.01 WMP 05-11-21.docx

Type of Waste Generated	Reuse	Recycling	Disposal	Method of on-site reuse, contractor and recycling outlet and /or waste depot to be used
	Estimate Volume (m ³) or Weight (t)	Estimate Volume (m ³) or Weight (t)	Estimate Volume (m ³) or Weight (t)	
Hazardous/special waste	0 m ³	0 m ³	0 m ³	0 m ³
Other	0 m ³	0 m ³	0 m ³	N/A
Total	0 m³	965 m³	<5 m³	

4.2 Construction Waste

The estimated monthly construction waste quantities are summarised in **Table 3**.

Table 3 – Estimated Monthly Construction Waste

Type of Waste Generated	Reuse	Recycling	Disposal	Method of on-site reuse, contractor and recycling outlet and /or waste depot to be used
	Estimate Volume (m ³) or Weight (t)	Estimate Volume (m ³) or Weight (t)	Estimate Volume (m ³) or Weight (t)	
Excavated materials (soil spoil)	60,350 m ³	0	0	NA (if disposal applies refer S. 3.6 and 7.1)
Green waste	0	0	0	NA
Bricks/pavers	0	0	<5 m ³ (offcuts)	Waste Management Centre
Tiles	0	0	<5 m ³ (offcuts)	Waste Management Centre
Concrete	0	0	<5 m ³	Waste Management Centre
Plasterboard	0	0	<5 m ³	Waste Management Centre
Asbestos	0	0	0	NA
Metal – specify	0	<5 m ³ (steel studs)	0	Recycling Outlet
Timber - specify	0	0	0	NA
Other waste – specify (eg. paints, PVC tubing)	0	0	<5 m ³ (offcuts)	Waste Management Centre
Packaging (used pallets, pallet wrap)	0	<5 m ³	0	Recycling Outlet
Containers (cans, plastic, glass)	0	<5 m ³	0	Recycling Outlet
Paper/cardboard	0	<5 m ³	0	Recycling Outlet
Total	60,350 m³	<20 m³	<25 m³	

4.3 Operational Waste

The estimated yearly operational waste quantities are summarised in **Table 4**.

Table 4 – Estimated Yearly Operational Waste

Type of Waste Generated	Reuse	Recycling	Disposal	Method of on-site reuse, contractor and recycling outlet and /or waste depot to be used
	Estimate Volume (m ³) or Weight (t)	Estimate Volume (m ³) or Weight (t)	Estimate Volume (m ³) or Weight (t)	
Office – paper/cardboard	0	8	0	Recycling Outlet
Office – food waste	0	0	5	Waste Management Centre
Office – general waste	0	0	5	Waste Management Centre
Process – packaging paper/cardboard	0	20	0	Recycling Outlet
Process – packaging plastics	0	20	0	Recycling Outlet
Process – wooden pallets	0	250	0	Recycling Outlet
Process – timber	0	0	15	Waste Management Centre
Process – powder dust	0	450	0	Recycling Outlet
Process – liquid solids	0	0	85	Waste Management Centre
Process – waste water	515	0	0	Licensed Sewer Discharge
Process – steel drums	0	50	0	Recycling Outlet
Process – packaging IBC's	0	100	0	Recycling Outlet
Process – general waste	0	0	250	Waste Management Centre
FG – EOL powder products	0	150	0	Recycling Outlet
FG – EOL liquids products	0	100	0	Recycling Outlet
FG – EOL other products	0	0	50	Waste Management Centre
Total	515	1,148	410	

5. Demolition and Construction Waste Reduction Plan

5.1 Waste Reduction Measures

Waste-type-specific reduction measures will be employed during demolition and construction stages, with the following specific procedures:

- Applying practical building designs and construction techniques;
- Appropriate sorting and segregation of demolition and construction wastes to ensure efficient recycling of wastes;
- Selecting construction materials taking into consideration to their long lifespan and potential for reuse;
- Ordering materials to size and ordering pre-cut and prefabricated materials;
- Reuse of formwork (where possible);
- Planned work staging;
- Reducing packaging waste on-site by returning packaging to suppliers where possible, purchasing in bulk, requesting cardboard or metal drums rather than plastics, requesting metal straps rather than shrink wrap and using returnable packaging such as pallets and reels;
- Careful on-site storage and source separation;
- Subcontractors informed of site waste management procedures; and
- Coordination and sequencing of various trades.

5.2 Beneficial Reuses

The anticipated beneficial reuses of demolition and construction waste are summarised as follows:

- All solid waste timber, concrete, tiles and rock that cannot be reused or recycled will be taken to an appropriate facility for treatment to recover further resources or for disposal to landfill in an approved manner;

- All asbestos, hazardous and/or intractable wastes are to be disposed of in accordance with SafeWork Authority and EPA requirements;
- Portable, self-contained toilet and washroom facilities will be provided at the site and will be regularly emptied and serviced by a suitably qualified contractor;
- Provision for the collection of batteries, fluorescent tubes and other recyclable resources will be provided onsite to enable offsite recycling;
- Drink container recycling should be provided onsite or these items sorted offsite for recycling at an appropriately licensed facility;
- All garbage will be disposed of via a council approved system; and
- Opportunities for materials exportation and reuse with other local construction operations will be investigated.

5.3 Waste Storage Locations

Waste storage locations will be accessible and allow sufficient space for storage and servicing requirements. These locations will also be flexible in order to cater for change of use throughout the demolition and construction stages.

Where space is restricted (during construction), dedicated stockpile areas are to be delineated on the site, with regular transfers to dedicated skip bins for sorting. The positions of the designated waste holding areas on site will change according to building works and the progression of the development, but must consider visual amenity, OH&S and accessibility in their selection.

All waste placed in stockpile areas/skips for disposal or recycling shall be adequately contained to ensure that the waste does not fall, blow, wash or otherwise escape from the site. Appropriate siting of waste stockpile locations will take into account slope and drainage factors to avoid contamination of stormwater drains during rain events.

Waste/recycling storage locations will be assigned during the demolition and construction works and will provide adequate space to accommodate all waste and recycling bins associated with the demolition (tree clearing) and construction (up to approximately 4 x 1,000 L bins) (refer **Figures 3** and **4**). Recycling bins must be accessible to all demolition and construction employees and must be clearly sign posted and colour coded to ensure segregation of waste and recycling is effective. Waste containers are to be kept clean and in a good state of repair.

6. Operational Waste Reduction Plan

6.1 Waste Reduction Measures

Waste-type-specific reduction measures will be employed during development operation, with the following specific procedures:

- Provision of take back services to clients to reduce waste further along the supply chain;
- Re-work/re-packaging of products prior to local distribution to reduce waste arising;
- Review of packaging design to reduce waste but maintain 'fit for purpose';
- Investigating leased office equipment and machinery rather than purchase and disposal;
- Establish systems with in-house and with supply chain stakeholders to transport products in re-useable packaging where possible;
- Development of 'buy recycled' purchasing policy;
- Flatten or bale cardboard to reduce number of bin lifts required; and
- Providing recycling collections within each of the offices and tearooms (e.g. plastics, cans and glass).

6.2 Beneficial Reuses

The anticipated beneficial reuses of operational waste are summarised as follows:

- Cardboard, paper, plastic, glass, cans and pallets and containers will be reused/recycled offsite;
- Provision for the collection of batteries, fluorescent tubes and other recyclable resources will be provided on site to enable offsite recycling;
- All waste materials that cannot be reused or recycled will be taken to an appropriate facility for treatment to recover further resources or for disposal to landfill in an approved manner;

- Waste oil (if any) used in equipment maintenance will be recycled or disposed of in an appropriate manner; and
- Opportunities for materials exportation and reuse with other local industrial operations will be investigated. This will have two benefits: minimising energy through reduction of material reprocessing, encouraging material reuse.

6.3 Waste Storage Locations

A designated waste storage area will be provided within the northern corner of the site (refer **Figure 5**) where the recycling bins, garbage skips, plastic and cardboard compactors will be stored prior to collection. Sufficient clearance will be necessary to enable collection vehicles to access the locations of bin storage. Where possible collection times should not coincide with peak operational delivery schedules however the designated area identified will not interfere with operational truck movements.

The construction of locations for garbage storage are to comply with BCA (Building Code of Australia) requirements and Australian Standards, including CoC requirements for screening and fencing.

The waste/recycling storage area will be constructed of an adequate size to accommodate all waste and recycling bins and bales associated with the development. Recycling bins must be accessible to all employees and must be clearly sign posted and colour coded to ensure segregation of waste and recycling is effective.

Sufficient space will be provided for the segregation and storage of varying waste types including provision for the collection of fluorescent tubes, smoke detectors, e-wastes and other recyclable resources.

Sufficient space will also be provided for reuse items such as crates and pallets for occupational safety purposes.

Doors/gates to the waste storage locations will be able to be opened from the outside and wide enough to allow for easy passage of waste/recycling containers.

7. Waste Classification and Removal

7.1 Waste Classification

All liquid and non-liquid wastes generated during development construction works (if any) shall be classified in accordance with the requirements of NSW EPA (2014) *Waste Classification Guidelines, Part 1: Classifying Waste*.

Samples shall be collected by appropriately trained and experienced personnel from stockpiled or in-situ waste materials by the use of a hand trowel. The hand trowel shall be thoroughly decontaminated using phosphate free detergent and distilled water between each sampling location.

During the collection of soil samples, features such as seepage, discolouration, staining, odours and other indications of contamination should be noted on the field documentation.

Collected soil samples shall be immediately transferred to sample containers of appropriate composition (glass jars). Sample labels shall record job number; sample identification number; and date and time of sampling.

Sample containers shall be transferred to a chilled ice box for sample preservation prior to and during shipment to the testing laboratory. A chain-of-custody form should be completed and forwarded with the samples to the testing laboratory.

Soil samples shall be analysed by both a primary and secondary (independent check) laboratory, both of which shall be NATA accredited for the required analyses. In addition, the laboratories will also be required to meet the environmental consultant's own internal quality assurance requirements.

The analytical data shall be compared against the waste criteria contained in NSW EPA (2014) *Waste Classification Guidelines, Part 1: Classifying Waste* for heavy metals, TRHs, BTEX, PAHs, total pesticides (OCPs and OPPs), PCBs and TCLP in benzo(a)pyrene, lead and nickel. A summary of the criteria is provided in **Table 5**.

Table 5 – Summary of Waste Classification Criteria

Contaminant	General ¹	Restricted ¹	General ²	Restricted ²	General ³	Restricted ³
	CT1	CT2	SCC1	SCC2	TCLP1	TCLP2
	(mg/kg)	(mg/kg)	(mg/kg)	(mg/kg)	(µg/L)	(µg/L)
Heavy metals						
Arsenic	100	400	500	2000	5.0	20
Cadmium	20	80	100	400	1.0	4
Lead	100	400	1500	6000	5	20
Mercury	4	16	50	200	0.2	0.8
Nickel	40	160	1050	4200	2	8
BTEX						
Benzene	10	40	18	72	0.5	2
Toluene	288	1152	518	2073	14.4	57.6
Ethylbenzene	600	2400	1080	4320	30	120
Xylenes (total)	1000	4000	1800	7200	50	200
Petroleum Hydrocarbons						
C₆-C₉	N/A	N/A	650	2600	N/A	N/A
C₁₀-C₃₆	N/A	N/A	10000	40000	N/A	N/A
PAHs						
Benzo(a)pyrene	0.8	3.2	10	23	0.04	0.16
PAHs (total)	N/A	N/A	200	800	N/A	N/A
Pesticides (total)	N/A	N/A	250	1000	N/A	N/A
PCBs (total)	N/A	N/A	<50	<50	N/A	N/A

Notes:

1. Contaminant threshold values for classifying waste by chemical assessment without the leaching (TCLP) test (Table 1) – NSW EPA (2014) *Waste Classification Guidelines, Part 1: Classifying Waste*.
2. Specific contaminant concentration (SCC) values for classifying waste by chemical assessment (Table 2) – NSW EPA (2014) *Waste Classification Guidelines, Part 1: Classifying Waste*.
3. Leachable concentration (TCLP) values for classifying waste by chemical assessment (Table 2) – NSW EPA (2014) *Waste Classification Guidelines, Part 1: Classifying Waste*.

7.2 Waste Transporting

All wastes removed from the site shall be transported in accordance with relevant road and transportation regulatory requirements. Where required (depending on the classification of the wastes), appropriately licensed transport contractors shall be used.

The appointed transporters shall be responsible for ensuring they are appropriately licensed to:

- Carry the particular type of waste; and
- Transport the materials to an appropriately licensed facility.

Where the waste is classified as Restricted Waste or Hazardous Waste, the transporter is required to carry (subject to a number of exceptions) appropriately completed waste data forms with each load, and provide a copy to the waste facility to which the waste is taken.

8. Limitation Statement


This report has been prepared for use by Altis Frasers JV Pty Ltd who commissioned the works in accordance with the project brief only and has been based in part on information obtained from other parties. The advice herein relates only to this project and all information provided should be reviewed by a competent person with experience in environmental investigations, before being used for any other purpose. Additionally, this report has been based on data documented by other parties in previous reports.

LG Consult accepts no liability for use or interpretation by any person or body other than Altis Frasers JV Pty Ltd. This report should not be reproduced without prior approval by Woolworths Group Limited, or amended in any way without prior approval by LG Consult, and should not be relied upon by other parties, who should make their own enquires.

Waste quantities and sources are based on documents made available to LG consult by Altis Frasers JV Pty Ltd.

This report does not provide a complete assessment of the environmental status of the site, and it is limited to the scope defined herein.

Figures

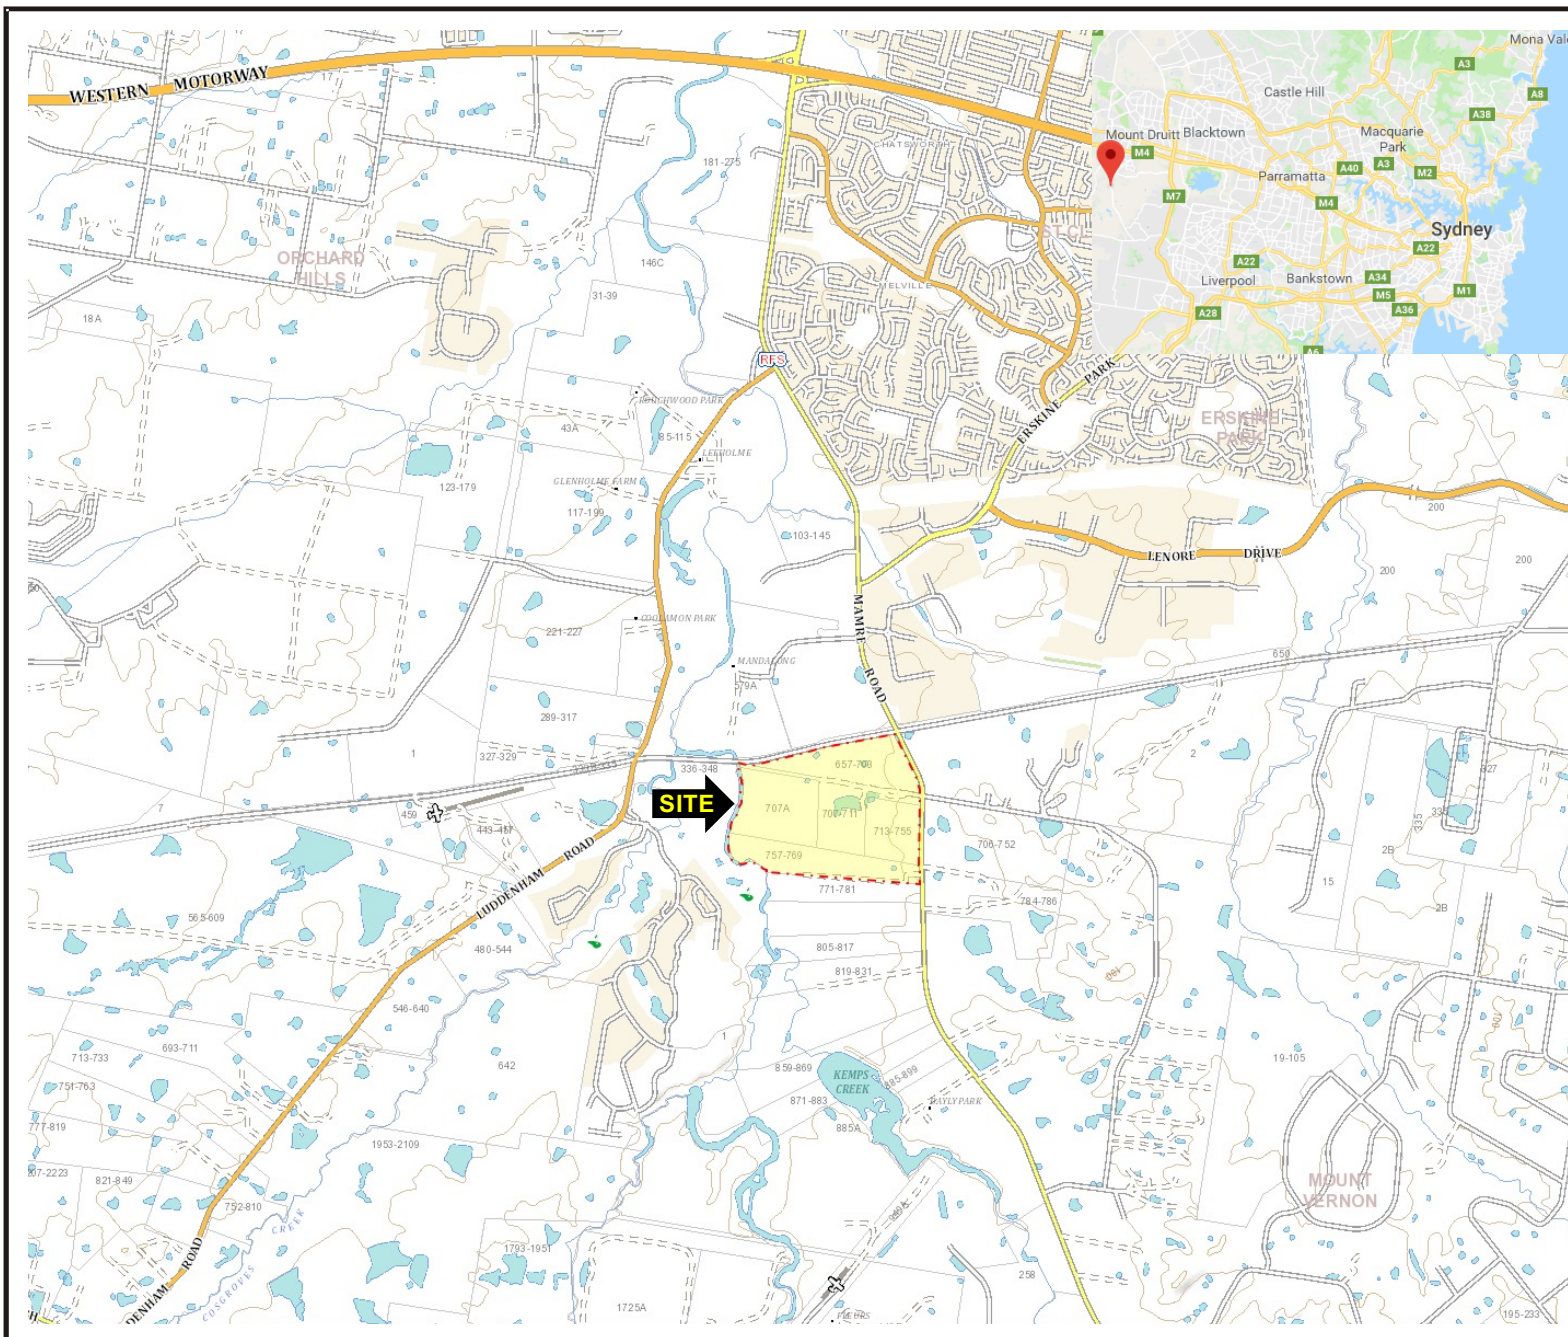

SCALE: DRAWN TO SCALE AS SHOWN

Not To Scale

NORTH

LEGEND:

 Site Boundary

Image courtesy of Google & Six Maps



REV: A
DATE: 13/08/2021
DRAWN: GP
APPROVED: GP
STATUS: Final
DWG NO:

CLIENT: **Frasers & Altis**
PROJECT: **657-769 Mamre Road
Kemps Creek, NSW**
PROJECT NUMBER: LG2042.01

TITLE: **Site Location Plan**

FIGURE:

1

A4



SCALE: DRAWN TO SCALE AS SHOWN

Not To Scale

NORTH

LEGEND:

 Site Boundary

Image courtesy of Frasers & Altis



REV: A
DATE: 13/08/2021
DRAWN: GP
APPROVED: GP
STATUS: Final
DWG NO:

CLIENT: **Frasers & Altis**

PROJECT: **657-769 Mamre Road
Kemps Creek, NSW**

PROJECT NUMBER: LG2042.01

TITLE: **Proposed
Development Layout**

FIGURE:

2

A4



SCALE: DRAWN TO SCALE AS SHOWN

Not To Scale

NORTH

LEGEND:

✚ 1000 L Mobile Garbage Bin (MGB) for General Garbage

✚ 1000 L MGB for Recycling

Image courtesy of Google Earth



REV: A
DATE: 13/08/2021
DRAWN: GP
APPROVED: GP
STATUS: Final
DWG NO:

CLIENT: **Frasers & Altis**

PROJECT: **657-769 Mamre Road
Kemps Creek, NSW**


PROJECT NUMBER: LG2042.01

TITLE:
Demolition Waste Bin Plan

FIGURE:

3

A4

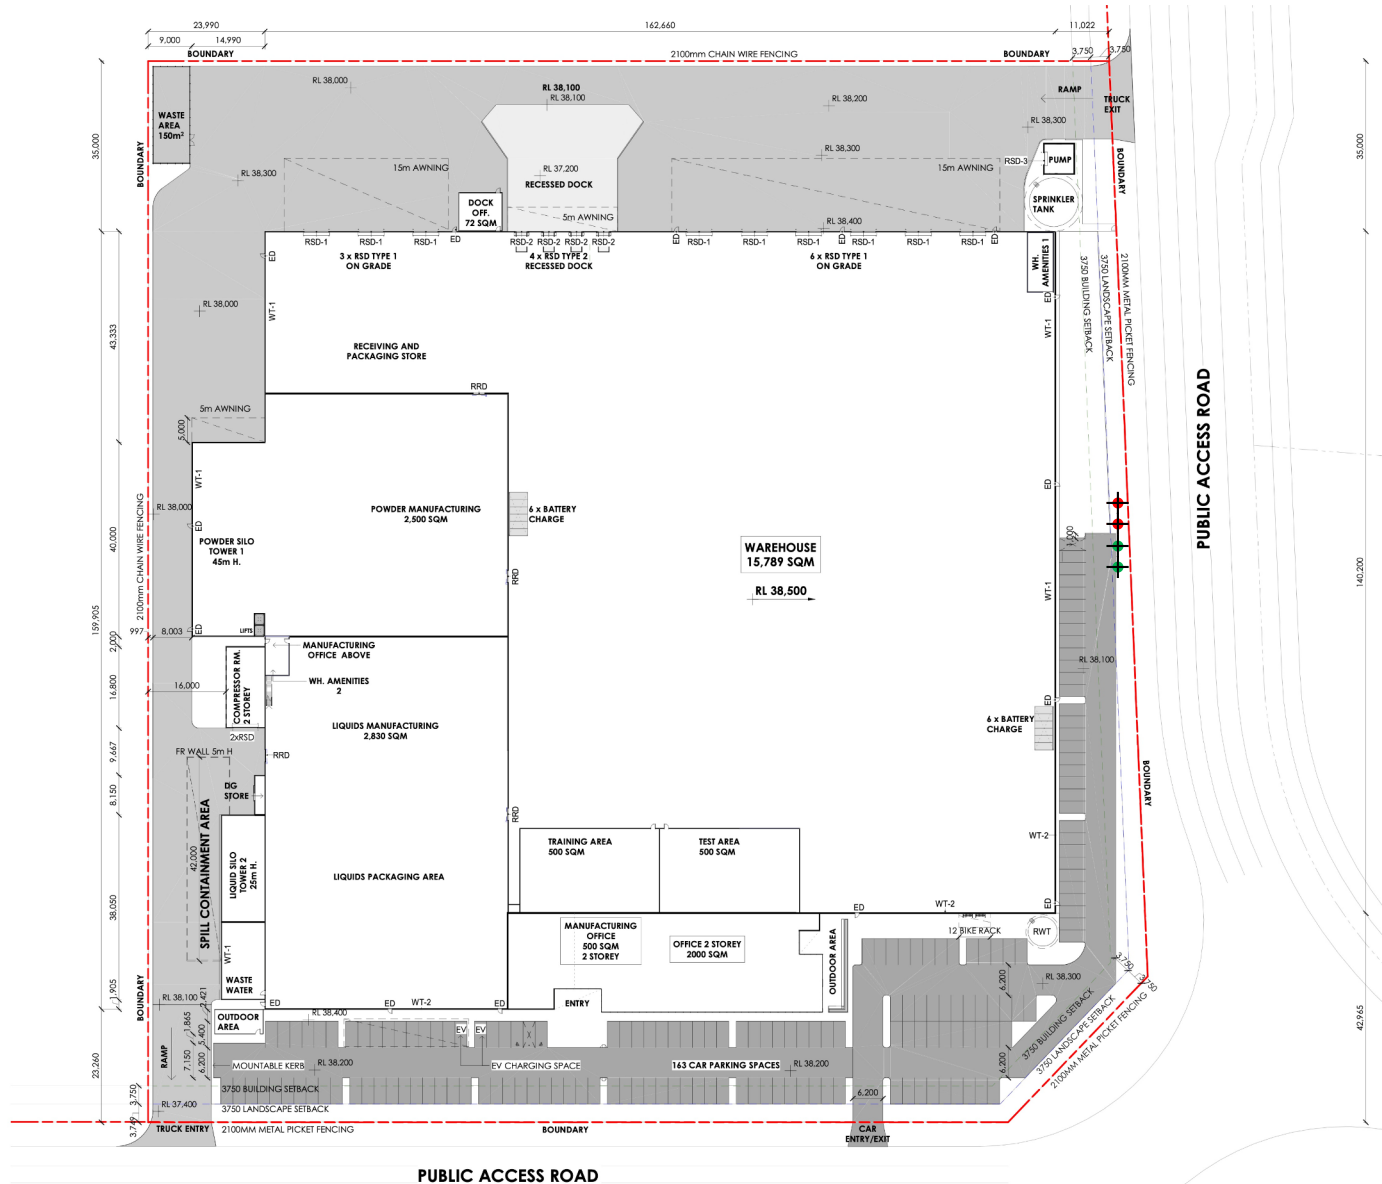

SCALE: DRAWN TO SCALE AS SHOWN

Not To Scale

NORTH

LEGEND:

Site Boundary

1000 L MGB for General Garbage

1000 L MGB for Recycling

Image courtesy of Google & Six Maps




REV: A
DATE: 13/08/2021
DRAWN: GP
APPROVED: GP
STATUS: Final
DWG NO:

CLIENT: **Frasers & Altis**
PROJECT: **657-769 Mamre Road
Kemps Creek, NSW**
PROJECT NUMBER: LG2042.01

TITLE:
**Construction Waste Bin
Plan**

FIGURE:
4
A4

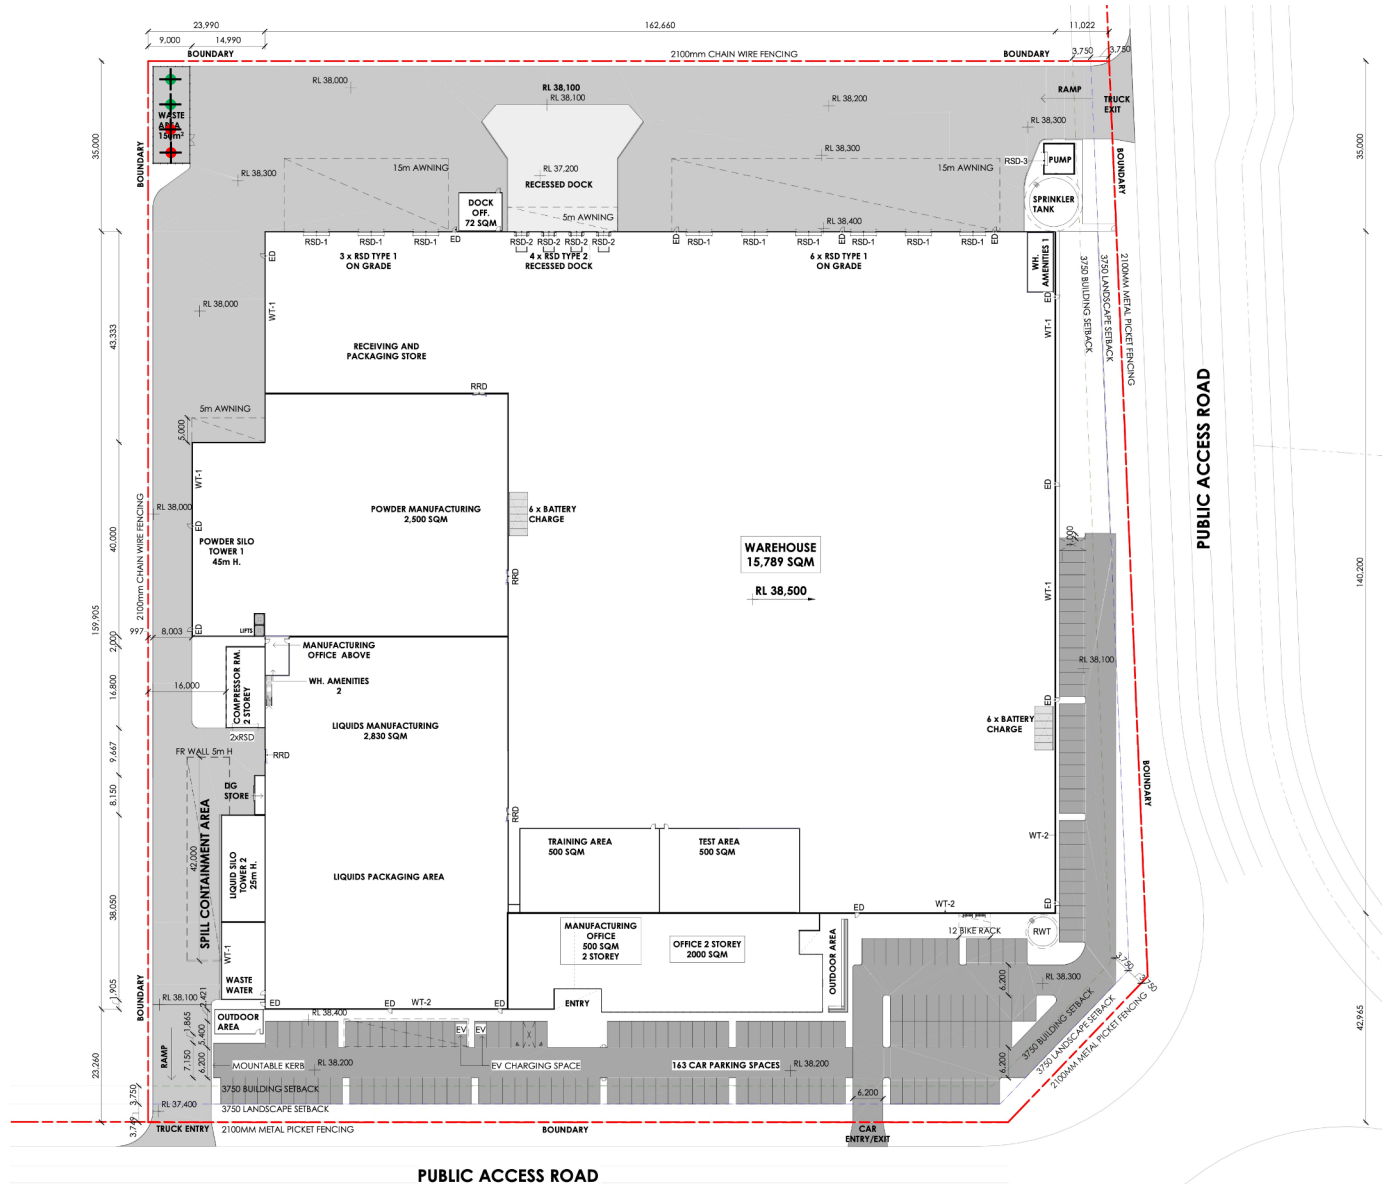

SCALE: DRAWN TO SCALE AS SHOWN

Not To Scale

NORTH

LEGEND:

Site Boundary

Image courtesy of Google & Six Maps



REV: A
DATE: 13/08/2021
DRAWN: GP
APPROVED: GP
STATUS: Final
DWG NO:

CLIENT: **Fraser's & Altis**
PROJECT: **657-769 Mamre Road
Kemps Creek, NSW**
PROJECT NUMBER: LG2042.01

TITLE: **Operational Waste Bin Plan**

FIGURE:

5

A4
