



**EROSION & SEDIMENT CONTROL**

1. THIS PLAN SHALL BE READ IN CONJUNCTION WITH THE ARCHITECTURAL AND ENGINEERING PLANS AND ANY OTHER PLANS OR WRITTEN INSTRUCTIONS THAT MAY BE ISSUED
2. THE CONTRACTOR SHALL ENSURE THAT ALL SOIL AND WATER MANAGEMENT WORKS ARE LOCATED AS SHOWN ON THIS DRAWING.
3. PROTECT ALL NEW PITS FROM SEDIMENT INFILTRATION PROGRESSIVELY, AS THEY ARE CONSTRUCTED.
4. ALL DOWNSTREAM STORMWATER PITS ARE TO BE PROTECTED FROM SEDIMENT INFILTRATION DURING CONSTRUCTION.
5. ALL SUB-CONTRACTORS ON SITE SHALL BE MADE AWARE OF THEIR RESPONSIBILITIES IN MINIMISING THE POTENTIAL FOR SOIL EROSION AND POLLUTION TO WATER COURSES AND WHERE PRACTICAL, THE SOIL EROSION HAZARD ON THE SIDE SHALL BE KEPT AS LOW AS POSSIBLE. TO ACHIEVE, WORKS SHOULD BE CARRIED OUT AS FOLLOWS.
6. 1) INSTALL ANY NECESSARY SECURITY/BOUNDARY FENCES FOR THE SITE.  
2) CONSTRUCT 'SILT' FENCING AS DETAILED ALONG BOTH DOWNSLOPE BOUNDARIES.
7. DURING WINDY WEATHER, LARGE UNPROTECTED AREAS SHALL BE KEPT MOIST (NOT WET) BY SPRINKLING WITH WATER TO KEEP DUST UNDER CONTROL.
8. FINAL SITE LANDSCAPING SHALL BE UNDERTAKEN AS SOON AS POSSIBLE, AND WITHIN TWENTY WORKING DAYS FROM COMPLETION OF CONSTRUCTION ACTIVITIES.
9. SAND USED IN THE CONCRETE CURING PROCESS SHALL BE REMOVED ASAP, AND WITHIN TEN WORKING DAYS FROM PLACEMENT.

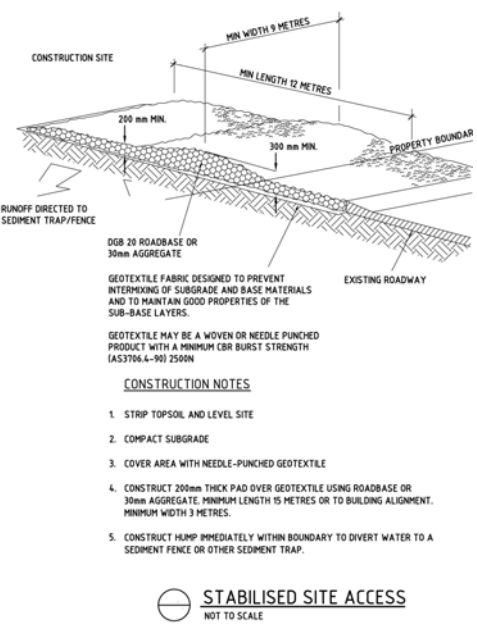

10. WATER SHALL BE PREVENTED FROM ENTERING THE PERMANENT DRAINAGE SYSTEM, UNLESS IT IS RELATIVELY SEDIMENT-FREE; ie. the CATCHMENT AREA HAS BEEN LANDSCAPED AND/OR ANY LIKELY SEDIMENT HAS BEEN FILTERED THROUGH AN APPROVED STRUCTURE.
11. TEMPORARY SOIL AND WATER MANAGEMENT STRUCTURES SHALL BE REMOVED ONLY AFTER THE LANDS THEY ARE PROTECTING ARE REHABILITATED.
12. THE CONTRACTOR SHALL PROVIDE ACCEPTABLE RECEPTORS FOR CONCRETE & MORTAR SLURRIES, PAINTS, ACID WASHINGS, LIGHT-WEIGHT WASTE MATERIALS AND LITTER.
13. RECEPTORS FOR CONCRETE AND MORTAR SLURRIES, PAINTS, ACID WASHINGS, LIGHT-WEIGHT WASTE MATERIALS AND LITTER ARE TO BE EMPTIED AS NECESSARY. DISPOSAL OF WASTE SHALL BE IN A MANNER APPROVED BY THE SITE SUPERINTENDENT.
14. EVERY WEEK, FOR THE DURATION OF WORKS THE CONTRACTOR SHALL INSPECT THE SITE FOR THE FOLLOWING ITEMS:  
- ENSURE DRAINS OPERATE EFFECTIVELY, AND INITIATE REPAIR OR MAINTENANCE AS REQUIRED.  
- REMOVE SPILLED SAND (OR OTHER MATERIALS) FROM HAZARD AREAS, INCLUDING LANDS CLOSER THAN 2 METRES FROM AREAS OF CONCENTRATED OR HIGH-VELOCITY FLOWS SUCH AS WATERCOURSES, OVERLAND FLOW PATHS, GUTTERS, PAVED AREAS, DRIVEWAYS AND ROADS.
15. CONSTRUCT ADDITIONAL EROSION AND/OR SEDIMENT WORKS IS NECESSARY TO ENSURE THE DESIRED PROTECTION IS GIVEN TO DOWNSLOPE LANDS AND WATERWAYS, ie: MAKE ONGOING CHANGES TO THE PLAN.
16. MAINTAIN EROSION AND SEDIMENT CONTROL MEASURES IN A FUNCTIONING CONDITION UNTIL ALL EARTHWORK ACTIVITIES ARE COMPLETED AND THE SITE REHABILITATED.
17. REMOVE TEMPORARY SOIL CONSERVATION STRUCTURES AS A LAST ACTIVITY IN THE REHABILITATION PROGRAM.

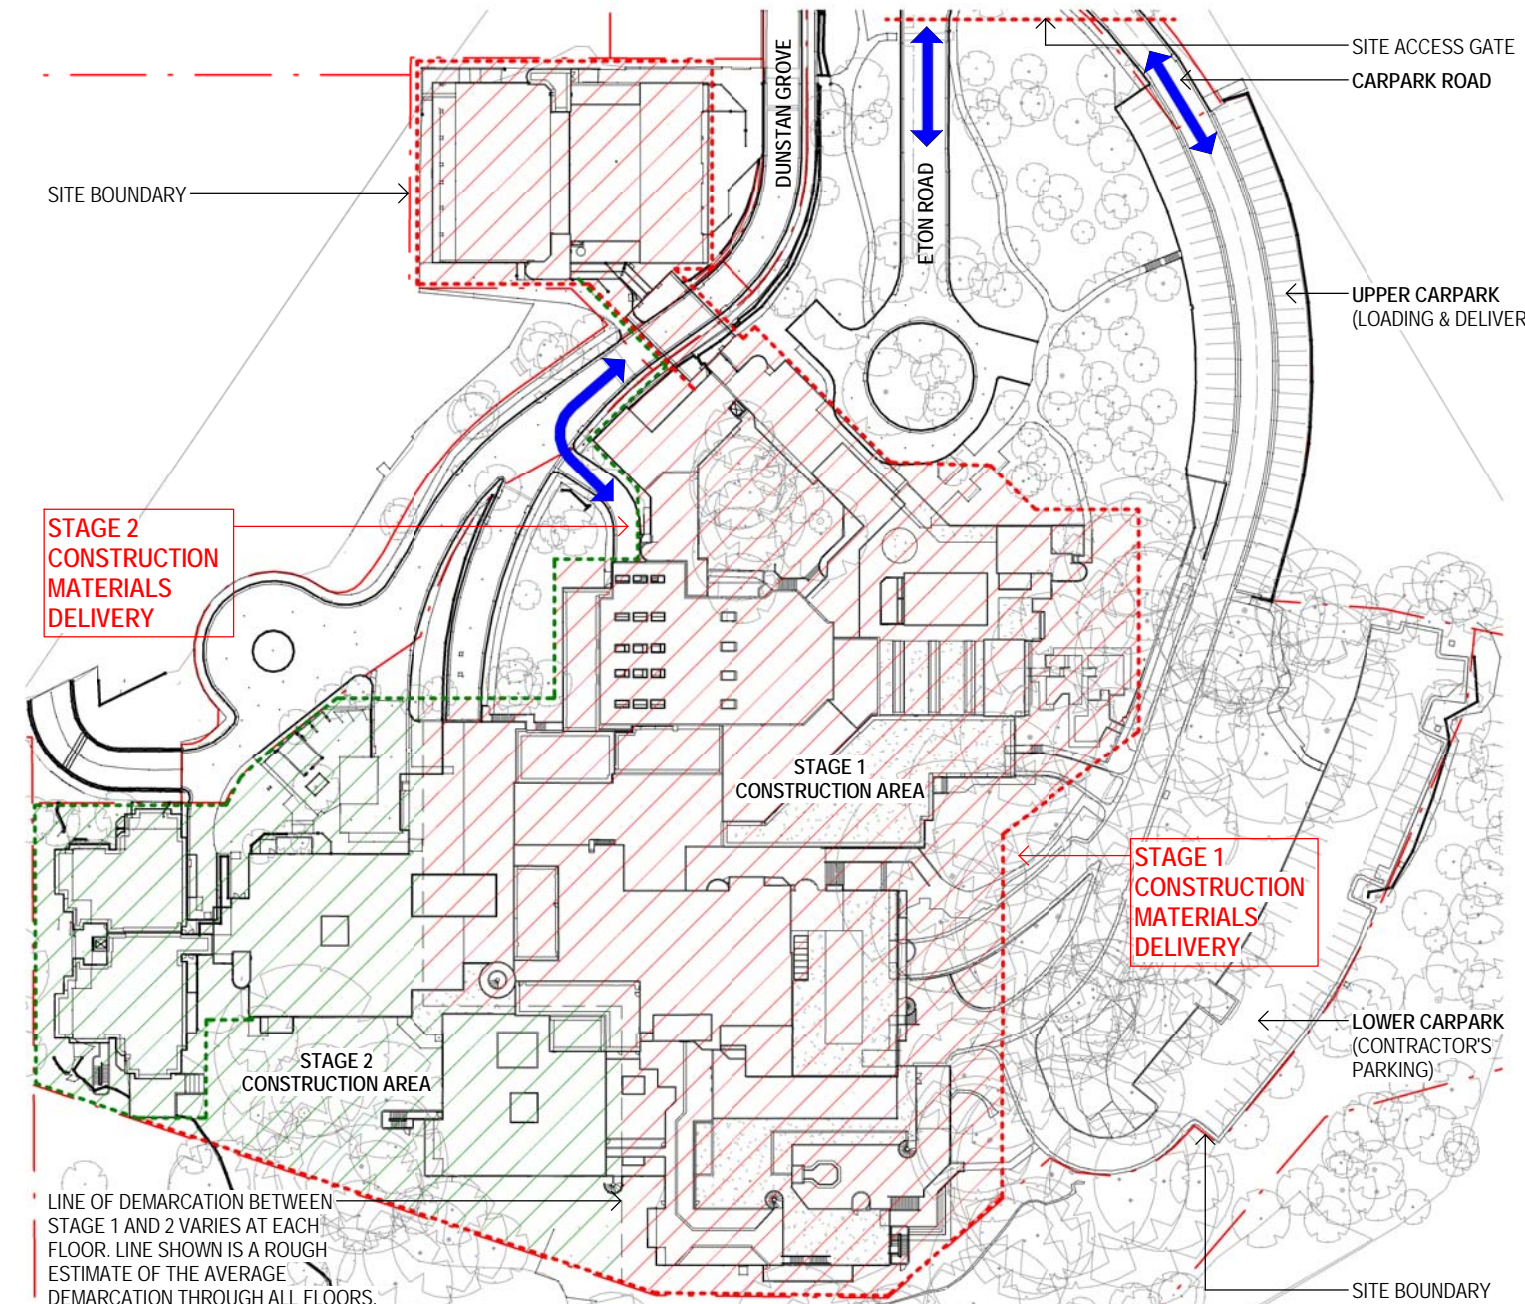

**CONSTRUCTION SITE PLAN & SITE ACCESS**

**CONSTRUCTION TRAFFIC MANAGEMENT PLAN NOTES**

- Construction Activity:**
1. The key proposed building works involve demolition of internal fixtures and the rebuilding of internal fixtures to the new room layouts. No major external works are proposed.
  2. The Contractor's compound will be set up within the existing building.
  3. The upper carpark will be available for site drop off, loading and deliveries.
  4. The lower carpark will be available for Contractors onsite parking.
- Access:**
1. Site Access: Vehicular Access to and from the site shall be from Eton Road. The site access gate will be set up at Eton Road southern end where the junction forks to the lower carpark. Access to Dunstan Grove and Shout Ridge Road shall be unaffected.
  2. Road Access: The main arterial road to the North East of the site is the Pacific Highway and to the South West is Lady Game Drive, with Grosvenor Road used as the main link road between the two. See the Construction traffic vehicle route diagram.
- Traffic Management:**
1. Local Impact: The site is accessed by the existing road network and no significant impact to the local traffic or the local environment is envisaged.
  2. Traffic Control: Disruption to all road users during the construction period would be kept to a minimum.

For further information see Arup Traffic and Transport Assessment dated 23 March 2017 - Section 10, Outline Construction Traffic Management Plan.

**SITE NOTES**

1. SITE FENCE TO ENCOMPASS FULL SITE BOUNDARY.
2. ALL ACCOMMODATION / CRANEAGE TO BE CONTAINED WITHIN THE SITE.
3. TRAFFIC CONTROLS IN PLACE FOR TRUCKS ENTERING / EXITING THE SITE.
4. SPECIFIC TP2 / MEASURES TO BE IDENTIFIED FOR TREES TO BE RETAINED.

**LEGEND**

- TEMPORARY STAGE 1 SITE FENCE
- TEMPORARY STAGE 2 SITE FENCE
- SITE ACCESS
- /// STAGE 1 CONSTRUCTION AREA
- /// STAGE 2 CONSTRUCTION AREA



**LOCATION PLAN & CONSTRUCTION VEHICLE ROUTES**

Copyright Designinc Sydney Pty Limited  
 This drawing is protected by copyright. All rights are reserved. Unless permitted under the Copyright Act 1968, no part of this drawing may in any form or by any means be reproduced, published, broadcast or transmitted without the prior written permission of the copyright owner.

**Please note**  
 If the status of this drawing is not signed off For Construction it may be subject to change, alteration or amendment at the discretion of Designinc Sydney Pty Limited. If so, Designinc Sydney Pty Limited is not liable for any loss, damage, harm or injury whether special, consequential, direct or indirect, suffered by you or any other person as a result of your use of this drawing for construction purposes.

Figured dimensions take preference to scale readings. Verify all dimensions on site.  
 Refer any discrepancies to the Architect for decision before proceeding with the work.

**Nominated Architects**  
 Anthony Quat 5421 | Sandeep Amin 7337 | Ian Armstrong 7290 | Richard Does 8126

No	DATE	REVISIONS	BY
A	29/03/2017	PRELIMINARY ISSUE	HC
B	31/03/2017	ISSUED FOR APPROVAL	HC

CONSULTANTS	TRAFFIC ENGINEER	ARUP	Ph: (02) 9320 9320
	SERVICES ENGINEER	ERBAS AND ASSOCIATES	Ph: (02) 9437 1022
	FIRE ENGINEER	AFFINITY FIRE ENGINEERING	Ph: (02) 9194 0590
	CIVIL AND STRUCTURAL ENGINEER	BIRZULIS ASSOCIATES	Ph: (02) 9555 7230
	BCA CONSULTANT	BCA LOGIC	Ph: (02) 9411 5380
	QUANTITY SURVEYOR	WILDE AND WOOLLARD	Ph: (02) 9411 2777
	PROJECT MANAGER	SAVILLS	Ph: (02) 8215 8888

**ARCHITECT**  
 DesignInc | Lacoste + Stevenson | bmc2  
 architects in association

Designinc Sydney PTY LIMITED ACN 003008820  
 L12 / 77 PACIFIC HWY NORTH SYDNEY NSW 2060 AUSTRALIA  
 PO BOX 651 NORTH SYDNEY NSW 2059 AUSTRALIA  
 T +612 8905 7100 F +612 8905 7199  
 E sydney@sydney.designinc.com.au www.designinc.com.au  
 Architecture Urban Design Interiors

**CLIENT**  
 NSW GOVERNMENT | Education

**PROJECT**  
 LINDFIELD LEARNING VILLAGE  
 Eton Road,  
 Lindfield NSW 2070

**TITLE**  
 INDICATIVE CONSTRUCTION TRAFFIC MANAGEMENT PLAN

DRAWN BY	HC	REVISION
SCALES	NTS @A3	B
PLOT DATE	29/03/2017	
PROJECT NO.	S151441	
DRAWING NO.	DA-101	
DRAWING STATUS FOR APPROVAL	REVIEWED BY	SIGNATURE
	JU	

Completion of the Drawing Status is evidence the design has been verified as conforming to the requirements of the Project M.S. Plan. Initiating the 'Drawn By' box confirms that this drawing has been prepared in conformity with Designinc Sydney M.S. procedures.

**DEVELOPMENT APPLICATION**
