

**Kyeemagh Public School (SSD 9391): Submission of Construction Soil and Water Management Sub-Plan (CSWMSP) in accordance with Condition B17**

Condition	Condition requirements	Document reference
<b>B17</b>	The Applicant must prepare a Construction Soil and Water Management Sub-Plan (CSWMSP) and the plan must address, but not be limited to the following: (a) be prepared by a suitably qualified expert, in consultation with Council;	SSD 9391 - B17 - CSWMSP - Birzulis - 19 Jun 2020 Appendix B (CV of author) & C Consultation record and evidence
	(b) describe all erosion and sediment controls to be implemented during construction; as a minimum, in accordance with the publication Managing Urban Stormwater: Soils & Construction (4th edition, Landcom 2004) commonly referred to as the 'Blue Book'.	Appendix D
	(c) include an Acid Sulfate Soils Management Plan, if required, including measures for the management, handling, treatment and disposal of acid sulfate soils, including monitoring of water quality at acid sulfate soils treatment areas.	Section 2.2, Appendix A
	(d) provide a plan of how all construction works will be managed in a wet-weather events (i.e. storage of equipment, stabilisation of the Site);	Section 5.4 & Appendix D
	(e) detail all off-Site flows from the Site; and	Section 2.5, & Appendix D
	(f) describe the measures that must be implemented to manage stormwater and flood flows for small and large sized events, including, but not limited to, 1 in 5-year ARI and 1 in 100-year ARI).	Section 5.4



**BIRZULIS ASSOCIATES Pty Ltd**  
Consulting Structural + Civil Engineers

ACN 003 797 911 ABN 99 003 797 911

**Sydney Office**

583 Darling Street, Rozelle NSW 2039

Telephone: 9555 7230

Email: office@birzulisassociates.com

**Newcastle Office**

105 Merewether Street, Merewether NSW 2291

Telephone: 4049 4855

Email: office@birzulisassociates.com

# **CONSTRUCTION SOIL AND WATER MANAGEMENT PLAN**

***OUR REF:7863***

**KYEEMAGH PUBLIC SCHOOL  
JACOBSON AVENUE,  
KYEEMAGH NSW 2261**

PREPARED BY: CAMERON AMRI

DATE: 03/07/2020

REVISION: C

**DIRECTORS**

B Fimmano B.E. (Hons), M.I.E. Aust., C.P.Eng.

M A Grogan B.E., M.Eng., M.I.E. Aust., C.P.Eng.

**ASSOCIATE DIRECTOR**

P W Grogan B.E. (Hons), M.E.(Struct), M.I.E. Aust., C.P.Eng.


**CONSULTANT**

A J Birzulis OAM, B.E., M.Eng. Sc., F.I.E. Aust., C.P.Eng.



## DOCUMENT VERIFICATION

<b>Project Title</b>	<b>Kyeemagh Public School</b>
<b>Document Title</b>	Construction Soil and Water Management Plan Report
<b>Project No.</b>	7863
<b>Description</b>	Construction soil and water management plan
<b>Client Contact</b>	Taylor Constructions

	<b>Name</b>	<b>Signature</b>
<b>Prepared by</b>	Cameron Amri	
<b>Checked by</b>	Michael Grogan	
<b>Issued by</b>	Michael Grogan	

## REPORT DELIVERABLES

This report is to meet condition B17 of the SSD Conditions.

This report shall be referenced to meet condition B12 & B17 of the SSD Condition of application number SSD 9439.

<b>Condition</b>	<b>Condition requirements</b>	<b>Document reference</b>
<b>B17</b>	The Applicant must prepare a Construction Soil and Water Management Sub-Plan (CSWMSP) and the plan must address, but not be limited to the following:	
	be prepared by a suitably qualified expert, in consultation with Council;	Appendix B & Appendix C.
	describe all erosion and sediment controls to be implemented during construction including, as a minimum, measures in accordance with the publication Managing Urban Stormwater: Soils & Construction (4th edition, Landcom 2004) commonly referred to as the 'Blue Book'.	Appendix D
	include an Acid Sulfate Soils Management Plan, including measures for the management, handling, treatment and disposal of acid sulfate soils, including monitoring of water quality at acid sulfate soils treatment areas;	Section 2.2 & Appendix A
	provide a plan of how all construction works will be managed in a wet-weather events (i.e. storage of equipment, stabilisation of the Site);	Section 5.4 & Appendix D
	detail all off-Site flows from the Site; and	Section 2.5 & Appendix D
	describe the measures that must be implemented to manage stormwater and flood flows for small and large sized events, including, but not limited to 1 in 1-year ARI and 1 in 5-year ARI.	Section 5.4

<b>B12</b>	Management plans required under this consent must be prepared in accordance with relevant guidelines, and include:	
	(a) detailed baseline data;	Section 2
	(b) details of: (i) the relevant statutory requirements (including any relevant approval, license or lease conditions);	Section 1.1
	(ii) any relevant limits or performance measures and criteria; and	Section 6

(iii) the specific performance indicators that are proposed to be used to judge the performance of, or guide the implementation of, the development or any management measures;	Section 6.5
(c) a description of the measures to be implemented to comply with the relevant statutory requirements, limits, or performance measures and criteria;	Section 6 & Appendix D
(d) a program to monitor and report on the: (i) impacts and environmental performance of the development;	Section 6.5.5 & 6.5.6 & 6.5.7
(ii) effectiveness of the management measures set out pursuant to paragraph (c) above;	6.5.7
(e) a contingency plan to manage any unpredicted impacts and their consequences and to ensure that ongoing impacts reduce to levels below relevant impact assessment criteria as quickly as possible;	Appendix A
(f) a program to investigate and implement ways to improve the environmental performance of the development over time;	Section 5
(g) a protocol for managing and reporting any: (i) incident and any non-compliance (specifically including any exceedance of the impact assessment criteria and performance criteria);	Section 6.4 & 6.5.5 & 6.5.6
(ii) complaint;	6.5.7
(iii) failure to comply with statutory requirements; and	6.5.6
(h) a protocol for periodic review of the plan and any updates in response to incidents or matters of non-compliance	6.5.5

## DOCUMENT HISTORY

Date	Revision	Issued to	Description
03/07/20	-A	DWP Suters	DRAFT Issue
30/07/20	-B	DWP Suters	DRAFT Issue
30/07/20	-C	DWP Suters	For CC1

## Table of Contents

Table of Contents .....	5
<b>1</b> .....	6
1 EXECUTIVE SUMMARY .....	6
1.1 PLANNING RELEVANCE, LEGISLATION & ACT .....	7
2 EXISTING CONDITIONS .....	10
2.1 LOCATION .....	10
2.2 ACID SULFATE SOILS .....	12
2.3 GROUND WATER PROTECTION .....	12
2.4 TEMPORARY EROSION AND SEDIMENT CONTROL BASINS .....	13
2.5 EXISTING STORMWATER DISCHARGE POINTS .....	14
3 GENERAL INSTRUCTIONS .....	14
4 LAND DISTURBANCE CONDITIONS .....	15
5 ASPECTS, IMPACTS AND RISKS .....	15
5.1 STORMWATER QUANTITY .....	15
5.2 STORMWATER QUALITY .....	16
5.3 FLOODING .....	17
5.4 WET WEATHER EVENT MANAGEMENT .....	17
6 CONSTRUCTION IMPACTS .....	20
6.1 EROSION CONTROL .....	20
6.2 SEDIMENT MANAGEMENT .....	20
6.3 STOCKPILE STABILISATION .....	20
6.4 HAZARDOUS MATERIALS .....	21
6.5 MANAGEMENT MEASURES .....	21
6.5.1 Topsoil management .....	21
6.5.2 Wind Erosion Management .....	21
6.5.3 Site Drainage .....	21
6.5.4 Revegetation Earthworks .....	21
6.5.5 Maintenance Controls .....	22
6.5.6 Auditing .....	22
6.5.7 Responsibility .....	22
7 REFERENCES .....	23
8 APPENDIX A – Acid Sulfate Soil Management Plan .....	24

9	Appendix B – CV of Engineer .....	25
10	Appendix C – Evidence of Consultation with Council.....	26
11	Appendix D – Erosion and Sediment Control design drawings .....	28

# 1

## 1 EXECUTIVE SUMMARY

Birzulis Associates have been commissioned by Taylor Constructions to prepare a Construction Soil and water Management Plan (CSWMP) for the proposed stage 1 and stage 2 construction at Kyeemagh Public School. This report addresses the site conditions and the management of such site conditions relevant to soil and water management in accordance with the requirements of the relevant Council DCP/SSD Guidelines.

The aim of this CSWMP is to address all risks associated with the water quality, erosion and sedimentation ensuring these are considered and managed effectively during construction. This reports aims to deliver a best-practice control and procedures to minimise or avoid erosion/sedimentation impacts and potential impacts to water quality.

The CSWMP will address and satisfy the following objectives:

- Relevant environmental legislation as it applies to this project
- Summarise and address potential water quality impacts on the environment from the proposed works on the proposed site
- Document procedures to control these possible and foreseeable environmental impacts.
- Ensure and demonstrate compliance to relevant legislation
- Ensure there are no adverse environmental impacts to the waterways and surrounding environment as a result of the proposed works.
- Address and comply with water quality discharge requirements for the site.
- Prevent pollution of surface water by sedimentation and excessive erosion of the site.
- Ensure staff and relevant construction personnel and procedures and an understanding of what is required to maintain and implement the required water quality elements and controls.
- Document all controls and mitigation for a 1 in 100 year flood event at the site.

Stage 1 of the proposed works involves the demolition of the existing buildings to the North-East of the site and construction of the buildings on that half of the site.

Stage 2 of the proposed works will occur approximately after practical completion (PC) of the stage 1 works and the demolition of the existing buildings to the South-West half of the site.

Both stages of the development will require:

- Demolition of the existing structures and removal of waste.
- Removal of topsoil and vegetation.
- Civil works and stormwater drainage works including connecting to the existing Council trunk drainage system.
- Construction of temporary roadway and turning circle for construction vehicles/equipment within the envelope of the stage works.
- Remediation of temporary works and construction of hardstand pavements
- Construction of landscaping works

## **1.1 PLANNING RELEVANCE, LEGISLATION & ACT**

The following legislation and regulatory framework relating to construction soil and water management are outlined below.

Immediate SSD Planning Requirement to be satisfied:

- As stipulated in the State Significant Development Conditions of Consent. Condition B17 required prior to the commencement of construction.

### **Environmental Planning and Assessment Act 1979 & Environmental Planning & Assessment Regulation 2000.**

This Act and regulation establishes a system of environmental planning and assessment of development proposals for the State. This project has been assessed and approved under Section 89E of the Environmental Planning and Assessment Act 1979.

Project Relevance; Approval process for a legal Consent to develop and considerations for such.

### **Protection of the Environment Operations Act 1997**

This Act includes all the controls necessary to regulate pollution and reduce degradation of the environment, provides for licensing of scheduled development work, scheduled activities and for offences and prosecution under this Act.

Project Relevance; This Act is of high relevance to the Project as it provides for the issuing of environmental protection notices to control work and activities not covered by licences. Section 148 of the Act requires a pollution incident-causing or threatening material harm to the environment to be notified to the EPA and other authorities immediately.



### **Contaminated Land Management Act 1997**

This Act provides for a process to investigate and remediate land that has been contaminated and presents a significant risk of harm to human health. Section 60 of the Act is a “Duty to Report Contamination”. This duty applied to owners of land and persons who become aware that their activities have contaminated the land.

Project Relevance; The relevance of this Act will be in the event that suspected or potentially contaminated ground is found during construction activities.

### **Commonwealth Environment Protection and Biodiversity Act 1999**

The main purpose of this Act is to provide for the protection of the environment especially those aspects that are of national environmental importance and to promote ecological sustainable development. The Act binds the Crown. Do not take, use, keep or interfere with “nationally significant” cultural and natural resources, protected wildlife and protected plants without approval.

Project Relevance; This Act is of little relevance to this project as it has been determined not to trigger the provisions of the act.

### **Soil Conservation Act 1938**

This Act makes for the provision for the conservation of soil resources, farm water resources and the mitigation of erosion. The Act is binding on the Crown; however, the Crown is not liable for prosecution. The Act provides for notification in the government gazette catchments where erosion is liable to cause degradation of rivers and lakes (i.e. protected land).

Project Relevance; This Act has low relevance as the site is not located within “protected land”. Further, such notification has not been given to the owner of the land.

### **Water Management Act 2000 & Water Management (General) Regulation 2004**

This Act and Regulation provide for the protection, conservation and ecologically sustainable development of water sources of the State and in particular to protect, enhance and restore water sources and their associated ecosystems.

Project Relevance; This Act has no direct relevance at this time to the construction work under this contract. The project approval does not trigger the provisions of this Act

### **Water Act 1912**

This Act provides for licences to extract water for construction purposes either from surface or artesian sources. Should construction water be extracted from surface (other than sedimentation ponds) or artesian sources, a licence will be required.

Project Relevance; This Act has no relevance as it is not proposed that construction water will be obtained from surface (for example, creeks, lakes) or artesian sources.

### **Rivers and Forseshores Improvement Act, 1948**

The Rivers and Foreshores Improvement Act, 1948, is administered by DIPNR for regulating operations involving excavation and fill within the immediate vicinity of coastal rivers, lakes and estuaries. Under this Act, a Part 3A Permit is required for the undertaking of works within 40 metres of the bed and banks of a watercourse. By late 2003, the Water Management Act 2000 (WMA) will have repealed the Rivers and Foreshores Improvement Act, 1948 (RFIA). When this occurs, activities that require a Permit under Part 3A Approvals under the RFIA will require Controlled Activity Approvals under the WMA

Project Relevance; Nil as not within 40m of the bed and banks of a watercourse.

## 2 EXISTING CONDITIONS

### 2.1 LOCATION

The site is located at 30A Jacobson Avenue, Kyeemagh NSW 2216 is broken up into two lots D.Ps (D.P.120095 & D.P. 335734). The current site is the operating site of Kyeemagh Public School. The site is generally sparsely planted and with minimal hard pavements.


To the North-West the site abuts a previous townhouse villa style development. To the South-East the site abuts Beehag Street. To the South-East the site abuts Jacobson Avenue. To the North-East the site abuts the school childcare centre which operates on the site and is not proposed to be altered. The site falls from the West to the South East at approximately 4%.

The total site area is 10 329m<sup>2</sup>.

The site is shown below represented as Figure 2.1



**Figure 2.1.1 – Total D.P. Envelope**

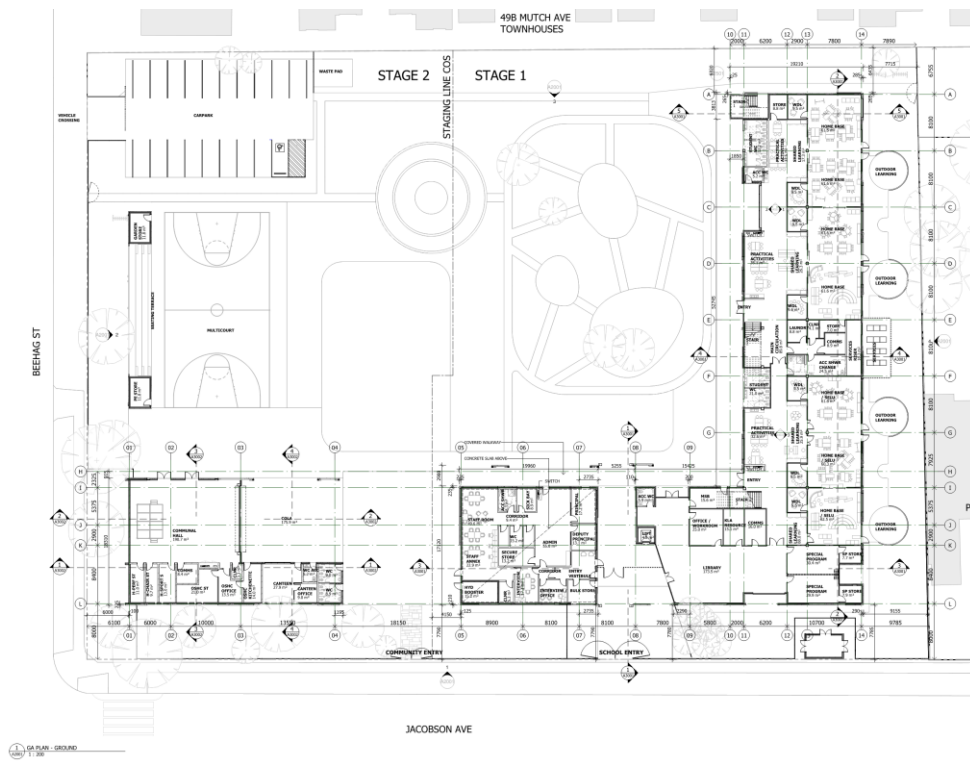

**Figure 2.1.2 - Overall Site Plan**



**Figure 2.1.3 - Aerial View of Kyeemagh Public School (Source: Google Map 2020)**

## **2.2 ACID SULFATE SOILS**

A review of the Geotechnical report completed by Cardno showed soil test pH levels from 6.1 to 7.7 which is considered neutral. Despite this, should acid sulfate soils be encountered they shall be dealt with in accordance with the Acid Sulfate Soils Management Plan located as Appendix A.

## **2.3 GROUND WATER PROTECTION**

Generally possible sources of ground water contamination can be linked to :

- Industrial effluent and manufacturing wastes
- Leaking underground storage tanks and pipe lines (not stormwater/rainwater)
- Landfill stockpiles or contaminated soil producing leachate '
- Intensive agricultural fertiliser and pesticide use or waste generation
- Contamination from septic tanks and from sewerage and wastewater lagoons

- Mining industry processes and wastes
- Contamination from wells
- Urban stormwater
- Atmospheric fallout
- Inter-aquifer contamination by alteration of flow
- Chemical storage

We assess the operation use of the site is not such as to generate a risk to ground water contamination subject to correct chemical storage in line with MSDS's and safe work guidelines.

## **2.4 TEMPORARY EROSION AND SEDIMENT CONTROL BASINS**

The requirement for sediment basins is carried out using a RUSLE calculation.

$$A = R K L S C P$$

Where A = Computed soil loss (tonnes/ha/yr)

R = rainfall erosivity factor = 2075

K = slope erodibility factor

LS = Slope length/gradient factor

C = ground cover factor

P = practice factor

Variable	Value	Remark
Rainfall Erosivity (R)	3075	From literature review
Soil erodibility (K)	0.06	Figure A3, The Blue Book
Site slopes av	Pre- 0.8% post 0.8%	
Slope Length (LS)	0.52	Table A1, The Blue Book
Erosion control practice (P)	1.3	Table A2, The Blue Book
Ground cover (C)	1.0	50% grass cover as construction completed in stages Figure A5, The Blue Book
Potential Erosion Hazard	Low	Figure 4.6, The Blue Book
Rainfall Zone	Zone 1	Figure 4.9, The Blue Book
Soil Density (kN/m <sup>3</sup> )	19	From geotechnical report
Calculation soil loss A (t/ha/yr)	125	

Soil Loss Class	1 (erosion hazard = very low)	Table 4.2, The Blue Book
Soil loss (m <sup>3</sup> /ha/yr)	96	
<b>Is a sediment basin required</b>	<b>No</b>	

Where the soil loss from the catchment/s is less than 150m<sup>3</sup>/ha/yr then a sediment is not required as per Section 6.3.2.d of the Blue Book.

Nil

## 2.5 EXISTING STORMWATER DISCHARGE POINTS

The site operating as a public school has an existing pit and pipe system with an existing discharge to the Council trunk drainage system on Jacobson Avenue (located in the stage 2 envelope of works). The site also has a small depression within the site which normally would contribute to saturation of the soil however is not considered to do so given the high permeability of the soil (marine sand).

The low point of the site is located at the Eastern corner. The low point of the site is not proposed to be altered from the current condition. The overland flow water that discharges the site from this low point falls to Jacobson Avenue.

The existing stormwater elements from a visual survey undertaken revealed the onsite system to be in poor condition and blocked in many cases. We are proposing to clean the existing system for the construction works to not be surcharged by storm flows during the Stage 1 works.

The indicative external stormwater network is shown in **Error! Reference source not found.** and is the Council trunk drainage system and is believed to be in a satisfactory condition.

## 3 GENERAL INSTRUCTIONS

This SWMP shall be read in conjunction with the latest engineering plans which have the Sediment and Erosion Control Plan and details, any other reports or design drawings and or any written instructions that concern themselves with water management of the site during construction and during the operational phase of the site.

The Principle Contractor shall ensure that all soil and water management works recommendations are incorporated in works and undertaken in accordance with the Blue Book.



## 4 LAND DISTURBANCE CONDITIONS

Where practical, the soil erosion onsite will be as recommended below so the hazard will be as low as reasonably possible.

Land Use	Scope	Remarks
Construction areas	Disturbance to be no greater than within 5m from the edge of any essential construction activity shown on the plans	Barrier fencing and sediment fencing or similar fencing to be used so all workers can clearly identify these zones were appropriate.
Access areas	Maximum 6m in width	Site manager to define the zones onsite and all workers to clearly be able to identify these zones
Remaining Lands	Fenced off	Identified by barrier fencing

## 5 ASPECTS, IMPACTS AND RISKS

### 5.1 STORMWATER QUANTITY

Normally the removal of existing stormwater elements during construction increases the surface flow volumes and velocities on a site. This can then increase movement of debris silt and scouring of water channels.

DRAINS software was used to generate runoff modelling that represents the existing and post development stormwater conditions. A summary of peak flows is shown below.

As the site discharge is located in stage 2 this is advantageous. There should be no significant change to the site runoff during construction as the envelope of the buildings being demolished in stage 1 is comparatively small. The intent is to maintain the existing stormwater pipe discharge from the site



for the majority of the buildings (which are in the stage 2 envelope) while the stage 1 works are constructed. As part of the stage 1 works a new stormwater discharge is to be constructed and a stage 1 infiltration system. Based on storm events up to the 50 year storm the infiltration tank will not overflow to the new connection. As such we consider stormwater quantity to be reduced post construction and during construction.

## **5.2 STORMWATER QUALITY**

Bulk earth works, vegetation clearing activities during construction phases, if not managed adequately, can lead to increased soil displacement. This element is considered adequately managed in the Sediment and Erosion Control Plan and relevant details.

The post construction stormwater quality runoff for the relevant catchments are required to meet requirements for Council compliance and for GreenStar Compliance.

The construction is proposing to meet a 2 point target under Credit 26 Stormwater for this project which places the pollution reduction target as per Column B shown below.

<b>Aim of Credit</b>	To reward projects that minimise peak storm water outflows from the site and reduce pollutants entering the public stormwater infrastructure or other water bodies.		
<b>Compliance Criteria</b>	All stormwater discharged from the site must meet the Pollution Reduction Targets outlined in column B or C as a minimum of the following table:		
	<b>Pollutants</b>	<b>Reduction Target (% of the typical urban annual load)</b>	
		<b>A</b>	<b>B</b>
	Total Suspended Solids (TSS) <sup>1</sup>	80	80
	Gross Pollutants	85	90
	Total Nitrogen (TN) <sup>2</sup>	30	45
	Total Phosphorus (TP) <sup>2</sup>	30	60
	Total Petroleum Hydrocarbons <sup>3</sup>	60	90
	Free Oils <sup>3</sup>	90	90

### 5.3 FLOODING

Construction works can sometimes generate additional site runoff contributing to flooding of adjacent or downstream sites during significant rainfall events or in the absence of relevant flood protection measures such as temporary water containment.

This has been provided for this site using the two infiltration tanks. As such the construction stormwater runoff will be less than the current site runoff.

The site flood level is RL 2.65m for the 100 year ARI storm event which places the site above this level meaning the site material stockpile locations will be safe from significant migration during this event.

### 5.4 WET WEATHER EVENT MANAGEMENT

As noted above the site is unaffected by flooding up to the 100 year even based on the site levels. This will be further safe guarded by the raised site levels as per the approval.

There is a risk during large rain events that water runoff will result in sediment washing off site and or damage to the sediment and erosion control systems in place.

The following mitigation measures will be implemented for the following scenarios

### **General Management**

- forecast for heavy rain and make decisions on the following accordingly.
- storage of hazardous materials and equipment away from flow paths and known drainage channel
- layout of site compound facilities to take into consideration of the flow paths which are shown on the sediment and erosion control plans and the civil drawings.
- ensure evacuation routes are kept clear during high risk periods based on weather and storm forecasts.
- ensure loose materials, fuel, chemicals and equipment can either be secured or removed during a flood event if required
- equipment shall be covered as required if runoff from equipment can be hazardous or create sediment or oil displacement.

### **1-year ARI**

- Brief personnel at prestart
- Review of all current ERSED controls and ensure ESCP is still current
- Stormwater would be managed using the following controls
  - o Sediment fencing
  - o Diversion bunds / swales
  - o Coir logs/ sandbags/ silt socks
- Upstream stormwater runoff is expected to bypass the site using the swale system proposed. Other runoff will be minimum given the moderate infiltration rate and be handled by the ESCP.

### **5 Year ARI**

- Implement as above for the 1-year ARI event
- Ensure all plant and equipment are removed from areas of concentrated flow
- Sedimentation basins maximum capacities will be maintained where practically possible

### **100 Year ARI**

- Implement as above for the 1-year ARI event
- Remove all plant and equipment from site areas where there is potential for inundation
- Perimeter controls are not expected to be breached.
- Flow will be directed to the street for the existing buildings in place prior to commencement of the stage 2 works. There will always be a site connection to the street for site water to be drained based on the stage 1 system or the existing system which is to remain prior to commencement of stage 2 works.

## 6 CONSTRUCTION IMPACTS

### 6.1 EROSION CONTROL

Erosion control is primary to a erosion and sediment control strategy. This can be achieved through:

- Limiting the area of disturbance and only disturbing what is required. Also limiting the time period of disturbance.
- Integrating elements that reduce or control the volume of water moving over surfaces. This includes, diversion through swales and table drains, and piped or lined channels to stabilised outlets.
- Measures to slow the velocity of water over exposed surfaces within the construction area such as hay bail barriers, introducing roughness, flow check measures, textiles, binding compounds or exposed surface protections. Binding products and surface protection can be spray on stabilisers, mulches, blankets, temporary vegetation and permanent progressive landscape construction.

The above is achieved using the correct implementation of the Erosion and Sediment Control Plan shown on the engineering drawings and any other recommendations in this report.

To achieve the requirements of not concentrating water flows which can lead to transportation of sediment off site it is recommended the swales on the stormwater design drawings be constructed as soon as practicable to divert upstream water around the site.

### 6.2 SEDIMENT MANAGEMENT

This is secondary to erosion control in minimising water pollution as a result of construction. Where required sediment basins are generally located at the low points of site discharges.

Requirements for sediment control basins are in accordance with Section 6.3.2.d of the Managing Urban Stormwater: Soils and Construction (the Blue Book). The soil loss from the catchment is less than that required for a sediment basin and as such one is not required.

### 6.3 STOCKPILE STABILISATION

As there is significant volumes of fill being proposed for the site it is foreseeable that material stockpiles will be required unless can be demonstrated as other by the Builder Taylor Constructions. Stockpiles within the site which will be in effect for more than 10 days should be stabilised. As per the Erosion and Sediment Control Plan all stockpiles are to have sediment fences on the downstream

slopes and generally should be located a minimum of 5m from overland flow swales. If unused for 10 days then stockpiles shall also be stabilised in accordance with the below relative to the relevant material in the stockpile:

- Coarse grained stockpiles
  - Downstream perimeter rock armouring.
- Less coarse grained stockpiles
  - Polymer binder application
  - Application of hydro-seed or hydromulch.

## **6.4 HAZARDOUS MATERIALS**

Hazardous material can often be transported to the site for construction purposes or from the site in the form of asbestos removal during demolition works. This will be addressed in accordance with the Construction Waste Management Sub-Plan (CWMSP) condition B16 prepared by others.

## **6.5 MANAGEMENT MEASURES**

### **6.5.1 Topsoil management**

As part of works topsoil is to be stripped and stockpiled for use later in the project. Stopsoil stockpiles shall be treated as per the requirements of stockpiles noted above.

### **6.5.2 Wind Erosion Management**

At a minimum, exposed areas will be watered regularly to minimise dust and water carts to be readily available as this is an ongoing process. Additional watering may be required on windy days.

### **6.5.3 Site Drainage**

As noted above, the swales are to be constructed as soon as practicable and treated in accordance with the above. This will prevent external catchment runoff penetrating the site. A bentonite impregnated geotextile liner will be used (Bentofix or equivalent) in unsealed sections of the working areas. This will form a suitable barrier to prevent contaminants from working areas entering the ground water or contaminating the soil of the site.

### **6.5.4 Revegetation Earthworks**

Areas where earthworks have been completed are to be stabilised within ten days in accordance with the above recommendations. All erosion and sediment control are to remain in place until stabilisation or revegetation is established. All stabilised areas are to be free of vehicle traffic to prevent disturbance.

Stabilisation of earthworks include, but are not limited to the following:

- Mulch covers
- Latex tape sprays
- Bitumen emulsion sprays
- Tarp cover
- Grass seeding

For areas stabilised with seeding, regular watering is required until an effective ground cover has been established. Re-seeding may be required in areas if inadequate coverage.

#### 6.5.5 Maintenance Controls

Erosion and sediment control measures should be inspected and maintained regularly, generally daily and within 24 hours of each rainfall event. The site supervisor should be responsible for this to be undertaken. It is recommended the daily inspection be recorded including the following relevant information:

- Condition of each element noted on the Erosion and Sediment Control Plan
- Any maintenance requirements of each element
- Volume of sediment removed and if the location of the element is appropriate. Disposal method of site trapped sediment.
- Condition of site entry and gravel rip/rap
- Condition of stockpile protection if relevant
- Site stormwater disposal location conditions
- Drains checked to ensure adequate site runoff and for signs of erosion
- Any sediment erosion control linings
- Condition of revegetation works if relevant.

It is recommended these are sent to the Superintendent weekly.

#### 6.5.6 Auditing

Auditing of the above and importing of soil material and controlled fill shall be monitored and tracked in accordance with the CEMP condition B13 of the CoC.

#### 6.5.7 Responsibility

The Contractor is deemed to have the following responsibilities in relation to Soil and Water Management of this site:

- To ensure all works noted above are undertaken as instructed and generally in accordance with the Blue Book (Managing Urban Stormwater – Soils and Construction, Landcom 2004.
- All sub-contractors are made aware of their responsibilities in this area and made accountable.
- Checks are completed in accordance with the above Maintenance Controls (6.5.5)

## 7 REFERENCES

Geotechnical report by Cardno reference 5017190151 dated 23 January 2019

Schematic Design Report – Civil prepared by Birzulis Associates Pty Ltd dated 24 June 2020 revision C

Rockdale LEP 2011 – Part 6.1 Acid sulphate soils

Rockdale DCP 2011

Landcom (2004) Managing Urban Stormwater: Soils and Construction known as the Blue Book



## 8 APPENDIX A – Acid Sulfate Soil Management Plan

<https://majorprojects.planningportal.nsw.gov.au/prweb/PRRestService/mp/01/getContent?AttachRef=SSD-9391%2120190313T012025.244%20GMT>

## 9 Appendix B – CV of Engineer



**CAMERON AMRI**  
**SENIOR CIVIL & STRUCTURAL ENGINEER**

Bachelor of Engineering in Civil Engineering  
University of Technology Sydney

### Professional memberships

Member of the Institution of Engineers, Australia  
Chartered Professional Engineer (CPEng)  
Registered on the National Engineering Register (NER)  
Registered Professional Engineer of Queensland

### Experience

Since completing his degree in 2007, Cameron has worked as a civil structural engineer for MLH, Kneebone & Beretta, E2 Design and for Birzulis Associates Pty Ltd.

### A selection of projects Cameron has been involved in:

#### Aged Care

- HammondGrove, Hammondville
- Scalabrini Village Bexley
- Scalabrini Village Drummoyne
- Scalabrini Village Austral
- Scalabrini Village Chipping Norton
- Scalabrini Village Griffith
- Scalabrini Village Yoogali

#### Religious

- Our Lady of Mount Carmel
- Catholic Parish of Mary Immaculate

#### Education

- Thomas Reddall High School
- Westmead Public School
- Springwood High School

- Chifley Campus
- Parramatta West Public School
- Blacktown Tafe
- Wiley Park Girls High School
- Chester Hill High School
- Doonside High School
- Westfield Sports High
- Ingleburn High School
- Wenona School, North Sydney
- Granville Public School
- Bellevue Hill Public School
- Riverstone High School
- Mount Annan Public School
- Matthew Pearce Primary School
- Mount Druitt Tafe
- NirimbaTafe

## 10 Appendix C – Evidence of Consultation with Council

### **Post Approval – Consultation**

Consultation needs to be meaningful, done with courtesy and respect and be well documented. These are people/ organisations that we need to be building meaningful relationships with.

Conditions of all consent can require consultation with a range of stakeholders. Consultation in the post approval world needs to be well documented to satisfy the condition requirements.

Examples include Council, service providers (eg. Electricity gas etc.), consult with local bus provider and TfNSW.

Read each condition carefully, any reference to consult triggers consultation.

Typically on State Significant Development, there will be a specific consultation condition as to how this piece can be appropriately addressed.

Consultation is not:

- A token gesture
- Done at the end of the piece of work,
- An email to the relevant stakeholder with no response;
- A meeting with the stakeholder with no meeting minutes.

Consultation is:

- Meaningful
- Done prior to the requirement,
- Captures an outcome,
- Identifies matters resolved,
- Identifies matters unresolved,
- Any disagreements are disclosed; and
- How we are going to address unresolved matters?

How to capture all the relevant details on consultation requirements? Any consultation requirement in a condition is required to be accompanied with the following table:

## Post Approval Consultation Record

Identified Party to Consult:	Bayside Council
Consultation type:	Phone and email correspondence
When is consultation required?	During the Design phase, prior to construction
Why	Condition Number B17 and Condition requiring consultation with Council requiring the report be prepared in Consultation with Council.
When was consultation scheduled/held	Phone conversation with 2 July 2020 and email correspondence. Email correspondence on 2 July 2020. Email correspondence on 3 July 2020. Email on 7 July 2020.
When was consultation held	As per the above.
Identify persons and positions who were involved	Christopher Thompson from Bayside Council
Provide the details of the consultation	<p>Phone conversation with the above and the author of this report 2 July 2020 and email discussing the project. Introduction to the type of project and the overall civil design intent. Specifically, the biological control and the infiltration system proposed.</p> <p>Email correspondence on 2 July 2020 with the above and the author of this report sending copy of the civil drawings to Bayside Council including DRAINS file.</p> <p>Email correspondence on 3 July 2020 with the above and the author of this report discussing infiltration system maintenance requirements and access to provide maintenance to infiltration system.</p> <p>Email on 7 July 2020 with the above and the author of this report sending copy of the first version of this report to Council as required under the requirements of Consulting with Council.</p>
What specific matters were discussed?	Biological control, Construction Soil and Water Management Plan, infiltration system types and maintenance, and software modelling.
What matters were resolved?	Infiltration system specific product was approved.
What matters are unresolved?	On phone conversation today Birzuilis has agreed to provide biological control upstream of infiltration system. Please note this is not related to Construction Soil and Water Management Plan. There are no unresolved matters regarding this report. We had to comment on the biological control as it comes up as unresolved in the attached email correspondence. We have verbal confirmation with Christopher Thompson from Bayside Council there are no unresolved matters pertaining to this report. We have agreed to continue consulting regarding the stormwater biological control.
Any remaining points of disagreement?	Nil regarding this report's scope.
How will SINSW address matters not resolved?	There are no matters unresolved for this report.

## Shanil Prasad

---

**From:** Cameron Amri <camri@birzulisassociates.com>  
**Sent:** 22 July, 2020 4:11 PM  
**To:** Shanil Prasad  
**Subject:** FW: KYEEMAGH Public School  
**Attachments:** Construction Soil and Water Management Plan Kyeemagh Public rev 0 (draft).pdf

fyi

Regards

**Cameron Amri**  
Civil & Structural Engineer  
  
583 Darling Street  
Rozelle NSW 2039  
☎ (02) 9555 7230  
📠 0456 316 513  
✉ [camri@birzulisassociates.com](mailto:camri@birzulisassociates.com)  
🌐 [www.birzulisassociates.com](http://www.birzulisassociates.com)

---

**From:** Cameron Amri  
**Sent:** Tuesday, 7 July 2020 12:35 PM  
**To:** Christopher Thompson <Christopher.Thompson@bayside.nsw.gov.au>  
**Subject:** RE: KYEEMAGH Public School

Hello again,

Hope you are having a great week. I'm required by the State Significant Development CoC to "consult with Council" regarding this report. Attached is the draft report.

I think the report will help to understand our argument that there is no significant need to treat water as part of biological control as the site is not an industrial site with a chemical operational cycle but I think we can add some for of treatment system for the car park water which would be good to filter prior to the infiltration system. I'm happy to update the plans to reflect that. 😊

Regards

**Cameron Amri**

Civil & Structural Engineer



583 Darling Street

Rozelle NSW 2039

☎ (02) 9555 7230

■ 0456 316 513

✉ [camri@birzulisassociates.com](mailto:camri@birzulisassociates.com)

🌐 [www.birzulisassociates.com](http://www.birzulisassociates.com)

---

**From:** Christopher Thompson <[Christopher.Thompson@bayside.nsw.gov.au](mailto:Christopher.Thompson@bayside.nsw.gov.au)>

**Sent:** Friday, 3 July 2020 11:33 AM

**To:** Cameron Amri <[camri@birzulisassociates.com](mailto:camri@birzulisassociates.com)>

**Subject:** RE: KYEEMAGH Public School

Hi Cameron,

I could not review the drains file for some reason. Anyway I have attached the calculation spreadsheet we have on file for your review.

The music model must be run and treatment measures shall be made prior to stormwater entering the infiltration system (infiltration system cant be used for stormwater treatment). The results should be attached to the stormwater plans at the end and details for treatment measures provided.

Happy to have ACO stormbrixx used, you just need to be certifying that design is acceptable with regards to achieving the requirements of Rockdale Technical Specification Stormwater Management.

Emergency overflow needs to be addressed to ensure that no ponding occurs within the school.

Maintenance needs to be provided for to ensure that the system can be readily and easily maintained. This should be via pits that are readily accessible I.e. 900x900mm wide. Does the manufacturer address maintenance for ACO strombrixx? Could you provide this information to me?

All pits are to be provided with Child proof J-Locks or similar.

Best regards,



**Christopher Thompson** Development Engineer  
444-446 Princes Highway, Rockdale NSW 2216  
**T** 02 9562 1645  
**E** [christopher.thompson@bayside.nsw.gov.au](mailto:christopher.thompson@bayside.nsw.gov.au) **W** [www.bayside.nsw.gov.au](http://www.bayside.nsw.gov.au)

---

**From:** Cameron Amri [<mailto:camri@birzulisassociates.com>]  
**Sent:** Thursday, 2 July 2020 1:47 PM  
**To:** Christopher Thompson <[Christopher.Thompson@bayside.nsw.gov.au](mailto:Christopher.Thompson@bayside.nsw.gov.au)>  
**Subject:** RE: KYEEMAGH Public School

DRAINS model is attached. There will be a balance pipe between the tanks which will make them work as one large tank but we have split in the design to take into account the staged construction.

Regards

**Cameron Amri**  
Civil & Structural Engineer



583 Darling Street  
Rozelle NSW 2039  
☎ (02) 9555 7230  
■ 0456 316 513

✉ [camri@birzulisassociates.com](mailto:camri@birzulisassociates.com)  
🌐 [www.birzulisassociates.com](http://www.birzulisassociates.com)

---

**From:** Cameron Amri  
**Sent:** Thursday, 2 July 2020 1:46 PM  
**To:** 'christopher.thompson@bayside.nsw.gov.au' <[christopher.thompson@bayside.nsw.gov.au](mailto:christopher.thompson@bayside.nsw.gov.au)>  
**Subject:** KYEEMAGH Public School

Hi Chris,

Thank you for your time. This is what I have in mind at this stage. I will be updating the plans to remove the granite paving as it doesn't comply with the EFS&G and upgrading infiltration tank 1 to a stronger product that can take vehicle loads. Also I will move tank 1 away from any possible vehicle loads as a safeguard just in case.

I will send the DRAINS file separately. There is also a MUSIC model but with infiltration and very little site run-off the targets are met very easily.

Basically all I'd like is Council approval for the use of this type of infiltration system and if you see any areas of noncompliance to Council's stormwater Guidelines.

Regards

**Cameron Amri**

Civil & Structural Engineer



583 Darling Street

Rozelle NSW 2039

☎ (02) 9555 7230

☎ 0456 316 513

✉ [camri@birzulisassociates.com](mailto:camri@birzulisassociates.com)

🌐 [www.birzulisassociates.com](http://www.birzulisassociates.com)

---

**From:** Ricketts, Luke <[Luke.Ricketts@aco.com](mailto:Luke.Ricketts@aco.com)>

**Sent:** Wednesday, 24 June 2020 10:43 AM

**To:** Cameron Amri <[camri@birzulisassociates.com](mailto:camri@birzulisassociates.com)>

**Subject:** FW: ACO STORMBRIXX KYEEMAGH

Hi Cameron,

Great to meet you yesterday.

ACO's StormBrixx HD tank is recommended for the Kyeemagh Public School project. See attached parts list, specification information and general installation drawings (2 Layer HD).

For the 100m<sup>3</sup> infiltration tank, the recommended StormBrixx HD tank has a size of 14.4m x 6m x 1.22m (2 layer). The tank has a net volume of 100.14m<sup>3</sup> (100.14kL) and gross volume of 105.41m<sup>3</sup>.

Customer to check and confirm tank size, geotextile, tank accessories and the number of access points are suitable for the project. Access shaft and access shaft riser recommended at the location of the inlet and outlet pipes, refer to page 24 in brochure.

The links below show the ACO StormBrixx products installed in recent projects:

<https://www.acostormbrixx.com.au/portfolio-item/canberra-data-centre-canberra-act/>

<https://www.acostormbrixx.com.au/portfolio-item/azure-retirement-village-and-hub-canberra-act/>

StormBrixx Technical Handbook and Product Catalogue can be downloaded at: [www.acostormbrixx.com.au](http://www.acostormbrixx.com.au)

Installation guidance: <https://www.acostormbrixx.com.au/product-support/installation/>




For design assistance on your next project, Click here.

Regards,

Luke Ricketts

Luke Ricketts | Specification Sales Representative  
ACO Pty Ltd  
134-140 Old Bathurst Road | Emu Plains NSW 2750  
Tel.+612 4747 4000 | Fax +612 4747 4040  
Mobile +61 413 750 708 | [Luke.Ricketts@aco.com](mailto:Luke.Ricketts@aco.com)  
<http://www.acoaus.com.au/>



This communication may contain CONFIDENTIAL information of ACO Pty Ltd (ABN 65 050 102 942). It may also be the subject of LEGAL PROFESSIONAL PRIVILEGE and/or under copyright. If you are not an intended recipient, you MUST NOT keep, forward, copy, use, save or rely on this communication, and any such action is unauthorised and prohibited. If you have received this communication in error, please reply to this e-mail to notify the sender of its incorrect delivery, and then delete both it and your reply. Thank you.

**From:** Cameron Amri <[camri@birzulisassociates.com](mailto:camri@birzulisassociates.com)>

**Date:** 23 June 2020 at 1:52:03 pm AEST

**To:** "Ricketts, Luke" <[Luke.Ricketts@aco.com](mailto:Luke.Ricketts@aco.com)>


**Subject:** RE: ACO STORMBRIXX KYEEMAGH

This email is intended solely for the addressee and may contain confidential information. Any disclosure, copying or distribution to others is not permitted without agreement of the sender. Council does not represent, warrant or guarantee this email is free of errors, virus or interference. Any views expressed or commitments made in this email are those of the individual sender, and may not necessarily be those of Council. With

## 11 Appendix D – Erosion and Sediment Control design drawings

Drawings prepared by Birzulis Associates Pty Ltd. The latest version of each of these documents and this report should be used at all stages during the construction.

regard to any personal information that may be included in this email, Council complies with the Privacy and Personal Information Protection Act, and expects the recipient to do likewise. This email may be made available to the public under various legislation.

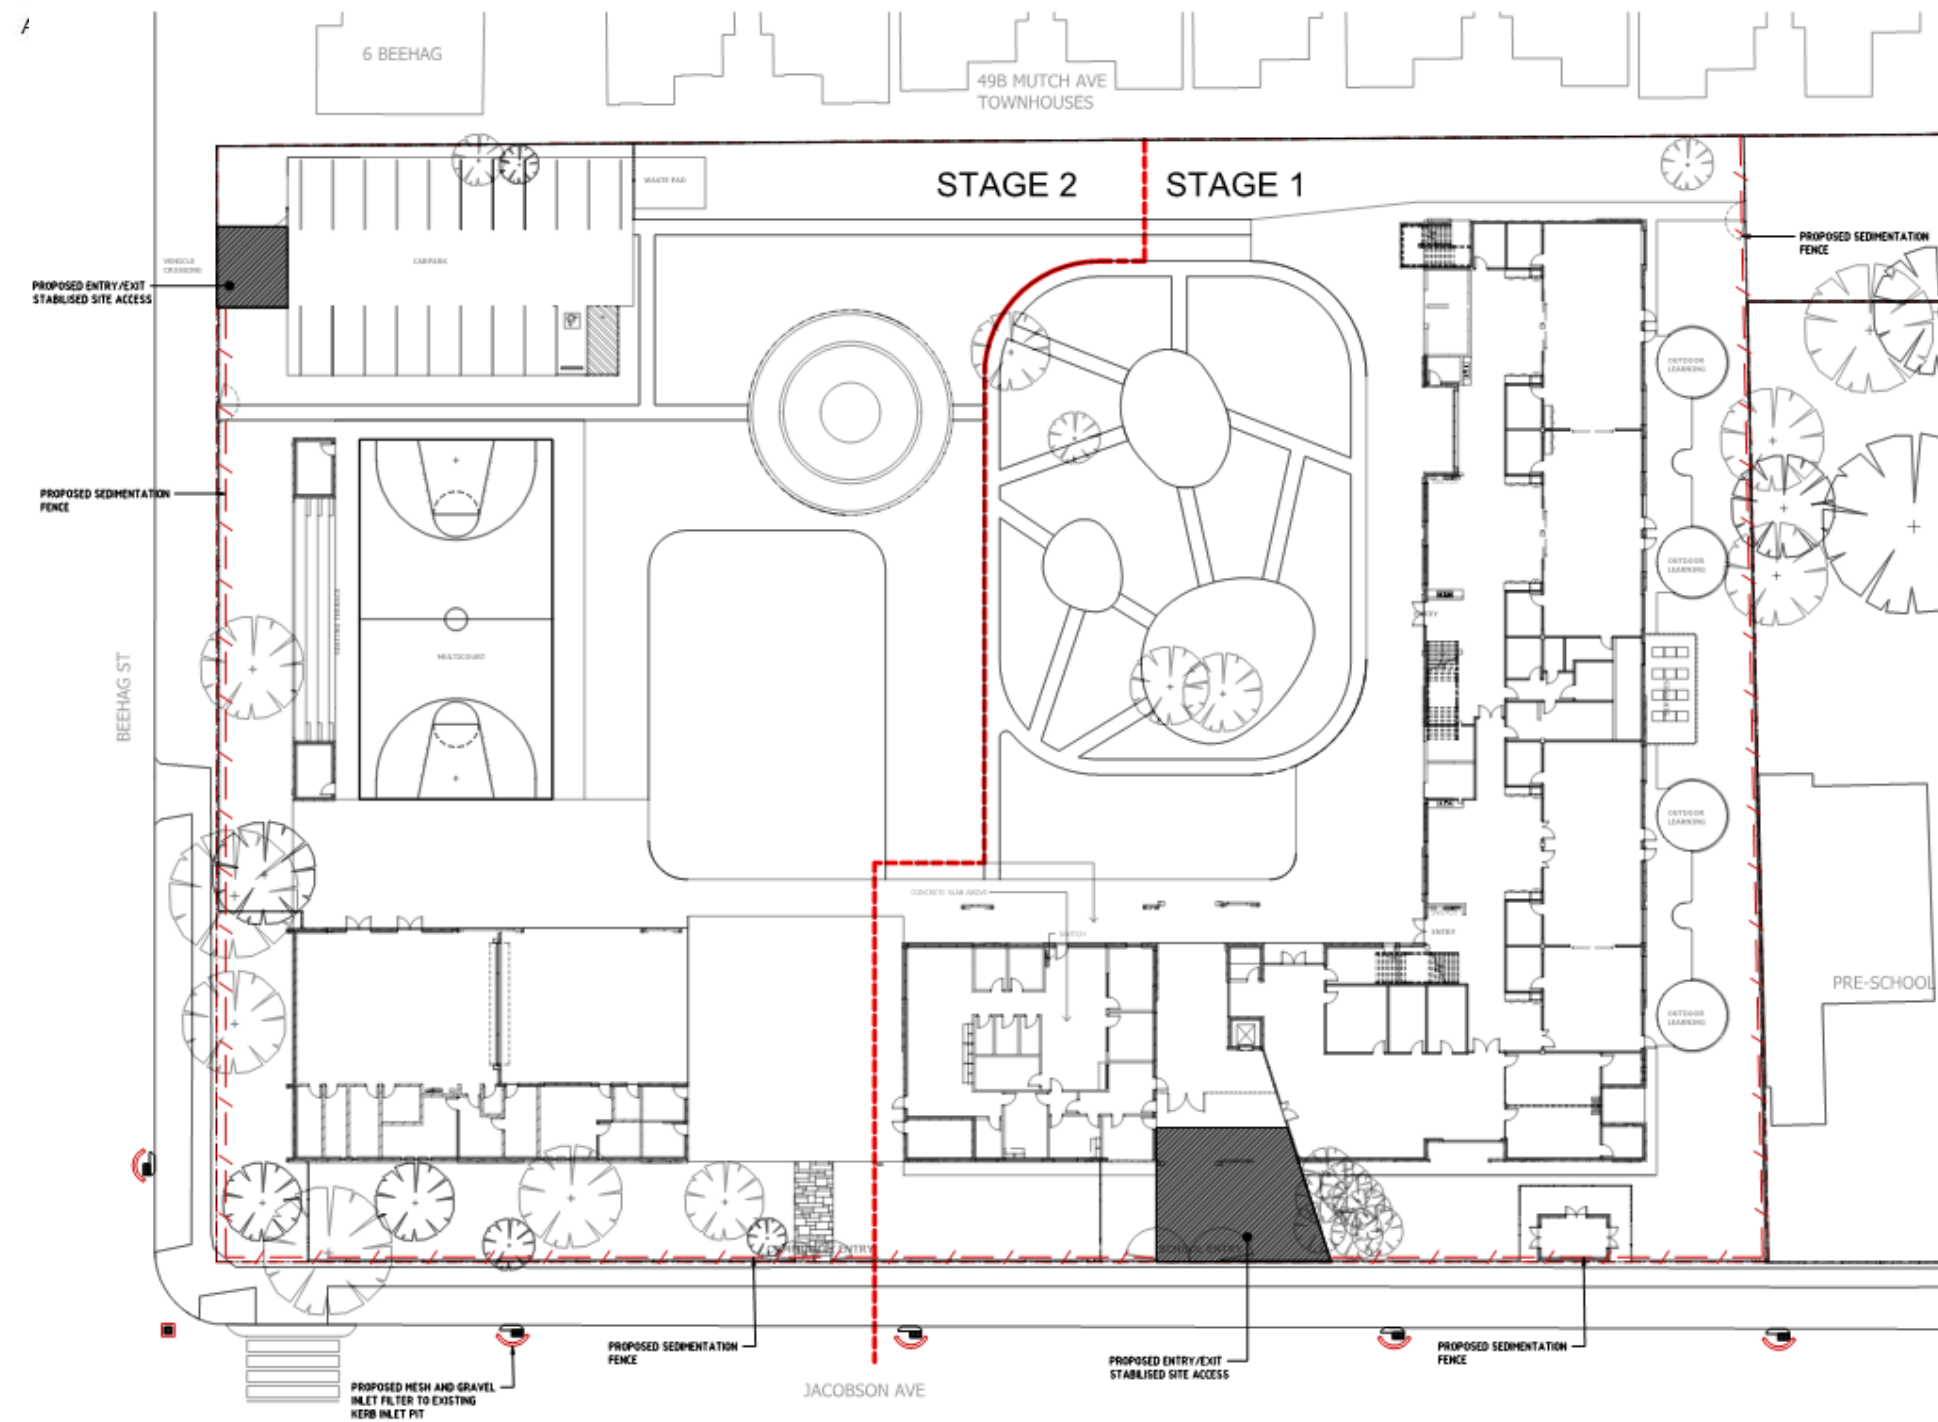

#### GENERAL NOTES

1. THIS PLAN IS A CONCEPT PLAN ONLY FOR STORMWATER DISPOSAL & EROSION CONTROL. IT IS NOT SUITABLE FOR CONSTRUCTION. THIS PLAN SHOULD BE ADAPTED BY THE BUILDER DURING DEMOLITION, EXCAVATION & CONSTRUCTION PHASES TO ENSURE ADEQUATE PERFORMANCE.
2. ALL DRAINAGE LAYOUT & DETAILS ARE DIAGNOSTIC & INDICATIVE ONLY. ACTUAL LOCATION, SIZES, LEVELS & GRADES MAY VARY WHEN DETAIL DESIGN WORKS ARE DOCUMENTED.

#### CLAY SOILS

A SYSTEM SHALL BE INSTALLED TO EITHER:

1. TRANSPORT STORMWATER RUNOFF WITH SUSPENDED SOLIDS FROM SITE VIA PUMP TRUCKS.
2. TREAT THE STORMWATER RUNOFF WITH SUSPENDED SOLIDS SO THE DISCHARGE WATER QUALITY TO COUNCIL STORMWATER DRAINAGE SYSTEM HAS A MAXIMUM CONCENTRATION OF SUSPENDED SOLIDS THAT DOES NOT EXCEED 50 MILLIGRAMS PER LITRE IN ACCORDANCE WITH THE PROTECTION OF THE ENVIRONMENT OPERATION ACT (POEO 1997) AND SHALL BE APPROVED BY THE LOCAL COUNCIL.

#### EROSION & SEDIMENTATION CONTROL NOTES

1. CONTRACTOR SHALL PROVIDE SEDIMENT FENCING MATERIAL DURING CONSTRUCTION TO THE LOW SIDE OF THE WORKS. THE SEDIMENT FENCING MATERIAL TO CYCLOPE WIRE SECURITY FENCE. SEDIMENT CONTROL FABRIC SHALL BE AN APPROVED MATERIAL (E.G. HUNES PROPEX SILT STOP) STANDING 300mm ABOVE GROUND & EXTENDING 150mm BELOW GROUND.
2. EXISTING DRAINS LOCATED WITHIN THE SITE SHALL ALSO BE ISOLATED BY SEDIMENT FENCING MATERIAL.
3. NO PARKING OR STOCKPILING OF MATERIAL IS PERMITTED ON THE LOWER SIDE OF THE SEDIMENT FENCE.
4. GRASS VERGES SHALL BE MAINTAINED AS MUCH AS PRACTICAL TO PROVIDE A BUFFER ZONE TO THE CONSTRUCTION SITE.
5. CONSTRUCTION ENTRY/EXIT SHALL BE VIA THE LOCATION NOTED ON THE DRAWING. CONTRACTOR SHALL ENSURE ALL DROPPABLE SOIL & SEDIMENT IS REMOVED PRIOR TO CONSTRUCTION TRAFFIC EXITING SITE. CONTRACTOR SHALL ENSURE ALL CONSTRUCTION TRAFFIC ENTERING & LEAVING THE SITE DO SO IN A FORWARD DIRECTION.

#### PRELIMINARY ISSUE NOT FOR CONSTRUCTION

DATE	DESCRIPTION	APPROVED	DATE
05.06.20	PRELIMINARY DESIGN ISSUE		05.06.20



**BIRZULIS ASSOCIATES**  
CONSULTING STRUCTURAL & CIVIL ENGINEERS  
583 DARLING STREET ROZELLE NSW 2039  
Tel: (02) 9555 7230 email: office@birzulisassociates.com  
www.birzulisassociates.com

PROJECT  
KYEEMAGH PUBLIC SCHOOL  
JACOBSON AVE, KYEEMAGH

TITLE  
SOIL EROSION AND SEDIMENT  
CONTROL PLAN

SCALE		as noted @ A1		DATE	
				MAY 2020	
DRAWN		DESIGN		VERIFIED	
JM		C.A/MG		-	
				APPROVED	
				-	
REPRODUCTION OF THIS DRAWING IS PROHIBITED WITHOUT THE CONSENT OF BIRZULIS ASSOCIATES PTY. LTD.					
ISSUE		PROJECT No.		DRAWING No.	
P2		7863		C.100	



#### DIRECTORS

B Fimmano B.E. (Hons), M.I.E. Aust., C.P.Eng.

M A Grogan B.E., M.Eng., M.I.E. Aust., C.P.Eng.


#### ASSOCIATE DIRECTOR

P W Grogan B.E. (Hons), M.E.(Struct), M.I.E. Aust., C.P.Eng.


#### CONSULTANT

A J Birzulis OAM, B.E., M.Eng. Sc., F.I.E. Aust., C.P.Eng.




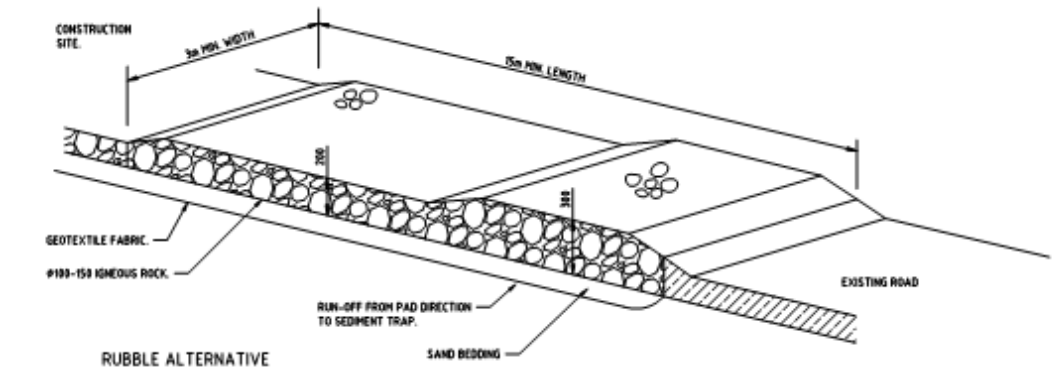


TEMPORARY CONSTRUCTION EXIT  
NOT TO SCALE

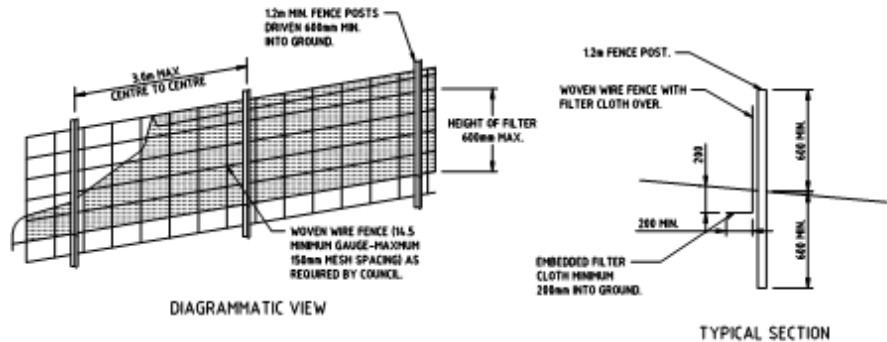

SEDIMENT FENCE DETAIL  
NOT TO SCALE




STOCKPILES DETAIL  
NOT TO SCALE

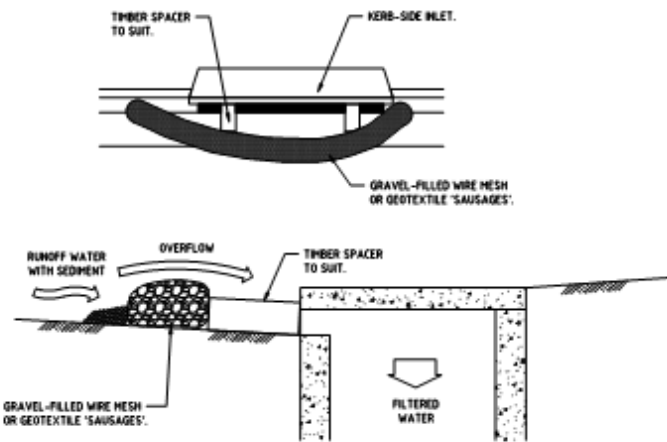

MESH AND GRAVEL INLET FILTER  
SCALE 1:20

- NOTES:
1. FABRICATE A SLEEVE MADE FROM GEOTEXTILE OR WIRE MESH LONGER THAN THE LENGTH OF THE INLET PIT AND FILL IT WITH 25mm TO 50mm GRAVEL.
  2. FORM AN ELLIPTICAL CROSS-SECTION ABOUT 150mm HIGH x 400mm WIDE.
  3. PLACE THE FILTER AT THE OPENING LEAVING AT LEAST A 100mm SPACE BETWEEN IT AND THE KERB INLET. MAINTAIN THE OPENING WITH SPACER BLOCKS.
  4. FORM A SEAL WITH THE KERB TO PREVENT SEDIMENT BYPASSING THE FILTER.
  5. SANDBAGS FILLED WITH GRAVEL CAN SUBSTITUTE FOR THE MESH OR GEOTEXTILE PROVIDING THEY ARE PLACED SO THAT THEY CAN FIRMLY ABUT EACH OTHER AND SEDIMENT/LADEN WATERS CANNOT PASS BETWEEN.



GEOTEXTILE FILTER FABRIC  
DROP INLET SEDIMENT TRAP  
NOT TO SCALE

PRELIMINARY ISSUE  
NOT FOR CONSTRUCTION

ISSUE	DESCRIPTION	APPROVED	DATE
P2	REVISIONS DESIGN ISSUE		21-JUN-20
P1	DESIGN ISSUE		10-JUL-20

ARCHITECT  
**TAYLOR**

**BIRZULIS ASSOCIATES**  
CONSULTING STRUCTURAL & CIVIL ENGINEERS  
583 DARLING STREET ROZELLE NSW 2059  
Tel: (02) 9555 7230 email: office@birzulisassociates.com  
www.birzulisassociates.com

PROJECT  
KYEEMAGH PUBLIC SHOOOL  
JACOBSON AVE, KYEEMAGH

TITLE  
TYPICAL DETAILS - SOIL EROSION  
AND SEDIMENT CONTROL

SCALES  
as noted @ A1  
DATE  
MAY 2020

DRAWN	DESIGN	VERIFIED	APPROVED
JM	CA/MG	-	-

REPRODUCTION OF THIS DRAWING IS PROHIBITED  
WITHOUT THE CONSENT OF BIRZULIS ASSOCIATES PTY. LTD.

ISSUE	PROJECT No.	DRAWING No.
P2	7863	C.30
