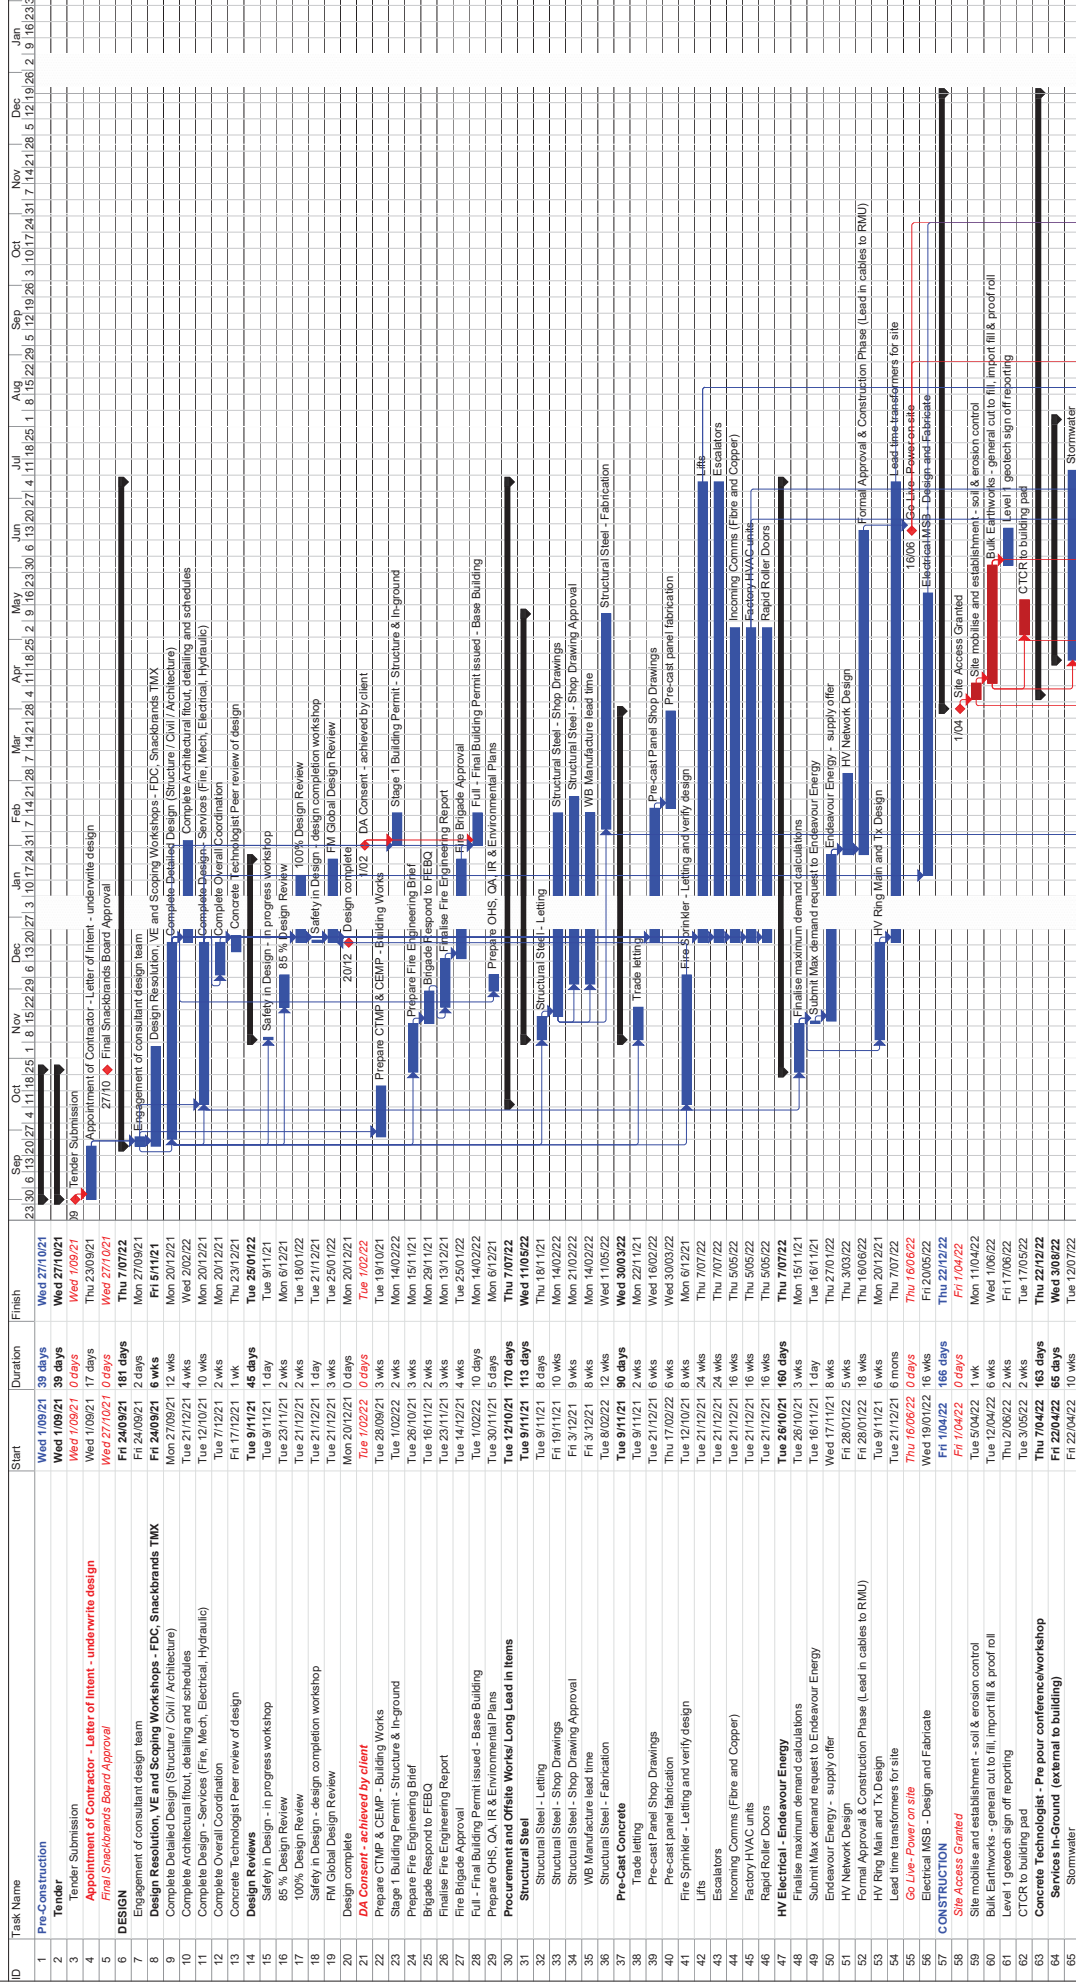


Excludes Authority, Inclement Weather and Covid Related delays

[illegible]

ID	Task Name	Start	Duration	Finish	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan
261	Prep & Pour Concrete Hardstand - on grade	Tue 16/08/22	3 wks	Wed 7/09/22																	
262	Footpaths & Misc Concrete	Thu 8/09/22	1 wk	Wed 14/09/22																	
263	Initial crushed rock truck hardstand (Optional)	Tue 16/08/22	2 wks	Tue 30/08/22																	
264	Carpark	Tue 6/09/22	12 days	Thu 22/09/22																	
265	Trim, Grade & Compact base	Tue 6/09/22	1 wk	Mon 12/09/22																	
266	Keibs	Tue 13/09/22	2 days	Wed 14/09/22																	
267	Final trim, rock and Asphalt	Thu 15/09/22	1 wk	Thu 22/09/22																	
268	Install Boomgates	Fri 23/09/22	1 wk	Thu 29/09/22																	
269	Project Close out	Fri 23/09/22	58 days	Thu 22/12/22																	
270	Landscapeing	Fri 19/10/22	3 wks	Wed 9/11/22																	
271	Linemarking	Thu 23/09/22	3 wks	Tue 8/10/22																	
272	Signage	Thu 6/10/22	1 wk	Wed 12/10/22																	
273	GLA Survey(s)	Fri 23/09/22	2 wks	Mon 10/10/22																	
274	Site Fencing & gates	Tue 8/11/22	2 wks	Tue 22/11/22																	
275	FRNSW & PCA Inspections and sign off	Tue 15/11/22	1 wk	Tue 22/11/22																	
276	Handover training	Tue 22/11/22	0 days	Tue 22/11/22																	
277	Bi-Lok door hardware change out	Tue 22/11/22	0 days	Tue 22/11/22																	
278	Target Date - Practical Completion	Wed 23/11/22	4 wks	Thu 22/12/22																	
279	Inclement Weather Contingency																				
280	Contract - Practical Completion																				

Task	Summary	External Tasks	Inactive Summary	Finish-only
Critical Task	Summary	Project Summary	Inactive Summary	Manual Progress
Critical	Rolled Up Task	Group By Summary	Manual Task	
Critical Split	Rolled Up Critical Task	Deadline	Duration-only	
Progress	Rolled Up Milestone	Inactive Task	Manual Summary Rollup	
Milestone	Rolled Up Progress	Inactive Milestone	Manual Summary	
	Split		Start-only	
Excludes Authority, Inclement Weather and Covid Related delays				
