

## New England Solar – Traffic Management Plan



Stage 1b – 400MWac – Operations

Stage 2a – 320MWac - Construction

Stage 3a – 200MW/2hr - Construction


21 December 2023

## Document Control

|                  |                         |
|------------------|-------------------------|
| Document:        | Traffic Management Plan |
| Project Name:    | New England Solar       |
| Revision Number: | 8                       |

### Revision History

| Revision No. | Date              | Revision Description | Prepared by   | Reviewed by   | Approved for Issue by |
|--------------|-------------------|----------------------|---------------|---------------|-----------------------|
| 0            | 9 September 2020  | For Client Review    | Bayzid Khan   | Andrew Brown  | Julie Tom             |
| 1            | 22 September 2020 | For Client Review    | Bayzid Khan   | Andrew Brown  | Julie Tom             |
| 2            | 19 October 2020   | For Client Review    | Bayzid Khan   | Andrew Brown  | Julie Tom             |
| 3            | 4 December 2020   | For Client Review    | Bayzid Khan   | Andrew Brown  | Julie Tom             |
| 4            | 10 December 2020  | For Client Review    | Bayzid Khan   | Andrew Brown  | Julie Tom             |
| 5            | 29 January 2021   | For Client Review    | Bayzid Khan   | Andrew Brown  | Julie Tom             |
| 6            | 16 February 2021  | For Client Review    | Bayzid Khan   | Andrew Brown  | Julie Tom             |
| 6.1          | 25 February 2021  | Issue for Use        | Andrew Brown  | Alen Krljic   | Julie Tom             |
| 7            | 27 September 2022 | Issue for Use        | Andrew Brown  | Alen Krljic   | Julie Tom             |
| 8            | 21 December 2023  | Issue for Use        | Tessa Verkerk | Patric Millar | Sarah Donnan          |

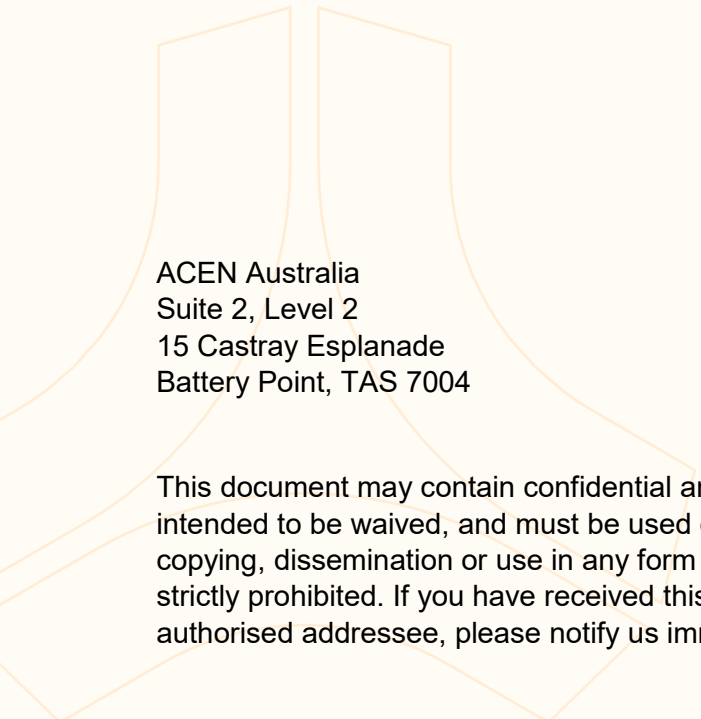

ACEN Australia  
Suite 2, Level 2  
15 Castray Esplanade  
Battery Point, TAS 7004

This document may contain confidential and legally privileged information, neither of which are intended to be waived, and must be used only for its intended purpose. Any unauthorised copying, dissemination or use in any form or by any means other than by the addressee, is strictly prohibited. If you have received this document in error or by any means other than as authorised addressee, please notify us immediately and we will arrange for its return to us.

## Table of Contents

|                                                                            |           |
|----------------------------------------------------------------------------|-----------|
| <b>Document Control</b>                                                    | <b>2</b>  |
| <b>1 Introduction</b>                                                      | <b>7</b>  |
| 1.1 Approved Project                                                       | 7         |
| 1.1.1 General project description                                          | 7         |
| 1.2 Working Hours                                                          | 9         |
| 1.2.1 Construction                                                         | 9         |
| 1.2.2 Operations                                                           | 9         |
| 1.2.3 Purpose of the Traffic Management Plan                               | 12        |
| 1.3 Objectives of the Traffic Management Plan                              | 12        |
| 1.4 Consent Conditions                                                     | 12        |
| 1.5 Duty of Care                                                           | 14        |
| 1.6 Site Visit                                                             | 14        |
| 1.7 Structure of the Plan                                                  | 14        |
| <b>2 Review of Development Traffic and Routes</b>                          | <b>16</b> |
| 2.1 Construction Period                                                    | 16        |
| 2.2 Traffic Generation                                                     | 16        |
| 2.2.1 Construction and Operations Phases                                   | 16        |
| 2.2.2 Decommissioning and Upgrading Phases                                 | 17        |
| 2.3 Access Routes                                                          | 17        |
| 2.3.1 Over Size Over Mass (OSOM) Vehicle Route                             | 18        |
| 2.3.2 Other Traffic Routes (Light and Heavy)                               | 19        |
| 2.4 Infrastructure Upgrades                                                | 19        |
| 2.5 Internal Roads and On-site Parking Facilities                          | 21        |
| <b>3 Traffic Management Plan</b>                                           | <b>23</b> |
| 3.1 Introduction                                                           | 23        |
| 3.2 TMP Registers                                                          | 23        |
| 3.3 Roles and Responsibilities                                             | 23        |
| 3.4 Work Health and Safety and Occupational Health and Safety Arrangements | 25        |
| 3.5 Induction for Vehicle Operators and Regular Toolbox Meetings           | 25        |
| 3.6 Consultation/ Notification Requirements                                | 26        |
| 3.6.1 Notification                                                         | 26        |
| 3.6.2 Consultation                                                         | 26        |
| 3.7 A Driver's Code of Conduct                                             | 27        |

|       |                                                                                                                                                                                                                                                                                                                                                                                                                                                |    |
|-------|------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|----|
| 3.7.1 | Vehicle Speeds                                                                                                                                                                                                                                                                                                                                                                                                                                 | 27 |
| 3.7.2 | Heavy Vehicle Driver Fatigue                                                                                                                                                                                                                                                                                                                                                                                                                   | 28 |
| 3.7.3 | Procedures                                                                                                                                                                                                                                                                                                                                                                                                                                     | 28 |
|       | All drivers are to adhere to the designated access route and ensure safe driving practices are being implemented.                                                                                                                                                                                                                                                                                                                              | 28 |
|       | The designated access route is as per Section 2.3 for both OSOM vehicles and heavy and light vehicles. Drivers travelling to or from the site must do so safely, in full compliance with the law, including in respect of speed limits, following distances, forward sight when overtaking, being able to stop within the length of road visible (or half the length on roads without centrelines), and not driving carelessly or dangerously. | 28 |
|       | These procedures will be reiterated during pre-start discussions and form part of site inductions. Failure to comply with the above procedures will result in the Disciplinary Procedure (Section 3.24) being implemented.                                                                                                                                                                                                                     | 30 |
| 3.8   | Dilapidation Survey                                                                                                                                                                                                                                                                                                                                                                                                                            | 30 |
| 3.8.1 | Dilapidation Methodology                                                                                                                                                                                                                                                                                                                                                                                                                       | 30 |
| 3.8.2 | Dilapidation Protocol                                                                                                                                                                                                                                                                                                                                                                                                                          | 30 |
| 3.9   | Protocol for monitoring daily traffic movements                                                                                                                                                                                                                                                                                                                                                                                                | 31 |
| 3.10  | Protocol for Barleyfields Road (North) and Big Ridge Road Repair Works                                                                                                                                                                                                                                                                                                                                                                         | 31 |
| 3.11  | Protocol for Operational Maintenance of Segment 4 and 5 of Big Ridge Road                                                                                                                                                                                                                                                                                                                                                                      | 31 |
| 3.12  | Temporary Traffic Controls, including Signage                                                                                                                                                                                                                                                                                                                                                                                                  | 32 |
| 3.13  | Safety Initiatives for Transport through Residential Areas and/or School Zones                                                                                                                                                                                                                                                                                                                                                                 | 33 |
| 3.14  | Management of Dirt Tracked onto the Public Road Network                                                                                                                                                                                                                                                                                                                                                                                        | 33 |
| 3.15  | Management of Employee Shuttle Bus Service                                                                                                                                                                                                                                                                                                                                                                                                     | 34 |
| 3.16  | Scheduling of Haulage Vehicle Movements to Minimise Convoy Lengths or Platoons                                                                                                                                                                                                                                                                                                                                                                 | 34 |
| 3.17  | Responding to Local Climate Conditions                                                                                                                                                                                                                                                                                                                                                                                                         | 34 |
| 3.18  | Over-Size and Over Mass Vehicles (OSOM)                                                                                                                                                                                                                                                                                                                                                                                                        | 34 |
| 3.19  | Framework for Handling/Approval of Exception (for emergency or other unforeseen circumstances) to the exclusion of heavy vehicles utilising the Barleyfields Road (south) during construction of the Project                                                                                                                                                                                                                                   | 35 |
| 3.20  | Coordination of Construction Traffic with Seasonal Agricultural Haulage                                                                                                                                                                                                                                                                                                                                                                        | 35 |
| 3.21  | Variation from Approved Traffic Management Plan                                                                                                                                                                                                                                                                                                                                                                                                | 35 |
| 3.22  | Traffic Management Plan Review                                                                                                                                                                                                                                                                                                                                                                                                                 | 36 |
| 3.23  | Traffic Management Plan Auditing                                                                                                                                                                                                                                                                                                                                                                                                               | 36 |
| 3.24  | Disciplinary Procedure                                                                                                                                                                                                                                                                                                                                                                                                                         | 37 |
| 3.25  | Complaints                                                                                                                                                                                                                                                                                                                                                                                                                                     | 37 |
| 3.26  | Notifiable Incidents                                                                                                                                                                                                                                                                                                                                                                                                                           | 38 |

|                                                                               |           |
|-------------------------------------------------------------------------------|-----------|
| 3.26.1 Incident Procedures                                                    | 38        |
| 3.26.2 Material Harm incidents                                                | 38        |
| 3.27 Non-Compliance                                                           | 39        |
| 3.27.1 Commitment                                                             | 39        |
| 3.27.2 Response                                                               | 39        |
| 3.27.3 Corrective Action                                                      | 40        |
| 3.27.4 Notification                                                           | 40        |
| <b>4 Summary</b>                                                              | <b>41</b> |
| <b>APPENDIX A Planning secretary Approval of this Traffic Management Plan</b> | <b>42</b> |
| <b>APPENDIX B Stakeholder Correspondence</b>                                  | <b>43</b> |
| <b>APPENDIX C Access Road Condition Inspection</b>                            | <b>44</b> |
| <b>APPENDIX D DRAFT THM12 Pavement management systems</b>                     | <b>45</b> |

### Table of Tables

|                                                                                                        |    |
|--------------------------------------------------------------------------------------------------------|----|
| Table 1-1 Key components of NES                                                                        | 8  |
| Table 1-2 Traffic Management Plan Development Consent Requirements                                     | 12 |
| Table 2-1 Road Upgrades completed on New England Highway, Barleyfields Road (North) and Big Ridge Road | 19 |
| Table 3-1 TMP Registers                                                                                | 23 |
| Table 3-2 TMP Roles and Responsibilities                                                               | 23 |
| Table 3-3 Road Distress Type and Potential Interventions                                               | 32 |
| Table 5-1 Non-compliance Response                                                                      | 39 |

### Table of Figures

|                                                                      |    |
|----------------------------------------------------------------------|----|
| Figure 1-1 New England Solar Locality Plan                           | 10 |
| Figure 1-2 Staging Plan NES                                          | 11 |
| Figure 1-3 Environmental Management Strategy Structure               | 15 |
| Figure 2-1 Proposed vehicle movement forecast                        | 17 |
| Figure 2-2 Over-Size Over Mass Vehicle Route to NES Site             | 18 |
| Figure 2-3 Light and Heavy Vehicle Access Routes to NES Site         | 19 |
| Figure 2-4 Location of Barleyfields Road and Big Ridge Road Segments | 20 |
| Figure 2-5 Indicative parking facilities and laydown areas           | 22 |

# 1 Introduction

## 1.1 Approved Project

New England Solar Project (NES) was granted Development Consent from the Department of Planning, Infrastructure and Environment (DPIE) (now the Department of Planning and Environment [DPE]) on 9 March 2020 (SSD 9255). The Development Consent was most recently modified on 26 May 2023 (Modification 2), after receiving approval for Modification 1 on 9 Feb 2021.

### 1.1.1 General project description

ACEN Australia Pty Ltd (ACEN Australia) (formerly named UPC Renewables Australia Pty Ltd) has approval to develop the New England Solar and Battery Project; a significant grid-connected solar and battery energy storage system (BESS) project along with associated infrastructure (the Project), approximately 6 kilometres (km) east of the township of Uralla, which lies approximately 19 km south of Armidale, in the Uralla Shire local government area (LGA) (hereafter referred to as NES). NES is within the New England Renewable Energy Zone (REZ). NES was approved, subject to conditions, by the New South Wales (NSW) Independent Planning Commission (IPC) on 9 March 2020 (SSD 9255).

NES will be constructed in the following stages:

- Stage 1a: Construction of a 400 megawatt (MW) solar farm within the Northern Array, which commenced on 7 February 2022 and is expected to be completed by Q4 2023
- Stage 1b: Operations of 400MW solar
- Stage 2a: Construction of a 320 megawatt (MW) solar farm within the Central Array, which is expected to commence by Q1 2024
- Stage 2b: Operations of 320MW solar
- Stage 3a: Construction of 200MW/2hr BESS within the approved Substation/BESS area, which is expected to commence by Q1 2024
- Stage 3b: Operations of 200MW/2hr BESS
- Stage 4a: Construction of 1200MW/2hr BESS within the approved Substation/BESS area
- Stage 4b: Operations of 1200MW/2hr BESS
- Stage 5: Decommissioning

Key components of NES development are summarised in Table 1-1.

Table 1-1 Key components of NES

| Aspect                       | Description                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                  |
|------------------------------|------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| NES project summary          | <p>The NES project includes:</p> <ul style="list-style-type: none"> <li>• A generating capacity of approximately 720 (MWac), including about 400 MWac generated by the northern arrays (Stage 1) and 320 MWac from the central arrays (Stage 2).</li> <li>• Approximately 1.4 million single-axis tracking solar panels (up to 4.3 metres (m) high) and 150 power conversion units (PCU) (up to 2.7 m high).</li> <li>• A grid substation in the northern array area and connection to TransGrid's 330 kilovolt (kV) transmission line.</li> <li>• A lithium-ion battery storage facility (1,400 MW/2,800 MWh) located adjacent to the substation and within a number of small enclosures (up to 2.9 m high) or larger battery buildings (up to 5.5 m high) (Stage 3 &amp; 4).</li> <li>• Internal access tracks, staff amenities, maintenance buildings (up to 8 m high), offices, laydown areas, car parking and security fencing.</li> <li>• Subdivision of land within the site for the TransGrid switchyard.</li> </ul> |
| Project area                 | <p>Site: 3,355 hectares (ha).</p> <p>Total NES footprint: 2,159 ha</p> <ul style="list-style-type: none"> <li>• Stage 1b footprint: 1,159 ha</li> <li>• Stage 2a footprint: 985 ha</li> <li>• Stage 3a footprint: 15 ha</li> </ul>                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                           |
| Access route                 | <p>All vehicles will access the site via the New England Highway, Barleyfields Road (North) and Big Ridge Road.</p>                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                          |
| Site entry and road upgrades | <p>Two new site entry points are constructed on Big Ridge Road with a rural property access type.</p> <p>Upgrades to the intersection of:</p> <ul style="list-style-type: none"> <li>• The New England Highway and Barleyfields Road (North), including a Channelised Right Turn (CHR) treatment.</li> <li>• Barleyfields Road (North) and Big Ridge Road, including a Basic Left Turn (BAL) treatment.</li> </ul> <p>Upgrades have been made to:</p> <ul style="list-style-type: none"> <li>• Barleyfields Road (North) between the New England Highway and Big Ridge Road, including sealing to a width of 7.2 m and 1 m gravel shoulders.</li> </ul>                                                                                                                                                                                                                                                                                                                                                                      |

|                                    |                                                                                                                                                                                                                                                                                                                                               |
|------------------------------------|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
|                                    | <ul style="list-style-type: none"> <li>Big Ridge Road including sealing sections to a width of 7.2 m and 1 m gravel shoulders, and upgrading a section with a gravel surface to a width of 8.7 m.</li> </ul>                                                                                                                                  |
| Rail transport                     | <p>Construction materials may be transported to the site via a combination of road and rail (average of 2 trains per week).</p> <p>A train unloading area and materials storage area may be constructed adjacent to the Main Northern Railway. Materials will be stored in shipping containers (up to 2.9 m high) until required on-site.</p> |
| Construction                       | <p>Construction materials may be transported to the site via a combination of road and rail (average of 2 trains per week).</p> <p>Construction hours limited to Monday to Friday 7 am to 6 pm, and Saturday 8 am to 1 pm.</p>                                                                                                                |
| Operation                          | <p>The expected operational life of NES is approximately 30 years. However, this may involve infrastructure upgrades that could extend the operational life.</p>                                                                                                                                                                              |
| Decommissioning and rehabilitation | <p>The NES project also includes decommissioning at the end of the NES project life, which will involve removing all infrastructure.</p>                                                                                                                                                                                                      |
| Hours of operation                 | <p>Daily operations and maintenance will be undertaken Monday to Friday 7 am to 6 pm, and Saturday 8 am to 1 pm. NES will be operational 24/7.</p>                                                                                                                                                                                            |
| Subdivision                        | <p>Subdivision of the lots on which the approved TransGrid Switchyard is located has been completed.</p>                                                                                                                                                                                                                                      |
| Employment                         | <p>Approximately 700 construction jobs and up to 15 full-time operational jobs.</p>                                                                                                                                                                                                                                                           |
| Capital investment value           | <p>\$1.268 billion.</p>                                                                                                                                                                                                                                                                                                                       |

## 1.2 Working Hours

### 1.2.1 Construction

Unless approval has been obtained from the Secretary, construction, upgrading and decommissioning activities on site can only be undertaken between the following hours:

- 7 am to 6 pm Monday to Friday;
- 8 am to 1 pm Saturdays; and
- at no time on Sundays and NSW public holidays.

### 1.2.2 Operations

Once commissioned, NES will operate 24 hours a day. The facility will be staffed during daylight hours, generally from:

- 7 am to 6 pm Monday to Friday (staff on-call during weekends and public holidays).

Figure 1-1 New England Solar Locality Plan


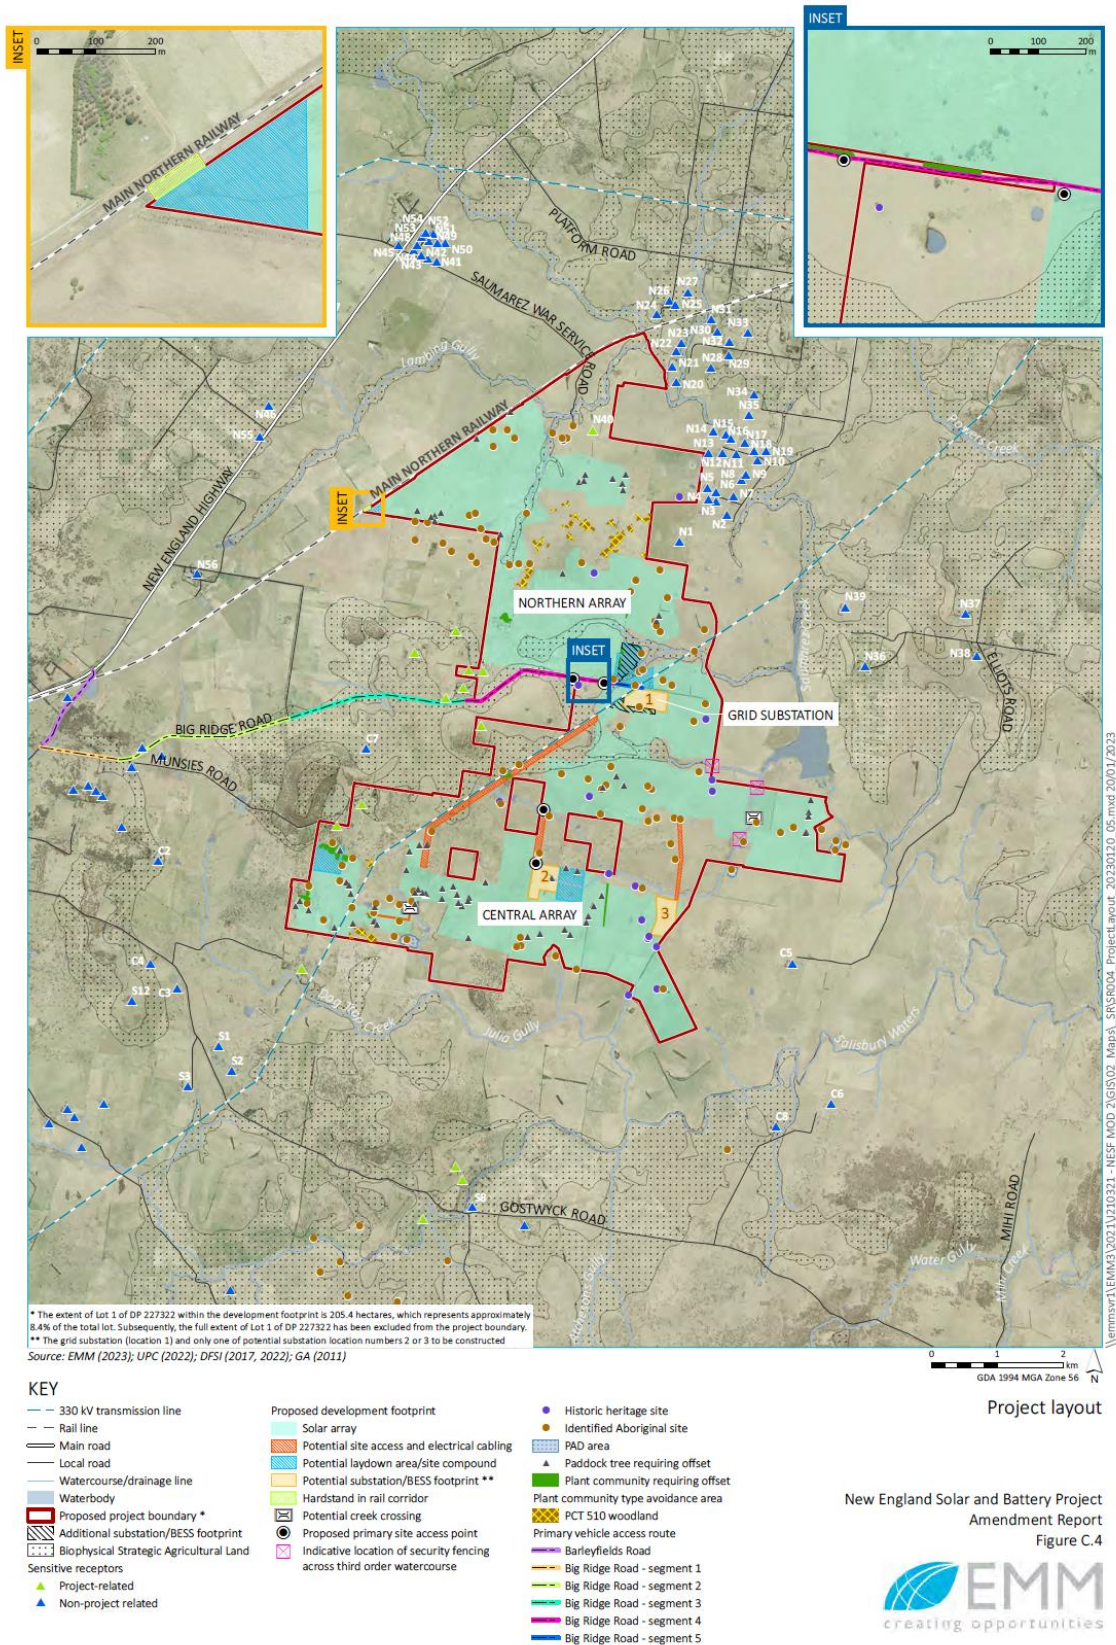


Figure 1-2 Staging Plan NES

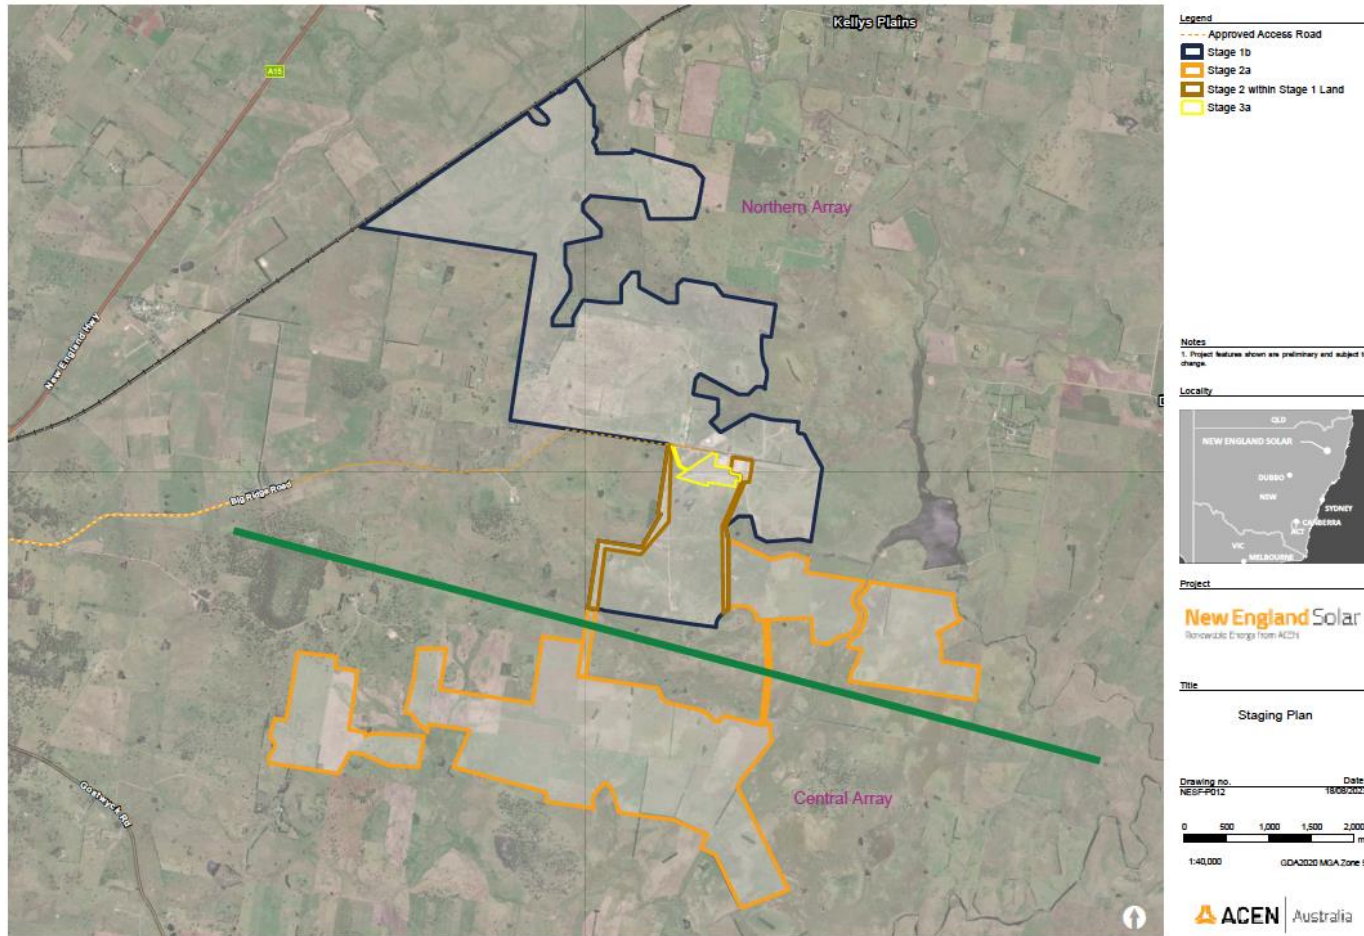

### 1.2.3 Purpose of the Traffic Management Plan

The purpose of the Traffic Management Plan (TMP) is to meet the requirements stipulated in Condition 6 of Schedule 3 of the Consolidated Development Consent for New England Solar, hereafter referred to as 'the Project'. Further details of requirements relating to consent conditions are contained in Section 1.4.

## 1.3 Objectives of the Traffic Management Plan

The principle objectives of the TMP include the following:

- Preserve public safety
- Minimise public inconvenience
- Minimise adverse changes to the efficiency and accessibility of the road network
- Minimise impact on road users and asset operation
- Maintain the integrity of the public road network
- Engage with the community and other key stakeholders where changes to normal traffic conditions occur
- Minimise traffic interactions and appropriately manage traffic interfaces during the Project
- Management of heavy vehicles used for the delivery of solar farm components, equipment and materials to/ from the Project site, as well as the management of light vehicles associated with personnel working on the Project site.

## 1.4 Consent Conditions

Table 1-2 details the elements to be included in this TMP as required by Condition 6 of Schedule 3 of the Development Consent and reference to the specific sections of this TMP where each of the requirements are addressed.

*Table 1-2 Traffic Management Plan Development Consent Requirements*

| TMP REQUIREMENTS                                                                                                                                                                                                                                                                   | REFERENCE TO SCHEDULE 3 DEVELOPMENT CONSENT | WHERE ADDRESSED IN TMP |
|------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|---------------------------------------------|------------------------|
| Details of the transport route to be used for all development-related traffic                                                                                                                                                                                                      | 6 (a)                                       | Section 2.3            |
| A protocol for undertaking independent dilapidation surveys to assess the: <ul style="list-style-type: none"> <li>• existing condition of Barleyfields Road and Big Ridge Road on the access route, prior to construction, upgrading or decommissioning activities; and</li> </ul> | 6 (b)                                       | Section 3.8            |

| TMP REQUIREMENTS                                                                                                                                                                                          | REFERENCE TO SCHEDULE 3 DEVELOPMENT CONSENT | WHERE ADDRESSED IN TMP |
|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|---------------------------------------------|------------------------|
| <ul style="list-style-type: none"> <li>condition of Barley fields Road and Big Ridge Road on the access route, following construction, upgrading or decommissioning activities</li> </ul>                 |                                             |                        |
| A protocol for the repair of Barleyfields Road and Big Ridge Road on the access route, if dilapidation surveys identify these roads to be damaged during construction, upgrading or decommissioning works | 6 (c)                                       | Section 3.8            |
| Details of the road works required by Condition 4 of Schedule 3 of the Development Consent                                                                                                                | 6 (d)                                       | Section 2.4            |
| A protocol for the maintenance of segments 4 and 5 of Big Ridge Road required by Condition 5(f) of Schedule 3 of the Development Consent                                                                  | 6 (e)                                       | Section 3.11           |
| <i>Details of the measures that would be implemented to minimise traffic impacts during construction, upgrading or decommissioning works , including:</i>                                                 | 6 (f)                                       |                        |
| <ul style="list-style-type: none"> <li>Temporary traffic controls, including detours and signage</li> </ul>                                                                                               |                                             | Section 3.12           |
| <ul style="list-style-type: none"> <li>Notifying the local community about project-related traffic impacts</li> </ul>                                                                                     |                                             | Section 3.6            |
| <ul style="list-style-type: none"> <li>Procedure for receiving and addressing complaints from the community about development-related traffic</li> </ul>                                                  |                                             | Section 3.25           |
| <ul style="list-style-type: none"> <li>Minimising potential for conflict with school buses, other motorists, road users and rail services as far as practicable</li> </ul>                                |                                             | Section 3.13           |
| <ul style="list-style-type: none"> <li>Implement measures to minimise dirt tracked onto the public road network from development-related traffic</li> </ul>                                               |                                             | Section 3.14           |
| <ul style="list-style-type: none"> <li>Details of the employee shuttle bus service and measures to encourage employee use of this service</li> </ul>                                                      |                                             | Section 3.15           |
| <ul style="list-style-type: none"> <li>Scheduling of haulage vehicle movements to minimise convoy length or platoons</li> </ul>                                                                           |                                             | Section 3.16           |
| <ul style="list-style-type: none"> <li>Responding to local climate conditions that may affect road safety such as fog, dust, wet weather and flooding</li> </ul>                                          |                                             | Section 3.17           |
| <ul style="list-style-type: none"> <li>Responding to any emergency repair or maintenance requirements</li> </ul>                                                                                          |                                             | Section 3.19           |
| <ul style="list-style-type: none"> <li>A traffic management system for managing over-dimensional vehicles</li> </ul>                                                                                      |                                             | Section 3.18           |
| A driver's code of conduct that addresses:                                                                                                                                                                | 6 (g)                                       | Section 3.7            |

| TMP REQUIREMENTS                                                                                                                                                                                                                                                                                               | REFERENCE TO SCHEDULE 3 DEVELOPMENT CONSENT | WHERE ADDRESSED IN TMP |
|----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|---------------------------------------------|------------------------|
| <ul style="list-style-type: none"> <li>• Travelling speed</li> <li>• Driver fatigue</li> <li>• Procedures to ensure that drivers adhere to the designated transport route</li> <li>• Procedures to ensure that drivers implement safe driving practice, including consideration of other road users</li> </ul> |                                             |                        |
| A program to ensure drivers working on the development receive suitable training on the code of conduct and any other relevant obligation under the Traffic Management Plan                                                                                                                                    | 6 (h)                                       | Section 3.5            |
| Following the Secretary's approval, the Applicant must implement the Traffic Management Plan.                                                                                                                                                                                                                  | -                                           | Appendix A             |

It is to be noted that relevant roads authorities, including TfNSW and Uralla Shire Council have been consulted and relevant sections of the Traffic Management Plan (TMP) have been updated based on feedback/comments received during consultation.

## 1.5 Duty of Care

The TMP together with other project level safety management plans addresses the duty of care on the part of ACEN Australia and its contractors who have an influence on the potential hazards associated with the Project to take reasonable care to protect the health and safety of others, including road users who may be at potential risk of harm.

## 1.6 Site Visit

In preparing the TMP a site visit was undertaken by a qualified person at the time of the dilapidation inspection on 25<sup>th</sup> of August 2020 to assist with identification of site-specific conditions. This enabled full appreciation and consideration of TMP requirements.

## 1.7 Structure of the Plan

This section of the Plan describes the Project and requirements of the TMP, the purpose of the TMP update, as well as reference to the relevant section of the Plan where each of the requirements are addressed.


Section 2 provides review of development related traffic generation and vehicle routes to be used by the heavy vehicles to transport construction materials to the project site.

Section 3 provides information on TMP administration, induction, consultation/ notification requirements, detailed traffic management measures to be implemented during construction of NES to manage heavy vehicle movements and to minimise adverse impacts on the road network, TMP review, as well as auditing and disciplinary procedures.

Section 4 provides a summary of the TMP.

This Plan sits within the broader Environmental Management Strategy framework, as shown in Figure 1-3.

Figure 1-3 Environmental Management Strategy Structure

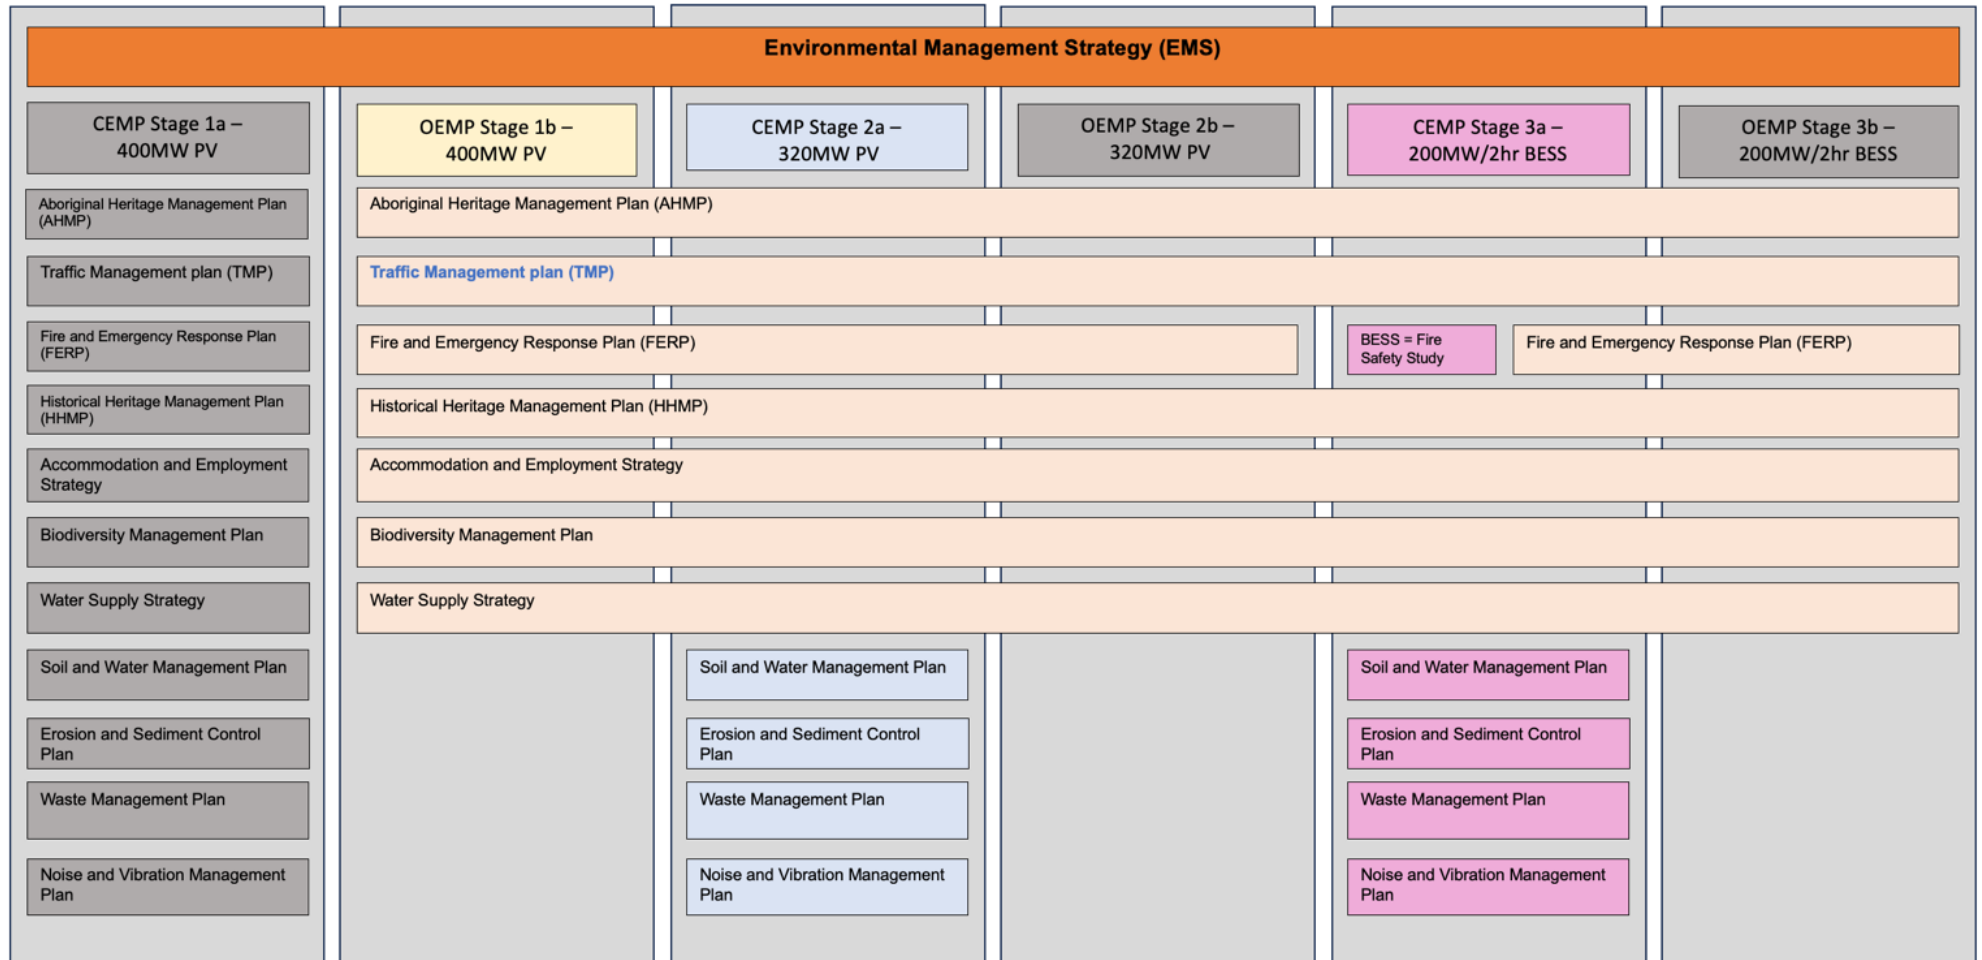

Blue text = This plan. Yellow Boxes = Site wide plans. Grey boxes = not active plans

## 2 Review of Development Traffic and Routes

### 2.1 Construction Period

Construction of New England Solar (NES), including the northern array (Stage 1) and central array (Stage 2) is anticipated to take approximately 40 months from start to completion.

The Stage 1 area, including the TransGrid substation, commenced construction in February 2022, and is expected to conclude in Q4 2023. After which it will move into operations (Stage 1b).

Stage 2a construction will include an Early Works package which is the construction of an access route between Stage 1 and Stage 2. Stage 2a works will start in Q4 2023 and with all works expected to be complete in Q4 2025.

Stage 3a is expected to commence in Q1 2024 and is expected to be complete in Q4 2025.

### 2.2 Traffic Generation

#### 2.2.1 Construction and Operations Phases

Traffic generated for the Construction and Operational phases of the project are to comply with Condition 1 of Schedule 3 of the NES Development Consent, which states:

***Over – dimensional and Heavy Vehicle Restrictions***

*The Applicant must ensure that the:*

- a) development does not generate more than:*
  - 84 heavy vehicle movements a day during construction, upgrading and decommissioning;*
  - 30 over-dimensional vehicle movements during construction, upgrading and decommissioning; and*
  - 5 heavy vehicle movements a day during operations; on the public road network;*
- b) length of any vehicles (excluding over-dimensional vehicles) used for the development does not exceed 26 metres,*

*unless the Secretary agrees otherwise.*


A total of 290 vehicles per day are allowed to travel for the purpose of the Project along the access road. Subject to the cap of 290 vehicles not being exceeded, 84 heavy vehicles are to be shared when construction of Stage 2a and Stage 3a works overlap and an additional 5 heavy vehicle movements for Stage 1b. The length of any vehicles (excluding over-dimensional vehicles) used for the development will not exceed 26 metres,

The remaining vehicle numbers will consist of light vehicles which are to be shared between all stages of the Project. The procedure of how the traffic numbers are managed is in Section 3.9.

Figure 2-1 shows the proposed vehicle movement forecast for all stages of work over the upcoming two years. With the construction Stage 1a expected to complete the transition into operations Stage 1b by Q4 2023 there will be a subsequent reduction in vehicle traffic.

Stage 2a and Stage 3a of works are expected to commence in Q4 2023 and will reach completion in Q4 2025.

Figure 2-1 Proposed vehicle movement forecast

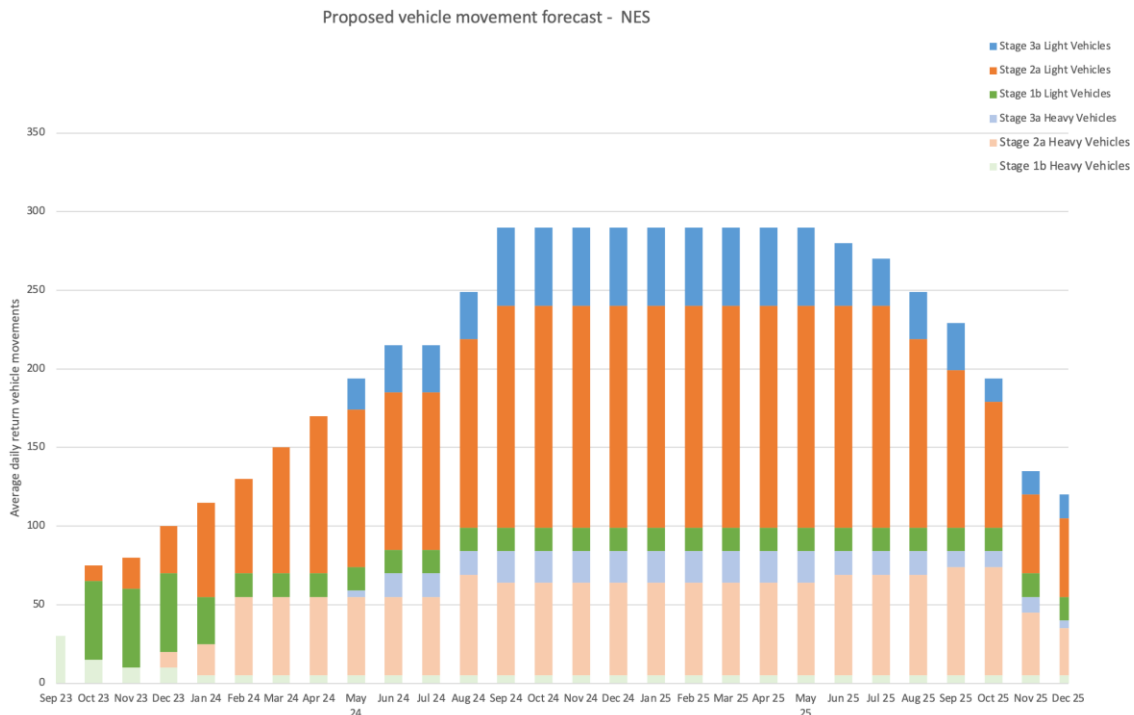

## 2.2.2 Decommissioning and Upgrading Phases

The project generated daily and peak hourly traffic movements have not been calculated and assessed for potential upgrade works required and decommissioning works. These movements are unlikely to exceed the daily and peak hourly project-related light vehicle and truck traffic movements generated during the construction stage, accounting for anticipated mechanical decommissioning processes and associated significantly reduced labour force.

## 2.3 Access Routes

The key components of the Project, including the solar panels, will be delivered to site via the Port of Brisbane. In this regard, heavy vehicle movements would travel from the north via New England Highway by-passing the township of Armidale.

Some construction materials may be sourced from other areas, including Port of Sydney and/ or Port of Newcastle and associated heavy vehicles would travel to the site from the south through the township of Uralla.

All heavy vehicles associated with the Project must travel to and from NES via the New England Highway, Barleyfields Road (North) and Big Ridge Road as stipulated in Condition 3 of Schedule 3 the Development Consent. All construction related vehicles have to cross the level crossing located on Barleyfields Road approximately 130m south-east of New England


Highway/Barleyfields Road intersection. This railway crossing has been upgraded, including road widening, to accommodate construction related vehicle movements. Design of this level crossing upgrade has been undertaken in accordance with the Development Consent and relevant standards.

### 2.3.1 Over Size Over Mass (OSOM) Vehicle Route

There will be a maximum of 30 OSOM vehicle movements that occur during construction, upgrading and decommissioning. OSOM vehicles travelling from the north will turn left from New England Highway into Barleyfields Road to access the site (Figure 2-2). OSOM vehicles coming from the south (Sydney and/or Newcastle) will turn right at the New England Highway/Barleyfields Road intersection to access the site. The New England Highway is a designated OSOM vehicle route and, as such, the geometry of this road is adequate to accommodate OSOM vehicle movements.

All OSOM vehicles will turn left at the Barleyfields Road (North)/ Big Ridge Road intersection to access NES. Whilst the New England Highway is a designated OSOM vehicle route, Barleyfields Road and Big Ridge Road are not designated OSOM routes. Conditions and loading capacities of these roads have been assessed during the design phase of the access road and these roads were used during Stage 1a. Additionally, all OSOM movements will need to be approved by the National Heavy Vehicle Regulator (NHVR) which will examine road suitability before approving and permitting the use of OSOM vehicles on the haulage route. Refer to section 3.17 for further details on the permitting requirements of OSOM vehicles.


Figure 2-2 Over-Size Over Mass Vehicle Route to NES Site

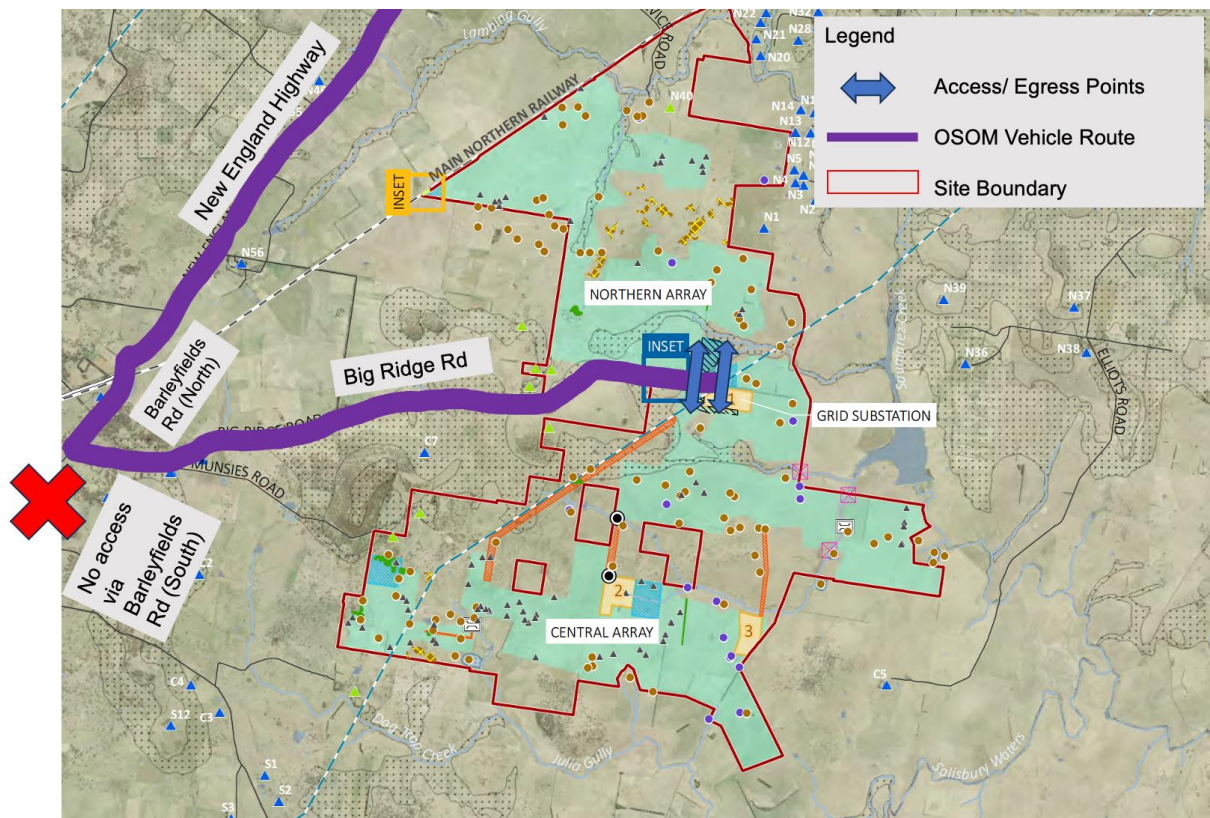

### 2.3.2 Other Traffic Routes (Light and Heavy)

Figure 2-3 shows the heavy and light vehicle routes to access the site. All heavy and light vehicles associated with the development must travel to and from the site via the New England Highway, Barleyfields Road (North) and Big Ridge Road, as shown in the Figure 2-3.

Figure 2-3 Light and Heavy Vehicle Access Routes to NES Site

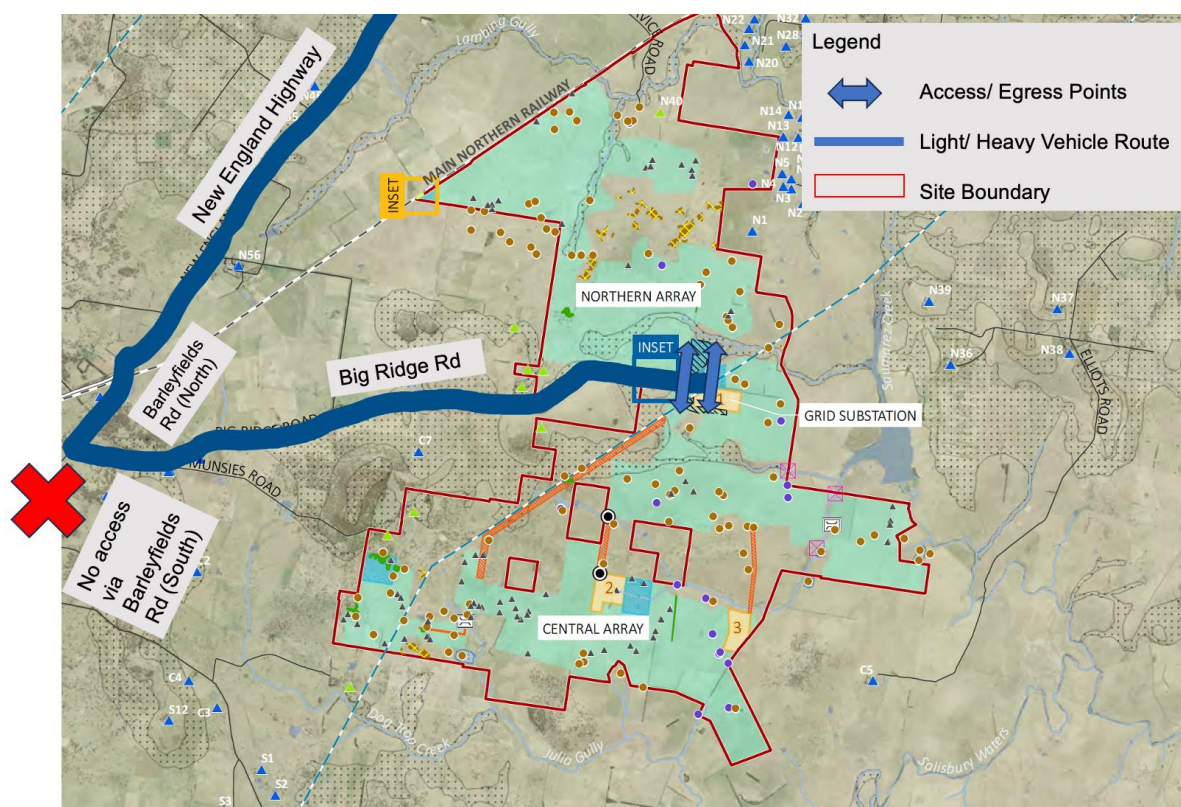

## 2.4 Infrastructure Upgrades

Table 2-1 shows the road upgrade/repair works undertaken on the access road prior to the commencement of Stage 1a construction of the NES project, as stipulated in Appendix 4 of Development Consent. This same access road will be used by all future stages of NES.


Table 2-1 Road Upgrades completed on New England Highway, Barleyfields Road (North) and Big Ridge Road

| ROAD                                      | LOCATION            | REQUIRED UPGRADE                                                                                                                                  |
|-------------------------------------------|---------------------|---------------------------------------------------------------------------------------------------------------------------------------------------|
| New England Highway and Barleyfields Road | Intersection        | Channelised Right Turn with a short turn slot [CHR(S)] treatment for the largest vehicle accessing the site (excluding over-dimensional vehicles) |
| Barleyfields Road                         | Between New England | Seal to a width of 7.2 m with 1 m unsealed shoulders (total carriageway 9.2 m)                                                                    |

| ROAD                                 | LOCATION                   | REQUIRED UPGRADE                                                                                                          |
|--------------------------------------|----------------------------|---------------------------------------------------------------------------------------------------------------------------|
|                                      | Highway and Big Ridge Road |                                                                                                                           |
| Barleyfields Road and Big Ridge Road | Intersection               | Basic Left Turn (BAL) treatment to cater for the largest vehicle accessing the site (excluding over-dimensional vehicles) |
| Big Ridge Road                       | Segment 1                  | Seal to a width of 7.2 m with 1 m unsealed shoulders (total carriageway of 9.2 m)                                         |
|                                      | Segment 3                  |                                                                                                                           |
|                                      | Segment 4                  | Gravel (unsealed) carriageway to a width of 8.7 m                                                                         |
|                                      | Segment 5                  |                                                                                                                           |
|                                      | Site access points         | Rural property access type                                                                                                |

Figure 2-4 shows the location of Barleyfields Road and Big Ridge Road segments where the abovementioned road upgrade works were undertaken.

*Figure 2-4 Location of Barleyfields Road and Big Ridge Road Segments*

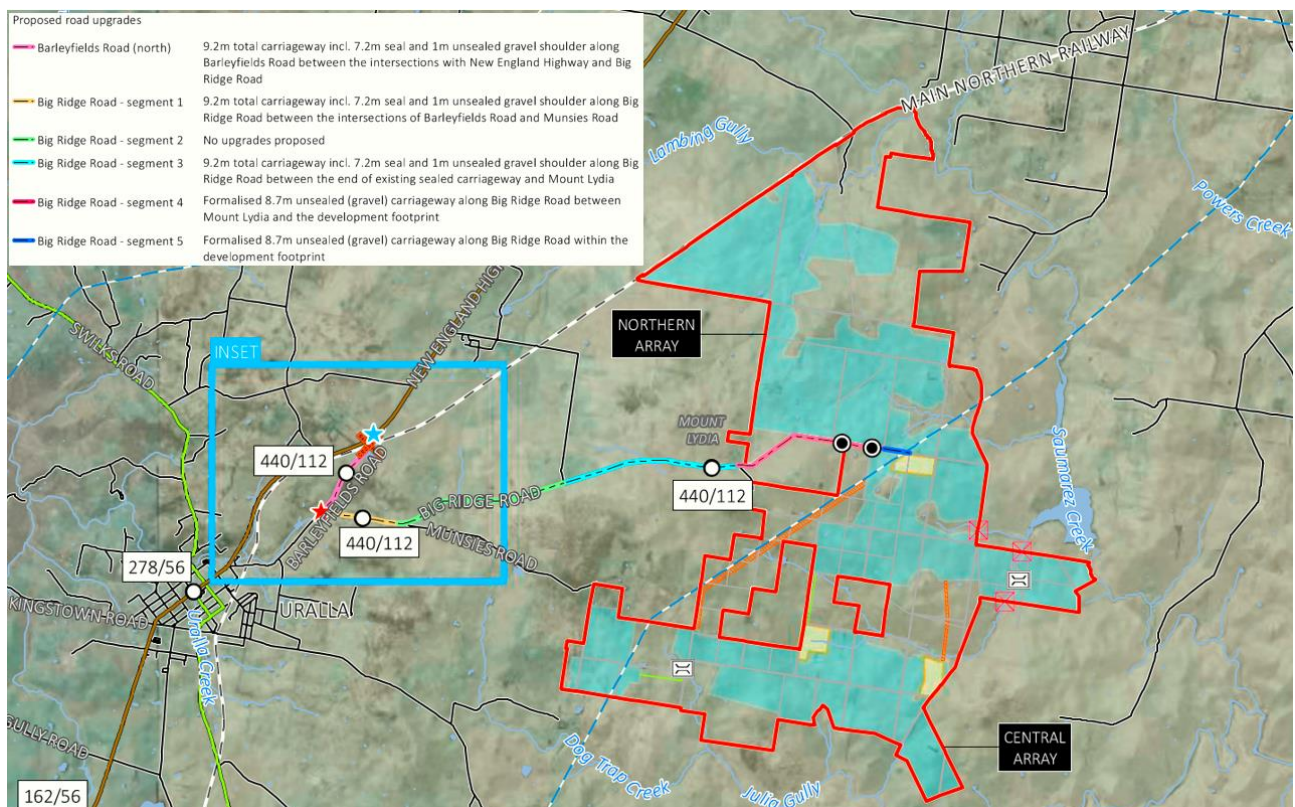

Source: Appendix 4, NES Development Consent

All road upgrades were undertaken in accordance with the Austroads Guide to Road Design and in consultation with and to the satisfaction of the relevant road authorities, including TfNSW

and Uralla Shire Council. Special consideration was also given to ensure that the capacity of the roadside drainage network relating to the abovementioned roads was not reduced.

A shortening of the conditioned Austroads treatment from a Channelised Right Turn (CHR) to a shortened Channelised Right Turn (CHR-S) was implemented at the New England Highway intersection with Barleyfields Road. A CHR-S treatment, in comparison to a CHR treatment reduces the storage capacity for vehicles waiting to turn right from the highway during peak project construction periods. The shortened storage lane introduces an increased risk of overflow of the right turn bay. In the event of overflow of the right turn bay, waiting vehicles would be placed in the northbound lane of the highway in a 100k/h speed environment.

The following management measures have been implemented to mitigate the risk associated with the Shortened Channelised Right Turn (CHR-S) treatment at the New England Highway intersection:

- Implementation of a traffic forecasting and scheduling regime, which aims to meet the key objective of construction traffic not exceeding the capacity of the CHR-S's storage lane.
- Implementation of a "drive-by" measure for northbound project-related vehicles on New England Highway. Such vehicles, who intend to turn right into Barleyfields Road but encounter insufficient space in the right-turn storage lane due to other vehicles already being present in the storage lane, must continue straight towards Armidale. The vehicle must then drive 14km north to the New England Highway/Uralla Road roundabout located on the New England Highway, prior to Armidale. At this roundabout, the vehicle will be able to perform the equivalent of a U-turn manoeuvre by navigating around the large roundabout. Upon exiting the roundabout, the vehicle will then travel in a southbound direction on the New England Highway and turn left at the intersection with Barleyfields Road, then continue to site via the approved access route


In addition, weekly monitoring of the New England Highway/ Barleyfields Road (North) intersection will also be conducted during peak times to confirm the current measures are adequate during the proposed period of increased heavy vehicle movements. If warranted, ACEN Australia could implement further measures, such as scheduling to minimise heavy vehicles (travelling north) from leaving site during the peak afternoon period, and/or implementing Traffic Guidance Scheme's (TGS) to prevent vehicles stopping on the rail crossing.

## **2.5 Internal Roads and On-site Parking Facilities**

All internal roads will be designed as all-weather roads and will be constructed in accordance with the Austroads Guide to Road Design.

A temporary laydown area will be provided to load and unload vehicles on site. All construction related heavy vehicles will enter and leave the site in a forward direction.


Sufficient number of temporary on-site parking facilities will be provided near the temporary lay down area during the construction stage of the Project. Permanent on-site parking facilities will be provided for staff vehicles and other vehicles near the Operation and Maintenance Building.

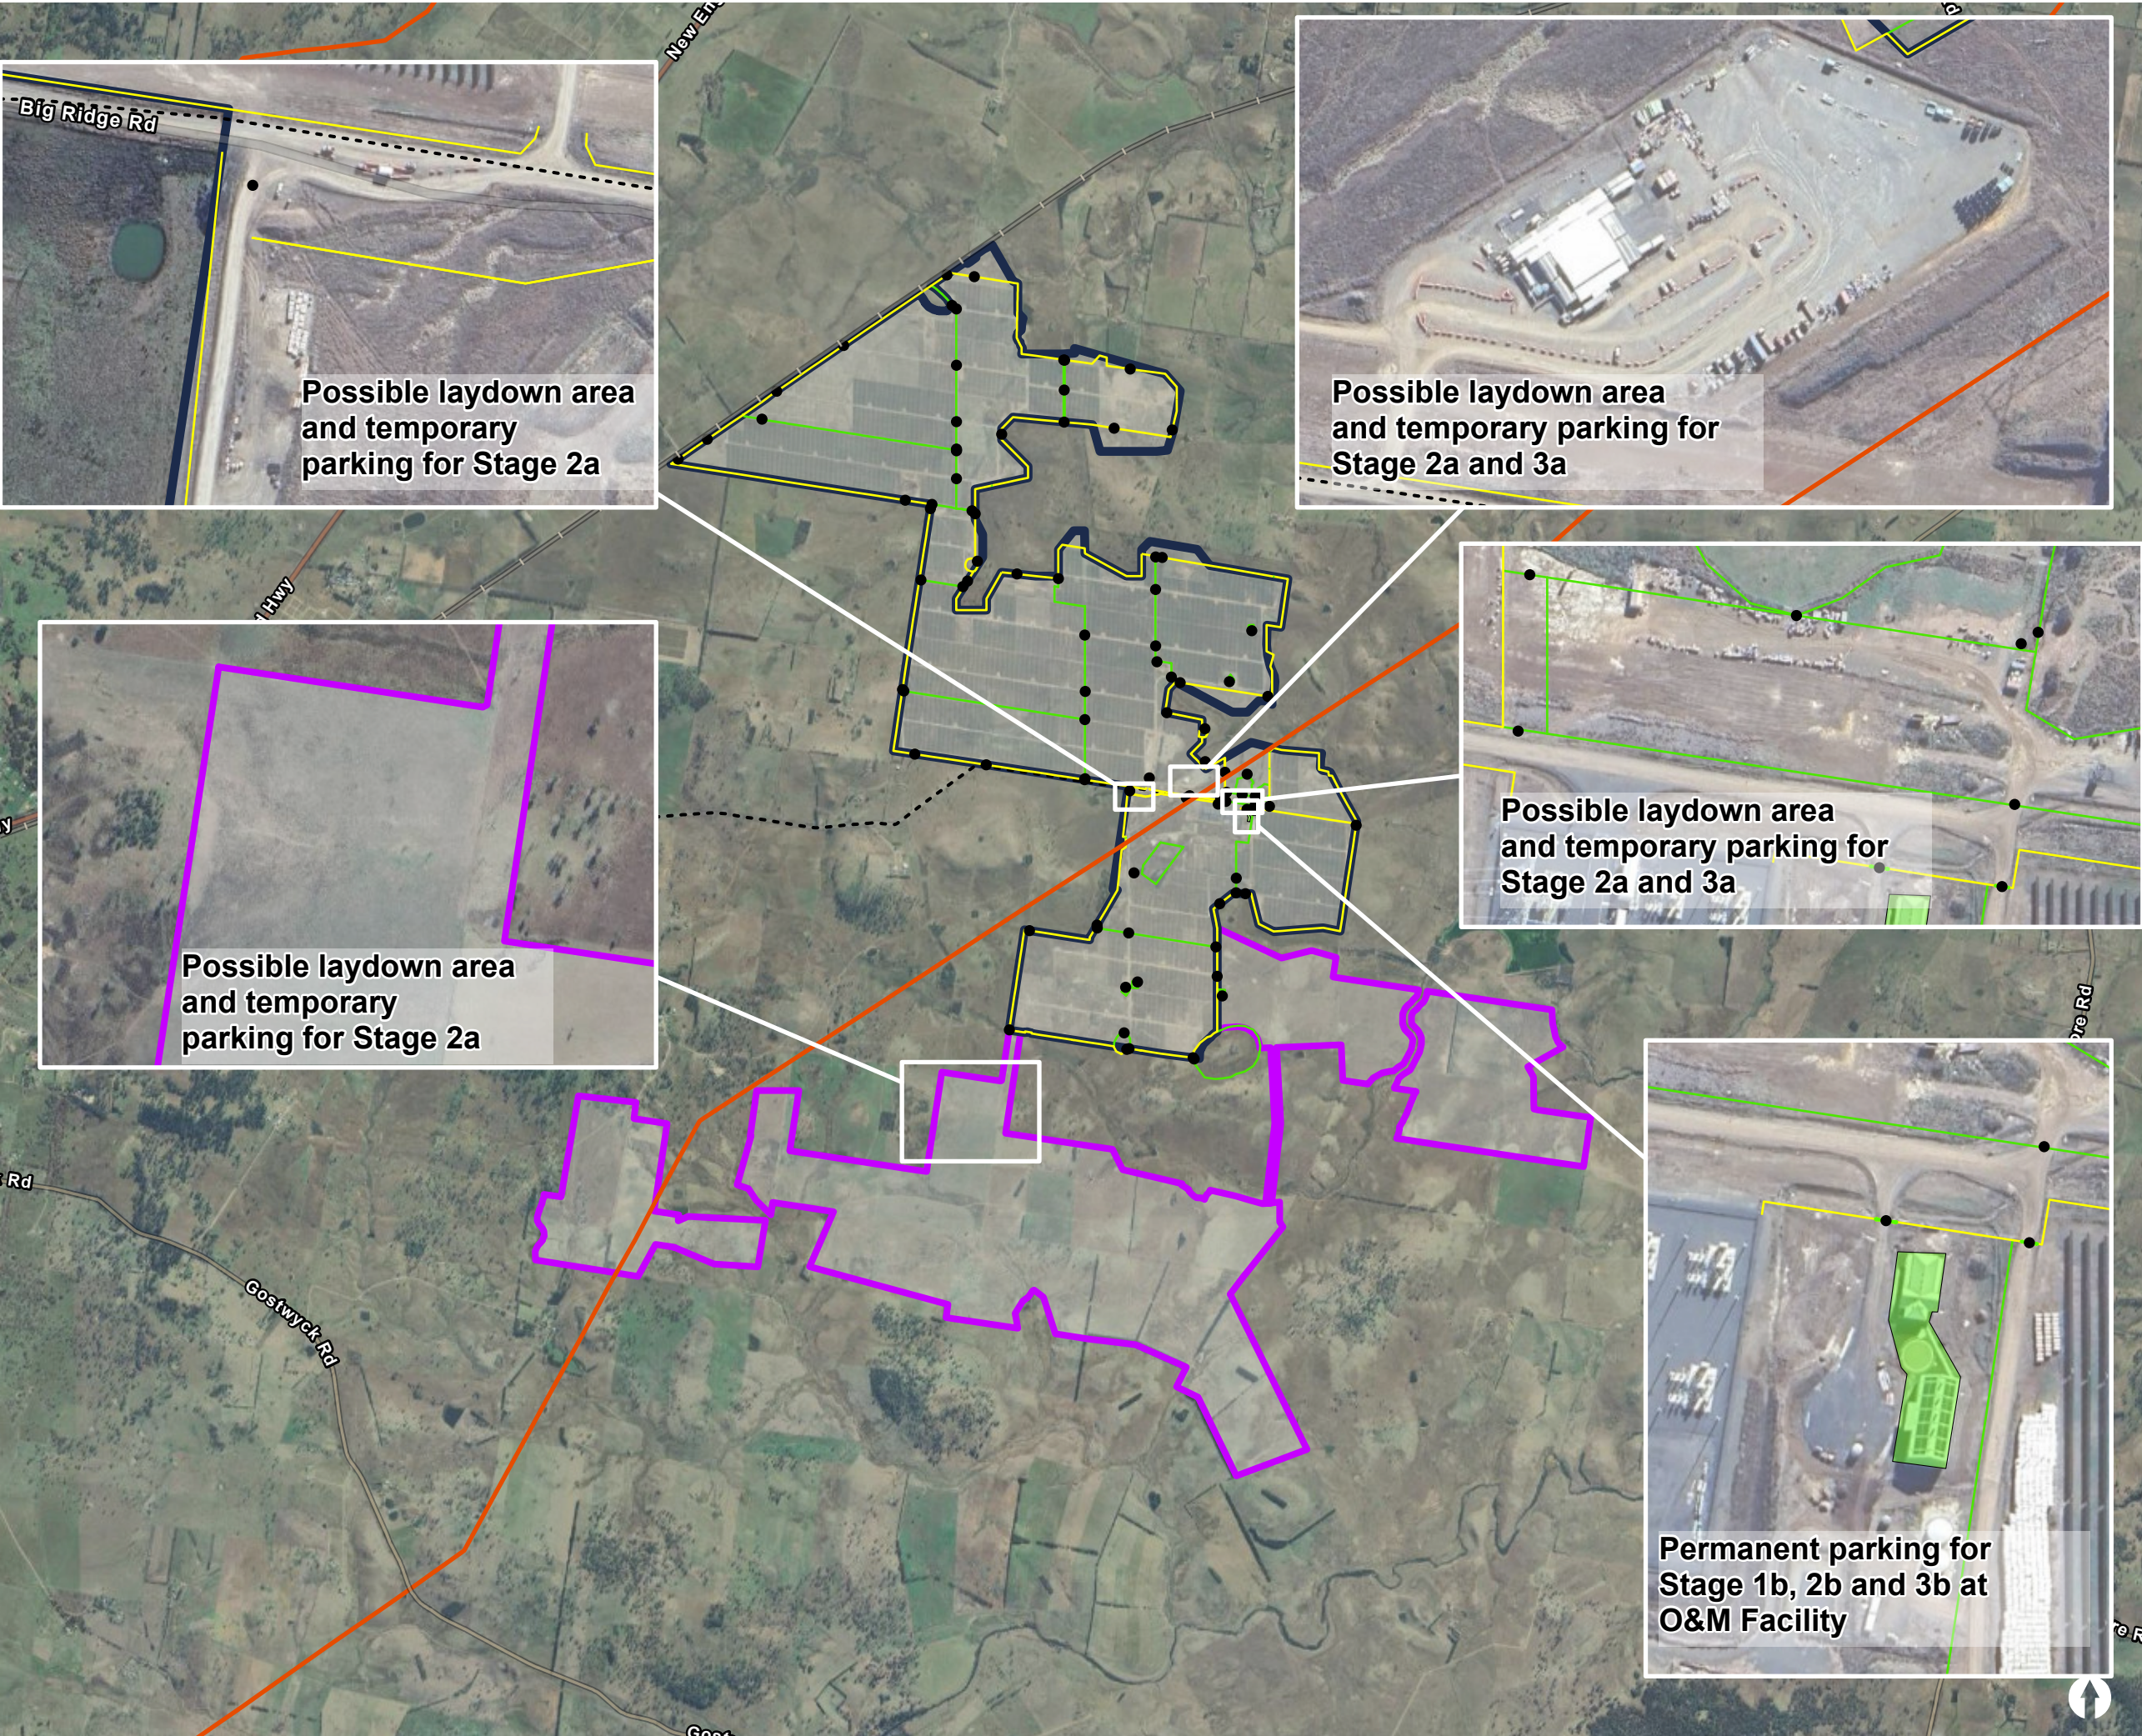

- Legend**
- Site Boundary (Stage 1)
  - Site Boundary (Stage 2)
  - O&M Building
  - Big Ridge Access Road
  - Gates
  - Perimeter Fence
  - Livestock Fence
  - Existing 330 kV Transmission Line

**Notes**

1. This plan is indicative only, parking and laydown areas will be contained within the NES development footprint and are subject to change

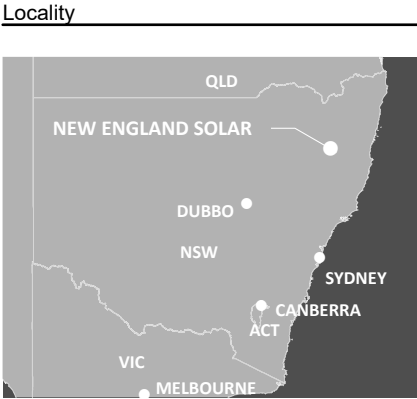


**Project**

**New England Solar**  
Renewable Energy from ACEN

**Title**

Indicative Parking and Laydown Area

**Drawing no.** NESF-P024 **Date** 16/11/2023



## 3 Traffic Management Plan

### 3.1 Introduction

This section provides information on TMP registers, administration, induction, consultation/ notification requirements, detailed traffic management measures to be implemented during construction of NES to manage heavy vehicle movements and to minimise adverse impacts on the road network, TMP review and improvement, as well as auditing and disciplinary procedures.

### 3.2 TMP Registers

Registers to allow for implementation and effective maintenance of the TMP throughout the duration of construction will be prepared by all contractors and reported to ACEN Australia. The registers are detailed in Table 3-1.

*Table 3-1 TMP Registers*

| REGISTER TYPE                | DESCRIPTION                                                                                                                                                                                                                                        |
|------------------------------|----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| Key personnel register       | This register will identify all key personnel and provide contact details for ACEN Australia's and each contractors; Project Manager, Site Supervisor, key subcontractors, as well as contact details for relevant roads authorities.              |
| NES Incident register        | The NES incident register will record all incidents that occur on site, including date and time of the incident, date-stamped photographs of signs and devices in the vicinity of the incident.                                                    |
| NES Variations register      | The purpose of the NES variations register will be to record any modifications to approved traffic management measures, including reason for the modification, date and time of modification and residual risk.                                    |
| NES Maintenance Log/Register | The purpose of the NES maintenance log/register is to record findings of periodic road inspections and road conditions in order to identify required maintenance/repair works                                                                      |
| NES Complaints register      | The NES complaints register will record any complaints received including party making the complaint, contact details, nature of the complaint, and any follow up actions that have been identified and subsequently taken.                        |
| NES Vehicle register         | The NES vehicle register will keep accurate records of the number of OSOM and heavy vehicles entering or leaving the site each day for the duration of the Project to ensure compliance with Condition 2 of Schedule 3 of the Development Consent. |

### 3.3 Roles and Responsibilities

A summary of key personnel on the project, including roles, responsibilities and contact details is provided in Table 3-2.

*Table 3-2 TMP Roles and Responsibilities*

| ROLE                                             | RESPONSIBILITIES                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                          |
|--------------------------------------------------|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| Stage 2a – Contractor Site Supervisor            | <p>The Stage 2a Site Supervisor is responsible for overseeing day-to-day activities and has responsibility for practical application of the TMP. The Site Supervisor's responsibilities include:</p> <ul style="list-style-type: none"> <li>– Facilitate induction of all project staff, including construction personnel and sub-contractors</li> <li>– Responsible for providing daily required HV and LV movements to ACEN Australia's Traffic Management Coordinator</li> <li>– Instruct workers on the relevant safety standards, including the correct wearing of high visibility safety vests</li> <li>– Ensure traffic control measures are implemented and maintained in accordance with the TMP</li> <li>– Render assistance to road users and stakeholders when incidences arising as a result of the Project affect network performance or the safety of road users and workers</li> <li>– Take appropriate action to correct unsafe conditions, including any necessary modifications to the TMP.</li> </ul>                 |
| Stage 3a & Stage 1b Contractor Project Manager   | <p>The Stage 3a and Stage 1b Project Managers are responsible for providing daily required HV and LV movements to the ACEN Australia's Traffic Management Co-Ordinator for approval for the following day. Once approved, the Project Manager is responsible for ensuring this number is not exceeded. Additional responsibilities include:</p> <ul style="list-style-type: none"> <li>– Facilitate induction of all project staff, including construction personnel and sub-contractors</li> <li>– Instruct workers on the relevant safety standards, including the correct wearing of high visibility safety vests</li> <li>– Ensure traffic control measures are implemented and maintained in accordance with the TMP</li> <li>– Render assistance to road users and stakeholders when incidences arising as a result of the Project affect network performance or the safety of road users and workers</li> <li>– Take appropriate action to correct unsafe conditions, including any necessary modifications to the TMP.</li> </ul> |
| ACEN Australia's Traffic Management Co-ordinator | <ul style="list-style-type: none"> <li>– Implement the TMP</li> <li>– Ensure daily HV and LV movements do not exceed permissible amounts.</li> <li>– Amend the TMP, if required,</li> <li>– Manage variations and contingencies and take overall responsibility for traffic management.</li> </ul>                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                        |
| ACEN Australia Project Manager                   | <ul style="list-style-type: none"> <li>– Responsible for incident and non-compliance notification to relevant agencies.</li> </ul>                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                        |
| ACEN Australia HSE Manager                       | <ul style="list-style-type: none"> <li>– Manage emergency situations</li> </ul>                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                           |
| All staff                                        | <ul style="list-style-type: none"> <li>– Correctly wear high visibility vests, in addition to other protective equipment required (e.g. footwear, eye protection, helmet sun protection).</li> <li>– Comply with the requirements of the TMP and ensure no activity is undertaken that will endanger the safety of other workers or the general public</li> <li>– Enter and leave the site by approved routes and in accordance with safe work practices.</li> </ul>                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                      |

| ROLE                                           | RESPONSIBILITIES                                                                                                                                             |
|------------------------------------------------|--------------------------------------------------------------------------------------------------------------------------------------------------------------|
|                                                | <ul style="list-style-type: none"> <li>– Schedule travel in advance in agreement with Traffic Management Co-ordinator for heavy vehicles and OSOM</li> </ul> |
| ACEN Australia<br>Community Liaison<br>Officer | <ul style="list-style-type: none"> <li>– Recording and actioning of complaints during construction and operations.</li> </ul>                                |

### 3.4 Work Health and Safety and Occupational Health and Safety Arrangements

The NES construction site is to be managed under the Contractor's Workplace Health and Safety (WH&S) Management System.

Road maintenance is to be managed under the Contractor's Workplace Health and Safety (OH&S) Management System and related safety management plans prepared by relevant sub-contractors.

Reporting, tracking and corrective action implementation associated with hazards, near-misses and incidents will take place in accordance with the Contractor's Workplace Health and Safety Management system.

### 3.5 Induction for Vehicle Operators and Regular Toolbox Meetings

Induction to the Traffic Management Plan will be undertaken by all project staff, including construction personnel and sub-contractors and will be a condition of engagement.

The purpose of the induction is to provide general awareness of the requirements of the Traffic Management Plan in order that the Plan may be implemented prior to commencement of works and to ensure that employees and sub-contractors are aware of the need to comply with the Plan.

All project staff will be required to complete the online component prior to accessing site. The on-site component will be completed by project staff upon their arrival to site.

Key actions and requirements of staff depending on work to be undertaken will be detailed and an opportunity provided for clarifications to be made, should this be necessary.

The aim of the online induction is to provide project staff the necessary information required to safely access the site as well as ensuring site access occurs in conformance with the conditions of the development consent. The online induction will include:

- Inform the participants of the "drive-by" measure to be executed where the CHR-S storage lane is occupied. Site-wide communications such as pre-start and toolbox talks will include reinforcement of the "drive-by" measure to be undertaken when the CHR-S storage lane occupied
- The permitted access routes to and from the construction site for site staff and delivery vehicles

- The need to adhere to local speed limits
- Standard environmental, WH&S, driver protocols and emergency procedures

Daily toolbox talks will highlight specific measures for activities being undertaken, which will include site-specific briefings for relevant personnel and are ongoing. The toolbox talks will also include daily weather forecasts and procedures to be followed during any adverse weather conditions as well as reinforcement of the “drive-by” measure to be undertaken at the New England Highway intersection when the CHR-S storage lane occupied.

A point of contact will be provided for any queries that workers may have, and the change management procedure explained so that workers know how changes to the Plan over time will be disseminated.

An audit process will be implemented to ensure driver compliance with the requirements of the Plan and details of enforcement protocols provided should drivers breach restrictions applied.

## **3.6 Consultation/ Notification Requirements**

### **3.6.1 Notification**

ACEN Australia will consult with local community representatives, landowners and statutory consultees, as required, before and throughout the construction and upgrading works.

The local community, sensitive receptors to the project along the access road and other relevant stakeholders will be provided information about proposed and ongoing activities and impacts, in particular, those which could have potential to cause disruption, such as abnormal load deliveries. This will be undertaken by way of direct communication with relevant stakeholders, as well as through regular Facebook updates led by ACEN Australia’s community liaison officer.

In addition, the project phone line (1800 844 889) is available for the general public to call if they have a query regarding traffic movements.

### **3.6.2 Consultation**

Consultation was completed for Version 7 of the TMP with TfNSW and Council, which was approved by the Planning Secretary on 23<sup>rd</sup> December 2022.

More recently, ACEN Australia conducted consultation with Uralla Shire Council regarding the version 8 of the TMP which reflects the inclusion of Stage 2a and 3a works. This includes a meeting with the Interim General Manager, Acting Executive Director Infrastructure & Development, executive Manager Civil Infrastructure, Manager Civil Infrastructure and Manager Development & Planning on 23 August 2023, as well as a meeting with Acting Executive Director Infrastructure & Development, Manager Development & Planning, Councillors and the Mayor on 20 September 2023. Council did not raise any concerns during this meeting and a copy of Version 8 of the TMP has been submitted for review and comment which will be noted in Appendix B.

ACEN Australia contacted TfNSW on the 26<sup>th</sup> of September requesting a review of Version 8 of the TMP as per Appendix B. TfNSW raised a number of comments, but no amendments were made to the TMP as a result of this consultation.

## **3.7 A Driver's Code of Conduct**

All staff of NES must:

- Undertake a visitor induction carried out by an approved member of project staff, or suitably qualified person under the direction of NES management, which is discussed in Section 3.5.
- Hold a valid driver's licence for the relevant class of vehicle
- Operate the vehicle in a safe manner within and external to the project site
- Comply with the direction of authorised site personnel when within the site
- Comply with any specific traffic control measures implemented for NES on the internal and external road networks. This includes any traffic control measures which ensures the safe and efficient operation of the CHR(s) treatment for the New England Highway and Barleyfields Road intersection. These measures will be outlined in the Traffic Guidance Scheme.
- Review a map of the local haulage route which shows any constraints or conditions along the roads.

The designated heavy vehicle routes will be discussed with all vehicle operators during the induction process as discussed in Section 3.5. Regular toolbox talks will emphasise the importance of safe driving and adherence to local posted speed limits and penalties for any valid complaints including speeding and inappropriate driving behaviour as per the Drivers Code of Conduct.

### **3.7.1 Vehicle Speeds**

Increased speed means an increase in the risk of a crash, as well as an increase in severity if an accident occurs. A study undertaken for the Australian Transport Safety Bureau found that travelling 10 km/h faster than the average traffic speed can more than double the risk of involvement in a casualty accident.

There are two types of speeding:

- Where a vehicle travels faster than the posted speed limit; and
- Where a driver travels within the speed limit but because of road conditions (e.g. fog or rain) this speed is inappropriate.

All posted speed limits are to be strictly adhered to at all times. The existing speed limit on Barleyfields Road and Big Ridge Road is 80 km/h. A temporary speed limit reduction will be implemented on these roads for the duration of construction of the solar farm to enhance and ensure appropriate road safety. The details of the reduced speed limit and other safety measures have been discussed with TfNSW and Uralla Shire Council as part of the Traffic Guidance Scheme and will be revised if necessary.

Vehicle speed on public roads is enforced by the NSW Police Service. There are three types of penalties established under Heavy Vehicle National Law and Regulations (HVNL):

- Infringeable offences – an offence which results in the issue of an infringement notice. It gives the person issued the notice the option of either paying the penalty set out in the notice or electing to have the matter dealt with by a court.
- Court imposed penalties – some offences are not infringeable and must be dealt with by a court. The HVNL sets out the maximum penalty level that the court may apply.
- Demerit points – are managed through each state and territories' road traffic law (NHVR, Penalties and infringements, 2017).

All vehicle drivers operating out of NES project site are to observe the posted speed limits, with speed adjusted appropriately to suit the road environment and prevailing weather conditions, to comply with the NSW Road Rules & Heavy Vehicle National Law. Vehicle speeds must be appropriate to ensure the safe movement of vehicles based on vehicle configuration.

### **3.7.2 Heavy Vehicle Driver Fatigue**

Driver fatigue or drowsy driving is a safety hazard for the road transport industry. The main causes of fatigue are not enough sleep, driving at night (during sleeping hours) and working or being awake for a long time (NHVR, 2017). It is one of the biggest causes of accidents for heavy vehicle drivers. National heavy vehicle driver fatigue laws apply to fatigue-regulated heavy vehicles, which are:

- A vehicle with a Gross Vehicle Mass (GVM) of over 12t
- A combination when the total of the GVM is over 12t
- A truck or a combination including a truck, with a GVM of over 12t with a machine or implement attached.

Under the law, working hour options for fatigue management are:

- Standard hours
- Basic fatigue management
- Advanced fatigue management

All heavy vehicle drivers operating out of the NES project site are to be aware of their adopted Fatigue Management Scheme and operate within its requirements. By law, all drivers have a duty to not drive a fatigue-regulated heavy vehicle on a road while impaired by fatigue.

### **3.7.3 Procedures**

All drivers are to adhere to the designated access route and ensure safe driving practices are being implemented.

The designated access route is as per Section 2.3 for both OSOM vehicles and heavy and light vehicles. Drivers travelling to or from the site must do so safely, in full compliance with the law, including in respect of speed limits, following distances, forward sight when overtaking, being able to stop within the length of road visible (or half the length on roads without centrelines), and not driving carelessly or dangerously.

All drivers must follow the following requirements at all times.

- Do not drive whilst under the influence of alcohol, drugs, nor any medication which may affect ability to drive.
- Be medically fit to drive and must inform site coordinators if they have any medical condition which may affect their ability to drive.
- Drive in a considerate manner and respect the rights of others to use and share the road space.
- Report all vehicle defects to their employer. Serious defects (e.g. e.g. brakes, steering) must be corrected immediately, or an alternative vehicle supplied.
- Any vehicle incident resulting in injury or significant damage to property must be reported to the police.
- Report any near misses.
- Always adhere to the site working hours
- Securely fasten and cover load with the appropriate use of ratchets straps, tarpaulins or covers (loose material), chains and load binders, for example. Relevant vehicular load limits are not to be exceeded and all loads are to be suitably balanced. The maximum rear overhang shall not exceed limits under by relevant road rules for respective vehicle types.
- Keep their vehicle clean, including suitable vision through all windows and mirrors and ensuring that their numberplate is always visible.
- In good mechanical condition.
- Extra care should be taken when driving at dawn or dusk, being particularly watchful for wildlife and/or livestock.
- Vehicles must give way to pedestrians, cranes, forklifts, mobile plant, emergency vehicles and livestock.
- Drivers must adhere to the required access route outlined within Section 2.3 which follows Barleyfields Road (north) and Big Ridge Road.

The following provides further guidance as the required safety procedures for specific incidences:

- Timing of deliveries are to be coordinated by the contractor in order to prevent heavy vehicles travelling through school zones during peak times;
- When aware of any emergency vehicles, approaching from in front or behind, drivers must pull over well in advance to provide unimpeded movement;
- Drivers must reduce their speed and or stop in accordance with the law when passing a school bus which is slowing down, stopped, or accelerating in relation to picking up or setting down children;
- Drivers must reduce their speed in accordance with the law when:
  - Passing children walking, cycling or waiting on the side of the road;
  - Passing an oncoming school bus;
  - Passing someone riding or leading a horse along the road;
  - Approaching an area where a stock shift is known to be occurring.
- Heavy vehicles must not use engine brakes in built up areas, except where the load being carried and the grade of the road make use of such braking absolutely necessary for safe driving;
- Heavy vehicles are to let traffic behind them pass at regular locations including those opportunities that occur at intersections, wide driveways, sections of road with adequate forward sight distance, gravel pits etc; and

- Dedicated rest stops are to be established and utilised by drivers to reduce driver fatigue.

These procedures will be reiterated during pre-start discussions and form part of site inductions. Failure to comply with the above procedures will result in the Disciplinary Procedure (Section 3.24) being implemented.

## **3.8 Dilapidation Survey**

The purpose of undertaking dilapidation surveys is to document the condition of Barleyfields Road (North) and Big Ridge Road prior to and following construction, upgrading or decommissioning of NES.

During construction, road condition inspections of Barleyfields Road (North) and Big Ridge Road will be carried out weekly during peak times as identified in Figure 2-1, by the ACEN Australia Traffic Coordinator. The road condition inspections will identify and categorise defects, and describe the proposed management measure and implementation timeframe. The access road condition inspection checklist is provided in Appendix C.

During operations these inspections will be completed every 6 months as per Appendix C.

Uralla Shire Council will be notified of any repairs identified during the road condition inspections.

### **3.8.1 Dilapidation Methodology**

The dilapidation survey will be undertaken by a qualified person. The survey will be conducted during daylight hours in clear weather and will include both sealed and unsealed roads. To gather sufficient evidence for the dilapidation survey, GoPro cameras, or similar should be used and attached to the survey vehicle. Cameras should be used to capture the road pavement, as well as the left and right side of the road surrounds, including GPS encoding. The GPS must be overlaid onto images to provide a deliverable that can be viewed on any standard PC.

Videos require to be reviewed by trained technical inspectors and any visible defects logged with a still image from the video, location and description all entered into a register. This serves as a record of the condition at a specific point in time.

### **3.8.2 Dilapidation Protocol**

#### **3.8.2.1 Reporting**

A suitably qualified civil engineer with road design and construction experience will review any defects recorded in the register prepared during the dilapidation survey.

A pre-assessment survey of Barleyfields Road (North) and Big Ridge Road conditions has been undertaken by a qualified person and the findings of are summarised in the 'Road Dilapidation Survey' report (dated: 30 September 2020).

A dilapidation report has been prepared after the access road upgrades works, which specifies any requisite road repair works, including details of the rehabilitation works.

Utilizing a similar template, a dilapidation survey will be performed at the following milestones:

- At the completion of Stage 1 construction.
- At the completion of Stage 2 construction.

- Prior to any upgrading activities.
- At the completion of any upgrading activities.
- Prior to any decommissioning activities.
- At the completion of decommissioning activities.

The dilapidation report will be submitted to Uralla Shire Council for its concurrence.

### **3.8.2.2 Consultation**

Uralla Shire Council is responsible for the operation and maintenance of Barleyfields Road and Big Ridge Road. A representative from Uralla Shire Council will be invited to participate in the future dilapidation inspections, as appropriate.

## **3.9 Protocol for monitoring daily traffic movements**

During peak periods as identified in Figure 2-1, weekly forecasting will be completed by all contractors for the following week's predicted daily traffic movements. These numbers are reported to ACEN Australia's Traffic Management Coordinator to ensure compliance is achieved with the development consent. These numbers will be verified the day prior to vehicle movements occurring to confirm the total cap per contractor.

If a contractor is close to exceeding their allocated daily cap, they will be notified by ACEN Australia's Traffic Management Coordinator and it will be the Contractor's Project Managers (or delegate) responsibility to ensure the cap is not being exceeded. If the cap is exceeded, this will be reported to ACEN Australia who will discuss with the contractor next steps. Failure to comply with the development consent may result in dismissal of the contractor.

## **3.10 Protocol for Barleyfields Road (North) and Big Ridge Road Repair Works**

A dilapidation survey will be undertaken as per Section 3.8.2.1.

The condition of Barleyfields Road (North) and Big Ridge Road after each stage is constructed will be compared to their condition prior to the commencement of construction.

Any degradation in the condition of the road, as identified through differences evident in the pre and post construction dilapidation surveys, will effectively become the road repair works required.

ACEN Australia or its contractor will then lodge a road opening permit application to undertake the works with the Uralla Shire Council, with the 'extent of proposed works' cross referenced back to the Dilapidation Report.

## **3.11 Protocol for Operational Maintenance of Segment 4 and 5 of Big Ridge Road**

Maintenance of Section 4 and 5 of Big Ridge Road during the operational stage of the Project will follow the general principles provided in Chapter 8 of the Austroads Guide to Pavement Technology (AGPT) Part 6. In particular:

- A visual inspection of the road shall be carried out every 2 years by an inspector with a minimum of 5 years' experience in road maintenance.
- The South African Approach (Section 8.5.1) shall be used to classify the road condition. A copy of the Draft TMH12 is provided in Appendix D.
- The Type, degree and extent of distress shall determine the intervention to be followed - see Table 3-3 below as a guide.
- Interventions shall be undertaken on road segments that are classified as poor and very poor

*Table 3-3 Road Distress Type and Potential Interventions*

| DISTRESS TYPE  | PATROL GRADING | RIP AND RESHAPING | REGRAVELLING | DUST SUPPRESSION | RECONSTRUCTION |
|----------------|----------------|-------------------|--------------|------------------|----------------|
| Loss of gravel |                |                   | X            |                  | X              |
| Potholes       |                | X                 |              |                  |                |
| Rutting        |                | X                 | X            |                  |                |
| Erosion        |                | X                 | X            |                  |                |
| Corrugations   | X              | X                 |              |                  |                |
| Loose material | X              |                   |              |                  |                |
| Stoniness      |                | X                 | X            |                  |                |
| Dust           | X              |                   |              | X                |                |
| Cracking       |                | X                 | X            |                  | X              |

Segment 4 and 5 of Big Ridge Road will be maintained to the standard identified in Appendix 4 of the Development Consent and Section 2.4 of this TMP for the life of the development.

### 3.12 Temporary Traffic Controls, including Signage

Stage 1a has prepared a Traffic Guidance Scheme (TGS) for signage and traffic control along the access road for NES. Subsequently this plan shows the type and location of temporary signage on Barleyfields Road and Big Ridge Road along the construction vehicle route. This temporary signage includes a reduction in the posted speed limit as described in Section 3.7.1 of this Plan. The signs have been installed and it is the intention to maintain signage as is to reduce confusion for returning workers.

Flagging and temporary signage has also been installed to ensure drivers are aware of the location of the gatekeepers' residence in the vicinity of the rail crossing on Barleyfields Road, given its close proximity to the road and potential accidental damage.

The Stage 2a Contractor will review and amend the Traffic Guidance Scheme (TGS) if required. TfNSW and Uralla Shire Council will be consulted of any amendments (if required) to the TGS prior to its implementation.

The Stage 2a contractor will seek formal direction from relevant roads authorities for installation of any temporary signage, including restoring the existing speed limit on completion of the Project.

### **3.13 Safety Initiatives for Transport through Residential Areas and/or School Zones**

Before construction starts, local and regional schools will be consulted, where appropriate, for current bus timetables on relevant construction traffic routes. Suitable windows of inactivity (curfew times) will be arranged in agreement with the relevant schools and local Councils, which will apply to both heavy vehicles and OSOM deliveries. School bus routes will be reviewed at the beginning of each school term in consultation with the local and regional schools and Uralla Shire Council and, if required, updated windows of inactivity (curfew times) will be arranged.

The local road network is used by school buses during typical school pick up and drop off times. Staff vehicles are unlikely to conflict with school bus services, as they will be accessing and egressing the site prior to and after school hours.

Heavy vehicles will be scheduled to minimise any potential conflict with local school buses by confirming typical times buses run through the area and scheduling heavy vehicle deliveries outside of these times.

UGL/TfNSW have been consulted for information relating to rail services and frequencies. This information will be used to assist in scheduling of construction materials to the site in order to minimise any impacts on roads and potential queuing on Barleyfields Road (North).

During Stage 1a, minimal consideration was required for potential interference with local school buses or rail services as it was found these services had limited impact on traffic.

### **3.14 Management of Dirt Tracked onto the Public Road Network**

In order to minimise the impact of dirt tracked onto the public road network, wheel cleaning facilities will be put in place at the site for the duration of construction work. In addition, each contractor will carry out inspections and deploy where necessary a road sweeper on routes affected by construction traffic and at construction access points prior to commencement of construction and subject to regular review.

During Stage 1a works, a main rumble grid and wheel wash bays were installed. The rumble grid was positioned in a central location near the access road. Wheel wash bays were located strategically at key areas near the construction boundary. With Stage 1b commencing and the internal access roads now construction, Stage 1b vehicles will rarely leave the roads and are not susceptible to mud and seeds. One wheel wash bay will remain during operations and all others have been removed.

It is expected that a similar approach will be undertaken for Stage 2a and Stage 3a.

### **3.15 Management of Employee Shuttle Bus Service**

Each company involved in the project will supply and operate their own minibuses. These minibuses will be used for transport to and from site and also for transport within the site. Each company will organise their own pick-ups and drop-offs. Prior to implementing a shuttle bus service, approval will be sought from Uralla Shire Council and TfNSW.

Further, there will be clauses in contracts to ensure private vehicles accessing site are minimised. A permitting process to bring a private vehicle to site may be implemented.

For Stage 1a the minibus usage was very successful and implemented by most subcontractors. Some subcontractors required specialized equipment from their 4WDs and vans so were unable to arrange minibuses.

### **3.16 Scheduling of Haulage Vehicle Movements to Minimise Convoy Lengths or Platoons**

Each Contractor will prepare a schedule for delivery of construction equipment and materials to site upon completion and finalisation of the construction program based on the total/daily number of constructions related heavy vehicle movements. In particular, scheduling for delivery of solar farm components from the Port will be undertaken to avoid convoy lengths or platooning on roads, including New England Highway, Barleyfields Road (North) and Big Ridge Road.

### **3.17 Responding to Local Climate Conditions**

Each contractor will liaise with construction personnel, sub-contractors and suppliers and develop a response to local climate conditions that may affect road safety, such as fog, dust, wind, wet weather and flooding, which will be communicated to relevant parties, as appropriate.

This will include, but is not limited to the following:

- Monitoring of daily weather forecast and provision of a report to staff and heavy vehicle operators
- Inclusion of any adverse weather forecast in toolbox talk topics
- Watering of roads during dry conditions to ensure appropriate mitigation of dust from traffic and construction activities.
- Monitoring bush fire forecasts and conditions during the dry season and conveyance of relevant information, as appropriate.
- monitoring of all flood ways on external access and egress roads
- monitoring of forested areas that may present additional hazards in the case of bushfire or damaging wind.

### **3.18 Over-Size and Over Mass Vehicles (OSOM)**

The site will generate up to a maximum of 30 OSOM vehicle movements associated with the delivery of substation components. The delivery may occur from Port of Brisbane (from north) or from Sydney/New Castle (from south). The routes from Brisbane (from north) and Sydney/New

Castle (from south) up to the New England Highway/Barleyfields Road intersection is an approved OSOM vehicle route and will be able to adequately cater for the OSOM movements generated as shown in Figure 2-2.

Barleyfields Road and Big Ridge Road are not approved OSOM routes and permission will be sought from relevant roads authorities for use these roads for OSOM vehicles.

Under the Heavy Vehicle National Law, when a heavy vehicle exceeds the general access class weights and/or dimensions a Permit for Heavy Vehicle Access must be obtained.

It will be the responsibility of the heavy vehicle operators involved in the project to obtain and manage their Permit for Heavy Vehicle Access in case it is required. To get the permit, the HV operators will need to lodge a permit application via the NHVR Portal and the NHVR will seek the relevant road managers consent.

The impact of OSOM deliveries will be managed under the use of pilot/escort vehicles as per TfNSW guidelines.

### **3.19 Framework for Handling/Approval of Exception (for emergency or other unforeseen circumstances) to the exclusion of heavy vehicles utilising the Barleyfields Road (south) during construction of the Project**

In case of emergency closure of Barleyfields Road (North) during the construction of NES, emergency vehicles will access the site using Barleyfields Road (South) via Wood Street, Uralla.

All construction related vehicles are not permitted to use Barleyfields Road (South) via Wood Street, Uralla to access the site. Therefore, all construction related heavy vehicle movements to the site will be halted during emergency closure of Barleyfields Road (North) and will recommence following reopening of the road.

Emergency arrangements for the wider Project are addressed in the Fire and Emergency Management Plan.

### **3.20 Coordination of Construction Traffic with Seasonal Agricultural Haulage**

Due to the nature of agricultural activities in the area primarily consisting of livestock grazing, the agricultural haulage along Big Ridge Road is not heavily seasonally dependent, but rather sporadic in nature and irregular in frequency and volumes.

There currently exists no property access arrangements that need to be maintained during the upgrade of Big Ridge Road so that farming activities are not compromised, but regular contact is held with neighbours along the access road.

### **3.21 Variation from Approved Traffic Management Plan**

Revisions to the Traffic Management Plan will be in accordance with relevant requirements and will be made in consultation with TfNSW and other key stakeholders to ensure they remain relevant to the work being undertaken.

The Traffic Management Plan will be updated in response to the identification of hazards, near misses, incidents, accidents, or other processes and procedures that require clarification, or where deficiencies and improvement opportunities have been identified.

Any changes to the TMP will comply with the requirements of Condition 2 of Schedule 4 of the Development Consent.

Amendments will be submitted by ACEN Australia to all relevant authorities and all necessary approvals sought, as required.

When amendments are made the entire document will be updated. The revision number will be updated, and amendments recorded on a revisions sheet. The latest up to date version of the TMP will be available on the New England Solar website ([www.newenglandsolar.com.au](http://www.newenglandsolar.com.au)).

### **3.22 Traffic Management Plan Review**

This plan will be reviewed (and updated if necessary) in the following circumstances:

- Prior to the commencement of a future Stage
- Prior to carrying out any upgrading or decommissioning activities on site (in accordance with Schedule 4, Condition 2a of the development consent).
- Within 1 month of the following (in accordance with Schedule 4, Condition 1 of the development consent):
  - Submission of an incident report under Schedule 4, Condition 7;
  - Submission of an audit report under Schedule 4, Condition 9; or
- Prior to carrying out works associated with any modification to the conditions of the development consent (in accordance with Schedule 4, Condition 2c of the development consent).

Any updates to the Traffic Management Plan are to be to the satisfaction of the Secretary.

### **3.23 Traffic Management Plan Auditing**

Independent environmental audits will be undertaken as per the requirements set out in the development consent to review the performance and progress of the Traffic Management Plan.

Auditing will report on compliance with processes, procedures and directions provided in the Traffic Management Plan. Any non-conformances will be identified, and corrective measures recommended and actioned to prevent the occurrences.

In addition, bi-monthly auditing will be conducted, which will include:

- A review of traffic management and control measures on site and on the access route.
- Ensuring dirt being tracked onto the sealed public road network is being minimised (i.e. development-related vehicles leaving the site are in suitably clean condition).
- Ensuring that development-related vehicles are using the approved access route and not travelling on Barleyfields Road (south).

- Bi-monthly auditing reports are to be maintained so as to provide evidence of conformity to the Traffic Management Plan.

### **3.24 Disciplinary Procedure**

All contractors will be required to adhere to the TMP. ACEN Australia will stipulate that all contractors disseminate requirements of the TMP to their sub-contractors by means of a toolbox talk or similar type meeting prior to commencement of construction. Follow-up /refresher talks will be held if found to be necessary.

Failure to follow the procedures outlined in this TMP will lead to disciplinary/ enforcement as follows:

- First offence: Representative receives a yellow card, and the supplier receives a warning letter.
- Second offence:
  - If by the same representative, then the representative receives a red card and is banned from site and the supplier receives a warning letter.
  - If by a different representative, then the second representative receives a yellow card, and the supplier receives a warning letter.
- Second red card: Supplier will be removed from the applicant's approved supplier list.

### **3.25 Complaints**

The local community and other relevant stakeholders will be provided information about proposed and ongoing activities and impacts, in particular, those which could have potential to cause disruption, such as abnormal load deliveries.

A Facebook page has been set up to ensure pro-active notification of all transport issues and impacts, proposed management and mitigation.

The following contact details are available for the community to make a complaint or send an enquiry:

- A 24 hour telephone number (1800 844 889)
- An email address to which electronic complaints may be transmitted ([info@newenglandsolar.com](mailto:info@newenglandsolar.com)).
- A Facebook page has been established (<https://www.facebook.com/newenglandsolarfarm>).

These details are provided on the NES website.

## **3.26 Notifiable Incidents**

### **3.26.1 Incident Procedures**

Incidents that occur within an area subject to the Traffic Management Plan and/ or Traffic Guidance Scheme will immediately be reported to ACEN Australia and TfNSW.

If a traffic incident occurs within a construction works zone or any other location affected by the works, this will be recorded and reported in accordance with the TfNSW Traffic Control at Work Sites Technical Manual.

Reporting will include recording traffic controls in place at the accident site, including traffic control devices and location, as well as photographic evidence of the signage and incident. The record will be maintained and provided to ACEN Australia immediately and TfNSW within 2 days of the incident.

Actions arising from the investigation of the incident will be actioned through the report and immediately corrected for prevention of further incidents.

### **3.26.2 Material Harm incidents**

The Development Consent defines an incident as:

*An occurrence or set of circumstances that causes or threatens to cause material harm.*

The Development Consent defines material harm as harm that:

- *involves actual or potential harm to the health or safety of human beings or to ecosystems that is not trivial; or*
- *results in actual or potential loss of property damage of an amount, or amounts in aggregate, exceeding \$10,000 (such loss includes the reasonable costs and expenses that would be incurred in taking all reasonable and practicable measures to prevent, mitigate or make good harm to the environment).*

This definition of 'material harm' is consistent with the definition in Section 147 of the *Protection of the Environment Operations Act 1997* and the associated legal obligations to notify the EPA where a 'pollution' incident occurs such that material harm to the environment is caused or threatened.

#### **3.26.2.1 Immediate Response**

Any incident that occurs that causes or threatens to cause material harm will be reported immediately to ACEN Australia's Project Manager (during construction and operations).

Upon receiving notification of an incident, ACEN Australia's Project Manager (or their nominee if off-site at the time of the incident) will immediately attend the incident and:

- Isolate the area affected by the incident
- Stop works around the area
- Implement containment measures to prevent the impact of the incident spreading
- Decide as to whether the incident has caused or threatens to cause material harm.

### **3.26.2.2 External Notifications**

#### **3.26.2.2.1 Duty to Report**

If ACEN Australia's Project Manager (or their nominee if off-site at the time of the incident) has determined the incident has caused or threatens to cause material harm, he/she will, pursuant to requirements under Section 148 of the *Protection of the Environment Operations Act 1997* immediately notify the EPA, the NSW Ministry of Health, Fire and Rescue NSW and SafeWork NSW by verbal means.

These authorities will be notified (verbally) and provided the following relevant information:

- The time, date, nature, duration and location of the incident
- The location of the place where pollution is occurring or is likely to occur
- The nature, the estimated quantity or volume and the concentration of any pollutants involved, if known
- The circumstances in which the incident occurred (including the cause of the incident, if known)
- The action taken or proposed to be taken to deal with the incident and any resulting pollution or threatened pollution, if known.

The EPA may direct ACEN Australia to notify such other persons of the incident as the EPA requires.

#### **3.26.2.2.2 Notifications**

All Agencies including DPE, are to be notified immediately after becoming aware of an incident, ACEN Australia will immediately notify DPE in writing. Consistent with Schedule 4 Condition 7 of the Development Consent, notification to DPE will be in writing via the Major Projects website portal, including the following information:

- Identify the development (i.e. the NES) and the application number (SSD 9255)
- Set out the location and nature of the incident.

Seven days after the incident, ACEN Australia will prepare a report as per Appendix 7 of the Development Consent.

## **3.27 Non-Compliance**

### **3.27.1 Commitment**

A failure to comply with a Condition of Development Consent or statutory approval will constitute a non-compliance.

### **3.27.2 Response**

In the event of a non-compliance, ACEN Australia and its contractor (where relevant) will undertake the five steps as outlined within Table 3-4 below, consistent with the guidance advice for ISO 14001 – Environmental management systems.

*Table 3-4 Non-compliance Response*

| Step     | Action                                                                                                                                                                                                                                                                                                                                                               |
|----------|----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| React    | React to the non-compliance and, as applicable:<br><ol style="list-style-type: none"> <li>1. Act to control and correct it</li> <li>2. Notify and communicate to relevant parties where required</li> <li>3. Deal with the consequences, including mitigating adverse environmental impacts.</li> </ol>                                                              |
| Evaluate | Evaluate the need for action to eliminate the cause of the non-compliance in order that it does not recur or occur elsewhere by:<br><ol style="list-style-type: none"> <li>1. Reviewing the non-compliances</li> <li>2. Determining the cause of the non-compliances</li> <li>3. Determining if similar non-compliances exist or could potentially occur.</li> </ol> |
| Act      | Implement any action required.                                                                                                                                                                                                                                                                                                                                       |
| Review   | Review the effectiveness of any corrective action taken.                                                                                                                                                                                                                                                                                                             |
| Change   | Make changes to the environmental management plans, if necessary                                                                                                                                                                                                                                                                                                     |

### 3.27.3 Corrective Action

Any non-compliance will trigger a Corrective Action appropriate to the significance of the effect of the non-compliance. ACEN Australia and its Contractor (where relevant) will retain documented information as evidence of the nature of the non-compliance and any subsequent actions taken, and the results of the Corrective Action.

### 3.27.4 Notification

Consistent with Schedule 4 Conditions 8-10 of the Development Consent, DPE will be notified in writing via the Major Projects website portal within seven days after ACEN Australia and its Contractor becomes aware of any non-compliance. A non-compliance which has been notified as an incident does not need to also be notified as a non-compliance.

The notification will:

- Identify the development (i.e. as NES) and the application number (SSD 9255)
- Set out the Condition/s of Development Consent that the NES is non-compliant with
- The way in which it does not comply
- The reasons for non-compliance (if known)
- What actions have been done, or will be, undertaken to address the non-compliance.

DPE can also be contacted via [the Major Projects Portal](#).

## 4 Summary

This TMP has been prepared to satisfy Condition 6 of Schedule 3 of the Development Consent, which requires a TMP along with other management plans to be provided.

The TMP sets out proposed traffic management and contingency planning measures to enhance road safety and limit the adverse effects of construction traffic on the surrounding road network.

ACEN Australia, each contractor and their sub-contractors will adhere to the proposed traffic management measures contained in this TMP. Any material deviation from the proposed measures will be agreed in writing with the relevant road's authorities prior to implementation.

# **APPENDIX A PLANNING SECRETARY APPROVAL OF THIS TRAFFIC MANAGEMENT PLAN**

## **APPENDIX B     STAKEHOLDER CORRESPONDENCE**

Shelley McPhee  
Energy Assessments  
NSW Department of Planning, Industry & Environment

4 August 2022

Dear Shelley,

**NEW ENGLAND SOLAR FARM (SSD-9255)  
REQUEST FOR TEMPORARY INCREASE IN ALLOWABLE HEAVY VEHICLE  
MOVEMENTS ON ACCESS ROAD TO SITE**

Planning approval for the New England Solar Farm ("**NESF**") was granted on 9 March 2020, and a subsequent development application modification on 19 February 2021. UPCVAC Renewables was the applicant for NESF, ACEN has increased its ownership in UPCVAC Renewables in 2021 to be 100% by early 2023. Therefore, the applicant is now known as "**ACEN Australia**". The project is separated out into two stages for construction. The first stage consists of 400MW (Stage 1) with the second stage constructing the remaining 320MW (Stage 2).

Schedule 3 Condition 1 of the project's Conditions of Consent ("**COC**") requires that the development does not generate more than 56 heavy vehicle movements a day during construction, upgrading and decommissioning, unless the Secretary agrees otherwise.

ACEN Australia is seeking the Secretary's discretion for a temporary heavy vehicle increase from 56 per day to 84 per day (a 50% increase) for a period of three months as detailed in this letter and in the attached letter (Attachment A) from Green Light Contractors ("**GLC**"), the Principal Contractor for NESF.

**Consultation**

ACEN Australia has undertaken consultation with Uralla Shire Council and local residents and neighbours of the project as noted in the attachments to this letter.

**Traffic Impact Assessment**

ACEN Australia has undertaken a Traffic Impact Assessment as noted in the attachments to this letter.

**New England Solar**  
96B Bridge Street  
Uralla, NSW 2358

ACN 616 856 672  
ABN 27 616 856 672

## **Request**

ACEN Australia is seeking the Secretary's discretion for a temporary increase in heavy vehicle movements a day from 56 to 84 (a 50% increase) for a period of three months during the construction of NESF Stage 1.

The expected result of such an increase would be to reduce the duration of Stage 1 construction works by approximately six weeks with an equivalent reduction in the duration of construction-related noise impacts on nearby receivers and the community.

Stage 1 construction works have been impacted by COVID-19 restrictions and the ongoing inclement weather being experienced across north-eastern New South Wales.

## **Design capacity of upgraded Access Roads**

A Traffic Impact Assessment ("TIA") was commissioned to determine the potential impacts of increasing the number of daily heavy vehicles from 56 to 84. The TIA was based on the technical considerations of safety, performance at the key intersection of the New England Highway with Barleyfields Road (north) and the operational capacity of the road network along the construction access route.

The TIA concluded that the increase in heavy vehicle volume, from a traffic and transport perspective, is considered acceptable in the event that daily construction light vehicles are reduced by 14. The revised permissible daily construction vehicle numbers would be 206 light vehicles and 84 heavy vehicles.

GLC, has addressed this requirement in further detail in Appendix A.

## **Community Consultation**

ACEN Australia conducted consultation with Uralla Shire Council including meeting with the Director of Infrastructure and Development on 24<sup>th</sup> June 2022 and with the General Manager, Manager of Development and Planning and Mayor on 21<sup>st</sup> July 2022. Council did not raise any concerns as the reduced duration of construction works was considered a positive.

ACEN Australia conducted consultation with neighbours to the project along Barleyfields Road as noted in the consultation register Appendix A. Two rounds of consultation were completed along with a letter drop to each of the residents. The second round of consultation targeted those who were not home during the first visit. Two of the 13 residents that were consulted noted they were not supportive of the proposal as they were not supportive in general of the development in this particular area of New England.

A more detailed description of the management measures that will be put in place by GLC is provided in Attachment A. ACEN Australia supports this request which will reduce the duration of Stage 1 construction works by approximately six weeks with an equivalent reduction in the duration of construction-related noise impacts on nearby receivers and the community.

Yours Sincerely



Sarah Donnan  
Principal's Representative

#### **Attachment A**

NESF1-GLC-EN-00GRL-APV-003 dated 4 August 2022 Green Light Contractor Letter plus the following attachments:

- Attachment 1 Technical Advisory Note SCT\_00107\_NESF\_TAN\_Transport assessment\_Heavy vehicles\_Rev 3 dated 20/07/2022
- Attachment 2 Stakeholder consultation:
  - o NESF1-GLC-EN-00GRL-APV-002 dated 20 July 2022 from Green Light Contractor to Uralla Shire Council
  - o NESF1-GLC-EN-00GRL-APV-001 dated 14 July 2022 from Green Light Contractor to Neighbours of the project
  - o Community Consultation Log

4 August 2022

Our reference: NESF1-GLC -EN -00GRL-APV-003

NESF Project Director  
UPC/AC Renewables Australia  
**Hobart: Battery Point, TAS, 7004**

Dear Tim,

**RE: New England Solar Farm – Temporary heavy vehicle increase**

## 1 Introduction

The New England Solar Farm (NESF) (the Project) is a significant grid-connected solar farm and battery energy storage system, located approximately 6 kilometres (km) east of Uralla in New South Wales (NSW). The Project was granted development consent under Section 4.38 of the *Environmental Planning & Assessment Act 1979* (NSW) (EP&A Act) by the NSW Independent Planning Commission (IPC) on 9 March 2020 (State significant development [SSD] 9255). The development consent for the Project was subsequently modified on 19 February 2021. ACEN Australia (ACEN) is the proponent of the NESF, and Green Light Contractors Pty Ltd (GLC) has been awarded the engineering, procurement and construction (EPC) contract.

The commencement of Project construction has been impacted due to COVID-19 restrictions, inclement weather, and completion of road upgrades required by the development consent.

To accelerate construction works and reduce the duration of construction-related noise on nearby receivers and the community, GLC is seeking approval from the Secretary (in accordance with Schedule 3, Condition 1) for a temporary increase in heavy vehicle movements from 56 a day to 84 a day (a 50% increase), for a period of three months. GLC would increase minibus usage during the period, which is expected to reduce daily light vehicle movements by approximately 14 (i.e. from around 220 to 206 a day).

The temporary heavy vehicle increase is expected to reduce the duration of Stage 1 construction works by approximately six weeks, with an equivalent reduction in the duration of construction-related noise impacts on nearby receivers and the community.

Monitoring, management and mitigation measures would be implemented during the period to ensure the road network capacity and safety of all road users is not affected.

The request does not involve changes to the following:

- expected total heavy vehicle movements required for Stage 1 construction;
- no heavy vehicle movements on Sundays and public holidays; and
- approved working hours.

ACEN is separately seeking a modification to the development consent to increase heavy vehicle movements to 84 a day for the remainder of construction, which will predominantly benefit the Stage 2 construction schedule and further reduce the duration of noise impacts on receivers and the community.

## 2 Background

The “additional information dated 31 October 2019” that forms part of the Project Environmental Impact Statement (EIS) estimated that the construction period for the Project would be 40 months. This included Stage 1 (construction of the northern array area including grid substation) taking approximately 29 months to complete.

Following Project approval, commencement of Stage 1 construction (i.e. 7 February 2022) was significantly impacted due to the following factors, including:

- COVID-19 effects:
  - border closures preventing delivery of key pre-construction project materials;
  - regional lockdowns preventing skilled labour travel;
  - and local cases preventing access of personnel to site;
- ongoing inclement weather, including significant rainfall and flooding in the region; and
- completion of road upgrades required by the development consent.


GLC has progressively identified several opportunities to accelerate construction works and is currently expecting that Stage 1 construction could be completed around the end of March 2023.

GLC recently conducted further review of the construction schedule to identify all work packages that could occur concurrently across the Stage 1 footprint (e.g. civil works associated with internal road development could occur concurrently with electrical works in other areas where internal roads have been completed). The resulting proposed schedule indicates that Stage 1 construction could be completed around the end of February 2023, which represents a further six-week reduction in Stage 1 construction relative to the current development schedule.


To achieve this, additional heavy vehicle movements would be required earlier during the Stage 1 construction period. GLC proposes to temporarily increase heavy vehicle movements to 84 a day for a period of three months. The total number of heavy vehicle movements required for Stage 1 construction is not expected to change.

To offset additional traffic generated by the heavy vehicles, GLC would increase minibus usage during the period, which is expected to reduce daily light vehicle movements by approximately 14 (i.e. from around 220 to 206 a day).

The indicative current and proposed movement forecasts are shown in Figure 1 and 2. The figures demonstrate the potential reduction in duration of Stage 1 construction.

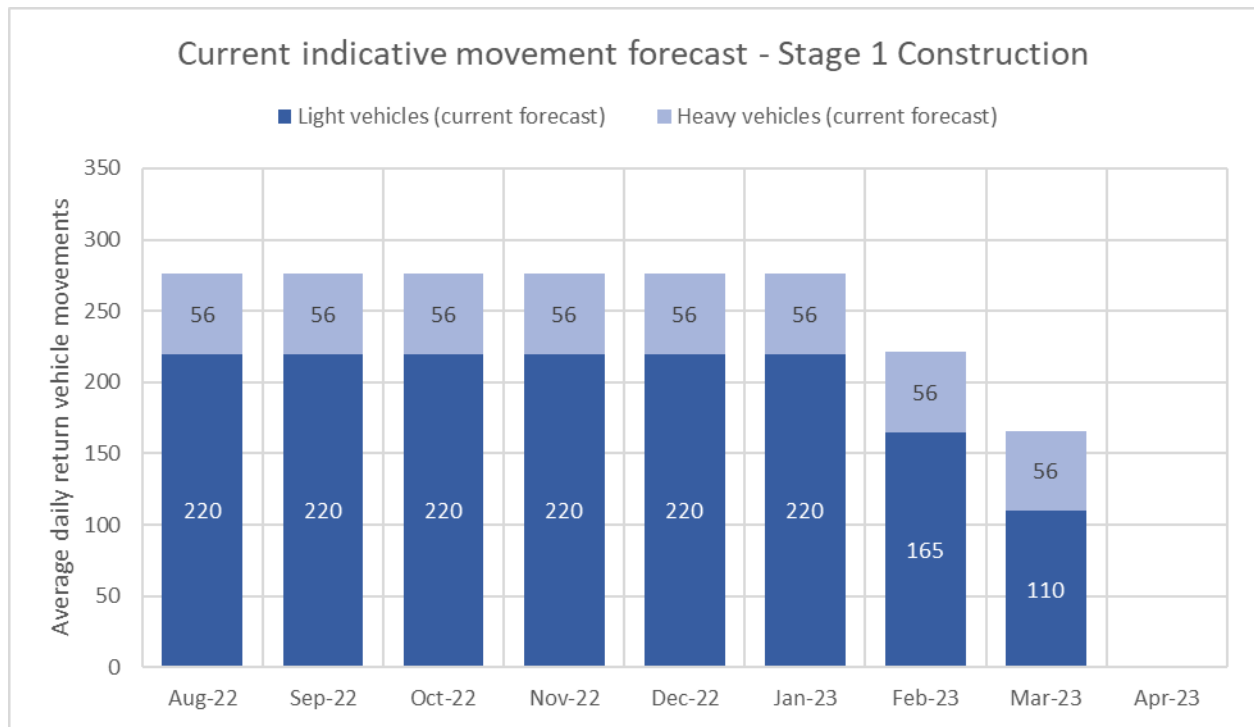

**Figure 1 Current indicative movement forecast**

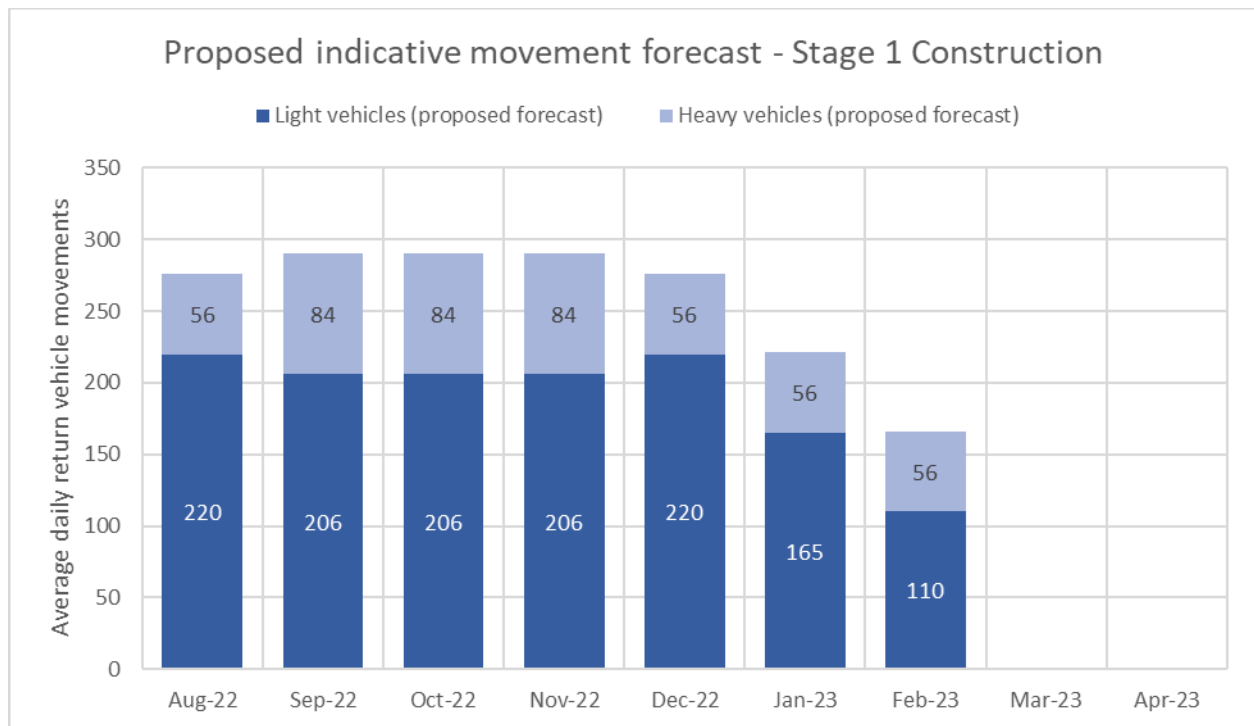

**Figure 2 Proposed indicative movement forecast**

*Note: The acceleration of Stage 1 is expected to allow Stage 2 of the Project to commence approximately six weeks earlier.*

An indicative breakdown of the daily heavy movements (consistent with the configuration and breakdown of heavy vehicles currently accessing site) would be:

- 15 movements for logistics deliveries (e.g. piles, torque tubes, cable drums, tracker equipment and PV modules).
- 10 movements for GLC substation deliveries (e.g. concrete, gravel for capping layer, substation equipment).
- 10 movements for TransGrid substation deliveries (similar to GLC substation deliveries).
- 22 movements for civil works deliveries (e.g. machinery, gravel for internal roads and hardstands, concrete for drainage works and PCU foundations).
- 16 movements for mechanical works deliveries (e.g. concrete trucks with stabilised sand, machines such as piling rigs and telehandlers).
- 10 movements for electrical works deliveries (e.g. thermal sands for trenches, excavators and trenching machines).
- 1 movement for other miscellaneous works (e.g. potable water and sewage).

### 3 Traffic considerations

Existing traffic management measures will continue to be implemented in accordance with the approved Traffic Management Plan (TMP) to ensure ongoing safety for all road users. Additional monitoring, management and mitigation measures are also proposed to be implemented during the period, as outlined in the sections below.

#### **Barleyfields Road (north) and Big Ridge Road capacity**

The completion of road upgrades (required by Appendix 4 of the development consent) has improved the local road network, and disruptions to road users associated with the upgrade road works have now concluded.

The Barleyfields Road and Big Ridge Road (Segments 1 and 3) carriageway width increases were designed based on the Austroads Design average annual daily traffic (AADT) of 500-1000 one-way movements.

A technical advisory note prepared by SCT Consulting (Attachment 1) states that:

*“the proposed increase in heavy vehicle volume, from a traffic and transport perspective, is considered acceptable in the event that daily construction light vehicles are reduced by 14. The revised permissible daily construction vehicle numbers would be 206 light vehicles and 84 heavy vehicles. This will ensure that the daily vehicle trips, also referred to as annual average daily traffic (AADT), across the construction access route remain within the intended design capacity of 1,000 vehicles.”*

The reduction in light vehicle movements would be achieved through increased use of minibuses by site personnel. Additional minibuses would be similar to the ones already used on site by GLC and subcontractors (refer Photo 1).



**Photo 1 Example of minibus used on site**

### **Barleyfields Road (north) intersection designs**

GLC has completed the road intersection upgrades described in Appendix 4 of the development consent.

Both intersection upgrades (New England Highway/Barleyfields Road, and Barleyfields Road/Big Ridge Road) were designed and constructed to accommodate the largest vehicle accessing the site (excluding over-dimensional vehicles). All non-over dimensional vehicles would continue to be restricted to 26 metres (as per Schedule 3, Condition 1b).

Accordingly, the requested temporary increase would not result in any requirement for further upgrade works on either intersection.

### **Traffic scheduling**

The completed channelised right turn lane (CHR-S) in the northbound direction and existing auxiliary left turn lane (AUL) in the southbound direction will enable increased traffic volumes to turn with minimal impact to general through traffic on the New England Highway.

As described in the approved TMP, key components of the Project are generally delivered to site via the Port of Brisbane, therefore would access Barleyfields Road (north) via the existing AUL on the New England Highway and would not travel through Uralla. Other materials would utilise both the AUL and CHR-S as they will travel north and south on the New England Highway.

The SCT Consulting Technical Advisory Note (Attachment 1) concludes that the intersection would continue to operate at the highest level of performance – Level of Service A.

Notwithstanding, traffic scheduling measures for the CHR-S will continue to be implemented in accordance with the TMP:

- Implementation of a traffic forecasting and scheduling regime, which aims to avoid convoy lengths or platooning on roads and to prevent exceeding the capacity of the highway intersection's shortened channelised right turn (CHR-S) storage lane.
- Implementation of a "drive-by" measure to be executed where the CHR-S storage lane is occupied (vehicle to travel to the New England Highway and Uralla Road roundabout and perform a U-turn).
- If required, implementation of TCPs to assist in managing vehicle movements through the intersection.

Weekly monitoring of the New England Highway intersection and Barleyfields Road (north) would be conducted to confirm the current measures are adequate during the proposed period of increased heavy vehicle movements. If warranted, GLC could implement additional measures, such as scheduling to minimise heavy vehicles (travelling north) from leaving site during the peak afternoon period, and/or implementing TCPs to prevent vehicles stopping on the rail crossing.

### **Road maintenance**

To address the potential for accelerated degradation along the access route, dilapidation surveys of Barleyfields Road and Big Ridge Road would occur at an increased frequency during the proposed period, occurring every month (as opposed to every two months as currently required). Any degradation in the condition of the roads, as identified through differences evident in the pre and post construction dilapidation surveys, will effectively become the road repair works required.

It is also understood that ACEN and USC would conduct weekly monitoring and inspection of Barleyfields Road (north) and Big Ridge Road.

## **4 Noise and dust considerations**

The proposed increase in heavy vehicle movements would result in temporary elevated noise levels on weekdays at some nearby receptors. Noise would be minimised as far as practicable in accordance with the development consent and TMP, including ensuring that deliveries are restricted to construction hours, and enforcing the driver's Code of Conduct (which addresses travelling speed and consideration of other road users). The location of receivers along Barleyfields Road and Big Ridge Road are shown on Figure 3.

The key advantage of increasing heavy vehicle deliveries would be to minimise the duration of construction-related noise impacts on nearby receivers and the community associated with Stage 1.

As required by the development consent, noise from construction activities on site would continue to be minimised in accordance with the Interim Construction Noise Guideline. Stage 1 construction activities would be spread across the footprint to minimise concentrated noise sources.

Dust from road traffic and construction activities would be managed through the increased use of water carts (particularly Big Ridge Road Segments 4 and 5). It is noted that, as part of the Project water supply strategy, GLC has entered a commercial agreement with an adjacent landholder which provides sufficient water supply for dust suppression even under dry conditions.

Consultation has been undertaken with sensitive receptors along Barleyfields Road (north) and Big Ridge Road regarding the temporary heavy vehicle increase. Correspondence regarding the request is provided in Attachment 2.

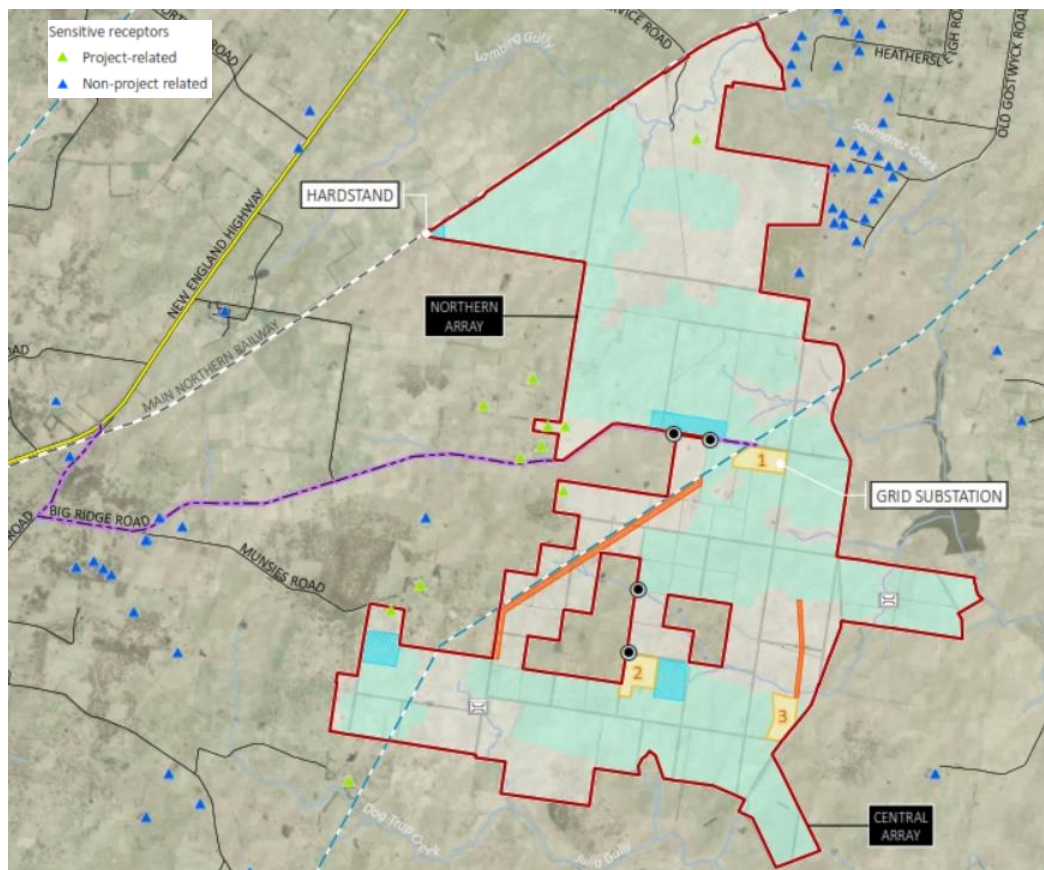


Figure 3 Location of sensitive receptors

## 5 Conclusion

To accelerate construction works and reduce the duration of construction-related noise on nearby receivers and the community, GLC is seeking approval from the Secretary (in accordance with Schedule 3, Condition 1) for a temporary increase in heavy vehicle movements from 56 a day to 84 a day (a 50% increase), for a period of three months. GLC would increase minibus usage during the period, which is expected to reduce daily light vehicle movements by approximately 14 (i.e. from around 220 to 206 a day).

The temporary heavy vehicle increase is expected to reduce the duration of Stage 1 construction works by approximately six weeks, with an equivalent reduction to the duration of Stage 1 construction-related noise impacts on nearby receivers and the community.

Monitoring, management and mitigation measures would be implemented during the period to ensure the road network capacity and safety of all road users is not affected.

Consultation has been undertaken with receptors near Barleyfields Road and Big Ridge Road and correspondence has been provided in Attachment 2.

It would be greatly appreciated if the Secretary could provide their support for the intent of this letter.

Regards

A handwritten signature in black ink, consisting of a stylized 'V' followed by a 'K'.

Volodymyr Koziy  
Project Manager

**Subject:** Re: NES\_TMP\_Submittal to TfNSW  
**Date:** Monday, 18 December 2023 at 6:47:02 pm Australian Eastern Daylight Time  
**From:** Sarah Donnan  
**To:** Alexandra Power  
**CC:** Development West, Tessa Verkerk  
**Attachments:** image001.png, image002.png, Brisbane example[69].pdf, Adelaide example.pdf, image003.png

Hi Alex,

Our response to your comments are as follows:

- Any temporary speed limits that were in place for the NEH are required to be removed post completion of the road works.
  - There are no temporary speed limits on TfNSW roads. There are temporary speed limits on Council roads for solar farm traffic which have been negotiated and agreed with Uralla Shire Council.
- There was a reference to the requirement to update the TMP however nothing within the TMP regarding consultation with TfNSW for further updates/revisions to the TMP and requiring the secretary agreement prior to commencing xyz stage.
  - The TMP notes under section 3.24 “Any updates to the Traffic Management Plan are to be to the satisfaction of the Secretary” where under Schedule 4 Condition 3 the Applicant may prepare any revised strategy, plan or program without undertaking consultation with all the parties referred to under the relevant condition of this consent, with the agreement of the Secretary.

ACEN is not required to consult with TfNSW if this is agreed with the Secretary. If this is not agreed, then consultation will be completed as per Schedule 3 Condition 6.

- Identify the weights, heights, widths, and lengths of the high risk loads and if any further road upgrades are required to facilitate the laden loads for the high risk OSOM (transformer/substation etc). *See below.*
- Any TGS required to facilitate the high risk OSOM movements.
  - For New England Solar Stage 1 (400MW) the OSOM routes used were from the Port of Brisbane and LAI, Ferryden Park in South Australia( i.e. Adelaide) as per the **attached Turn by Turn assessments**. For Stage 2 (320MW) and NE BESS (200MW) it is anticipated the same ports will be used requiring no further road upgrades nor assessments.

Prior to commencing with OSOM movements, consultation will be undertaken with TfNSW as part of the Turn by Turn assessments. This will provide further detail around sizing, loads and any further documentation required such as TGS.

Please let me know if TfNSW has any additional comments.

Kind regards, Sarah

Sarah Donnan  
Project Manager



ACEN Australia  
M: +61 402 206 088

E: [sarah.donnan@acenrenewables.com.au](mailto:sarah.donnan@acenrenewables.com.au)

Suite 2, Level 2, 15 Castray Esplanade, Battery Point, TAS 7004

[www.acenrenewables.com.au](http://www.acenrenewables.com.au)

**ACEN Australia acknowledges the resilience and knowledge of the Traditional Custodians of this nation. We pay our respects to elders past and present, the many Aboriginal people that did not make their elder status and to those that continue to care for country.**

This e-mail and its contents is intended solely for the individual to whom it is specifically and originally addressed and may contain confidential or privileged information. If you are not the intended recipient, please notify me immediately by return email and delete the email from your system. Retaining, disclosing, distributing or taking any action in reliance on this email or its contents is strictly prohibited.

---

**From:** Alexandra Power <[Alexandra.Power@transport.nsw.gov.au](mailto:Alexandra.Power@transport.nsw.gov.au)>  
**Date:** Thursday, 30 November 2023 at 9:38 am  
**To:** Sarah Donnan <[sarah.donnan@acenrenewables.com.au](mailto:sarah.donnan@acenrenewables.com.au)>  
**Cc:** Development West <[development.west@transport.nsw.gov.au](mailto:development.west@transport.nsw.gov.au)>  
**Subject:** RE: NES\_TMP\_Submittal to TfNSW

**CAUTION:** This email originated from outside of the organisation. Do not click links or open attachments unless you recognise the sender and know the content is safe.

Hello Sarah,

- Any temporary speed limits that were in place for the NEH are required to be removed post completion of the road works.
- There was a reference to the requirement to update the TMP however nothing within the TMP regarding consultation with TfNSW for further updates/revisions to the TMP and requiring the secretary agreement prior to commencing xyz stage.
- Identify the weights, heights, widths, and lengths of the high risk loads and if any further road upgrades are required to facilitate the laden loads for the high risk OSOM (transformer/substation etc).
- Any TGS required to facilitate the high risk OSOM movements.

Kind regards

Alexandra Power  
Team Leader Development Services-Renewables  
West  
Regional and Outer Metropolitan Division | TfNSW  
T 02 6861 1428

Please be advised that I work flexible hours.



**Before printing, please consider the environment**

**IMPORTANT NOTICE:** This email and any attachment to it are intended only to be read or used by the named addressee. It is confidential and may contain legally privileged information. No confidentiality or privilege is waived or lost by any mistaken transmission to you. Roads and Maritime Services is not responsible for any unauthorised alterations to this email or attachment to it. Views expressed in this message are those of the individual sender, and are not necessarily the views of Roads and Maritime Services. If you receive this email in error, please immediately delete it from your system and notify the sender. You must not disclose, copy or use any part of this email if you are not the intended recipient.

This email is intended for the named recipient only. The information it contains may be confidential or commercially sensitive. If you are not the intended recipient you must not reproduce or distribute any part of this email, disclose its contents to any other party, or take any action in reliance on it. If you have received this email in error, please contact the sender immediately and delete the message from your computer.

---

OFFICIAL

**From:** Sarah Donnan <[sarah.donnan@acenrenewables.com.au](mailto:sarah.donnan@acenrenewables.com.au)>  
**Sent:** Monday, 27 November 2023 1:10 PM  
**To:** Alexandra Power <[Alexandra.Power@transport.nsw.gov.au](mailto:Alexandra.Power@transport.nsw.gov.au)>  
**Cc:** Tessa Verkerk <[tessa.verkerk@acenrenewables.com.au](mailto:tessa.verkerk@acenrenewables.com.au)>; Kate Leonard <[Kate.LEONARD@transport.nsw.gov.au](mailto:Kate.LEONARD@transport.nsw.gov.au)>; David McKay <[david.mckay@acenrenewables.com.au](mailto:david.mckay@acenrenewables.com.au)>; Katie Weekes <[katie.weekes@dpie.nsw.gov.au](mailto:katie.weekes@dpie.nsw.gov.au)>  
**Subject:** Re: NES\_TMP\_Submittal to TfNSW

**CAUTION:** This email is sent from an external source. Do not click any links or open attachments unless you recognise the sender and know the content is safe.

Hi Alex,

Thank you for your phone call on Friday to discuss the next phases of New England Solar.

Sorry that technology let us down and your email of a month ago with your comments never made it into my inbox!

As noted on the phone, two issues of concern are:

- Any temporary speed limits on upgraded Council Roads during peak construction period.
  - We will review the TMP in regard to any historical comments in regards to this and discuss further with Council.
- OSOM travel routes
  - Noting that our Consent does not restrict OSOM travel routes, we are keen to use the experience from NES Stage 1a Construction in the successful OSOM travel routes from both Brisbane and Adelaide. I've asked our Contractor to forward details of the traffic routes for your information.

Where there any other comments you would like addressed?

Kind regards, Sarah

**Sarah Donnan**  
Project Manager



**ACEN Australia**

M: +61 402 206 088

E: [sarah.donnan@acenrenewables.com.au](mailto:sarah.donnan@acenrenewables.com.au)

Suite 2, Level 2, 15 Castray Esplanade, Battery Point, TAS 7004

[www.acenrenewables.com.au](http://www.acenrenewables.com.au)

**ACEN Australia acknowledges the resilience and knowledge of the Traditional Custodians of this nation. We pay our respects to elders past and present, the many Aboriginal people that did not make their elder status and to those that continue to care for country.**

This e-mail and its contents is intended solely for the individual to whom it is specifically and originally addressed and may contain confidential or privileged information. If you are not the intended recipient, please notify me immediately by return email and delete the email from your system. Retaining, disclosing, distributing or taking any action in reliance on this email or its contents is strictly prohibited.

OFFICIAL

**From:** Sarah Donnan <[sarah.donnan@acenrenewables.com.au](mailto:sarah.donnan@acenrenewables.com.au)>  
**Date:** Friday, 24 November 2023 at 11:16 am  
**To:** Alexandra Power <[Alexandra.Power@transport.nsw.gov.au](mailto:Alexandra.Power@transport.nsw.gov.au)>  
**Cc:** Tessa Verkerk <[tessa.verkerk@acenrenewables.com.au](mailto:tessa.verkerk@acenrenewables.com.au)>, Kate Leonard <[Kate.LEONARD@transport.nsw.gov.au](mailto:Kate.LEONARD@transport.nsw.gov.au)>  
**Subject:** Re: NES\_TMP\_Submittal to TfNSW  
Hi Alex,

Are we able to organise a quick call to discuss?

Kind regards, Sarah

**Sarah Donnan**  
Project Manager



**ACEN Australia**

M: +61 402 206 088

E: [sarah.donnan@acenrenewables.com.au](mailto:sarah.donnan@acenrenewables.com.au)

Suite 2, Level 2, 15 Castray Esplanade, Battery Point, TAS 7004

[www.acenrenewables.com.au](http://www.acenrenewables.com.au)

**ACEN Australia acknowledges the resilience and knowledge of the Traditional Custodians of this nation. We pay our respects to elders past and present, the many Aboriginal people that did not make their elder status and to those that continue to care for country.**

This e-mail and its contents is intended solely for the individual to whom it is specifically and originally addressed and may contain confidential or privileged information. If you are not the intended recipient, please notify me immediately by return email and delete the email from your system. Retaining, disclosing, distributing or taking any action in reliance on this email or its contents is strictly prohibited.

---

**From:** Sarah Donnan <[sarah.donnan@acenrenewables.com.au](mailto:sarah.donnan@acenrenewables.com.au)>  
**Date:** Tuesday, 14 November 2023 at 1:44 pm  
**To:** Tessa Verkerk <[tessa.verkerk@acenrenewables.com.au](mailto:tessa.verkerk@acenrenewables.com.au)>, Alexandra Power <[Alexandra.Power@transport.nsw.gov.au](mailto:Alexandra.Power@transport.nsw.gov.au)>, Kate Leonard <[Kate.LEONARD@transport.nsw.gov.au](mailto:Kate.LEONARD@transport.nsw.gov.au)>  
**Subject:** Re: NES\_TMP\_Submittal to TfNSW

Hi Alex,

Sorry to hassle you, have you had a chance to review the updated TMP?

We have had feedback from Uralla Shire Council and I'm just keen to understand if TfNSW have any concerns.

Kind regards, Sarah

**Sarah Donnan**  
Project Manager



**ACEN Australia**

M: +61 402 206 088

E: [sarah.donnan@acenrenewables.com.au](mailto:sarah.donnan@acenrenewables.com.au)

Suite 2, Level 2, 15 Castray Esplanade, Battery Point, TAS 7004

[www.acenrenewables.com.au](http://www.acenrenewables.com.au)

**ACEN Australia acknowledges the resilience and knowledge of the Traditional Custodians of this nation. We pay our respects to elders past and present, the many Aboriginal people that did not make their elder status and to**

those that continue to care for country.

This e-mail and its contents is intended solely for the individual to whom it is specifically and originally addressed and may contain confidential or privileged information. If you are not the intended recipient, please notify me immediately by return email and delete the email from your system. Retaining, disclosing, distributing or taking any action in reliance on this email or its contents is strictly prohibited.

---

**From:** Sarah Donnan <[sarah.donnan@acenrenewables.com.au](mailto:sarah.donnan@acenrenewables.com.au)>  
**Date:** Tuesday, 7 November 2023 at 3:21 pm  
**To:** Tessa Verkerk <[tessa.verkerk@acenrenewables.com.au](mailto:tessa.verkerk@acenrenewables.com.au)>, Alexandra Power <[Alexandra.Power@transport.nsw.gov.au](mailto:Alexandra.Power@transport.nsw.gov.au)>, Kate Leonard <[Kate.LEONARD@transport.nsw.gov.au](mailto:Kate.LEONARD@transport.nsw.gov.au)>  
**Subject:** Re: NES\_TMP\_Submittal to TfNSW

Hi Alex,

Is it worth setting up a call to talk through any particular concerns you have with the update to the TMP for New England Solar?

Many thanks, Sarah

**Sarah Donnan**  
Project Manager



**ACEN Australia**

M: +61 402 206 088

E: [sarah.donnan@acenrenewables.com.au](mailto:sarah.donnan@acenrenewables.com.au)

Suite 2, Level 2, 15 Castray Esplanade, Battery Point, TAS 7004

[www.acenrenewables.com.au](http://www.acenrenewables.com.au)

**ACEN Australia acknowledges the resilience and knowledge of the Traditional Custodians of this nation. We pay our respects to elders past and present, the many Aboriginal people that did not make their elder status and to those that continue to care for country.**

This e-mail and its contents is intended solely for the individual to whom it is specifically and originally addressed and may contain confidential or privileged information. If you are not the intended recipient, please notify me immediately by return email and delete the email from your system. Retaining, disclosing, distributing or taking any action in reliance on this email or its contents is strictly prohibited.

---

**From:** Tessa Verkerk <[tessa.verkerk@acenrenewables.com.au](mailto:tessa.verkerk@acenrenewables.com.au)>  
**Date:** Thursday, 5 October 2023 at 12:49 pm  
**To:** Alexandra Power <[Alexandra.Power@transport.nsw.gov.au](mailto:Alexandra.Power@transport.nsw.gov.au)>, Sarah Donnan <[sarah.donnan@acenrenewables.com.au](mailto:sarah.donnan@acenrenewables.com.au)>, Kate Leonard <[Kate.LEONARD@transport.nsw.gov.au](mailto:Kate.LEONARD@transport.nsw.gov.au)>  
**Subject:** Re: NES\_TMP\_Submittal to TfNSW

Hi Alexandra,

Sarah is away on training today however please find attached a copy of Rev 8 tracked changes of the TMP attached.

Warmest Regards,

Tessa

**Tessa Verkerk**  
Developer

**ACEN Australia**

M: +61 477 489 552

E: [tessa.verkerk@acenrenewables.com.au](mailto:tessa.verkerk@acenrenewables.com.au)

Level 22, 8 Exhibition Street, Melbourne, Vic, 3000

[www.acenrenewables.com.au](http://www.acenrenewables.com.au)

**ACEN Australia acknowledges the resilience and knowledge of the Traditional Custodians of this nation. We pay our respects to elders past and present, the many Aboriginal people that did not make their elder status and to those that continue to care for country.**

This e-mail and its contents is intended solely for the individual to whom it is specifically and originally addressed and may contain confidential or privileged information. If you are not the intended recipient, please notify me immediately by return email and delete the email from your system. Retaining, disclosing, distributing or taking any action in reliance on this email or its contents is strictly prohibited.

---

**From:** Alexandra Power <[Alexandra.Power@transport.nsw.gov.au](mailto:Alexandra.Power@transport.nsw.gov.au)>  
**Date:** Thursday, 5 October 2023 at 1:44 pm  
**To:** Sarah Donnan <[sarah.donnan@acenrenewables.com.au](mailto:sarah.donnan@acenrenewables.com.au)>, Kate Leonard <[Kate.LEONARD@transport.nsw.gov.au](mailto:Kate.LEONARD@transport.nsw.gov.au)>  
**Cc:** Tessa Verkerk <[tessa.verkerk@acenrenewables.com.au](mailto:tessa.verkerk@acenrenewables.com.au)>  
**Subject:** RE: NES\_TMP\_Submittal to TfNSW

**CAUTION:** This email originated from outside of the organisation. Do not click links or open attachments unless you recognise the sender and know the content is safe.

Hello Sarah,

Can you send me the revised TMP with track changes.

Kind regards

Alexandra Power  
Team Leader Development Services-Renewables  
West  
Regional and Outer Metropolitan Division | TfNSW  
T 02 6861 1428

Please be advised that I work flexible hours.



**Before printing, please consider the environment**

**IMPORTANT NOTICE:** This email and any attachment to it are intended only to be read or used by the named addressee. It is confidential and may contain legally privileged information. No confidentiality or privilege is waived or lost by any mistaken transmission to you. Roads and Maritime Services is not responsible for any unauthorised alterations to this email or attachment to it. Views expressed in this message are those of the individual sender, and are not necessarily the views of Roads and Maritime Services. If you receive this email in error, please immediately delete it from your system and notify the sender. You must not disclose, copy or use any part of this email if you are not the intended recipient.

This email is intended for the named recipient only. The information it contains may be confidential or commercially sensitive. If you are not the intended recipient you must not reproduce or distribute any part of this email, disclose its contents to any other party, or take any action in reliance on it. If you have received this email in error, please contact the sender immediately and delete the message from your computer.

---

OFFICIAL

**From:** Sarah Donnan <[sarah.donnan@acenrenewables.com.au](mailto:sarah.donnan@acenrenewables.com.au)>  
**Sent:** Thursday, 5 October 2023 8:15 AM  
**To:** Kate Leonard <[Kate.LEONARD@transport.nsw.gov.au](mailto:Kate.LEONARD@transport.nsw.gov.au)>  
**Cc:** Tessa Verkerk <[tessa.verkerk@acenrenewables.com.au](mailto:tessa.verkerk@acenrenewables.com.au)>; Alexandra Power <[Alexandra.Power@transport.nsw.gov.au](mailto:Alexandra.Power@transport.nsw.gov.au)>  
**Subject:** Re: NES\_TMP\_Submittal to TfNSW

You don't often get email from [sarah.donnan@acenrenewables.com.au](mailto:sarah.donnan@acenrenewables.com.au). [Learn why this is important](#)

**CAUTION:** This email is sent from an external source. Do not click any links or open attachments unless you recognise the sender and know the content is safe.

Thank you Kate.

And lovely to meet you Alexandra. Feel free to give me a call for further context.

This plan is an update of an approved plan based on the revision of the staging of the project as agreed with DPE. We have talked the updates through with local Council and they are performing a review in parallel.

Kind regards, Sarah

**Sarah Donnan**  
Project Manager  
**ACEN Australia**

M: +61 402 206 088

E: [sarah.donnan@acenrenewables.com.au](mailto:sarah.donnan@acenrenewables.com.au)

Suite 2, Level 2, 15 Castray Esplanade, Battery Point, TAS 7004

[www.acenrenewables.com.au](http://www.acenrenewables.com.au)

**ACEN Australia acknowledges the resilience and knowledge of the Traditional Custodians of this nation. We pay our respects to elders past and present, the many Aboriginal people that did not make their elder status and to those that continue to care for country.**

**We're rebranding.** ACEN has increased its ownership in UPC\AC Renewables in 2021 to be 100% by early 2023.

This e-mail and its contents is intended solely for the individual to whom it is specifically and originally addressed and may contain confidential or privileged information. If you are not the intended recipient, please notify me immediately by return email and delete the email from your system. Retaining, disclosing, distributing or taking any action in reliance on this email or its contents is strictly prohibited.

---

OFFICIAL

**From:** Kate Leonard <[Kate.LEONARD@transport.nsw.gov.au](mailto:Kate.LEONARD@transport.nsw.gov.au)>  
**Sent:** Thursday, October 5, 2023 6:50:40 AM  
**To:** Sarah Donnan <[sarah.donnan@acenrenewables.com.au](mailto:sarah.donnan@acenrenewables.com.au)>  
**Cc:** Tessa Verkerk <[tessa.verkerk@acenrenewables.com.au](mailto:tessa.verkerk@acenrenewables.com.au)>; Alexandra Power <[Alexandra.Power@transport.nsw.gov.au](mailto:Alexandra.Power@transport.nsw.gov.au)>  
**Subject:** RE: NES\_TMP\_Submittal to TfNSW

**CAUTION:** This email originated from outside of the organisation. Do not click links or open attachments unless you recognise the sender and know the content is safe.

Hi Sarah,

Your request was forwarded to our Renewables Team Leader, Alexandra Power for review. I have copied her in on this email so she can make contact if a meeting is required.

Kind regards,  
Kate

---

OFFICIAL

**From:** Sarah Donnan <[sarah.donnan@acenrenewables.com.au](mailto:sarah.donnan@acenrenewables.com.au)>  
**Sent:** Wednesday, 4 October 2023 5:40 PM  
**To:** Kate Leonard <[Kate.LEONARD@transport.nsw.gov.au](mailto:Kate.LEONARD@transport.nsw.gov.au)>  
**Cc:** Tessa Verkerk <[tessa.verkerk@acenrenewables.com.au](mailto:tessa.verkerk@acenrenewables.com.au)>  
**Subject:** Re: NES\_TMP\_Submittal to TfNSW

**CAUTION:** This email is sent from an external source. Do not click any links or open attachments unless you recognise the sender and know the content is safe.

Good afternoon Kate,

Referring to the email below, do you have any comments on Rev 8 of the New England Solar Traffic Management Plan?

Happy to talk through the updates in a meeting if that assists.

Kind regards, Sarah

**Sarah Donnan**  
Project Manager



**ACEN Australia**

M: +61 402 206 088

E: [sarah.donnan@acenrenewables.com.au](mailto:sarah.donnan@acenrenewables.com.au)

Suite 2, Level 2, 15 Castray Esplanade, Battery Point, TAS 7004

[www.acenrenewables.com.au](http://www.acenrenewables.com.au)

**ACEN Australia acknowledges the resilience and knowledge of the Traditional Custodians of this nation. We pay our respects to elders past and present, the many Aboriginal people that did not make their elder status and to those that continue to care for country.**

This e-mail and its contents is intended solely for the individual to whom it is specifically and originally addressed and may contain confidential or privileged information. If you are not the intended recipient, please notify me immediately by return email and delete the email from your system. Retaining, disclosing, distributing or taking any action in reliance on this email or its contents is strictly prohibited.

---

**From:** Sarah Donnan <[sarah.donnan@acenrenewables.com.au](mailto:sarah.donnan@acenrenewables.com.au)>  
**Date:** Tuesday, 26 September 2023 at 3:43 pm  
**To:** Kate Leonard <[Kate.LEONARD@transport.nsw.gov.au](mailto:Kate.LEONARD@transport.nsw.gov.au)>  
**Cc:** Tessa Verkerk <[tessa.verkerk@acenrenewables.com.au](mailto:tessa.verkerk@acenrenewables.com.au)>

## **Subject: NES\_TMP\_Submittal to TfNSW**

Good afternoon Kate,

You may remember reviewing the TMP for New England Stage One Revision 7 last year.

We have been through a review process with Department of Planning regarding the staging of the New England Solar Project and they have approved our staging plan.

Therefore the TMP has been updated to reflect this staging plan as we move from completion of Stage 1a, Operations of Stage 1b and Construction of Stage 2a.

Please find attached Revision 8 of the TMP for your review. Attached is a tracked changes version in word as well as a clean word version and pdf.

As you may be aware, the public road use remains the same for all stages of the project and there have been no major changes to how this is managed.

Happy to talk through any queries you may have. We have talked through Revision 8 with Uralla Shire Council and DPE. They are all reviewing in parallel with TfNSW.

Kind regards, Sarah

**Sarah Donnan**  
Project Manager



**ACEN Australia**

M: +61 402 206 088

E: [sarah.donnan@acenrenewables.com.au](mailto:sarah.donnan@acenrenewables.com.au)

Suite 2, Level 2, 15 Castray Esplanade, Battery Point, TAS 7004

[www.acenrenewables.com.au](http://www.acenrenewables.com.au)

**ACEN Australia acknowledges the resilience and knowledge of the Traditional Custodians of this nation. We pay our respects to elders past and present, the many Aboriginal people that did not make their elder status and to those that continue to care for country.**

This e-mail and its contents is intended solely for the individual to whom it is specifically and originally addressed and may contain confidential or privileged information. If you are not the intended recipient, please notify me immediately by return email and delete the email from your system. Retaining, disclosing, distributing or taking any action in reliance on this email or its contents is strictly prohibited.

This email is intended only for the addressee and may contain confidential information. If you receive this email in error please delete it and any attachments and notify the sender immediately by reply email. Transport for NSW takes all care to ensure that attachments are free from viruses or other defects. Transport for NSW assume no liability for any loss, damage or other consequences which may arise from opening or using an attachment.



**Consider the environment. Please don't print this e-mail unless really necessary.**

This email is intended only for the addressee and may contain confidential information. If you receive this email in error please delete it and any attachments and notify the sender immediately by reply email. Transport for NSW takes all care to ensure that attachments are free from viruses or other defects. Transport for NSW assume no liability for any loss, damage or other consequences which may arise from opening or using an attachment.



**Consider the environment. Please don't print this e-mail unless really necessary.**

This email is intended only for the addressee and may contain confidential information. If you receive this email in error please delete it and any attachments and notify the sender immediately by reply email. Transport for NSW takes all care to ensure that attachments are free from viruses or other defects. Transport for NSW assume no liability for any loss, damage or other consequences which may arise from opening or using an attachment.



**Consider the environment. Please don't print this e-mail unless really necessary.**

**Subject:** Re: New England Solar Farm (SSD 9255) - Traffic Management Plan for review  
**Date:** Friday, 22 January 2021 at 12:29:31 pm Australian Eastern Daylight Time  
**From:** Tim Kirk  
**To:** Development Northern  
**Priority:** High  
**Attachments:** image001.png, image002.jpg, image003.png, image004.png, NESF1-SMEC-CW-00GRL-PLN-001 - Rev4\_UPC.docx

Hi Leisa,

Thank you for your comments. I have amended the Traffic Management Plan to address your feedback as attached.

Please give me a call today to discuss if UPC's responses are satisfactory.

Kind Regards,

Tim Kirk | Project Development Manager  
UPC\AC Renewables Australia  
A UPC Renewables and AC Energy Company



M: +61 403 857 079  
E: [tim.kirk@upc-ac.com](mailto:tim.kirk@upc-ac.com)

Hobart: Suite 2, Level 2, 15 Castray Esplanade, Battery Point, TAS 7004  
Melbourne: 61 Cromwell Street, Collingwood VIC 3066  
Sydney: Level 14, 77 King Street, Sydney, NSW 2000

[www.upc-ac.com](http://www.upc-ac.com)

 Your role in protecting our environment is important. Please think before printing this email.

The information contained in this e-mail is intended solely for the individual to whom it is specifically and originally addressed. This e-mail and its contents may contain confidential or privileged information. If you are not the intended recipient, you are hereby notified that retaining, disclosing or distributing, or taking any action in reliance on the contents of this information, is strictly prohibited.

---

**From:** Development Northern <[development.northern@rms.nsw.gov.au](mailto:development.northern@rms.nsw.gov.au)>  
**Date:** Wednesday, 20 January 2021 at 4:42 pm  
**To:** Tim Kirk <[Tim.Kirk@upc-ac.com](mailto:Tim.Kirk@upc-ac.com)>  
**Subject:** RE: New England Solar Farm (SSD 9255) - Traffic Management Plan for review

Afternoon Tim

Please find attached TfNSW response to your Draft TMP.

In addition to this response, I am currently drafting an email to DPIE regarding the OSOM vehicle quantities they have forwarded to us for comment.

If you have any questions regarding this matter, I am able to be contacted on the number below, alternatively Matt Adams will return from leave during the week ending 5 February 2021.

Kind regards

*Leisa Sedger*

A/Manager, Land Use Assessment  
Regional Customer Services | Region North  
Regional & Outer Metropolitan Division  
Transport for NSW



Transport  
for NSW

---

**From:** Tim Kirk [mailto:Tim.Kirk@upc-ac.com]  
**Sent:** Thursday, 7 January 2021 9:46 AM  
**To:** Development Northern <development.northern@rms.nsw.gov.au>  
**Subject:** Re: New England Solar Farm (SSD 9255) - Traffic Management Plan for review

Hi Matt,

Hope you enjoyed the festive season.

Can you please advise how you are tracking with your review of the Traffic Management Plan, as requested in my earlier email.

Kind Regards,

**Tim Kirk** | Project Development Manager  
UPC\AC Renewables Australia  
*A UPC Renewables and AC Energy Company*



**M:** +61 403 857 079  
**E:** [tim.kirk@upc-ac.com](mailto:tim.kirk@upc-ac.com)

**Hobart:** Suite 2, Level 2, 15 Castray Esplanade, Battery Point, TAS 7004  
**Melbourne:** 61 Cromwell Street, Collingwood VIC 3066  
**Sydney:** Level 14, 77 King Street, Sydney, NSW 2000

[www.upc-ac.com](http://www.upc-ac.com)

Your role in protecting our environment is important. Please think before printing this email.  
The information contained in this e-mail is intended solely for the individual to whom it is specifically and originally addressed. This e-mail and its contents may contain confidential or privileged information. If you are not the intended recipient, you are hereby notified that retaining, disclosing or distributing, or taking any action in reliance on the contents of this information, is strictly prohibited.

---

**From:** Tim Kirk <[Tim.Kirk@upc-ac.com](mailto:Tim.Kirk@upc-ac.com)>  
**Date:** Tuesday, 15 December 2020 at 11:48 am  
**To:** Development Northern <[development.northern@rms.nsw.gov.au](mailto:development.northern@rms.nsw.gov.au)>  
**Subject:** New England Solar Farm (SSD 9255) - Traffic Management Plan for review

Dear Matthew,

### **New England Solar Farm – Traffic Management Plan (TMP)**

UPC/AC Renewables is seeking your feedback on the New England Solar Farm Traffic Management Plan (TMP). As you are aware, we are required by the NSW Department of Planning, Infrastructure, and Environment (DPIE) to consult with Transport for New South Wales (TfNSW) regarding the TMP before construction of the project can commence. Our construction contractor has prepared this plan, which is attached to this email.

We appreciate your support on this project to date and please let me know how long you will require to complete this review of the plan.

Kind Regards,

**Tim Kirk** | Project Development Manager  
UPC\AC Renewables Australia  
*A UPC Renewables and AC Energy Company*

---



**M:** +61 403 857 079  
**E:** [tim.kirk@upc-ac.com](mailto:tim.kirk@upc-ac.com)

**Hobart:** Suite 2, Level 2, 15 Castray Esplanade, Battery Point, TAS 7004  
**Melbourne:** 61 Cromwell Street, Collingwood VIC 3066  
**Sydney:** Level 14, 77 King Street, Sydney, NSW 2000

[www.upc-ac.com](http://www.upc-ac.com)

 **Your role in protecting our environment is important. Please think before printing this email.**

The information contained in this e-mail is intended solely for the individual to whom it is specifically and originally addressed. This e-mail and its contents may contain confidential or privileged information. If you are not the intended recipient, you are hereby notified that retaining, disclosing or distributing, or taking any action in reliance on the contents of this information, is strictly prohibited.



**Transport  
for NSW**

**Before printing, please consider the environment**

**IMPORTANT NOTICE:** This email and any attachment to it are intended only to be read or used by the named addressee. It is confidential and may contain legally privileged information. No confidentiality or privilege is waived or lost by any mistaken transmission to you. Roads and Maritime Services is not responsible for any unauthorised alterations to this email or attachment to it. Views expressed in this message are those of the individual sender, and are not necessarily the views of Roads and Maritime Services. If you receive this email in error, please immediately delete it from your system and notify the sender. You must not disclose, copy or use any part of this email if you are not the intended recipient.



20 January 2021

File No: NTH18/00058/16

Your Ref:

UPCAC Renewables  
Level 14  
77 King Street  
SYDNEY NSW 2000

Attention: Tim Kirk – Project Development Manager

Dear Sir,

**RE: State Significant Development SSD 9255  
New England Solar Farm - Traffic Management Plan.**

I refer to your email of 7 January 2021 requesting comment from Transport for NSW (TfNSW) in relation to the abovementioned Traffic Management Plan (TMP). TfNSW has reviewed the TMP and provides the following comments for your consideration;

- The proposed northbound CHR(s) on the New England Highway at North Baileyfields Road will only have a limited storage capacity for right-turning vehicles. Consideration needs to be given to how the safety and efficiency of the CHR(s) treatment will be managed in relation to storage capacity. This should be included in the Code of Conduct.
- *2.4 - Access Routes* - indicates the existing level crossing on North Barleyfields Road will be upgraded. The inherent details of this upgrade will need to be provided for review.

If any work is undertaken between the level crossings stop lines, approval will be required from TfNSW prior to commencing work.

Note: The heavy vehicle access route is incorrectly named Barleyfields Road, this will need to be corrected to read North Barleyfields Road.

- *2.4.2 – Other Traffic Routes (Light & HGV)* – Identified a proposal to use South Barleyfields Road. Clarification of the acronym HGV is required, however TfNSW was of the understanding that South Barleyfields Road was not to be used for access by any vehicles.

If UPCAC are proposing to utilise South Barleyfields Road a safety assessment will need to be undertaken and submitted for review by TfNSW and Council.

- *2.6.1 - New England Highway/Barleyfields Road Priority Intersection* – This section indicates the largest design vehicle will be a 26m B-Double. Currently North Baileyfields and Big Ridge Road is not approved for use by 26m B-Doubles. A request will need to be lodged with the National Heavy Vehicle Regulator for consideration.
- *3.7 – Code of Conduct* - will need to include a map that shows any constraints or conditions relating to the local haulage route.

- **3.7.1 – Vehicle Speeds** – The TMP proposes a speed limit reduction to 40km/h for the duration of construction.

North Barleyfields Road has an existing speed limit of 80km/h. Therefore, the proposal for a 40km/h speed limit for a long construction phase would have compliance issues.

Please clarify if this is for the duration of the road upgrade; or, for the duration of stage 1 construction phase only.

- **3.11 – Temporary Traffic Controls, Including Signage** – The TMP has non standard signs proposed for installation on the New England Highway at the intersection of Wood Street, South Barleyfields and Big Ridge Road.

Proposed signs on the New England Highway will require prior approval from TfNSW.

Traffic Control Plans (TCPs) should be prepared by a suitably qualified person and included in the TMP.

- **3.14 – Management of Employee Shuttle Bus Service** - details of the pick-up points and parking arrangements will be required to be submitted to the Council and/or TfNSW for comments prior to approval.

Any roadwork on classified (State) road/s is to be designed and constructed in accordance with the current Austroads Guidelines, Australian Standards and [TfNSW Supplements](#).

It is emphasised that the following comments are based on the information provided to TfNSW at this time, they are not to be interpreted as binding upon TfNSW and further comment will be provided following formal review of the final Traffic Management Plan (TMP) when referred by the appropriate Consent Authority.

If you have any further enquiries regarding the above comments please do not hesitate to contact the undersigned on (02) 6640 1362 or via email at: [development.northern@rms.nsw.gov.au](mailto:development.northern@rms.nsw.gov.au)

Yours faithfully,



for Leisa Sedger  
A/Manager Land Use Assessment Northern  
Regional NSW and Outer Metropolitan  
Transport for NSW

Cc; Department of Planning Industry and Environment  
GPO Box 39  
SYDNEY NSW 2001

Attention: Lander Robinson

**Subject:** Re: NESF (SSD 9255) - Traffic Management Plan review email to Tim Kirk 21 January 2021  
**Date:** Thursday, 21 January 2021 at 4:40:27 pm Australian Eastern Daylight Time  
**From:** Tim Kirk  
**To:** Matt Clarkson  
**Attachments:** image001.png, image002.png, image003.png, image004.png

Great, thank you Matt.

Regards,

Tim Kirk | Project Development Manager  
UPC\AC Renewables Australia  
A UPC Renewables and AC Energy Company



M: +61 403 857 079  
E: [tim.kirk@upc-ac.com](mailto:tim.kirk@upc-ac.com)

Hobart: Suite 2, Level 2, 15 Castray Esplanade, Battery Point, TAS 7004  
Melbourne: 61 Cromwell Street, Collingwood VIC 3066  
Sydney: Level 14, 77 King Street, Sydney, NSW 2000

[www.upc-ac.com](http://www.upc-ac.com)

 Your role in protecting our environment is important. Please think before printing this email.

The information contained in this e-mail is intended solely for the individual to whom it is specifically and originally addressed. This e-mail and its contents may contain confidential or privileged information. If you are not the intended recipient, you are hereby notified that retaining, disclosing or distributing, or taking any action in reliance on the contents of this information, is strictly prohibited.

---

**From:** Matt Clarkson <MClarkson@uralla.nsw.gov.au>  
**Date:** Thursday, 21 January 2021 at 12:43 pm  
**To:** Tim Kirk <Tim.Kirk@upc-ac.com>  
**Cc:** Terence Seymour <TSeymour@uralla.nsw.gov.au>, 'Lander Robinson' <Lander.Robinson@planning.nsw.gov.au>, 'Iwan Davies' <iwan.davies@planning.nsw.gov.au>  
**Subject:** RE: NESF (SSD 9255) - Traffic Management Plan review email to Tim Kirk 21 January 2021

Hello Tim

Council has reviewed the TMP and does not propose any amendments.

Regards  
Matt Clarkson  
Manager of Development and Planning

Uralla Shire Council | Po Box 106 Uralla NSW 2358  
p 02 6778 6310 | f 02 6778 6349 | m 0419 861 719



---

**From:** Tim Kirk [mailto:Tim.Kirk@upc-ac.com]  
**Sent:** Tuesday, 5 January 2021 11:04 AM  
**To:** Matt Clarkson  
**Cc:** Terence Seymour  
**Subject:** Re: NESF (SSD 9255) - Traffic Management Plan review

Hi Matt,

Hope you enjoyed your New Year.

Just wondering if you have any updates on your review of the traffic management plan, as per the below email?

Cheers,

**Tim Kirk** | Project Development Manager  
UPC\AC Renewables Australia  
*A UPC Renewables and AC Energy Company*



**M:** +61 403 857 079  
**E:** [tim.kirk@upc-ac.com](mailto:tim.kirk@upc-ac.com)

**Hobart:** Suite 2, Level 2, 15 Castray Esplanade, Battery Point, TAS 7004  
**Melbourne:** 61 Cromwell Street, Collingwood VIC 3066  
**Sydney:** Level 14, 77 King Street, Sydney, NSW 2000

[www.upc-ac.com](http://www.upc-ac.com)

Your role in protecting our environment is important. Please think before printing this email.

The information contained in this e-mail is intended solely for the individual to whom it is specifically and originally addressed. This e-mail and its contents may contain confidential or privileged information. If you are not the intended recipient, you are hereby notified that retaining, disclosing or distributing, or taking any action in reliance on the contents of this information, is strictly prohibited.

---

**From:** Tim Kirk <[Tim.Kirk@upc-ac.com](mailto:Tim.Kirk@upc-ac.com)>  
**Date:** Tuesday, 15 December 2020 at 12:45 pm  
**To:** Matt Clarkson <[MClarkson@uralla.nsw.gov.au](mailto:MClarkson@uralla.nsw.gov.au)>  
**Cc:** Terence Seymour <[TSeymour@uralla.nsw.gov.au](mailto:TSeymour@uralla.nsw.gov.au)>  
**Subject:** NESF (SSD 9255) - Traffic Management Plan review

Dear Matt,

### **New England Solar Farm – Traffic Management Plan (TMP)**

UPC/AC Renewables is seeking Uralla Shire Council's (USC) feedback on the New England Solar Farm Traffic Management Plan (TMP). As you are aware, we are required by the NSW Department of Planning, Infrastructure, and Environment (DPIE) to consult with USC regarding the TMP before construction of the project can commence. Our construction contractor has prepared this plan, which is attached to the email.

We appreciate your support on this project to date and please let me know how long you will require to complete this review. We hope to receive it by the end of this week if possible.

Kind Regards,

Tim Kirk | Project Development Manager  
UPC\AC Renewables Australia  
*A UPC Renewables and AC Energy Company*

---



M: +61 403 857 079

E: [tim.kirk@upc-ac.com](mailto:tim.kirk@upc-ac.com)

**Hobart:** Suite 2, Level 2, 15 Castray Esplanade, Battery Point, TAS 7004

**Melbourne:** 61 Cromwell Street, Collingwood VIC 3066

**Sydney:** Level 14, 77 King Street, Sydney, NSW 2000

[www.upc-ac.com](http://www.upc-ac.com)

 Your role in protecting our environment is important. Please think before printing this email.

The information contained in this e-mail is intended solely for the individual to whom it is specifically and originally addressed. This e-mail and its contents may contain confidential or privileged information. If you are not the intended recipient, you are hereby notified that retaining, disclosing or distributing, or taking any action in reliance on the contents of this information, is strictly prohibited.

**Subject:** Re: CM: New England Solar: Closure of USC paper roads within project footprint  
**Date:** Wednesday, 15 November 2023 at 6:47:12 pm Australian Eastern Daylight Time  
**From:** Sarah Donnan  
**To:** Michael Raby  
**CC:** Council, Tessa Verkerk, Richard de Bruin, Kate Blackwood, Toni Averay, Tim Greenaway, Sylvia Baxter  
**Attachments:** image002.png, image005.png, image006.png, image001.png, image003.png, NES2-SMEC-CW-10ROA-DWG-502\_.pdf, NES2-SMEC-CW-10ROA-DWG-521\_.pdf

Good afternoon Mick,

Thank you for our discussion yesterday.

In summary:

**1. Traffic Management Plan**

Would Council be comfortable with amended text below in relation to regularity of inspections?

In relation to detail of maintenance works identified in these inspections, please refer to Appendix C. This form was agreed to with Council during consultation of Revision 7 of the document and has not been amended. As noted below, the inspections would be completed using this form.

To your point regarding the current un-sealed portions of the access roads, we confirm that the TMP would be amended once the sealing works have occurred. Unfortunately we are not able to amend this section in Revision 8 of the document, DPE have noted this is to be updated once the sealing works have been completed.

**3.8 Dilapidation Survey**

The purpose of undertaking dilapidation surveys is to document the condition of Barleyfields Road (North) and Big Ridge Road prior to and following construction, upgrading or decommissioning of NES.

During construction, road condition inspections of Barleyfields Road (North) and Big Ridge Road will be carried out weekly during peak times as identified in Figure 2-1, by the ACEN Australia Traffic Coordinator. The road condition inspections will identify and categorise defects, and describe the proposed management measure and implementation timeframe. The access road condition inspection checklist is provided in Appendix C.

During operations these inspections will be completed every 6 months as per Appendix C.

Uralla Shire Council will be notified of any repairs identified during the road condition inspections.

**2. Sealing of Big Ridge Road**

Please find attached Drawing 502 identifying the extent of the proposed seal and drawing 521 which identifies the wearing course as "14/7 Two Coat Seal with 10mm Primer Seal to Uralla Council Construction Specification". Notes 10 and 11 on the drawing also refer to requirements. These drawings are part of a package of works that are out for tender at the moment. Happy to talk through with your team as required.

We agree with Council's other requirements regarding regular inspections during construction (as noted in text above) and condition for handover back to Council at the conclusion of the project.

### 3. Road closures.

I understand you are looking into this and will come back to us with framework on how to proceed.

Kind regards, Sarah

**Sarah Donnan**  
Project Manager



#### ACEN Australia

M: +61 402 206 088

E: [sarah.donnan@acenrenewables.com.au](mailto:sarah.donnan@acenrenewables.com.au)

Suite 2, Level 2, 15 Castray Esplanade, Battery Point, TAS 7004

[www.acenrenewables.com.au](http://www.acenrenewables.com.au)

**ACEN Australia acknowledges the resilience and knowledge of the Traditional Custodians of this nation. We pay our respects to elders past and present, the many Aboriginal people that did not make their elder status and to those that continue to care for country.**

This e-mail and its contents is intended solely for the individual to whom it is specifically and originally addressed and may contain confidential or privileged information. If you are not the intended recipient, please notify me immediately by return email and delete the email from your system. Retaining, disclosing, distributing or taking any action in reliance on this email or its contents is strictly prohibited.

---

**From:** Michael Raby <[MRaby@uralla.nsw.gov.au](mailto:MRaby@uralla.nsw.gov.au)>

**Date:** Thursday, 9 November 2023 at 9:05 am

**To:** Sarah Donnan <[sarah.donnan@acenrenewables.com.au](mailto:sarah.donnan@acenrenewables.com.au)>

**Cc:** Council <[council@uralla.nsw.gov.au](mailto:council@uralla.nsw.gov.au)>, Tessa Verkerk <[tessa.verkerk@acenrenewables.com.au](mailto:tessa.verkerk@acenrenewables.com.au)>, Richard de Bruin <[Richard.debruin@acenrenewables.com.au](mailto:Richard.debruin@acenrenewables.com.au)>, Kate Blackwood <[KBlackwood@uralla.nsw.gov.au](mailto:KBlackwood@uralla.nsw.gov.au)>, Toni Averay <[TAveray@uralla.nsw.gov.au](mailto:TAveray@uralla.nsw.gov.au)>, Tim Greenaway <[tim.greenaway@acenrenewables.com.au](mailto:tim.greenaway@acenrenewables.com.au)>, Sylvia Baxter <[SBaxter@uralla.nsw.gov.au](mailto:SBaxter@uralla.nsw.gov.au)>

**Subject:** RE: CM: New England Solar: Closure of USC paper roads within project footprint

**CAUTION:** This email originated from outside of the organisation. Do not click links or open attachments unless you recognise the sender and know the content is safe.

Thanks Sarah.

I'm happy to discuss lower intensity of inspections during periods of lower activity. Maybe Friday?

Regards,  
Mick Raby

**Acting Director Infrastructure & Development**  
Uralla Shire Council | PO Box 106, Uralla NSW 2358



---

**From:** Sarah Donnan [mailto:[sarah.donnan@acenrenewables.com.au](mailto:sarah.donnan@acenrenewables.com.au)]  
**Sent:** Wednesday, 8 November 2023 10:11 PM  
**To:** Michael Raby <[MRaby@uralla.nsw.gov.au](mailto:MRaby@uralla.nsw.gov.au)>  
**Cc:** Council <[council@uralla.nsw.gov.au](mailto:council@uralla.nsw.gov.au)>; Tessa Verkerk <[tessa.verkerk@acenrenewables.com.au](mailto:tessa.verkerk@acenrenewables.com.au)>; Richard de Bruin <[Richard.debruin@acenrenewables.com.au](mailto:Richard.debruin@acenrenewables.com.au)>; Kate Blackwood <[KBlackwood@uralla.nsw.gov.au](mailto:KBlackwood@uralla.nsw.gov.au)>; Toni Averay <[TAveray@uralla.nsw.gov.au](mailto:TAveray@uralla.nsw.gov.au)>; Tim Greenaway <[tim.greenaway@acenrenewables.com.au](mailto:tim.greenaway@acenrenewables.com.au)>  
**Subject:** Re: CM: New England Solar: Closure of USC paper roads within project footprint

Good evening Mick,

Thank you for your response.

I'm on a training course tomorrow, but will call on Friday to discuss.

In the meantime, a couple of comments:

1. ACEN is comfortable with regular inspections of the access roads in order to identify defects and timely repair program. Weekly inspections during the peak of construction works (during peak vehicle movements) would certainly be appropriate. Would Council consider a reduced frequency during the Operations period of the project when vehicle movements are considerably less? Perhaps a monthly inspection?
2. ACEN thanks Council for their support in this request. I will source details from our Consultant and send them across for your consideration.

Kind regards, Sarah

**Sarah Donnan**  
Project Manager



**ACEN Australia**

M: +61 402 206 088

E: [sarah.donnan@acenrenewables.com.au](mailto:sarah.donnan@acenrenewables.com.au)

Suite 2, Level 2, 15 Castray Esplanade, Battery Point, TAS 7004

[www.acenrenewables.com.au](http://www.acenrenewables.com.au)

**ACEN Australia acknowledges the resilience and knowledge of the Traditional Custodians of this nation. We pay our respects to elders past and present, the many Aboriginal people that did not make their elder status and to those that continue to care for country.**

This e-mail and its contents is intended solely for the individual to whom it is specifically and originally addressed and may contain confidential or privileged information. If you are not the intended recipient, please notify me immediately by return email and delete the email from your system. Retaining, disclosing, distributing or taking any action in reliance on this email or its contents is strictly prohibited.

---

**From:** Michael Raby <[MRaby@uralla.nsw.gov.au](mailto:MRaby@uralla.nsw.gov.au)>  
**Date:** Wednesday, 8 November 2023 at 2:44 pm  
**To:** Sarah Donnan <[sarah.donnan@acenrenewables.com.au](mailto:sarah.donnan@acenrenewables.com.au)>, Toni Averay <[TAveray@uralla.nsw.gov.au](mailto:TAveray@uralla.nsw.gov.au)>, Kate Blackwood <[KBlackwood@uralla.nsw.gov.au](mailto:KBlackwood@uralla.nsw.gov.au)>  
**Cc:** Council <[council@uralla.nsw.gov.au](mailto:council@uralla.nsw.gov.au)>, Tessa Verkerk <[tessa.verkerk@acenrenewables.com.au](mailto:tessa.verkerk@acenrenewables.com.au)>, Richard de Bruin <[Richard.debruin@acenrenewables.com.au](mailto:Richard.debruin@acenrenewables.com.au)>  
**Subject:** RE: CM: New England Solar: Closure of USC paper roads within project footprint

**CAUTION:** This email originated from outside of the organisation. Do not click links or open attachments unless you recognise the sender and know the content is safe.

Good afternoon Sarah,

Apologies for the delay in this response. Please feel free to forward future public road/infrastructure related correspondence to me directly.

Our feedback on the TMP and the Sealing of Big Ridge Road is below. I am happy to discuss any item if that is required. My mobile No. (the most effective method) is 0438 648 473. I will take carriage of the paper road closure request directly and respond as soon as possible.

1. *The Traffic Management Plan identifies long term strategies to bring Big Ridge Road back to a standard level. There is a lack of detail around the inspection and repair of short term defects and how they are to be repaired. Additionally, there has been a request to USC to approve the sealing of the current unsealed portion of Big Ridge Road. The current Traffic Management Plan seems to relate more to the maintenance of unsealed roads for that portion. These sections would need to be updated to include sealed road.*

*TMP needs to include Weekly Road inspection - in order to identify defects and develop a timely repair program for the defects (e.g. Roads and Transport Directorate 'Road Inspection Manual'). This weekly report should consist of a record of inspection, the defects identified, and defect repairs undertaken and when. The Manual also discusses risk based intervention (or target dates) based on location and severity of the defect (e.g. a deep pothole in the travel lanes will have a shorter target date than a pothole forming on a shoulder) which allows a reasonably flexible approach to the timing of the repairs based on actual risk.*

2. *The sealing of Big Ridge Road – This request is supported by Council. We would expect to see the scope of works before the bitumen sealing is to occur, as a sign off on the proposed works. Throughout the life of the project, the road is to be regularly inspected and defects are repaired (as above). At the end of the project the road is to be renewed back to new condition (as agreed to by Council, at the time of the decommissioning of the solar array).*

Regards,  
Mick Raby

**Acting Director Infrastructure & Development**

Uralla Shire Council | PO Box 106, Uralla NSW 2358

p 02 6778 6309 | [mraby@uralla.nsw.gov.au](mailto:mraby@uralla.nsw.gov.au)

[council@uralla.nsw.gov.au](mailto:council@uralla.nsw.gov.au) | [www.uralla.nsw.gov.au](http://www.uralla.nsw.gov.au)



---

**From:** Sarah Donnan [<mailto:sarah.donnan@acenrenewables.com.au>]  
**Sent:** Tuesday, 7 November 2023 4:17 PM  
**To:** Toni Averay <[TAveray@uralla.nsw.gov.au](mailto:TAveray@uralla.nsw.gov.au)>; Kate Blackwood <[KBlackwood@uralla.nsw.gov.au](mailto:KBlackwood@uralla.nsw.gov.au)>  
**Cc:** Council <[council@uralla.nsw.gov.au](mailto:council@uralla.nsw.gov.au)>; Tessa Verkerk <[tessa.verkerk@acenrenewables.com.au](mailto:tessa.verkerk@acenrenewables.com.au)>; Richard de Bruin <[Richard.debruin@acenrenewables.com.au](mailto:Richard.debruin@acenrenewables.com.au)>; Michael Raby <[MRaby@uralla.nsw.gov.au](mailto:MRaby@uralla.nsw.gov.au)>  
**Subject:** Re: CM: New England Solar: Closure of USC paper roads within project footprint

Hi all,

Are there any particular comments we can work through on the proposed:

1. Road closures as per this email
2. Amended Traffic Management Plan
3. Proposed sealing of Big Ridge Road

Many thanks, Sarah

**Sarah Donnan**  
Project Manager



**ACEN Australia**

M: +61 402 206 088

E: [sarah.donnan@acenrenewables.com.au](mailto:sarah.donnan@acenrenewables.com.au)

Suite 2, Level 2, 15 Castray Esplanade, Battery Point, TAS 7004

[www.acenrenewables.com.au](http://www.acenrenewables.com.au)

**ACEN Australia acknowledges the resilience and knowledge of the Traditional Custodians of this nation. We pay our respects to elders past and present, the many Aboriginal people that did not make their elder status and to those that continue to care for country.**

This e-mail and its contents is intended solely for the individual to whom it is specifically and originally addressed and may contain confidential or privileged information. If you are not the intended recipient, please notify me immediately by return email and delete the email from your system. Retaining, disclosing, distributing or taking any action in reliance on this email or its contents is strictly prohibited.

---

**From:** Toni Averay <[TAveray@uralla.nsw.gov.au](mailto:TAveray@uralla.nsw.gov.au)>  
**Date:** Wednesday, 1 November 2023 at 5:10 pm  
**To:** Sarah Donnan <[sarah.donnan@acenrenewables.com.au](mailto:sarah.donnan@acenrenewables.com.au)>, Kate Blackwood <[KBlackwood@uralla.nsw.gov.au](mailto:KBlackwood@uralla.nsw.gov.au)>  
**Cc:** Council <[council@uralla.nsw.gov.au](mailto:council@uralla.nsw.gov.au)>, Tessa Verkerk <[tessa.verkerk@acenrenewables.com.au](mailto:tessa.verkerk@acenrenewables.com.au)>, Richard de Bruin <[Richard.debruin@acenrenewables.com.au](mailto:Richard.debruin@acenrenewables.com.au)>, Michael Raby <[MRaby@uralla.nsw.gov.au](mailto:MRaby@uralla.nsw.gov.au)>  
**Subject:** RE: CM: New England Solar: Closure of USC paper roads within project

footprint

**CAUTION:** This email originated from outside of the organisation. Do not click links or open attachments unless you recognise the sender and know the content is safe.

Good afternoon Sarah

Thanks for your email.

Kate will review and provide advice but I have also copied Mick Raby into this email as he is now acting Exec Director Infrastructure.

Mick will provide input on the roads approvals.

Regards

Toni

---

**From:** Sarah Donnan [<mailto:sarah.donnan@acenrenewables.com.au>]

**Sent:** Wednesday, 1 November 2023 12:49 PM

**To:** Kate Blackwood

**Cc:** Toni Averay; Council; Tessa Verkerk; Richard de Bruin

**Subject:** CM: New England Solar: Closure of USC paper roads within project footprint

Good morning Kate,

As discussed at a number of meetings, ACEN would like to continue with the process to close Council paper roads within the New England Solar Project Footprint.

Attached are the following documents and reasons why they have been submitted to Council:

1. **Stage 2 Roads 138 Application** : Further to my email of 7<sup>th</sup> September and our subsequent discussion, ACEN would like to formally submit this S138 application for construction of infrastructure for Stage 2 works which are proposed for next year. Contractor Details have not been submitted as this is not yet finalised. Please advise if this document is suitable for Council approval.
2. **23 10 17 NES Council Road map and Section 138 Approval – Segment 5 Closure – Big Ridge Road Uralla – 31 July 2023** : As you may be aware, we have been able to facilitate sheep back in the paddocks under the panels. We have approval under this S138 document for construction and would like to pursue ultimate closure of the roads, but in the meantime, would it be possible to have a license across these portions of land? In order to maintain this Council Road and reduce the potential fire danger, we would like to graze sheep in this area to keep the grass levels low.
3. **Approved Section 138 application in favour of NESF over unformed road wi...** : Prior to construction of Stage 1 works, this document was approved by Council for construction of works over unformed (paper) roads within the project footprint. Following the approval of Item 1 above, we would like to formally apply to Council regarding the permanent closure as discussed previously. The attached is included for your information only at this stage.

Next steps.

If Council could please advise regarding:

1. S138 approval of the Stage 2 paper roads as per the attached application (or if further information is required)
2. Agreement to license Segment 5 of Big Ridge Road to allow sheep grazing.

Following this, we would be keen to discuss further the next steps regarding permanent closure of paper roads.

If you have any questions, happy to discuss on the phone or a meeting.

Kind regards, Sarah

**Sarah Donnan**  
Project Manager



**ACEN Australia**

M: +61 402 206 088

E: [sarah.donnan@acenrenewables.com.au](mailto:sarah.donnan@acenrenewables.com.au)

Suite 2, Level 2, 15 Castray Esplanade, Battery Point, TAS 7004

[www.acenrenewables.com.au](http://www.acenrenewables.com.au)

**ACEN Australia acknowledges the resilience and knowledge of the Traditional Custodians of this nation. We pay our respects to elders past and present, the many Aboriginal people that did not make their elder status and to those that continue to care for country.**

This e-mail and its contents is intended solely for the individual to whom it is specifically and originally addressed and may contain confidential or privileged information. If you are not the intended recipient, please notify me immediately by return email and delete the email from your system. Retaining, disclosing, distributing or taking any action in reliance on this email or its contents is strictly prohibited.

## APPENDIX C ACCESS ROAD CONDITION INSPECTION

|                             |                   |              |                                              |
|-----------------------------|-------------------|--------------|----------------------------------------------|
| <b>Project Name:</b>        | New England Solar | <b>Area:</b> | Barleyfields Road (North) and Big Ridge Road |
| <b>Inspector Name:</b>      |                   | <b>Date:</b> |                                              |
| <b>Inspector Signature:</b> |                   | <b>Time:</b> |                                              |

| Item # | Chainage | Category (minor, major) | Description | Management | Target completion date |
|--------|----------|-------------------------|-------------|------------|------------------------|
|        |          |                         |             |            |                        |
|        |          |                         |             |            |                        |
|        |          |                         |             |            |                        |
|        |          |                         |             |            |                        |

### Notes:

Category should be assigned as follows:

- Minor – defects that do not create material risk to road users, including isolated potholes, bleeding from heat, minor rutting, minor drainage issues, damaged signage, guide posts or linemarkings.
- Major – defects that create material risk to road users and will continue to deteriorate, including concentrated or extensive potholes, major rutting.

Management should be assigned as follows (or otherwise as designated by a suitably qualified person):

- Isolated potholes – Cold mix patch. Remove loose DGB20 from larger potholes before applying cold mix patch.
- Concentrated or extensive potholes – lime stabilisation and re-seal.
- Minor rutting – monitor and re-assess during next inspection. Conduct lime stabilisation and re-seal if required.
- Major rutting – lime stabilisation and re-seal affected area.
- Bleeding from heat – treatment to reactivate seal (e.g. Gilsabind) and add aggregate.
- Corrugation or potholes on unsealed road – maintenance grading.
- Accumulation of gravel or scour adjacent unsealed road – drainage maintenance and profiling.
- Signage, guide posts and linemarking – repair or replace as required.
- Other – manage as recommended by a suitably qualified engineer.

Target completion date should be assigned as follows:

- Cold mix patch – 1 week.
- Other minor works including repairing signage – 1 week.
- Maintenance on unsealed road – 1 to 2 weeks.
- Lime stabilisation and re-seal – 6 weeks.
- Treatment to reactivate seal and add aggregate – 6 weeks.

# **APPENDIX D     DRAFT THM12 PAVEMENT MANAGEMENT SYSTEMS**

Contract Report CR-2000/66

**Draft TMH12**  
**Pavement Management Systems:**  
**Standard Visual Assessment**  
**Manual for Unsealed Roads**  
**Version 1**

**Authors:** D Jones and P Paige-Green

**PREPARED FOR:**

Committee of Land Transport Officials

**PRETORIA**  
South Africa

**PREPARED BY:**

CSIR Transportek  
PO Box 395  
**PRETORIA**  
South Africa  
0001

Tel: +27 12 841-2905

Fax: +27 12 841-3232

|                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                 |                                                 |                               |                                                                                                                                |
|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------------------------------------------|-------------------------------|--------------------------------------------------------------------------------------------------------------------------------|
| <b>DOCUMENT RETRIEVAL PAGE</b>                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                  |                                                 | <b>REPORT No: CR-2000/66</b>  |                                                                                                                                |
| <b>Title:</b> Draft TMH12: Pavement Management Systems: Standard Visual Assessment Manual for Unsealed Roads (Version 1)                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                        |                                                 |                               |                                                                                                                                |
| <b>Authors:</b> D Jones and P Paige-Green                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                       |                                                 |                               |                                                                                                                                |
| <b>Client:</b><br>COLTO                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                         | <b>Client Report No:</b><br>CR-2000/66          | <b>Date:</b><br>December 2000 | <b>Distribution:</b><br>Client Confidential                                                                                    |
| <b>Project No:</b><br>9400/9431/TIJ21                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                           | <b>Programme:</b><br>Infrastructure Engineering |                               | <b>ISBN:</b>                                                                                                                   |
| <b>Preface:</b> <p>TMH12 provides guidelines for the visual assessment of the condition of unsealed roads at network and/or project level for use in unsealed road management systems. A modular approach to information collection is introduced. Attributes of distress are defined and requirements for training and calibration of visual assessors, quality control, assessment procedures and road segment information data are specified. The different assessment parameters are classified and detailed descriptions of degree and distress, including photographic plates illustrating each condition, for each parameter are given. Examples of assessment forms are provided. Simple guidelines on material identification using an engineering geological classification are included.</p> <p>The use of the data collected in management systems and maintenance management planning falls outside the scope of the document.</p> |                                                 |                               |                                                                                                                                |
| <b>Keywords:</b> Unsealed roads, Road Management System, Road Assessment                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                        |                                                 |                               |                                                                                                                                |
| <b>Proposals for implementation:</b> <p>This document has been issued in Draft format under CSIR cover for a limited period. Comments should be forwarded to D Jones who will compile a comments register for discussion by the working group. The document will be updated, if required, and released under a Committee of Transport Officials (COTO) cover in the standard TMH format.</p>                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                    |                                                 |                               |                                                                                                                                |
| <b>Related documents:</b>                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                       |                                                 |                               |                                                                                                                                |
| TMH9, TRH22                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                     |                                                 |                               |                                                                                                                                |
| <b>Signatures:</b>                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                              |                                                 |                               |                                                                                                                                |
| Language editor:                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                | Technical reviewer:                             | Prog Manager:<br>B Verhaeghe  | Information Centre: <div style="float: right; text-align: right;">           Division Director:<br/>P Hendricks         </div> |

---

## TERMS OF REFERENCE

---

The objectives of this project were to:

- Identify the inputs that need to be collected to ensure that the GRMS's in use can operate cost-effectively and that the outputs can be used with confidence;
- Prepare a document to guide assessors of unsealed roads, which fulfils the needs of the various road authorities in South Africa.
- Incorporate modularity into the system identifying the absolute minimum requirements and various other alternatives to comply with the requirements of the various management systems in use.
- Provide uniformity in unsealed road assessment in South Africa.

---

## ACKNOWLEDGEMENTS

---

This manual was compiled by the Division of Roads and Transport Technology of the CSIR on behalf of the South African Committee of Transport Officials (COTA). The contributions of the following individuals in the preparation of the document is gratefully acknowledged:

|                   |                                                            |
|-------------------|------------------------------------------------------------|
| Mr K Arnold       | Free State Department of Public Works, Roads Branch        |
| Mr P Bester       | V and V Consulting Engineers                               |
| Ms C Davis        | North West Department of Transport, Roads and Public Works |
| Mr E Djelebov     | Mpumalanga Department of Public Works, Roads and Transport |
| Mr B Heynes       | VKE Consulting Engineers                                   |
| Mr D Judd         | Jeffares and Green Consulting Engineers                    |
| Mr M de Lange     | Northern Cape Department of Transport                      |
| Mr M Henderson    | Provincial Administration Western Cape, Transport Branch   |
| Mr R Lindsay      | KwaZulu Natal Department of Transport                      |
| Mr C Mathiassen   | Eastern Cape Department of Public Works, Roads Branch      |
| Ms E Sadzik       | Gauteng Department of Transport and Public Works           |
| Mr M van Heerden  | V and V Consulting Engineers                               |
| Mr A van der Gryp | Provincial Administration Western Cape, Transport Branch   |
| Ms V van Staden   | Gauteng Department of Transport and Public Works           |
| Mr F van Staden   | Northern Cape Department of Transport                      |

---

## TABLE OF CONTENTS

|           |                                                         |           |
|-----------|---------------------------------------------------------|-----------|
| <b>A.</b> | <b>GENERAL INFORMATION.....</b>                         | <b>1</b>  |
| A.1.      | Introduction.....                                       | 1         |
| A.1.1     | Terminology.....                                        | 1         |
| A.1.2     | Information to be Collected – The Modular Approach..... | 2         |
| A.1.3     | Structure of the Manual.....                            | 3         |
| A.2.      | Attributes Of Distress .....                            | 3         |
| A.2.1     | General.....                                            | 3         |
| A.2.2     | Types of Distress.....                                  | 3         |
| A.2.3     | Degree.....                                             | 4         |
| A.2.4     | Extent .....                                            | 6         |
| A.2.5     | Examples of the use of Degree and Extent.....           | 7         |
| A.3.      | Training and Calibration of Visual Assessors .....      | 8         |
| A.4.      | Quality Control.....                                    | 9         |
| <b>B.</b> | <b>UNSEALED ROAD ASSESSMENT .....</b>                   | <b>10</b> |
| B.1.      | Introduction.....                                       | 10        |
| B.2.      | Purpose .....                                           | 10        |
| B.3.      | Defining Segments.....                                  | 11        |
| B.4.      | Assessment Forms .....                                  | 11        |
| B.5.      | Assessment Procedure .....                              | 12        |
| B.6.      | Road Information.....                                   | 13        |
| B.6.1     | Material Type.....                                      | 13        |
| B.7.      | General Information .....                               | 14        |
| B.8.      | Parameters to be Assessed.....                          | 14        |
| B.8.1     | General Performance .....                               | 15        |
| B.8.2     | Moisture Condition .....                                | 15        |
| B.8.3     | Gravel Quantity/Layer Thickness .....                   | 16        |
| B.8.4     | Gravel Quality and Influencing Factors .....            | 18        |
| B.8.5     | Road Profile/Shape .....                                | 21        |
| B.8.6     | Drainage from the road .....                            | 23        |
| B.8.7     | Riding Quality and Influencing Factors .....            | 26        |
| B.8.8     | Dust .....                                              | 30        |
| B.8.9     | Trafficability .....                                    | 34        |
| B.8.10    | Potholes.....                                           | 36        |
| B.8.11    | Rutting .....                                           | 38        |
| B.8.12    | Erosion .....                                           | 40        |
| B.8.13    | Corrugation.....                                        | 43        |
| B.8.14    | Loose Material .....                                    | 45        |
| B.8.15    | Stoniness.....                                          | 47        |
| B.8.16    | Slipperiness and Skid Resistance .....                  | 51        |
| B.8.17    | Cracks .....                                            | 54        |
| B.8.18    | Isolated Problems.....                                  | 56        |
| B.8.19    | Maintenance Action.....                                 | 59        |
| B.9.      | Dust Palliative/Chemical Stabiliser Treatments .....    | 59        |
| B.10.     | Material Sampling .....                                 | 59        |
| B.11.     | Use of Data .....                                       | 60        |
| <b>C.</b> | <b>GLOSSARY .....</b>                                   | <b>62</b> |
| <b>D.</b> | <b>TYPICAL ASSESSMENT FORMS .....</b>                   | <b>65</b> |

---

|           |                                         |           |
|-----------|-----------------------------------------|-----------|
| <b>E.</b> | <b>MATERIAL IDENTIFICATION .....</b>    | <b>70</b> |
| <b>F.</b> | <b>REFERENCES .....</b>                 | <b>72</b> |
|           | F.1. Other Relevant Documentation ..... | 72        |

---

## **A. GENERAL INFORMATION**

---

### **A.1. Introduction**

This document provides national guidelines for the visual assessment of the condition and performance of unsealed roads for use in gravel road management systems, maintenance programming and the monitoring of experiments. Sealed flexible and rigid pavements should be assessed in accordance with TMH 9<sup>1</sup>, the Department of Transport Manual for visual assessment of pavement distress: Part 2<sup>2</sup> and TRH 6<sup>3</sup>.

Visual assessments on any road can be used to determine:

- Condition indices
- Maintenance and rehabilitation needs
- Priorities at network level

Assessment of the condition of unsealed roads differs significantly from that of sealed roads: unsealed roads are highly dynamic systems with the appearance and condition varying almost from day to day. Although sealed roads are also dynamic systems, the rate of change of typical performance characteristics is much slower and annual observation is generally sufficient to identify changes and provide timeous inputs for maintenance intervention activities. This is considerably more difficult for unsealed roads, and for routine use the visual assessment is most applicable for determining:

- Regravelling requirements
- Whether current blading frequencies are sufficient
- Whether the gravel on the road is suitable for the traffic and environment and what type of distress is typical of the road/gravel combination

Unlike sealed roads, the performance of unsealed roads depends primarily on the functional characteristics. Localised structural failures are usually “repaired” during routine grader maintenance (occasionally spot regravelling is necessary) whereas structural failures of sealed roads require intensive repair to restore functional performance.

This manual is intended for persons undertaking visual assessments of the condition of unsealed roads for:

- Input for gravel road management systems
- Project level assessments for specific roads
- Ad hoc assessments of road condition after significant events (e.g. severe rainfall)
- Training of assessors to rate unsealed roads in a consistent and repeatable manner
- Assessing the condition of specific roads during experiments

#### **A.1.1 Terminology**

Various terminologies are used for roads where vehicles travel directly on the natural material (i.e. the road has no formal surfacing). Terms include earth and dirt, usually

applied to roads that are not formally constructed, on in situ material, and gravel, unpaved, unsealed, unsurfaced and metalled, usually applied to roads constructed with an imported compacted gravel layer. Since the concepts discussed in this guide are applicable to all types of roads without a formal surfacing (e.g. bitumen, concrete and block paving), the accepted international term of **unsealed roads** will be used throughout the document.

However, the term **Gravel Road Management System (GRMS)** is widely used and understood and has been retained for use in this document.

### **A.1.2 Information to be Collected – The Modular Approach**

The document has been compiled to allow the content to be adapted for different needs and for different Gravel Road Management Systems (GRMS's). It is therefore not necessary to assess every characteristic illustrated in this manual for every situation. Assessments for strategic network level evaluation require less detailed information than necessary for detailed network level assessments.

Evaluations for **strategic network level analyses** need to provide the information necessary to make strategic decisions such as budgeting, planning and evaluation of the influence of budget constraints on the network performance. Typical characteristics assessed include gravel quantity and quality, road profile and drainage and riding quality, which are necessary for estimating regravelling and maintenance requirements. Evaluations for **detailed network level analyses** include significantly more detail, which can be used for both strategic decision-making as well as for maintenance planning and budgeting at operational level. In these cases, more information regarding the performance characteristics is collected and both severity and extent are usually assessed. More detail regarding the use and interpretation of the data collected is provided in Section B.11.

By using a modular approach, minimum requirements can be used for most applications whilst more specific requirements are suggested for detailed network level analyses, project level and research activities. The minimum requirements for each province will usually have been identified during development and installation of their specific GRMS.

The information required will dictate the structure and content of the assessment forms used. Each road authority should develop an assessment form for their specific needs. Assessment forms are discussed in more detail in Section B.4.

The following can be achieved by processing the visual assessment data:

- (a) Calculation of a **visual condition index** for each assessment length through the combination of the rating for degree and extent for each distress type, together with a weight factor based on the importance of the distress type. The condition index can be used to:
  - Give an indication of the condition of each segment of the road assessed.
  - Indicate changes in the overall condition of a road network, or individual segments over time.
  - Classify a road section into one of five condition categories for statistical or visual presentation, as follows:

| VERY GOOD | GOOD | FAIR | POOR | VERY POOR |
|-----------|------|------|------|-----------|
| 1         | 2    | 3    | 4    | 5         |

- (b) Identification of certain required maintenance and/or improvement measures and priorities for use as input for programming and budgeting.
- (c) Identification of required maintenance or improvement measures for use at network or project level (implementation) by maintenance teams.

### A.1.3 Structure of the Manual

The manual comprises six parts:

- Part A contains general information for the assessor, which should be studied as background to the assessment descriptions in Part B.
- Part B provides detailed guidelines on the functional assessment of unsealed roads and descriptions of the various distress types and descriptions of the various degrees of distress that can be encountered on unsealed roads, the data from which will be used as input for gravel road management systems. The method aims to provide a degree of harmony for capturing relevant information by different road authorities in order that output can be realistically compared. Detailed descriptions and colour photographs of typical examples of each distress type for severity levels 1,3 and 5 are provided.
- Part C contains a glossary of terms used in the document.
- Part D contains examples of assessment forms.
- Part E describes a simple method to assist with identification of material type.
- Part F lists documents referred to in the text.

## A.2. Attributes Of Distress

### A.2.1 General

The appearance of distress is varied and often extremely complex. The task of describing this is achieved by recording its main characteristics – the so-called attributes of distress. The attributes referred to in this manual are the:

- Type
- Degree
- Extent

These attributes are defined below in general terms. Each of these attributes is described in more detail in Part B. In some cases, information is also provided on the mechanisms and causes of distress.

### A.2.2 Types of Distress

The type of distress evaluated will depend on the purpose of carrying out the assessment. The modes of distress needing assessment for strategic network level decisions may differ from those needed for detailed network level decisions. A number of assessment parameters are considered essential for any type of evaluation, while detailed descriptions of distress are often desirable, particularly for detailed network level investigations, project level investigations and research investigations. This manual also

---

includes other assessment items that have proved useful in research studies and for complementing the more detailed distress attributes and material properties. Typical types of distress encountered on unsealed roads include:

- Loss of gravel
- Potholes
- Rutting
- Erosion
- Corrugations
- Loose material
- Stoniness
- Dust
- Cracking

These can be assessed individually or in terms of their interactive effect on the functional performance of the road together with material properties, road profile, drainage etc. An example of this is the development of corrugations or potholes, which result in deterioration of overall functionality, particularly riding quality. For more detailed investigations, aspects such as cracking or rutting, although not directly related to riding quality for instance, are indicative of material quality or a potentially problematic situation such as periodic slipperiness or water ponding respectively.

### **A.2.3 Degree**

The degree of a particular type of distress is a measure of its severity. Since the degree of distress can vary over the pavement section, the degree to be recorded should, in connection with the extent of occurrence, give the predominant severity of a particular type of distress. The degree is described by a number where:


- Degree 1 indicates the first evidence of a particular type of distress (“slight”).
- Degree 3 indicates a warning condition. This would normally indicate that intervention might be required in order to avoid the distress deteriorating to a severe condition.
- Degree 5 indicates the worst degree (“severe”). Urgent attention is required.

The general descriptions of degree of each type of distress are presented in Table A.1. These descriptions relate to the possible consequences of each type of distress and therefore also to the urgency of maintenance or rehabilitation. Degree 0 is recorded if the defect does not occur. Degree 1 generally indicates that no attention is required; degree 3 indicates that maintenance/improvement might be required in the near future, whereas degree 5 indicates that immediate maintenance/improvement is required. Specific classifications for the various types of distress have been compiled, based on these general descriptions (see Part B).

**TABLE A1: General description of degree classification**

| Degree | Severity                   | Description                                                                                                                                                                                              |
|--------|----------------------------|----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| 0      | None                       | No distress visible                                                                                                                                                                                      |
| 1      | Slight                     | Distress difficult to discern. Only the first signs of distress are visible.                                                                                                                             |
| 2      | Between slight and warning |                                                                                                                                                                                                          |
| 3      | Warning                    | Distress is distinct. Start of secondary defects. (Distress notable with respect to possible consequences. Maintenance might be required in near future e.g. potholes can be removed by blading)         |
| 4      | Between warning and severe |                                                                                                                                                                                                          |
| 5      | Severe                     | Distress is extreme. Secondary defects are well-developed (high degree of secondary defects) and/or extreme severity of primary defect. (Urgent attention required e.g. potholes require manual repair). |

A flow diagram illustrating the use of the five-point classification system is shown in Figure A.1. The most important categories of degree are 1, 3 and 5. If there is any uncertainty regarding the condition between degrees 1 and 3 or 3 and 5, the defect may be marked as 2 or 4, respectively. This is particularly relevant for research purposes (where frequent visual assessments are carried out), or detailed project level studies.

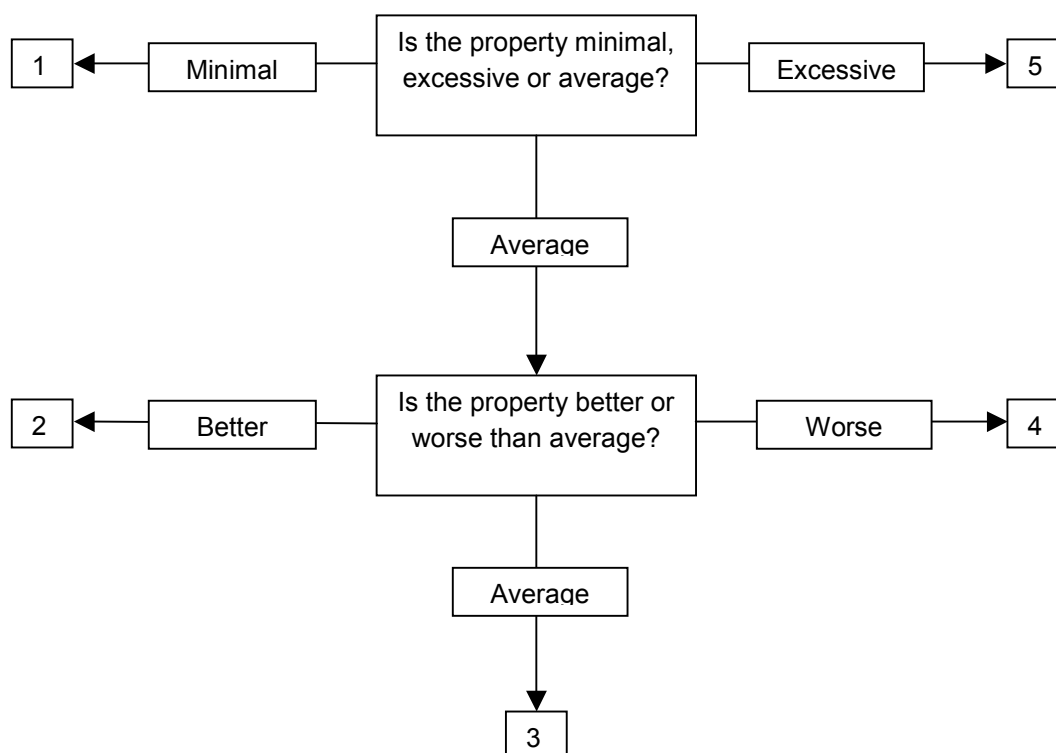**FIGURE A.1: Flow diagram – five point classification system**


**A.2.4 Extent**

The extent of distress is a measure of how widespread the distress is over the length of the road segment. The extent is also indicated on a five-point scale in which the length of road affected by the distress is estimated as a percentage. The general description of the extent classifications is given in Table A.2 and illustrated diagrammatically in Figure A.2.

**The extent of the distress should be recorded only for that width of the road affecting the traffic.**

**TABLE A.2: General description of extent classifications**

| Extent | Description                                                                                                                                                                                                                                                                                                                                                                                   | Estimate (%) |
|--------|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|--------------|
| 1      | Isolated occurrence, not representative of the segment length being evaluated. They are usually associated with localised changes in the material, subgrade or drainage conditions. Intersections, steep grades or sharp curves may also result in isolated occurrences.                                                                                                                      | < 5          |
| 2      |                                                                                                                                                                                                                                                                                                                                                                                               | 5 – 20       |
| 3      | Intermittent occurrence, over most of the segment length, or extensive occurrence over a limited portion of the segment length. When occurring over most of the segment length, problems are usually associated with the material quality or maintenance procedures. When occurring over limited portions, the problem is usually a result of local material variations or drainage problems. | 20 – 60      |
| 4      |                                                                                                                                                                                                                                                                                                                                                                                               | 60 – 80      |
| 5      | Extensive occurrence. This is usually a result of poor quality or insufficient wearing course material, or inadequate maintenance.                                                                                                                                                                                                                                                            | 80 - 100     |

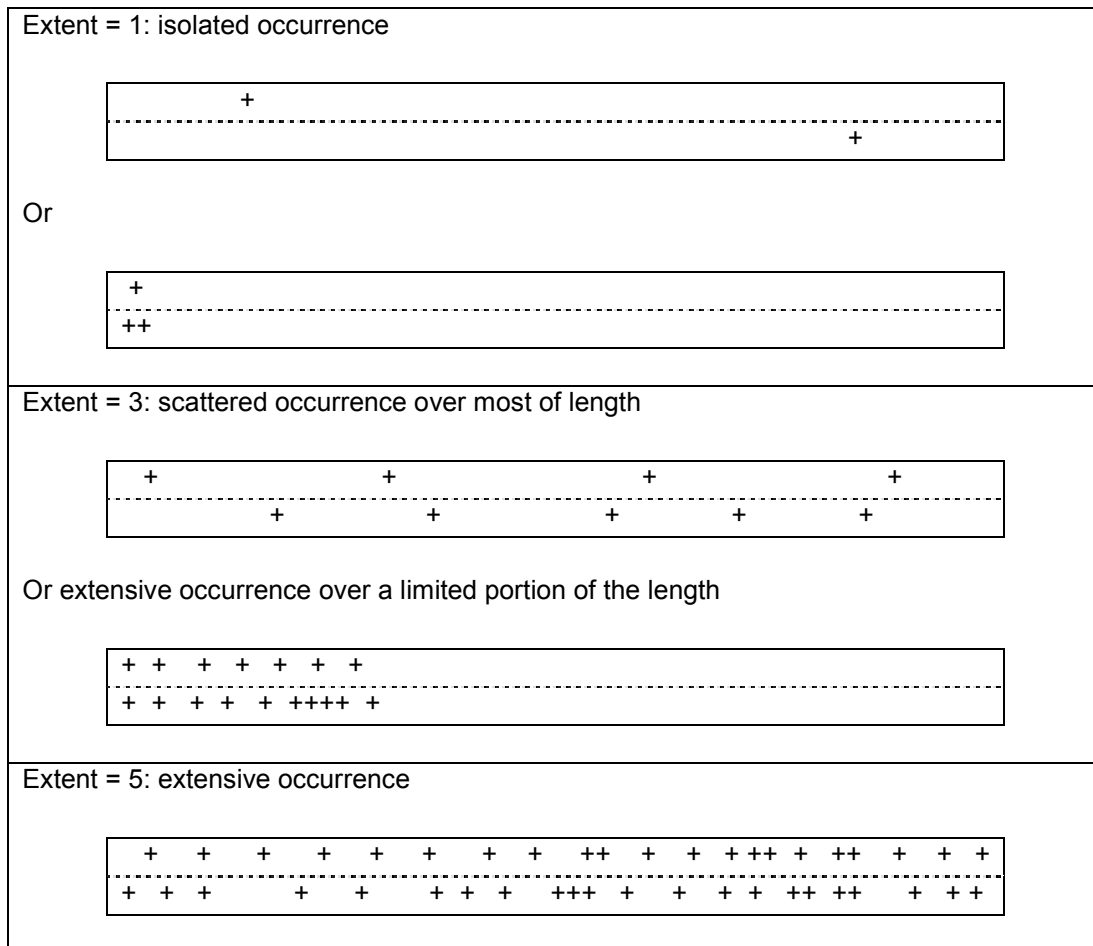

**FIGURE A.2: Diagrammatical illustration of extent**

Experience has shown that even amongst experienced raters, there is a general tendency to overestimate the extent of defects. This tendency increases with severity of the defect.

Estimation of the extent is not required for strategic network level assessments. However, provision must be made for recording localised problems. The extent is, however, essential for detailed network level assessments, project level assessments and for research purposes.

#### **A.2.5 Examples of the use of Degree and Extent**

The following examples illustrate the combined use of degree and extent:

- (a) If potholing of degree 5 occurs seldom (i.e. extent 1) and potholing of degree 3 occurs extensively (i.e. extent 5), the degree 3/extent 5 potholing is recorded as the predominant indication of the severity of potholing over the specific road segment in terms of possible maintenance action. In such a case, the degree 5 potholing will be viewed as an area of localised distress requiring routine attention.
- (b) If potholing of degree 5 and extent 2, and potholing of degree 1 and extent 4 occurs, degree 5/extent 2 is recorded as the average indication of the problem that is most significant in terms of possible action. (Potholing of degree 1 is not considered significant in terms of possible action.)

- 
- (c) For research purposes, the maximum severity possible is of greater interest and not the predominant severity.

### **A.3. Training and Calibration of Visual Assessors**

The accuracy of the visual assessment data depends largely on the knowledge, experience and commitment of the assessors. To minimise the element of subjectivity and to ensure good knowledge of the assessment procedures, it is essential to train and calibrate all assessors before visual assessments are carried out. The intensity and duration of the training session will depend on the experience of the assessors.

It is recommended therefore that an annual training and calibration session be held even if all the assessors were trained during previous years. Changes to guidelines and procedures should also be presented and problems with the previous assessments should be discussed.

The training and calibration programme for assessors should include the following:

- An overview of the objectives of the visual assessment together with a brief description of the data processing procedures and applications of the final results.
- An overview of the causes of the various types of distress. It is essential that the raters understand the causes of the problems to get a realistic rating and to make recommendations on corrective action if required.
- An overview of the method of assessment, including identification of materials, descriptions of various types of distress and ratings for each type. The use of colour slides to show examples is recommended. The visual assessment manual should be studied by all before the training session.
- An overview of the format of the assessment sheet.
- Practical training, assessing at least 10 road segments, preferably in different conditions exhibiting a full range of defects. The method of rating should be discussed on the first segment which should then be rated jointly with further discussion until agreement and understanding is reached. Each assessor should then evaluate each of the remaining segments individually without discussion with other assessors. The assessment forms should then be compared afterwards and any major discrepancies should be discussed. If necessary, more segments should be assessed and discussed individually until acceptable consistency of rating is achieved.

Problems may be encountered with the estimation of remaining gravel particularly where subgrade is extensively exposed. Assessors may consider the exposures as an imported wearing course, thereby overestimating the gravel quantity/layer thickness. The assessors therefore need to be aware of the need to interpret the road environment and characteristics in distinguishing between imported gravel wearing course and subgrade/road formation.

It is recommended that, during the practical training, those attributes for which estimates of actual depths and sizes are required should be physically measured to enhance/check the capability of accurate quantitative assessment.

In addition, it is advisable for each project leader to meet with all the assessors within days after the start of the formal assessment to check the initial assessments.

It is essential that raters go through this process of training prior to any visual assessment programme. Post assessment calibrations have shown that where assessors were inadequately trained, the assessment has had to be redone. Where the original assessment was done on contract, they have had to redo it at their own cost.

#### **A.4. Quality Control**

An independent assessment of at least 10 to 15 per cent of the gravel road network should be carried out within one week of the roads being assessed to ensure that the study was carried out to an acceptable standard and to ensure that the raters have been consistent.

The following issues should be considered during the quality control exercise:

- Roads totalling between 10 and 15 per cent of the network should be selected, ensuring a good representation of the entire network. The results of the previous years assessment should be used to refine the selection in order that the majority of the roads selected are likely to have a visual condition index in the 3 to 5 bracket. Larger variations between raters are likely on roads in poor condition than on roads in good condition.
- The raters should not be informed of which roads are included in the quality control assessment.
- The person undertaking the quality control assessment should attend the training session together with the other raters.
- Based on the raters' plans, the selected roads should be assessed by the quality control rater within one week of the original assessment. This will ensure that the roads will be in a similar condition when being assessed.
- The results of the original and quality control assessments should be statistically compared. The variation should not exceed 15 per cent. It should be noted that, due to the subjective nature of visual assessments on unsealed roads, the practitioner undertaking the quality control assessment might not necessarily be correct. This will be revealed if different results are obtained by the quality control assessor to that of each of the original raters. If this occurs, the quality control assessment will have to be repeated. Alternatively, if discrepancies of more than one unit occur on two of the essential fields on the assessment form, the original assessment should be queried.
- If the variation in results exceeds the acceptable limit, the assessment forms should be compared to determine where the discrepancy occurs. If it is derived from the entire assessment, the rater and quality controller (and the client if quality control is also contracted out) should visit the sites to understand the discrepancy. If the fault lies with the rater, the assessment will have to be repeated. The rater should either be replaced or retrained.

---

## **B. UNSEALED ROAD ASSESSMENT**

---

### **B.1. Introduction**

The objective of a gravel road management system (GRMS) is to obtain a general overview of an unsealed road network for budgeting and strategic planning purposes. The system does not usually identify needs at project level, but is used for high-level decision-making. Project level assessments are more detailed than those done for strategic decision making and are carried out on specific roads identified as requiring attention from the GRMS. They can also be used by district staff for routine management activities, or for specific evaluations such as experimentation, feasibility for upgrading and justification for chemical improvement or dust control. The quantity and quality of data collected will differ between assessments depending on the reason for carrying out the assessment. The level of detail is usually far greater at project level than at strategic level. Direct measurement of certain properties and collection of samples for laboratory testing may also be included.

In order to provide reliable outputs and allow direct comparison between projects, it is essential that the data used in a GRMS is consistent and of high quality. The data capture also needs to be repeatable and done in the most cost-effective manner.

For most project level assessments, the items identified as desirable provide additional value to the essential items. Those items identified as optional need only be collected if required.

With independent road authorities in the provinces, a uniform procedure for the collection of data will allow direct comparisons between the strategic and tactical decisions made in the different provinces.

### **B.2. Purpose**

The data collected for use in the gravel road management system should provide the road authority with objective information to assist with strategic and tactical decision making. This includes aspects such as:

- An indication of the current level of service provided by the network
- The cost of maintaining the current level of service
- The cost of an improvement in service
- An indication of the social and economic impact of these improvements
- The effect of current policies on the future levels of service
- Prioritising roads to be upgraded to sealed standard
- Frequency of blading and regravelling
- Distribution of funds between blading and regravelling
- Benefits from predictions

---

### **B.3. Defining Segments**

In order to cost-effectively evaluate unsealed roads, it is necessary to segment them into manageable units. Each segment should be relatively uniform in terms of its material type and general performance and should be about 5 km long. They should not be less than 2.5 km to avoid the collection of excessive and repetitive data, unless the segment will be used for experimentation or where a variety of different materials is used. For ease of use and application, the start and end-points of each segment should be related to fixed datum points (e.g. intersections, bridges etc), but this is often not possible on rural roads, in which case, durable marker boards should be erected. The segments remain fixed.

Defining segments in the urban environment is carried out on a different basis. Segment lengths are relatively short and are typically defined by intersections.

The increasing availability, affordability and accuracy of Global Positioning Systems (GPS) technology, will in future allow the specification and easy relocation of arbitrary datum points (e.g. every 5 km, or the change of gravels).

### **B.4. Assessment Forms**

The information required by various road authorities will dictate the parameters used on and layout of the form. A number of examples of assessment forms are provided in Part D. Many authorities already have standard forms, but the examples could be used as a basis for upgrading these or developing new forms for those authorities that do not have any. In keeping with the modular approach advocated in this document, it is recommended that the following minimum information be captured for any assessment. As the intensity of the analysis increases, additional or more information needs to be captured. This is illustrated in the sequence of the four forms in Part D

- Gravel quantity/layer thickness
- Gravel quality and influencing factors or estimates of selected material properties
- Road profile/shape as an assessment of water shedding capacity
- Road drainage in terms of removal of water from roadside
- Riding quality/safety and influencing factors
- Dust
- Trafficability
- Moisture condition

Additional information fields can be added to the forms to suit the individual requirements of any road authority.

It is critical that the data collection form has the same reference to the segment identification as the data inventory. All data must be captured on a standard data sheet to ensure consistency and completeness.

---

## **B.5. Assessment Procedure**

The successful implementation of a GRMS relies on accurate and repeatable data. These data are captured during the periodic visual assessment of the entire gravel road network. At network level, there is a large volume of data to be collected and assessment needs to be carried out in as short a time as possible.

The results of the assessment are recorded on field assessment forms, which are the links between the rater and the GRMS or any other use. The assessment can be enhanced if the rater has a clear understanding of the desired output of the GRMS. (i.e. will the data be used primarily for strategic planning purposes, or will more tactical applications be derived from them?)

Visual assessments should preferably be carried out in the dry season, as many of the important defects are not easily identified when the road is wet. The dry season is also longer than the wet season over most of South Africa allowing a longer window for this data collection. If detailed assessments are made throughout the year, then cognisance should be taken of the recent weather conditions. Surveys should, however, be completed as quickly as possible to ensure repeatability and to exclude seasonal influences. For GRMS data collection, the daily length of survey should generally not exceed 130 km, based on the ability to assess three segments of 5 km each per hour in an 8-hour day. Shorter daily lengths may be expected if the condition of the road is very variable, in the case of shorter segment lengths, or if detailed assessments are being made.

The assessors should drive at a speed not exceeding 40 km/h when gathering data and should include at least one stop on each segment for a closer assessment of the material quality, layer thickness and general performance. However, for detailed or research assessments, assessors should initially drive over the length of the segment in both directions at a speed not exceeding 20 km/h. While driving, suitable locations for detailed visual assessments and sampling should be identified. The assessment of defects is generally restricted to the trafficked portion of the carriageway and excludes the shoulders and windrows left during blading.

**Suitable safety precautions should be taken at all times.**

Individual road authorities may require more frequent stops for information gathering and material assessment and sampling. During these stops, actual gravel thickness may be determined. The accuracy of the assessor's rating will generally be influenced by the frequency of stops made, this frequency depending on the condition of the road and its variability. During assessment of the first segment, more stops will probably be required in order to relate the appearance of the road from within the vehicle while moving to that when stationary. Additional stops may be required on segments showing isolated areas of severe distress. The assessor should leave the vehicle during the stops to examine the road more closely. The use of a geological pick during the assessment is recommended.

Unlike assessments for GRMS input, that are carried out at regular intervals (usually annually), detailed assessments may be carried out on a more ad hoc basis. For problem evaluation, a once off assessment may suffice, while for experimentation purposes, frequent assessments over a period will be required. In these types of

---

assessments, data that is more detailed is often required, which implies that more time needs to be spent on the selected segments.

The first road segment to be evaluated in any assessment requires a thorough orientation to adjust the assessors to the prevailing conditions, because the position of the sun (preferably from the rear), the amount and variability of cloud cover and a wet surface will influence the visibility of the defect (e.g. dust and corrugations). This may entail doubling back in order to acquire sufficient data.

As detailed network level and project level assessments require more detail than network level assessments, it is rarely possible to undertake them only from a moving vehicle. More measurements and material sampling are often required and the locations for these activities should be predetermined or selected once on site. The assessment is usually best carried out by walking the road in both directions.

During the visual assessment of segments, dots can be made on the assessment form in the appropriate positions to indicate the degree of any type of distress that is observed. At the end of the segment, these dots are used to mark a predominant degree of distress for each type of defect. All fields on the form must be completed (none, where no distress is observed) to ensure that no assessment parameters have been overlooked. After completing the form, the assessor should also check road segment information (i.e. correct start and finish information, etc).

## **B.6. Road Information**

The information regarding each road and its segments is required for the data inventory. These are summarised in the list below. They are stored in the GRMS database. Only road number, start and end kilometre of the segment are required on the assessment form.

- Road number
- Start km of segment
- End km of segment
- Node description
- District/region
- Weinert N-value
- Terrain
- Road type (i.e. earth, gravel, treated)
- Design road width
- Traffic data (this will vary from authority to authority)
- Material type (this may change during the life of the road)

It is important, however, that any obvious changes, particularly in the road width, material type or traffic volume, are captured on the form during the assessment and reflected in the section inventory. Fields to check these items can be included on the assessment form if required.

### **B.6.1 Material Type**

Basic classification of the material type is used by some road authorities in conjunction

with the gravel quality (e.g. clay, sand and gravel) to predict performance in their GRMS's. Typical material properties (e.g. grading modulus, plastic limit, various particle size fractions) are linked to standard material types as input parameters for algorithms in the GRMS to predict gravel loss and blading frequencies. In other GRMS's, material type is used purely as a check of the road inventory information.

The general classification of materials minimises laboratory testing and is the most practical method for estimating material property inputs for network level evaluations. However, calibration of the material properties will be necessary for each area. The best results would be obtained by carrying out laboratory testing on representative samples removed from the road, but the resources required usually render this prohibitive. Regravelling of roads over time will make material properties available for more accurate determinations. Accurate identification of the material type is not always necessary and it is suggested that the more general engineering geological classification developed by Weinert<sup>4</sup> be used. Commonly used road construction materials are classified into their engineering geological groups in Table B.1 below.

**TABLE B.1: Engineering geological classification and example materials**

| Group             | Material type                                       |
|-------------------|-----------------------------------------------------|
| Basic crystalline | Dolerite, andesite, basalt, diabase, gabbro, norite |
| Acid crystalline  | Granite, felsite, rhyolite, gneiss                  |
| High silica       | Chert, quartzite, quartz porphyry                   |
| Arenaceous        | Sandstone, arkose, conglomerate                     |
| Argillaceous      | Shale, mudstone                                     |
| Diamictites       | Tillite, breccia                                    |
| Pedocretes        | Ferricrete, calcrete, silcrete, dorbank             |
| Transported       | Sand, river gravel                                  |

A simple material identification procedure is included in Part E. This is based on the quantity of quartz and the ability of the rater to identify it with a magnifying glass.

## **B.7. General Information**

The general information that needs to be captured includes the name of the evaluator, the date of the evaluation, the road and section numbers and their start and end km's.

## **B.8. Parameters to be Assessed**

The following road characteristics should be assessed as a minimum in a GRMS assessment:

- General performance
- Moisture condition
- Gravel quantity/layer thickness
- Gravel quality and influencing factors or estimates of selected material properties
- Road profile/shape as an assessment of water shedding capacity

- 
- Road drainage in terms of removal of water from roadside
  - Riding quality and influencing factors
  - Dust
  - Trafficability
  - Isolated problems
  - Maintenance action required

Some road authorities may require additional information for specific needs. For example:

- A road authority that plans to use sand cushioning as a maintenance option for controlling corrugations would need to capture additional information regarding this defect.
- A road authority with ready access to in situ stone processing equipment (e.g. Rockbuster) would need more information on stoniness.

Under certain circumstances, e.g. when assessing in remote areas, it may be cost-effective to assess the road in more detail than would normally be necessary. The extra time involved is minimal compared to the disadvantages of having to return to the site at a later date to gather additional information.

#### **B.8.1 General Performance**

An estimate of the general performance should be made. This should be representative of how the travelling public would view the condition and performance of the road. This parameter is recorded for possible use as a crosscheck with any visual condition index calculated from the full assessment (e.g. if general condition is rated as good, but corrugations are rated as severe over most of the road, a misjudgement has been recorded). It can also be used as a first indication of the overall performance of the road network.

General performance is assessed on a scale of **one to five** (where one is very good and five is very poor) primarily in terms of driver and passenger comfort and the drivers perception of safety. It should be estimated after driving the segment before the detailed assessment is carried out in order to eliminate any bias that may result after completing the detailed assessment.

#### **B.8.2 Moisture Condition**

The moisture condition affects the visual assessment of properties such as dust, corrugations, loose material and skid resistance. It is therefore necessary to estimate the moisture condition for later use if there are queries regarding the influence of any of these properties.

Assessment of the condition is limited to a subjective rating of “**wet**” (damp) or “**dry**” taking the consequences into account (e.g. the road will not be wet if dustiness is significant). Disturbance of windrows or loose material will usually indicate whether the material is wet.

In project level or experimental assessments, more accurate indications of moisture content may be required and can be obtained by sampling the material, placing it in a sealed container and determining the moisture content gravimetrically in an oven. Output from this type of assessment will be the percentage moisture by dry mass of the soil.

### B.8.3 Gravel Quantity/Layer Thickness

Most unsealed roads are constructed with a wearing course of about 150 mm of compacted selected gravel. Under traffic and environmental influences, this gradually wears away and requires periodic replacement. If it is not replaced, the subgrade is exposed to traffic. This material is usually unsuitable as a wearing course and results in trafficability problems and shear failures. In flat areas, drainage of water away from the road will be retarded or even impeded.

The rate of gravel loss is a function of the material properties and the traffic. However, as the traffic increases, or the material quality deteriorates, this annual loss increases significantly. The rate also increases if profile and drainage are poor.

During the visual assessment, it is necessary to estimate whether sufficient gravel remains to provide adequate service until the next assessment period. This requires actual measurements of the layer thickness, or judgement by the rater taking into account the material quality, traffic and any evidence of subgrade exposure.

Gravel quantity is either rated on a five-point scale as described in Table B.2, or physically measured on the road by excavating small holes in the wheel tracks. This should be done at a sufficient frequency (e.g. 5 holes on a 5 km segment) to determine a representative average for the segment. Output from the assessment will be millimetres of material remaining. It should be noted that the direct measurement of layer thickness is essentially a measure of the severity of gravel loss, while estimation of the subgrade exposure represents an extent. Although the former is the optimum solution, the latter is a more readily obtained proxy for the severity.

**TABLE B.2: Visual assessment of gravel quantity**

| Rating                                                                    | Descriptor          | Description                                         | mm        |
|---------------------------------------------------------------------------|---------------------|-----------------------------------------------------|-----------|
| 1                                                                         | Plenty              | Good shape, and no stone protrusion                 | >125      |
| 2                                                                         | Sufficient          | No exposures of subgrade, but some stone protrusion | 100 – 125 |
| 3                                                                         | Isolated exposures  | Less than 25 per cent exposure of the subgrade      | 50 – 100  |
| 4                                                                         | Extensive exposures | Up to 75 per cent exposure of the subgrade          | 25 – 50   |
| 5                                                                         | None                | 75 to 100 per cent exposure*                        | 0 – 25    |
| * Total exposure of subgrade should not be confused with plenty of gravel |                     |                                                     |           |

When visually assessing gravel thickness, adequate cover of material over pipe drains and culverts can be a good indicator, bearing in mind that all culverts/pipes should have sufficient cover to protect the structures from traffic loads. Exposure of pipe drains, culverts and bedrock indicates neglect of the road and inadequate gravel cover. The same applies to stone exposure. If it is assumed that the surface of the road was level after compaction, the height of stones above the surrounding road surface will give an indication of the amount of gravel that has been lost.

When less than 25 per cent of the imported gravel wearing course material remains, but the exposed subgrade material appears to be performing adequately, the gravel quantity should still be rated as “none” to ensure that the road is prioritised for regravelling by the GRMS.

| GRAVEL QUANTITY                                                                     |                    |   |          |   |          |
|-------------------------------------------------------------------------------------|--------------------|---|----------|---|----------|
|    | Degree 1           |   |          |   |          |
|                                                                                     | <b>X</b>           | 2 | 3        | 4 | 5        |
|                                                                                     | Plenty             |   |          |   |          |
|   | Degree 3           |   |          |   |          |
|                                                                                     | 1                  | 2 | <b>X</b> | 4 | 5        |
|                                                                                     | Isolated exposures |   |          |   |          |
|  | Degree 5           |   |          |   |          |
|                                                                                     | 1                  | 2 | 3        | 4 | <b>X</b> |
|                                                                                     | None               |   |          |   |          |

#### B.8.4 Gravel Quality and Influencing Factors

The performance of an unsealed road depends primarily on the quality of the gravel used to construct the wearing course. The properties contributing to good gravel are particle size distribution and cohesion. The gravel should have a range of particle sizes ranging from very fine up to about 40 mm in order to provide a strong framework of stones interlocked by a tight matrix of fines. An excessive number of large stones results in poor riding quality and difficulties with maintenance. The fines need to have some plasticity to provide cohesion when dry. However, plasticity should not be so high that the road becomes slippery and impassable when wet. Optimally, samples of the gravel should be tested for these properties in a laboratory. However, this is usually not feasible during annual assessments and a more subjective evaluation will usually suffice. Training and calibration before the assessment will minimise the subjectivity.

Gravel quality is rated on a five-point scale, as described in Table B.3.

**TABLE B.3: Visual assessment of gravel quality**

| Rating | Descriptor | Description                                                                                                                                                                                               |
|--------|------------|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| 1      | Very good  | Evenly distributed range of particle sizes and sufficient plasticity that the material will leave a shiny streak when scratched with a pick. No significant cracking, ravelling and/or excessive oversize |
| 2      | Good       | Minor ravelling or cracking and/or minimal                                                                                                                                                                |
| 3      | Average    | Cracking, loose material or stones clearly visible,                                                                                                                                                       |
| 4      | Poor       | Poor particle size distribution with excessive oversize. Plasticity high enough to cause slipperiness. Ravelling is sufficient to cause loss of traction.                                                 |
| 5      | Very poor  | Poorly distributed range of particle sizes and/or zero or excessive plasticity. Cracking and/or quantity of loose material/stones are significant and affect safety of road user. Excessive oversize.     |

The factors influencing the rating must also be recorded. The following factors can be marked:

- Excessive clay and/or silt (i.e. plasticity too high)
- Excessive sand – loose with insufficient fines (i.e. plasticity too low)
- Excessive oversize stones and/or loose gravel

Some GRMS's require estimates of the material properties, particularly the plasticity index. This is usually assessed in three categories, e.g. less than 6, 6 to 15 and greater than 15.

Although the gravel quantity may be rated as “extensive exposures” or “none”, it is still necessary to rate the related performance. This should be applied to the predominant surface material on the carriageway, whether it is subgrade or the remaining wearing course. This assessment should be carried out in terms of the road users perception of the road and the ability to carry out effective maintenance

| GRAVEL QUALITY                                                                      |           |   |          |   |          |
|-------------------------------------------------------------------------------------|-----------|---|----------|---|----------|
|    | Degree 1  |   |          |   |          |
|                                                                                     | <b>X</b>  | 2 | 3        | 4 | 5        |
|                                                                                     | Very good |   |          |   |          |
|   | Degree 3  |   |          |   |          |
|                                                                                     | 1         | 2 | <b>X</b> | 4 | 5        |
|                                                                                     | Average   |   |          |   |          |
|  | Degree 5  |   |          |   |          |
|                                                                                     | 1         | 2 | 3        | 4 | <b>X</b> |
|                                                                                     | Very poor |   |          |   |          |

| GRAVEL QUALITY – INFLUENCING FACTORS                                                |                    |  |  |  |  |
|-------------------------------------------------------------------------------------|--------------------|--|--|--|--|
|    |                    |  |  |  |  |
|                                                                                     |                    |  |  |  |  |
|                                                                                     | Excessive clay     |  |  |  |  |
|   |                    |  |  |  |  |
|                                                                                     |                    |  |  |  |  |
|                                                                                     | Loose sand         |  |  |  |  |
|  |                    |  |  |  |  |
|                                                                                     |                    |  |  |  |  |
|                                                                                     | Excessive oversize |  |  |  |  |

**B.8.5 Road Profile/Shape**


The profile (shape) of a road has a major impact on the performance of that road. Roads with good profile tend to shed water rapidly avoiding the development of potholes and potentially impassable conditions. Where the profile is flat, water tends to pond in localised depressions resulting in softening of the wearing course and the development of potholes and other deterioration. Failure to timeously repair a flat road will usually result in the development of ruts under traffic. These may become preferential water paths resulting in erosion, accelerated gravel loss and significant deterioration in riding quality.

It should be noted that rutting in unsealed roads is generally the result of loosening and whip-off of material and is only seldom the result of subgrade deformation/settlement. Routine grader blading usually reduces rutting.

The road profile is rated on a five-point scale where one is very good and the trafficked surface will shed water easily, and five is very uneven resulting in potential localised ponding and/or surface drainage occurring in a longitudinal direction. These are defined in Table B.4 and illustrated in Figure B.1. It should be noted that on grades, the impact of the gravel profile becomes less dominant than the actual grade.

**TABLE B.4: Visual assessment of gravel profile**

| Rating | Descriptor      | Description                                                                                                                                                               |
|--------|-----------------|---------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| 1      | Very good shape | Well formed camber (about 3 - 4 per cent)                                                                                                                                 |
| 2      | Good shape      | Good camber (about 2 per cent)                                                                                                                                            |
| 3      | Flat            | Some unevenness with camber mostly less than 2 per cent                                                                                                                   |
| 4      | Uneven          | Obvious development of irregularities that will impede drainage and form depressions                                                                                      |
| 5      | Very uneven     | Development of severe irregularities impeding drainage and likely to cause extensive localised ponding. Water tends to flow to the centre of the road or individual lanes |

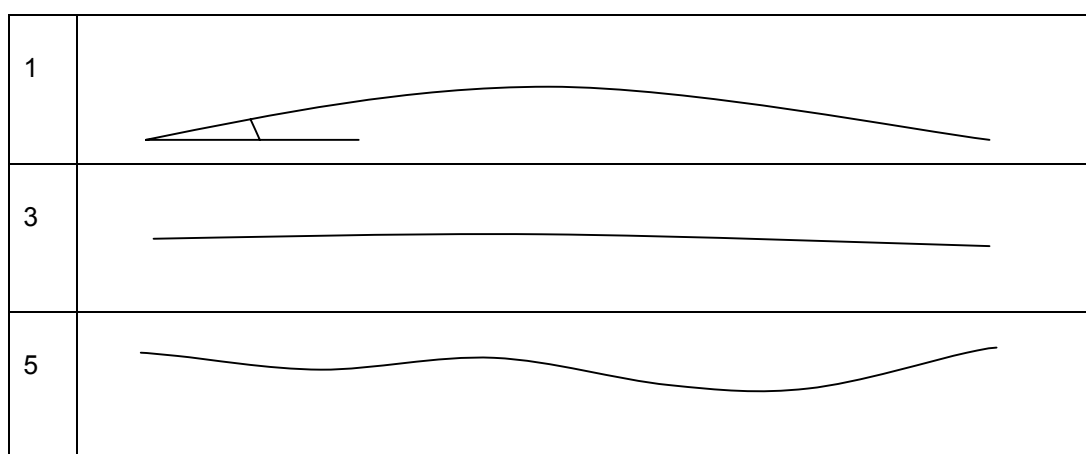**FIGURE B.1 Gravel profile schematics**

| GRAVEL PROFILE                                                                      |             |   |          |   |          |
|-------------------------------------------------------------------------------------|-------------|---|----------|---|----------|
|    | Degree 1    |   |          |   |          |
|                                                                                     | <b>X</b>    | 2 | 3        | 4 | 5        |
|                                                                                     | Very good   |   |          |   |          |
|   | Degree 3    |   |          |   |          |
|                                                                                     | 1           | 2 | <b>X</b> | 4 | 5        |
|                                                                                     | Flat        |   |          |   |          |
|  | Degree 5    |   |          |   |          |
|                                                                                     | 1           | 2 | 3        | 4 | <b>X</b> |
|                                                                                     | Very uneven |   |          |   |          |

### B.8.6 Drainage from the road


There is obviously a strong interrelationship between the road profile discussed previously (drainage off the road) and drainage from the road. However, the profile relates more directly to the capacity of the road to shed water without causing erosion, while drainage from the road relates more closely to the impact of standing water on both the wearing course and underlying road structure. Effective operation of adequate side drains is the predominant aspect to be considered during this rating. This includes removal of water from the zone of influence adjacent to the road as well as erosion effects associated with shoulders and undercutting of the road.

Drainage from the road is rated on a five-point scale where one indicates that the road is well above ground level and has effective side drains leading water away from the road formation. Five is classified as a canal where the road acts as the drainage path in the area. These are defined in Table B.5 and illustrated in Figure B.2. The descriptors are essentially applicable to roads in flat or slightly sloping terrain. Where grades are steeper, roads assessed as degrees 4 and 5 will act as drainage courses during periods of intensive rainfall leading to severe erosion.

**TABLE B.5: Visual assessment of drainage/road formation**

| Rating | Descriptor                    | Description                                                                                                                      |
|--------|-------------------------------|----------------------------------------------------------------------------------------------------------------------------------|
| 1      | Well above ground level       | Edges of road are at least 300 mm* above natural ground level with effective side drains                                         |
| 2      | Slightly above ground level   | Road is between 50 and 300 mm above natural ground level. Side drains are present. Stormwater could cross in isolated places.    |
| 3      | Level with ground             | Road is generally at ground level with ineffective side drains. Stormwater could cross in most places.                           |
| 4      | Slightly beneath ground level | Isolated areas of the road are below natural ground level. No side drains are present and localised ponding of water will occur. |
| 5      | Canal                         | Road is the lowest point and serves to drain the entire area.                                                                    |

\* If pipes are laid under the road for drainage, then the formation should be at least 500 mm above natural ground level

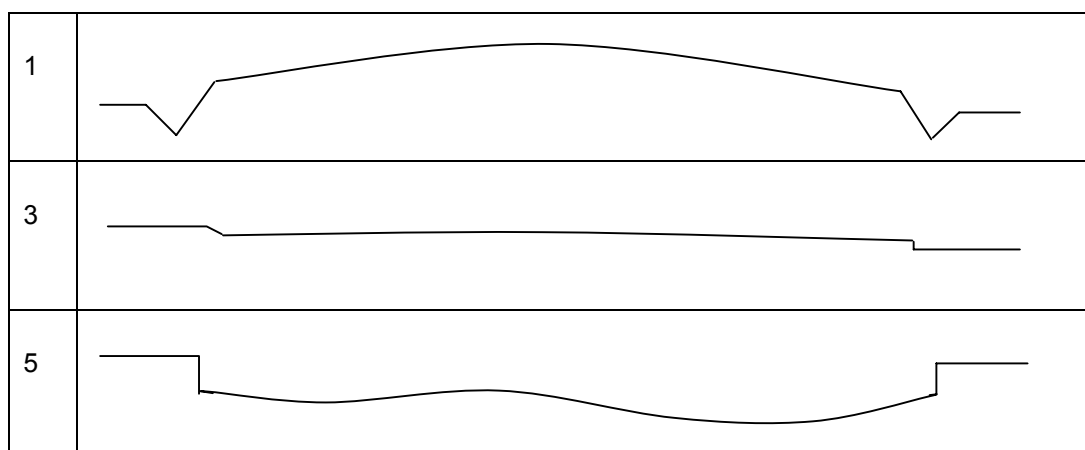

**FIGURE B.2: Schematics of road drainage**

Additional information may be required on the presence, condition and effectiveness/adequacy of culverts and mitre drains. This will entail written information on the facilities with recommendations on maintenance or upgrading if this is required. In many instances, these are assessed separately during routine maintenance inspections.

| DRAINAGE                                                                            |                   |   |          |   |          |
|-------------------------------------------------------------------------------------|-------------------|---|----------|---|----------|
|    | Degree 1          |   |          |   |          |
|                                                                                     | <b>X</b>          | 2 | 3        | 4 | 5        |
|                                                                                     | Well above ground |   |          |   |          |
|   | Degree 3          |   |          |   |          |
|                                                                                     | 1                 | 2 | <b>X</b> | 4 | 5        |
|                                                                                     | Level with ground |   |          |   |          |
|  | Degree 5          |   |          |   |          |
|                                                                                     | 1                 | 2 | 3        | 4 | <b>X</b> |
|                                                                                     | Canal             |   |          |   |          |

### B.8.7 Riding Quality and Influencing Factors

The riding quality of the road is probably the major performance parameter affecting driver and passenger comfort and safety. It also has a significant impact on the overall vehicle operating cost associated with the road. Road roughness is best quantified using one of the many items of equipment dedicated to roughness evaluation. However, for the purposes of network assessment, it is usually acceptable to rate the riding quality subjectively.

Road roughness is influenced primarily by maintenance frequency, quality of grader maintenance and material properties. Other factors such as intensive rainfall and heavy seasonal traffic will also have an influence. Certain pavement defects are the direct result of deficiencies in the material properties. These defects influencing riding quality are:

- Corrugation
- Loose material
- Stoniness
- Potholes
- Ruts
- Erosion

More detail is given on these defects in later sections.

Riding quality is most easily rated as a function of the “estimated” comfortable and safe driving speed (unaffected by geometric constraints or road width) that could be driven in a privately owned saloon car. This is estimated while travelling at the speed recommended for visual assessment (40 km/h) and is interpreted as follows (Table B.6):

**TABLE B.6: Assessment of riding quality**

| Rating | Descriptor | Description                                              |
|--------|------------|----------------------------------------------------------|
| 1      | Very good  | Estimated comfortable/safe speed in excess of 100 km/h   |
| 2      | Good       | Estimated comfortable/safe speed between 80 and 100 km/h |
| 3      | Average    | Estimated comfortable/safe speed between 60 and 80 km/h  |
| 4      | Poor       | Estimated comfortable/safe speed between 40 and 60 km/h  |
| 5      | Very poor  | Estimated comfortable/safe speed less than 40 km/h       |

Riding quality is usually measured in conjunction with an assessment of the parameters that influence it.

For detailed assessment, appropriate purpose-built equipment (e.g. Linear Displacement Integrator) should be used to provide a quantitative measure. Output from the assessment will be a roughness index over the road segment assessed (e.g. International Roughness Index (IRI) or Quarter Car Index (QI)).

| RIDING QUALITY                                                                      |           |          |          |          |          |
|-------------------------------------------------------------------------------------|-----------|----------|----------|----------|----------|
|    | Degree 1  |          |          |          |          |
|                                                                                     | <b>X</b>  | <b>2</b> | <b>3</b> | <b>4</b> | <b>5</b> |
|                                                                                     | Very good |          |          |          |          |
|   | Degree 3  |          |          |          |          |
|                                                                                     | <b>1</b>  | <b>2</b> | <b>X</b> | <b>4</b> | <b>5</b> |
|                                                                                     | Average   |          |          |          |          |
|  | Degree 5  |          |          |          |          |
|                                                                                     | <b>1</b>  | <b>2</b> | <b>3</b> | <b>4</b> | <b>X</b> |
|                                                                                     | Very poor |          |          |          |          |

| RIDING QUALITY – INFLUENCING FACTORS                                                |                |  |  |  |  |
|-------------------------------------------------------------------------------------|----------------|--|--|--|--|
|    |                |  |  |  |  |
|                                                                                     |                |  |  |  |  |
|                                                                                     | Corrugation    |  |  |  |  |
|   |                |  |  |  |  |
|                                                                                     |                |  |  |  |  |
|                                                                                     | Loose material |  |  |  |  |
|  |                |  |  |  |  |
|                                                                                     |                |  |  |  |  |
|                                                                                     | Stoniness      |  |  |  |  |

## RIDING QUALITY – INFLUENCING FACTORS



Potholes



Rutting



Erosion

---

**B.8.8 Dust**Definition and cause

Road dust is the dry solid matter consisting of clay and silt-sized particles that is entrained by wind, the wind shear forces created by vehicles and the interaction of vehicle tyres with the road and which disperses and remains in suspension for a period before eventually falling back to the earth's surface. The aerodynamic shape, tyre size and number of wheels on trucks imply that dust generation by heavy vehicles is more severe than light vehicles.

Problem

Dust is undesirable from a number of points of view including safety (loss of visibility), economic (accelerated gravel loss as a result of the loss of fines), comfort of vehicle occupants, health (respiratory diseases), vehicle damage (filters and exposed moving parts), damage to road side vegetation (crops) and environmental impact (air pollution). Dust is generally considered unacceptable by the travelling public when the vehicle generating the dust cannot be seen by a following vehicle.

Measurement

At network level, assessment of dust is necessary as input for prioritising a potential dust problem and determining the costs of applying a dust palliative. In assessing the dustiness of a road, the moisture condition at the time of assessment plays a major role. Dust generation is influenced by many factors and some subjectivity during assessment is inevitable. The following procedure has been developed in an attempt to bring some uniformity to dust assessment.

For the purposes of strategic network level assessments, dust is usually rated as either **acceptable** or **unacceptable** with safety being the major factor taken into account. If the dust generated by a vehicle is perceived to be dangerous, it should be rated as unacceptable. Dustiness should be rated in the rear view mirror while travelling at 60 km/h. This may require that short distances within the segment are monitored at this higher speed. Wind speed and lighting conditions (position of the sun) can influence rating in this way and should be taken into consideration.

For detailed network level, project level and research investigations, dust is best measured with specialised equipment following a prescribed methodology. However, a visual evaluation as well as a subjective assessment of dust on vehicle occupant comfort will suffice in most instances. This is carried out either by the driver of the vehicle travelling at 60 km/h and using the rear-view mirror to assess the dust generated by the raters vehicle, or by an observer at roadside. Occupant discomfort is judged on the necessity to close windows and ventilation systems. Runs should be made in both directions to determine the effect of the sun, with an average degree recorded (rounded upwards where necessary). Trucks generate significantly more dust than cars and LDVs and ratings will usually be unacceptable on most roads. Dust ratings on roads with a daily high percentage of heavy vehicles (e.g. >30 per cent) should be weighted to unacceptable.

The description of degrees of dustiness is given in Table B.7. The extent of dust is not normally estimated.

**TABLE B.7: Degrees of dustiness**

| <b>Degree</b> | <b>Description</b>                                    |
|---------------|-------------------------------------------------------|
| 1             | No loss of visibility                                 |
| 3             | Some loss of visibility – no discomfort               |
| 5             | Dangerous loss of visibility – significant discomfort |

| DUST (GRMS assessment)                                                             |              |  |          |
|------------------------------------------------------------------------------------|--------------|--|----------|
|   | Degree 1     |  |          |
|                                                                                    | <b>X</b>     |  | <b>5</b> |
|                                                                                    | Acceptable   |  |          |
|  | Degree 5     |  |          |
|                                                                                    | <b>1</b>     |  | <b>X</b> |
|                                                                                    | Unacceptable |  |          |

| DUST (Detailed assessment)                                                          |                                                       |   |          |   |          |
|-------------------------------------------------------------------------------------|-------------------------------------------------------|---|----------|---|----------|
|    | Degree 1                                              |   |          |   |          |
|                                                                                     | <b>X</b>                                              | 2 | 3        | 4 | 5        |
|                                                                                     | No loss of visibility                                 |   |          |   |          |
|   | Degree 3                                              |   |          |   |          |
|                                                                                     | 1                                                     | 2 | <b>X</b> | 4 | 5        |
|                                                                                     | Some loss of visibility – no discomfort               |   |          |   |          |
|  | Degree 5                                              |   |          |   |          |
|                                                                                     | 1                                                     | 2 | 3        | 4 | <b>X</b> |
|                                                                                     | Dangerous loss of visibility – significant discomfort |   |          |   |          |

**B.8.9 Trafficability**Definition and cause

Trafficability (or passability) is the capacity of a normal saloon car to negotiate the road without losing traction or without excessive use of low gears. The terms trafficability and impassability are used interchangeably throughout this document (however, impassability should not be confused with the inability to overtake in dusty conditions). The mechanism affecting trafficability is the loss of traction between the tyres and the road resulting from the low shear strength of the material. This results in churning of the material and sinking of the vehicle into the weak layer. Sandy materials are more prone to impassability when dry, while clayey materials are strong when dry, but often become impassable when wet. Impassable conditions may result from continued trafficking of slippery roads.

Problem

The primary objective of importing wearing course gravel during the construction of an unsealed road is to provide an all-weather surface. This objective is not met if the material becomes impassable in wet weather. This is often a particular problem with earth roads where in situ materials are used.

Assessment

Impassability is difficult to assess unless the rater actually experiences the condition at its worst. However, evidence of earlier impassable conditions often remains after the event. This includes:

- Deep depressions and evidence of potholes
- Detouring on the shoulders and verges to avoid wet areas
- Spurious material used to fill depressions and to provide temporary traction (often includes vegetation)

For assessment purposes, trafficability is rated as either **acceptable** or **unacceptable**, the latter only being used when definite evidence is observed over a major portion of the segment.

| TRAFFICABILITY                                                                     |              |  |          |
|------------------------------------------------------------------------------------|--------------|--|----------|
|   | Degree 1     |  |          |
|                                                                                    | <b>X</b>     |  | <b>5</b> |
|                                                                                    | Acceptable   |  |          |
|  | Degree 5     |  |          |
|                                                                                    | <b>1</b>     |  | <b>X</b> |
|                                                                                    | Unacceptable |  |          |

## B.8.10 Potholes

### Definition and cause

Potholes are round or elongated depressions in the road surface and arise from the following:

- Poor road shape and drainage
- Poor grader operation practice (e.g. plucking of oversize material and destruction of the crown)
- Compaction of material behind oversize stones under wheel loads
- Poor compaction
- Material and moisture variability
- Enlargement of corrugation troughs
- Deformation of weak subgrades and wearing courses
- Subsidence or excavation of animal and insect burrows
- Disintegration of highly cracked roads (i.e. excessive plasticity)
- Disintegration of soft oversize materials
- Dispersive soils

### Problem

Potholes play a significant role in the development of roughness on unsealed roads and may cause substantial damage to vehicles if they are allowed to develop and increase in size. The effect of potholes on vehicles depends on both the depth and diameter of the pothole. The potholes, which affect vehicles the most, are those between 250 and 1 500 mm in diameter with a depth of more than 50 to 75 mm.

Once pothole formation has been initiated (irrespective of the cause), the drainage deteriorates, water ponds in the depressions and the potholes are enlarged by traffic. Enlargement occurs through compaction and remoulding of the weakened material (in the wet state) and removal of the material from the hole by the wheels and splashing. Materials with a low soaked strength are thus likely to develop larger and deeper potholes in shorter periods. The influence of drainage on pothole formation is clearly manifested by the general absence of potholes on grades. Potholes are usually worst at the bottom of vertical sag curves, on level road sections with poor shape, and near bridges. The influence of potholes on riding quality is a function of both the degree and extent of the potholing (i.e. many degree 3 potholes have a greater impact on riding quality than a few degree 5 potholes). The descriptions of degrees of potholing are given in Table B.8.

**TABLE B.8: Degrees of potholing**

| Degree | Description                                                      |
|--------|------------------------------------------------------------------|
| 1      | Depressions just visible. Cannot be felt in the vehicle          |
| 2      | <20 mm deep                                                      |
| 3      | Larger potholes affecting safety - 20 – 50 mm deep               |
| 4      | 50 – 75 mm deep                                                  |
| 5      | Large, dangerous potholes requiring evasive action - >75 mm deep |

| POTHOLES                                                                            |                 |   |          |   |          |
|-------------------------------------------------------------------------------------|-----------------|---|----------|---|----------|
|    | Degree 1        |   |          |   |          |
|                                                                                     | <b>X</b>        | 2 | 3        | 4 | 5        |
|                                                                                     | < 10 mm deep    |   |          |   |          |
|   | Degree 3        |   |          |   |          |
|                                                                                     | 1               | 2 | <b>X</b> | 4 | 5        |
|                                                                                     | 20 – 50 mm deep |   |          |   |          |
|  | Degree 5        |   |          |   |          |
|                                                                                     | 1               | 2 | 3        | 4 | <b>X</b> |
|                                                                                     | > 75 mm deep    |   |          |   |          |

## B.8.11 Rutting

### Definition and cause

Ruts are parallel depressions of the surface in the wheel tracks. They generally form as a result of loss of gravel from the wearing course by traffic abrasion and less commonly by deformation (compaction) of the subgrade and compaction of the wearing course.

### Problem

Under local conditions, rutting is usually insignificant in terms of the overall unsealed road surface performance. The probable reason for this is the typically strong, free draining, sandy subgrade prevalent over much of southern Africa, as well as the deep water tables.

Ruts, however, pose potential problems, as they tend to retain rainwater having a negative impact on road safety and also softening the wearing course leading to deformation under traffic. Routine blading of unsealed roads replaces gravel in the ruts and simultaneously compensates for any subgrade deformation that may have occurred. The material graded into the ruts is generally compacted by traffic only when in a moist condition.

Excessively wide roads lead to the formation of definite ruts in both directions, which tend to be deeper than those on roads of normal width (8 m). The probable reason is that lateral movement of vehicles is unnecessary when they pass from both directions and all vehicles travelling in each direction thus consistently travel in the clearly demarcated ruts. This ultimately leads to deep, wide depressions in each direction.

### Assessment

Ruts are assessed in terms of their capacity to retain water using a visual estimate of their average depth. If greater accuracy is required, (e.g. for investigation or research purposes) a 2.0 m straightedge and wedge should be used. Because of their high variability, the average of a number of readings should be determined and the rutting in different directions and wheel paths should be provided separately. The descriptions of degrees of rutting are given in Table B.9.

**TABLE B.9: Degree of rutting**

| Degree | Description                                                      |
|--------|------------------------------------------------------------------|
| 1      | Rutting is just visible                                          |
| 2      | <20 mm deep                                                      |
| 3      | Rutting between 20 – 40 mm deep                                  |
| 4      | 40 – 60 mm deep                                                  |
| 5      | Rutting >60 mm deep affecting directional stability of a vehicle |

| RUTTING                                                                             |                 |   |          |   |          |
|-------------------------------------------------------------------------------------|-----------------|---|----------|---|----------|
|    | Degree 1        |   |          |   |          |
|                                                                                     | <b>X</b>        | 2 | 3        | 4 | 5        |
|                                                                                     | Just visible    |   |          |   |          |
|   | Degree 3        |   |          |   |          |
|                                                                                     | 1               | 2 | <b>X</b> | 4 | 5        |
|                                                                                     | 20 – 40 mm deep |   |          |   |          |
|  | Degree 5        |   |          |   |          |
|                                                                                     | 1               | 2 | 3        | 4 | <b>X</b> |
|                                                                                     | > 60 mm deep    |   |          |   |          |

## B.8.12 Erosion

### Definition and cause

Erosion or scour is the loss of surfacing material caused by the flow of water over the road. The ability of a material to resist erosion depends on the shear strength (equal to the cohesion, as the normal stress is zero) under the conditions at which the water flow occurs. If the shear strength of the material is less than the tractive forces induced by the water flowing over the materials, grains will become detached and erosion will occur.

### Problem

The result of erosion is runnels (run-off channels) which, when occurring transversely, result in extreme roughness and dangerous driving conditions, and when occurring longitudinally (on grades), form deep "ruts". Associated with this road defect is a significant loss of gravel. Much of this gravel is deposited in the drains and culverts necessitating extensive labour intensive maintenance. Erosion of the wearing course also results in a change in the properties of the material as various fractions of the material are selectively removed.

### Assessment

Transverse or diagonal erosion channels can be quantified by their depth and width. However, they are best assessed in terms of their effect on riding quality. Longitudinal erosion channels are assessed in a similar way to ruts by visual estimation or measuring depth with a 2.0 m straight edge and wedge. Assessments should only relate to the trafficked area and not to the side drains. The descriptions of degrees of transverse and longitudinal erosion are given in Tables B.10 and B.11.

**TABLE B.10: Degrees of transverse and diagonal erosion**

| Degree | Description                                                            |
|--------|------------------------------------------------------------------------|
| 1      | Minor evidence of water damage                                         |
| 2      | Seen, but not felt or heard (channels 10 mm deep x 50 mm wide)         |
| 3      | Can be felt and heard – speed reduction necessary (30 mm x 75 mm)      |
| 4      | Significant speed reduction necessary (50 mm x 150 mm)                 |
| 5      | Vehicles drive very slowly and attempt to avoid them (>60 mm x 250 mm) |

**TABLE B.11: Degrees of longitudinal erosion**

| Degree | Description              |
|--------|--------------------------|
| 1      | Evidence of water damage |
| 2      | Channels <20 mm deep     |
| 3      | Channels 20 – 40 mm deep |
| 4      | Channels 40 – 60 mm deep |
| 5      | Channels >60 mm deep     |

| EROSION – TRANSVERSE                                                                |                                                                                             |          |          |          |          |
|-------------------------------------------------------------------------------------|---------------------------------------------------------------------------------------------|----------|----------|----------|----------|
|    | Degree 1                                                                                    |          |          |          |          |
|                                                                                     | <b>X</b>                                                                                    | <b>2</b> | <b>3</b> | <b>4</b> | <b>5</b> |
|                                                                                     | Minor Evidence of water damage                                                              |          |          |          |          |
|   | Degree 3                                                                                    |          |          |          |          |
|                                                                                     | <b>1</b>                                                                                    | <b>2</b> | <b>X</b> | <b>4</b> | <b>5</b> |
|                                                                                     | Can be felt and heard – speed reduction necessary – channels 30 mm deep x 75 mm wide        |          |          |          |          |
|  | Degree 5                                                                                    |          |          |          |          |
|                                                                                     | <b>1</b>                                                                                    | <b>2</b> | <b>3</b> | <b>4</b> | <b>X</b> |
|                                                                                     | Vehicles drive very slowly and avoid erosion channels – channels > 60 mm deep x 250 mm wide |          |          |          |          |

| EROSION - LONGITUDINAL                                                              |                          |   |          |   |          |
|-------------------------------------------------------------------------------------|--------------------------|---|----------|---|----------|
|    | Degree 1                 |   |          |   |          |
|                                                                                     | <b>X</b>                 | 2 | 3        | 4 | 5        |
|                                                                                     | Evidence of water damage |   |          |   |          |
|   | Degree 3                 |   |          |   |          |
|                                                                                     | 1                        | 2 | <b>X</b> | 4 | 5        |
|                                                                                     | 20 – 40 mm deep          |   |          |   |          |
|  | Degree 5                 |   |          |   |          |
|                                                                                     | 1                        | 2 | 3        | 4 | <b>X</b> |
|                                                                                     | > 60 mm deep             |   |          |   |          |

### B.8.13 Corrugation

#### Definition and cause

Corrugations can be either “loose” or “fixed”. Loose corrugations consist of parallel alternating crests of loose, fine-sandy material and troughs of compacted material at right angles to the direction of travel. Fixed corrugations on the other hand consist of compacted crests and troughs of hard, fine sandy-gravel material. Loose corrugations are easily removed by blading, whereas fixed corrugations need cutting or even tining with the grader before the material is re-spread. The wavelength of the corrugations is dependent on the modal speed (i.e. most frequently occurring speed) of the vehicles using the road, with longer wavelengths formed by faster traffic.

Corrugations are caused by the initiation of wheel bounce by some irregularity in the road (or possibly even worn suspension components such as shock absorbers) that results in kick-back of non-cohesive material, followed by compression and redistribution of the wearing course as the wheel regains contact with the road. Only low plasticity materials corrugate significantly, especially those with a high sand and fine-gravel fraction. However, many roads with gravels having plasticity indices of up to nine have produced corrugations. These form when the material is continually spread from the sides of the road back onto the road during grader maintenance. This material is usually deficient in binder (most of it having been blown away with time as dust) and the material forming the corrugations is non-plastic.

#### Problem

Corrugations are one of the most disturbing defects of unsealed roads causing excessive roughness and poor vehicle directional stability. Corrugations seldom form to any significant extent during the wet season, as the material effectively remains slightly “cohesive” in its wet state through capillary suction and is not adequately mobile to form corrugations. Corrugations are frequently associated with areas of acceleration, deceleration and cornering.

#### Assessment

Corrugations should be scraped with a geological pick to determine whether they are loose or fixed – this will dictate the type of maintenance that will be required. The severity of corrugations is best assessed from within a moving vehicle at the average speed of the road. The descriptions of degrees of corrugation are given in Table B.12. Dedicated roughness measurement equipment can also be used to determine the road roughness if this level of detail is required.

**TABLE B.12: Degrees of corrugation**

| Degree | Description                                                               |
|--------|---------------------------------------------------------------------------|
| 1      | Not felt or heard in a light vehicle                                      |
| 2      | Can be felt and heard – no speed reduction necessary                      |
| 3      | Can be felt and heard – speed reduction necessary                         |
| 4      | Significant speed reduction necessary                                     |
| 5      | Drivers select a different path and drive very slowly. Safety is affected |

| CORRUGATION                                                                         |                                                                    |   |          |   |          |
|-------------------------------------------------------------------------------------|--------------------------------------------------------------------|---|----------|---|----------|
|    | Degree 1                                                           |   |          |   |          |
|                                                                                     | <b>X</b>                                                           | 2 | 3        | 4 | 5        |
|                                                                                     | Not felt or heard in a light vehicle                               |   |          |   |          |
|   | Degree 3                                                           |   |          |   |          |
|                                                                                     | 1                                                                  | 2 | <b>X</b> | 4 | 5        |
|                                                                                     | Can be felt and heard – speed reduction necessary                  |   |          |   |          |
|  | Degree 5                                                           |   |          |   |          |
|                                                                                     | 1                                                                  | 2 | 3        | 4 | <b>X</b> |
|                                                                                     | Vehicles select a different part of the road and drive very slowly |   |          |   |          |

**B.8.14 Loose Material**Definition and cause

Loose material (that material less than 26 mm in size) is formed by the ravelling of the wearing course gravel under traffic. This may be distributed over the full width of the road but more frequently, it is concentrated in windrows between the wheel tracks, or alongside the travelled portion of the road. It is mainly caused by a deficiency of fine material (because of lack of cohesion), a poor particle size distribution (e.g. gap grading) in the wearing course gravel and inadequate compaction. Ravelling is generally worse in the dry season than in the wet season when capillary suction results in apparent cohesion.

Problems

The major problems with roads susceptible to ravelling are:

- The windrows are a safety hazard
- Stones from the loose material may damage vehicles or windscreens
- The rolling resistance of the vehicle is increased by loose material with concomitant increases in fuel consumption and vehicle operating costs
- Windrows of loose material adjacent to the trafficked portion of the road impede surface drainage

Assessment

Loose material is assessed by estimating or measuring its thickness. This is achieved by scraping "paths" through the material to the hard surface with a geological pick and estimating the thickness or measuring it with a straightedge and wedge. The descriptions of degrees of loose material are given in Table B.13.

**TABLE B.13: Degrees of loose material**

| Degree | Description                     |
|--------|---------------------------------|
| 1      | Just visible                    |
| 2      | Loose material < 20 mm thick    |
| 3      | Loose material 20 – 40 mm thick |
| 4      | Loose material 40 – 60 mm thick |
| 5      | Loose material > 60 mm thick    |

**Note:**

It is important to assess the extent of the loose material as well as the degree in order to differentiate between traffic associated and maintenance associated loose material. Traffic associated loose material is usually limited to windrows, whilst maintenance associated loose material is usually distributed across the road. However, traffic induced windrows should not be confused with windrows left by the grader operator as a source of material for future blading operations. These windrows are usually on the very edge of the road and not along the wheelpaths.

| LOOSE MATERIAL                                                                      |                                    |   |          |   |          |
|-------------------------------------------------------------------------------------|------------------------------------|---|----------|---|----------|
|    | Degree 1                           |   |          |   |          |
|                                                                                     | <b>X</b>                           | 2 | 3        | 4 | 5        |
|                                                                                     | Just visible                       |   |          |   |          |
|  | Degree 3                           |   |          |   |          |
|                                                                                     | 1                                  | 2 | <b>X</b> | 4 | 5        |
|                                                                                     | Loose material is 20 – 40 mm thick |   |          |   |          |
|  | Degree 5                           |   |          |   |          |
|                                                                                     | 1                                  | 2 | 3        | 4 | <b>X</b> |
|                                                                                     | Loose material is > 60 mm thick    |   |          |   |          |

**B.8.15 Stoniness**Definition and cause

Stoniness is the relative percentage of material embedded in the road that is larger than a recommended maximum size (usually 37.5 mm). This is one of the few defects that can be controlled, but usually it is not.

The blading process periodically leaves loose stones (larger than 37.5 mm sieve) lying on the surface.

Problem

Excessively stony roads result in the following problems:

- Unnecessarily rough roads
- Difficulty with grader maintenance
- Poor compaction of areas adjacent to stones (leading to potholes and ravelling)
- The development of corrugations
- Thick, loose material is necessary to cover the stones
- Loose stones left after blading are likely to cause vehicle damage and potentially unsafe conditions.

Many geological materials, particularly shale and hornfels, produce flaky or sharp stones under crushing or grid rolling. These can cause extensive damage to tyres and affect the safety of the roads significantly. Some mudrocks may deteriorate rapidly on exposure to the atmosphere from a hard material to a soft, fine-grained “soil”. This causes significant problems, including dust, potholing and rapid gravel loss.

Assessment

Stones can be measured to determine the percentage that the maximum size limit has been exceeded by. This is time-consuming and an estimate of their severity and extent is usually sufficient. It should be noted that the extent of stoniness is usually overestimated by a significant margin. The impact of stoniness on riding quality is best evaluated from a moving vehicle. This can be supplemented by assessing the impact of the stones on the ease of blading. The descriptions of degrees of stoniness are given in Tables B.14 (embedded stones) and B.15 (loose stones). Dedicated roughness measuring equipment can also be used to determine the road roughness if this level of detail is required.

**TABLE B.14: Degrees of embedded stoniness**

| Degree | Description                                                                                          |
|--------|------------------------------------------------------------------------------------------------------|
| 1      | Seen, but not felt or heard in a light vehicle                                                       |
| 2      | Protruding stones can be felt and heard, but speed reduction not necessary. Blading is not affected. |
| 3      | Speed reduction necessary. Road is bladed with difficulty.                                           |
| 4      | Protruding stones require evasive action                                                             |
| 5      | Vehicles avoid protruding stones or drive slowly. Road cannot be effectively bladed.                 |

**TABLE B.15: Degrees of loose stoniness**

| <b>Degree</b> | <b>Description</b>                                                                                                                      |
|---------------|-----------------------------------------------------------------------------------------------------------------------------------------|
| 1             | Few loose stones 25 – 40 mm. Driver can change lanes safely                                                                             |
| 3             | Many loose stones 25 - 50 mm or few loose stones > 50 mm. Stones influence drivers actions when changing lanes.                         |
| 5             | Windrows of loose stones 25 – 50 mm or many loose stones >50 mm. Any lateral movement of the vehicle poses a significant safety hazard. |

| STONINESS - EMBEDDED                                                                |                                               |   |          |   |          |
|-------------------------------------------------------------------------------------|-----------------------------------------------|---|----------|---|----------|
|    | Degree 1                                      |   |          |   |          |
|                                                                                     | <b>X</b>                                      | 2 | 3        | 4 | 5        |
|                                                                                     | Seen but not felt or heard in a light vehicle |   |          |   |          |
|  | Degree 3                                      |   |          |   |          |
|                                                                                     | 1                                             | 2 | <b>X</b> | 4 | 5        |
|                                                                                     | Can be felt and heard in the vehicle          |   |          |   |          |
|  | Degree 5                                      |   |          |   |          |
|                                                                                     | 1                                             | 2 | 3        | 4 | <b>X</b> |
|                                                                                     | Vehicles avoid or drive slowly                |   |          |   |          |

| STONINESS – LOOSE                                                                   |                                                                                                                                                  |          |          |          |          |
|-------------------------------------------------------------------------------------|--------------------------------------------------------------------------------------------------------------------------------------------------|----------|----------|----------|----------|
|    | Degree 1                                                                                                                                         |          |          |          |          |
|                                                                                     | <b>X</b>                                                                                                                                         | <b>2</b> | <b>3</b> | <b>4</b> | <b>5</b> |
|                                                                                     | <p>Few loose stones 26 – 40 mm. Driver can change lanes safely.</p>                                                                              |          |          |          |          |
|   | Degree 3                                                                                                                                         |          |          |          |          |
|                                                                                     | <b>1</b>                                                                                                                                         | <b>2</b> | <b>X</b> | <b>4</b> | <b>5</b> |
|                                                                                     | <p>Many loose stones 26 – 50 mm or few loose stones &gt;50 mm. Stones influence drivers actions when changing lanes.</p>                         |          |          |          |          |
|  | Degree 5                                                                                                                                         |          |          |          |          |
|                                                                                     | <b>1</b>                                                                                                                                         | <b>2</b> | <b>3</b> | <b>4</b> | <b>X</b> |
|                                                                                     | <p>Windrows of loose stones 26 - 50 mm or many loose stones &gt;50 mm. Any lateral movement of the vehicle pose a significant safety hazard.</p> |          |          |          |          |

## B.8.16 Slipperiness and Skid Resistance

### Definition and cause

Slipperiness is the loss of traction caused by an accumulation of excessively fine or plastic material on the surface of the wearing course in wet conditions. Skid resistance is affected by an excess of loose, fine gravel (between 2 and 7 mm in diameter) that accumulates on the road surface through ravelling under traffic or poor blading practices during dry conditions. This behaves like a layer of ball bearings and the skid resistance is reduced to practically zero. This is especially a problem on corners and at intersections.

### Problem

The main problems with slipperiness and skid resistance are the safety implications for road users.

### Assessment

Slipperiness is difficult to assess unless the rater actually experiences the condition. However, it can often be evaluated by observing wheel tracks formed during wet weather that are retained in the road after drying and other indicators. Slipperiness is rated as either acceptable or unacceptable. Skid resistance, also rated as either acceptable or unacceptable, should be evaluated in terms of the effect of loose material on vehicle stability and the general impression gained while driving and braking on the dry road. These ratings are summarised in Tables B.16 and B.17

**TABLE B.16: Rating of slipperiness**

| Rating                                                                                                                                                                                                                           | Description                                                                                                                                                                                                                                                                           |
|----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|---------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| Acceptable                                                                                                                                                                                                                       | Exposed and protruding gravel on road surface.<br>No significant cracking (> Degree 3 (Table B.18)).<br>No evidence of tyre impressions remaining on the road surface.                                                                                                                |
| Unacceptable                                                                                                                                                                                                                     | Smooth clayey surface with few protruding gravel particles.<br>Significant cracking (> Degree 3 (Table B.18)).<br>Evidence of tyre impressions remaining on the road surface.<br>Evidence of compaction and shearing under traffic.<br>Loss of control when driving on a wet surface. |
| <b>NB</b> The absence of evidence of slipperiness does not necessarily mean that the road will not be slippery. The evidence described above tends to be worn away under traffic within 6-8 weeks, or may be removed by blading. |                                                                                                                                                                                                                                                                                       |

**TABLE B.17: Rating of skid resistance**

| Rating       | Description                                                                                                                                        |
|--------------|----------------------------------------------------------------------------------------------------------------------------------------------------|
| Acceptable   | No excessive fine gravel (2-7 mm) in the wheel tracks.<br>Exposed and protruding gravel on road surface.<br>Good directional control when braking. |
| Unacceptable | Presence of layer of fine gravel (2-7 mm) in the wheel tracks.<br>Loss of directional control when braking.                                        |

| SLIPPERINESS                                                                       |              |          |          |          |          |
|------------------------------------------------------------------------------------|--------------|----------|----------|----------|----------|
|   | Degree 1     |          |          |          |          |
|                                                                                    | <b>X</b>     | <b>2</b> | <b>3</b> | <b>4</b> | <b>5</b> |
|                                                                                    | Acceptable   |          |          |          |          |
|  | Degree 5     |          |          |          |          |
|                                                                                    | <b>1</b>     | <b>2</b> | <b>3</b> | <b>4</b> | <b>X</b> |
|                                                                                    | Unacceptable |          |          |          |          |

| SKID RESISTANCE                                                                    |              |          |          |          |          |
|------------------------------------------------------------------------------------|--------------|----------|----------|----------|----------|
|   | Degree 1     |          |          |          |          |
|                                                                                    | <b>X</b>     | <b>2</b> | <b>3</b> | <b>4</b> | <b>5</b> |
|                                                                                    | Acceptable   |          |          |          |          |
|  | Degree 5     |          |          |          |          |
|                                                                                    | <b>1</b>     | <b>2</b> | <b>3</b> | <b>4</b> | <b>X</b> |
|                                                                                    | Unacceptable |          |          |          |          |

**B.8.17 Cracks**

Cracks are usually not required as input into GRMS's, but information can be used to support other assessments (e.g. severe cracking is indicative of high plasticity gravels as well as potential for unacceptable slipperiness). These data may also be useful for project level or research assessments.

Definition and cause

Cracking of the wearing course (which usually occurs only during the dry season) is a result of the plasticity being too high or the material being very fine-grained.

Problem

Cracks as such are not a major problem on unsealed roads, but bad cracking may lead to the formation of potholes during the dry season. Materials that crack badly also tend to become slippery when wet. Roads with 100 to 150 mm diameter cracked blocks will often break up under traffic and form potholes.

Assessment

Cracks should be visually assessed on the basis of crack width, which may be measured if necessary as described in Table B.18.

**TABLE B.18: Degrees of cracking**

| Degree | Description                           |
|--------|---------------------------------------|
| 1      | Faint – requires close scrutiny       |
| 2      | Distinct – seen at walking pace       |
| 3      | Distinct – seen from a moving vehicle |
| 4      | Open cracks - $\leq 3$ mm wide        |
| 5      | Open cracks - $> 3$ mm wide           |

| CRACKS                                                                              |                                       |          |          |          |          |
|-------------------------------------------------------------------------------------|---------------------------------------|----------|----------|----------|----------|
|    | Degree 1                              |          |          |          |          |
|                                                                                     | <b>X</b>                              | <b>2</b> | <b>3</b> | <b>4</b> | <b>5</b> |
|                                                                                     | Faint – Require close scrutiny        |          |          |          |          |
|   | Degree 3                              |          |          |          |          |
|                                                                                     | <b>1</b>                              | <b>2</b> | <b>X</b> | <b>4</b> | <b>5</b> |
|                                                                                     | Distinct – seen from a moving vehicle |          |          |          |          |
|  | Degree 5                              |          |          |          |          |
|                                                                                     | <b>1</b>                              | <b>2</b> | <b>3</b> | <b>4</b> | <b>X</b> |
|                                                                                     | Open cracks - > 3 mm wide             |          |          |          |          |

**B.8.18 Isolated Problems**

During the assessment of unsealed roads, problematic localised areas may be noted. These are such that they should not influence the overall rating of the segment, but a record should be made of the problems for possible later attention. The problem could be indicative of non-uniformity within the segment resulting from different materials, localised drainage problems or excessive material loss. Where isolated problems are identified and indicated as such on the assessment form, it is useful to provide more information in the space allocated on the form for comments.

The isolated problems that should be recorded are:

- Potholes
- Subgrade exposure
- Transverse erosion
- Longitudinal erosion
- Rough areas
- Slippery areas

These problems have been discussed individually in the document.

## ISOLATED PROBLEMS



Potholes



Subgrade exposure



Transverse erosion

## ISOLATED PROBLEMS



Longitudinal erosion



Rough area



Slippery area

**B.8.19 Maintenance Action**

During the assessment for GRMS data, the opportunity should be taken to identify possible maintenance action requirements for the segment. Although this would normally be done at project level, the information can be useful to cross-check other parameters rated as well as for overall network level budgeting as a first approximation. Typical maintenance actions include:

- Local repairs – labour intensive spot gravelling often associated with impassability, drainage/erosion problems or removal of excessive oversize material.
- Routine blading – identify the need for continuation of routine blading, or adjustment of the blading programme to be more appropriate to that specific segment.
- Reshaping – where the road profile is incorrect resulting from insufficient or poor maintenance, this option can be marked. Depending on the severity of the problem, reshaping will entail heavy blading with watering and compaction, but could require limited ripping and recompaction in exceptional circumstances.
- Reworking – rip, rebuild to correct width, add additional material and reshape with watering and compaction. Breaking down or removal of oversize material may also be necessary.
- Regravelling – where there is insufficient material to provide the required service until the next assessment, this option should be selected.
- Drainage improvement – where drainage maintenance has been ineffective or insufficient drainage exists, corrective action needs to be taken. This could involve labour intensive clearing and reshaping of side drains and mitre drains, or the installation of new pipes.

Rehabilitation in the traditional sense is not applicable to unsealed roads. Regravelling essentially replaces rehabilitation. The closest possible equivalent is road betterment where geometrics and alignment are improved during the regravelling operation.

**B.9. Dust Palliative/Chemical Stabiliser Treatments**

Dust palliatives and chemical stabilisers are being increasingly used on unsealed roads to reduce dust and improve material properties, thereby reducing the rate of gravel loss and the number of bladings required per year. Treated segments should be assessed in the same way as untreated unsealed roads. However, comment should be made on whether the product is achieving the purpose for which it was applied (e.g. dust control, improved trafficability) and whether it requires rejuvenation.

**B.10. Material Sampling**

Material sampling is usually not required for GRMS assessments, but certain road authorities may excavate a hole to measure layer thickness. However, for project level and research investigations, accurate data on the material properties are often required and the materials will have to be sampled from the road. Sampling will usually be required in the following situations:

- Problem identification
- Experimental sections
- If the existing material is to be treated or used as a layer during upgrading of the road

This necessitates the collection of representative samples for laboratory testing. Samples should be removed from holes sufficiently large to provide adequate material for testing according to the method described in TMH5<sup>5</sup>. These holes should be excavated to the full depth of the layer and must have vertical sides. **All material excavated from the hole must be included in the sample.** All sample and observation holes must be repaired by backfilling them with material with similar properties to that excavated. This material should be moistened and compacted into the hole.

## **B.11. Use of Data**

It is not the intention of this document to instruct on the use of the data collected. However, a number of simple preliminary exercises are discussed below.

The primary use of the data collected during the assessment is for input into the gravel road management system. It is thus essential that the visual assessment forms be completed fully and accurately. The success of the decision making process depends on this.

The data collected can be used for determining various indices (e.g. Visual Condition Index (VCI)), similar to that determined for sealed roads as discussed in TRH22<sup>6</sup> (to date there is no TRH document published for GRMS's). It should, however, be noted that comparison of different unsealed road VCI estimates is often not valid in the same way as that for sealed roads. The VCI determined for unsealed roads is a function of the time elapsed since the last regravelling and blading as well as traffic and climatic influences immediately prior to rating. The data collected can also be used:

- As a basis for predicting gravel loss and blading frequency
- For prioritising maintenance actions (e.g. defects with a severity of 4 or 5 should be given immediate attention, while defects with a severity of three should be considered as a warning that will require attention in the near future)
- For monitoring improvement or deterioration in the overall road network as a result of funding fluctuations
- For direct comparisons of the performance of various roads
- For location of specific problems
- As a basis for project level investigations.

For project level and research investigations, the data can be entered into a spreadsheet. The data collected is best assessed by highlighting certain parameters or ratings. This can be rapidly done using simple spreadsheet macros. For instance:

- All segments with corrugation severity ratings in excess of 3 could be highlighted and this could be used to identify possible areas for sand cushioning.
- Highlighting all severity ratings of 4 or 5 could indicate specific segments of road with unacceptably severe problems.

- By combining various ratings and extent, it is possible to prioritise those segments requiring urgent maintenance or upgrading.
- Identify modes of distress for specific roads – i.e. is it material -, maintenance -, or environmentally – related? Remedial measures can then be defined.
- Gravel thicknesses can be plotted over time to indicate the rates of gravel loss for different scenarios.

Further detail regarding the use of data is beyond the scope of this document.

---

## C. GLOSSARY

---

**Assessment segment:** An assessment segment is the length of road for which one assessment rating is recorded. In the case of rural road networks, a road link is normally divided into road segments for visual assessment. For urban road networks where road links may be very short, links may be grouped together to form an assessment segment.

**Earth road:** An unsealed road in which the in situ material is directly travelled by vehicles.

**Gravel road:** An unsealed road in which an imported material has been placed to provide a riding surface for vehicles.

**Gravel Road Management System (GRMS):** is part of a Road Management System, which is a set of procedures aimed at maximising the potential serviceability of a road network. These procedures are used by the managers of the road network (usually with the aid of computerised facilities) to evaluate maintenance, improvement and upgrading alternatives, and the establishment of new facilities when needed.

**Gravel wearing course:** the exposed material imported to protect the foundation from wear by vehicles.

**Link:** A road link is the length of road from one intersection or interchange to the next.

**Overall performance:** is a single rating of how the travelling public view the condition and performance of the road. This should include all functional and safety aspects.

**Rehabilitation:** of unsealed roads generally involves improvement in geometrics as well as pavement structure and materials. Regravelling alone is not regarded as rehabilitation, but as a routine maintenance operation.

**Road section:** A road section is a length of road with a unique section number (refer to Section A.4.2).

**Surfaced road:** A road on which a bituminous, concrete or block layer has been placed to provide an all-weather surface for traffic.


**Traffic volume:** A single value representative of the quantity of/type of traffic using a road. Different road authorities use different parameters, e.g. Annual Average Daily Traffic (AADT), Average daily traffic (ADT), Equivalent Vehicle Units (EVU) etc.

**“Warning”:** The condition of various defects is often referred to as “warning”. This term indicates a condition that requires some action in the near future and/or a problem that may develop into a more serious one.

**Weinert N-value:** A climatic index based on evaporation in the warmest month of the year, and annual rainfall. The minerals found during weathering of rocks are a function of the Weinert N-value. A map of Weinert N-values for South Africa is provided in Figure C.1.

**Width:** Two different road widths need to be considered during visual assessments on unsealed roads.

- Total width, which includes shoulders and is used for calculation of gravel quantities for regravelling
- The trafficked width usually demarcated by windrows at each side, which is used for assessment purposes.

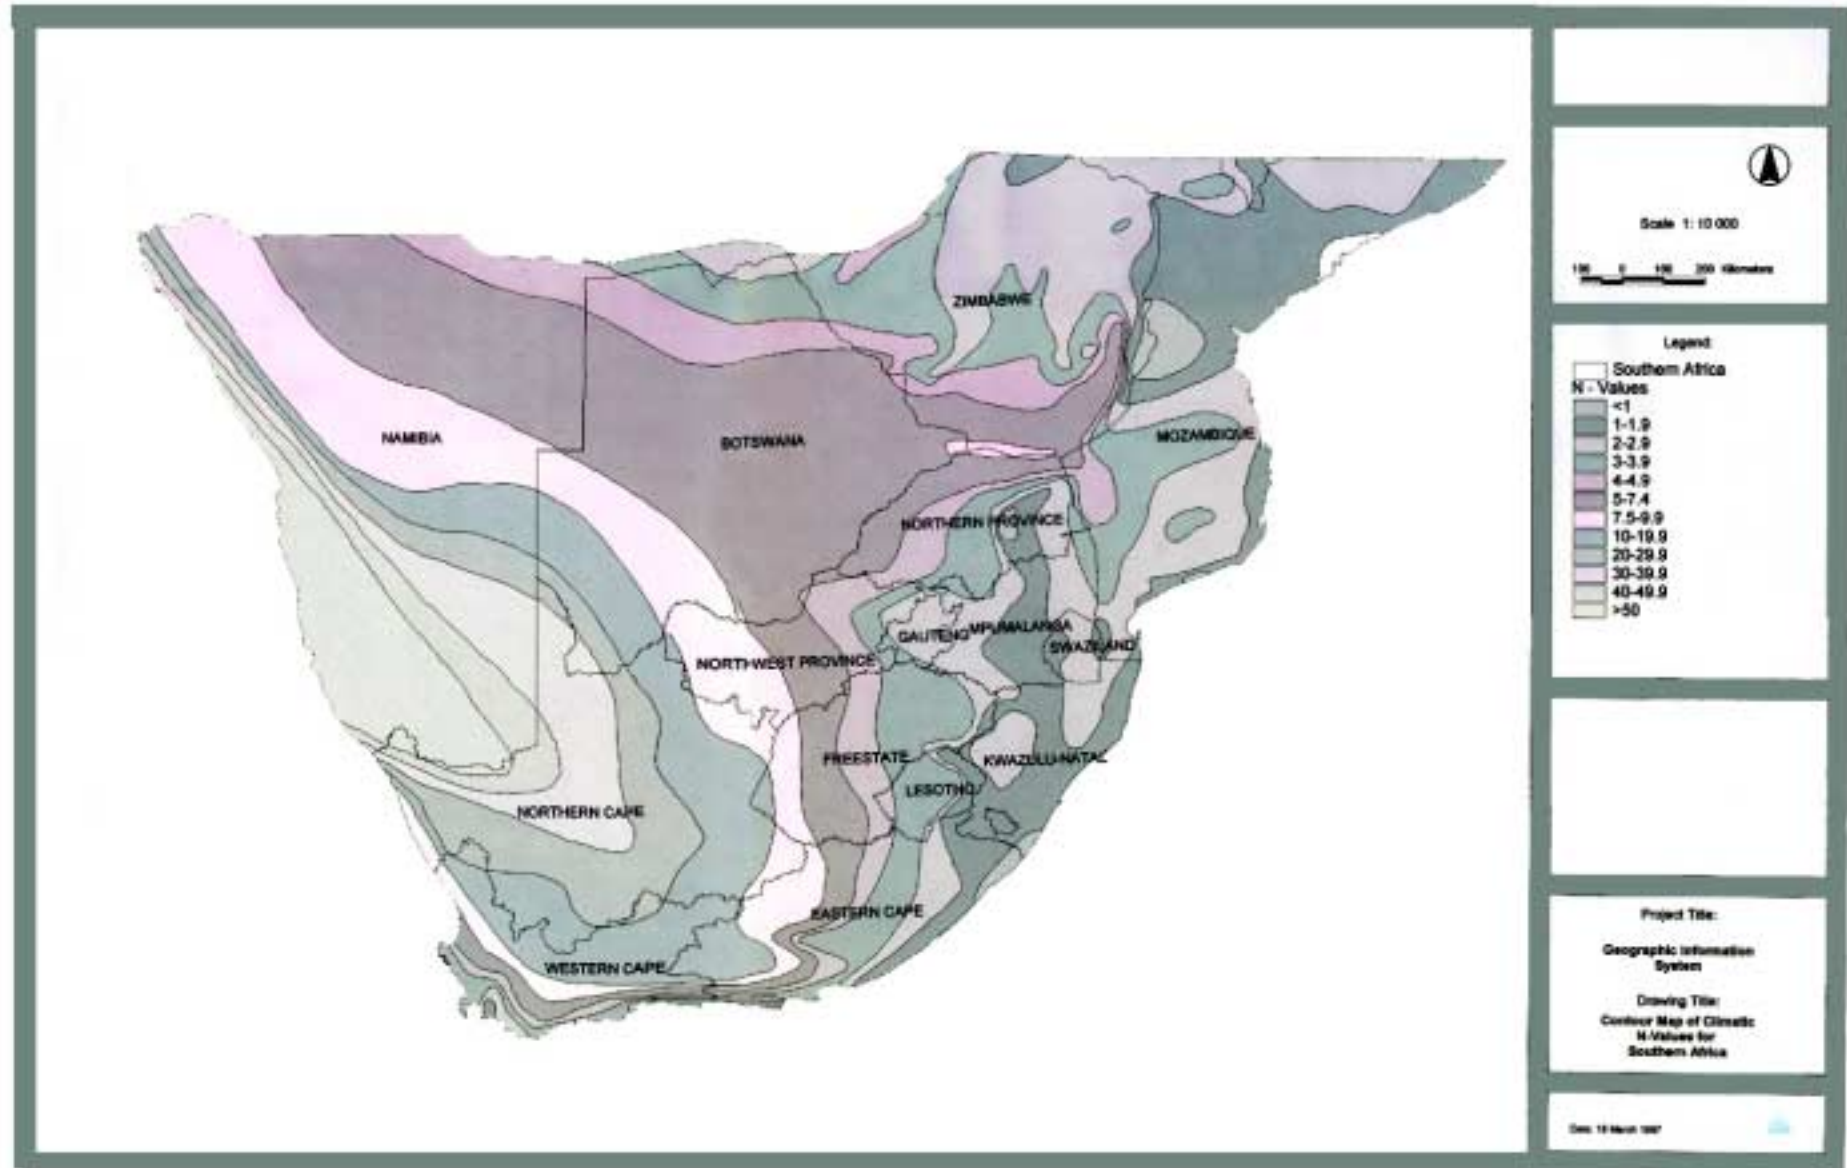

## **D. TYPICAL ASSESSMENT FORMS**

---

Example forms for the following types of assessment are included:

- Form 1 - input for strategic network level assessment
- Form 2 - input for strategic network level assessments with some detailed information for project level maintenance
- Form 3 - input for detailed network level assessment
- Form 4 - evaluation of experimental sections

| UNSEALED ROAD ASSESSMENT FORM         |                   |                       |                  |                   |                 |                    |            |                      |              |            |                     |              |
|---------------------------------------|-------------------|-----------------------|------------------|-------------------|-----------------|--------------------|------------|----------------------|--------------|------------|---------------------|--------------|
| Evaluator                             |                   |                       |                  |                   |                 |                    |            | Date                 |              |            |                     |              |
| Road No                               |                   |                       | Section          |                   |                 |                    |            |                      |              |            |                     |              |
| Start km                              |                   |                       | End km           |                   |                 |                    |            |                      |              |            |                     |              |
| Segment No                            |                   |                       |                  |                   | Start km        |                    |            |                      | End km       |            |                     |              |
| General performance                   | 1                 | 2                     | 3                | 4                 | 5               | Moisture           |            |                      | Wet          |            | Dry                 |              |
| Gravel quantity                       | 1                 | Plenty                |                  | 2                 | Sufficient      |                    | 3          | Isolated exposures   |              | 4          | Extensive exposures |              |
| Gravel quality                        | 1                 | Very good             |                  | 2                 | Good            |                    | 3          | Average              |              | 4          | Poor                |              |
| Influencing factors                   |                   | Clay                  |                  |                   | Sand            |                    |            | Gravel/stones        |              |            |                     |              |
| Road profile/shape                    | 1                 | Very good (4%)        |                  | 2                 | Good (2%)       |                    | 3          | Flat                 |              | 4          | Uneven              |              |
| Drainage from the road                | 1                 | Well above ground     |                  | 2                 | Slightly above  |                    | 3          | Level with ground    |              | 4          | Slightly below      |              |
| Riding quality/safety                 | 1                 | Very good (>100 km/h) |                  | 2                 | Good (100 km/h) |                    | 3          | Average (80 km/h)    |              | 4          | Poor (60 km/h)      |              |
| Influencing factors                   | Corrugation       |                       |                  | Loose material    |                 | Stoniness          |            | Potholes             |              | Ruts       |                     | Erosion      |
| Dust                                  | 1                 | Acceptable            |                  |                   | 5               | Unacceptable       |            |                      |              |            |                     |              |
| Trafficability                        | 1                 | Acceptable            |                  |                   | 5               | Unacceptable       |            |                      |              |            |                     |              |
| Isolated problems                     | Potholes          |                       |                  | Subgrade exposure |                 | Transverse erosion |            | Longitudinal erosion |              | Rough area |                     | Slipperiness |
| Maintenance action                    | Local repairs     |                       |                  | Routine blading   |                 | Heavy blading      |            | Regravelling         |              | Reshaping  |                     | Drains       |
| Comments (Not captured in the system) |                   |                       |                  |                   |                 |                    |            |                      |              |            |                     |              |
|                                       |                   |                       |                  |                   |                 |                    |            |                      |              |            |                     |              |
|                                       |                   |                       |                  |                   |                 |                    |            |                      |              |            |                     |              |
|                                       |                   |                       |                  |                   |                 |                    |            |                      |              |            |                     |              |
|                                       |                   |                       |                  |                   |                 |                    |            |                      |              |            |                     |              |
|                                       |                   |                       |                  |                   |                 |                    |            |                      |              |            |                     |              |
|                                       |                   |                       |                  |                   |                 |                    |            |                      |              |            |                     |              |
|                                       |                   |                       |                  |                   |                 |                    |            |                      |              |            |                     |              |
| Inventory check                       |                   |                       |                  |                   |                 |                    |            |                      |              |            |                     |              |
| Material                              | Basic Crystalline |                       | Acid Crystalline |                   | High silica     |                    | Arenaceous |                      | Argillaceous |            | Diamictite          |              |
|                                       | Metaliferous      |                       | Carbonate        |                   | Pedocrete       |                    | Fer        | Cal                  | Gyp          | Sil        | Transported         |              |
| Road width                            | <8 m              | 8-10 m                |                  | >10m              |                 | Road type          |            | Gravel               |              | Earth      |                     | Treated      |

| UNSEALED ROAD ASSESSMENT FORM |                   |                       |                  |                   |                 |                    |            |                      |              |            |                     |              |   |                     |
|-------------------------------|-------------------|-----------------------|------------------|-------------------|-----------------|--------------------|------------|----------------------|--------------|------------|---------------------|--------------|---|---------------------|
| Evaluator                     |                   |                       |                  |                   |                 |                    |            |                      |              |            | Date                |              |   |                     |
| Road No                       |                   |                       | Section          |                   |                 |                    |            |                      |              |            |                     |              |   |                     |
| Start km                      |                   |                       | End km           |                   |                 | Position           |            |                      |              |            |                     |              |   |                     |
| Segment No                    |                   |                       |                  | Start km          |                 |                    |            |                      | End km       |            |                     |              |   |                     |
| General performance           | 1                 | 2                     | 3                | 4                 | 5               | Moisture           |            |                      | Wet          |            | Dry                 |              |   |                     |
| Gravel quantity               | 1                 | Plenty                |                  | 2                 | Sufficient      |                    | 3          | Isolated exposures   |              | 4          | Extensive exposures |              | 5 | None                |
| Gravel quality                | 1                 | Very good             |                  | 2                 | Good            |                    | 3          | Average              |              | 4          | Poor                |              | 5 | Very poor           |
| Influencing factors           |                   | Clay                  |                  |                   | Sand            |                    |            | Gravel/stones        |              |            |                     |              |   |                     |
| Road profile/shape            | 1                 | Very good (4%)        |                  | 2                 | Good (2%)       |                    | 3          | Flat                 |              | 4          | Uneven              |              | 5 | Very uneven         |
| Drainage from the road        | 1                 | Well above ground     |                  | 2                 | Slightly above  |                    | 3          | Level with ground    |              | 4          | Slightly below      |              | 5 | Canal               |
| Riding quality/safety         | 1                 | Very good (>100 km/h) |                  | 2                 | Good (100 km/h) |                    | 3          | Average (80 km/h)    |              | 4          | Poor (60 km/h)      |              | 5 | Very poor (40 km/h) |
| Influencing factors           | Corrugation       |                       |                  | Loose material    |                 | Stoniness          |            | Potholes             |              | Ruts       |                     | Erosion      |   |                     |
| Maintenance action            | Local repairs     |                       |                  | Blading           |                 | Heavy blading      |            | Regravelling         |              | Reshaping  |                     | Drains       |   |                     |
|                               | Degree            |                       |                  |                   |                 |                    |            | Extent               |              |            |                     |              |   |                     |
| Potholes                      | 0                 | 1                     | 2                | 3                 | 4               | 5                  |            | 1                    | 2            | 3          | 4                   | 5            |   |                     |
| Rutting                       | 0                 | 1                     | 2                | 3                 | 4               | 5                  |            | 1                    | 2            | 3          | 4                   | 5            |   |                     |
| Erosion - transverse          | 0                 | 1                     | 2                | 3                 | 4               | 5                  |            | 1                    | 2            | 3          | 4                   | 5            |   |                     |
| Erosion – longitudinal        | 0                 | 1                     | 2                | 3                 | 4               | 5                  |            | 1                    | 2            | 3          | 4                   | 5            |   |                     |
| Corrugation                   | 0                 | 1                     | 2                | 3                 | 4               | 5                  |            | 1                    | 2            | 3          | 4                   | 5            |   |                     |
| Loose material                | 0                 | 1                     | 2                | 3                 | 4               | 5                  |            | 1                    | 2            | 3          | 4                   | 5            |   |                     |
| Stoniness – embedded          | 0                 | 1                     | 2                | 3                 | 4               | 5                  |            | 1                    | 2            | 3          | 4                   | 5            |   |                     |
| Stoniness - loose             | 0                 | 1                     | 2                | 3                 | 4               | 5                  |            | 1                    | 2            | 3          | 4                   | 5            |   |                     |
| Dustiness                     | 0                 | 1                     | 2                | 3                 | 4               | 5                  |            |                      |              |            |                     |              |   |                     |
| Slipperiness                  | Acceptable        |                       |                  | Unacceptable      |                 |                    |            |                      |              |            |                     |              |   |                     |
| Skid resistance               | Acceptable        |                       |                  | Unacceptable      |                 |                    |            |                      |              |            |                     |              |   |                     |
| Trafficability                | Acceptable        |                       |                  | Unacceptable      |                 |                    |            |                      |              |            |                     |              |   |                     |
| Isolated problems             | Potholes          |                       |                  | Subgrade exposure |                 | Transverse erosion |            | Longitudinal erosion |              | Rough area |                     | Slipperiness |   |                     |
| Comments                      |                   |                       |                  |                   |                 |                    |            |                      |              |            |                     |              |   |                     |
|                               |                   |                       |                  |                   |                 |                    |            |                      |              |            |                     |              |   |                     |
|                               |                   |                       |                  |                   |                 |                    |            |                      |              |            |                     |              |   |                     |
| Inventory check               |                   |                       |                  |                   |                 |                    |            |                      |              |            |                     |              |   |                     |
| Material                      | Basic crystalline |                       | Acid Crystalline |                   | High Silica     |                    | Arenaceous |                      | Argillaceous |            | Diamictite          |              |   |                     |
|                               | Metaliferous      |                       | Carbonate        |                   | Pedocrete       |                    | Fer        | Cal                  | Gyp          | Sil        | Transported         |              |   |                     |
| Road width                    | <8m               | 8-10m                 | >10m             | Road type         |                 | Gravel             |            | Earth                |              | Treated    |                     |              |   |                     |

| UNSEALED ROAD ASSESSMENT FORM |                   |                       |                   |                 |                    |                   |                      |                |              |                     |              |   |   |  |
|-------------------------------|-------------------|-----------------------|-------------------|-----------------|--------------------|-------------------|----------------------|----------------|--------------|---------------------|--------------|---|---|--|
| Evaluator                     |                   |                       |                   |                 |                    |                   |                      |                |              |                     | Date         |   |   |  |
| District                      |                   |                       |                   |                 |                    | Road No           |                      |                |              | Section             |              |   |   |  |
| Start km                      |                   |                       | End km            |                 |                    | Position          |                      |                |              |                     |              |   |   |  |
| Segment No                    |                   |                       |                   | Start km        |                    |                   |                      |                | End km       |                     |              |   |   |  |
| General performance           | 1                 | 2                     | 3                 | 4               | 5                  | Moisture          |                      |                | Wet          |                     | Dry          |   |   |  |
| Layer thickness (mm)          |                   |                       |                   |                 |                    |                   |                      |                |              |                     |              |   |   |  |
| Layer thickness category      | 0-25mm            |                       | 25-50mm           |                 | 50-100mm           |                   | >100mm               |                |              |                     |              |   |   |  |
| Subgrade exposure             | None              |                       | Isolated          |                 | General            |                   |                      |                |              |                     |              |   |   |  |
| Gravel quality                | Classification    |                       | Course            |                 | Medium             |                   | Fine                 |                |              |                     |              |   |   |  |
|                               | Max size (mm)     |                       | >50               |                 | 25-50              |                   | 13-25                |                | <13          |                     |              |   |   |  |
|                               | Estimated PI      |                       | <6                |                 | 6-15               |                   | >15                  |                |              |                     |              |   |   |  |
| Road profile/shape            | 1                 | Very good (4%)        | 2                 | Good (2%)       | 3                  | Flat              | 4                    | Uneven         | 5            | Very uneven         |              |   |   |  |
| Drainage from the road        | 1                 | Well above ground     | 2                 | Slightly above  | 3                  | Level with ground | 4                    | Slightly below | 5            | Canal               |              |   |   |  |
| Riding quality/safety         | 1                 | Very good (>100 km/h) | 2                 | Good (100 km/h) | 3                  | Average (80 km/h) | 4                    | Poor (60 km/h) | 5            | Very poor (40 km/h) |              |   |   |  |
| Influencing factors           | Corrugation       |                       | Loose material    |                 | Stoniness          |                   | Potholes             |                | Ruts         |                     | Erosion      |   |   |  |
| Maintenance action            | Local repairs     |                       | Blading           |                 | Heavy blading      |                   | Regravelling         |                | Reshaping    |                     | Drains       |   |   |  |
|                               | Degree            |                       |                   |                 |                    |                   |                      |                | Extent       |                     |              |   |   |  |
| Potholes                      | 0                 | 1                     | 2                 | 3               | 4                  | 5                 |                      |                | 1            | 2                   | 3            | 4 | 5 |  |
| Rutting                       | 0                 | 1                     | 2                 | 3               | 4                  | 5                 |                      |                | 1            | 2                   | 3            | 4 | 5 |  |
| Erosion - transverse          | 0                 | 1                     | 2                 | 3               | 4                  | 5                 |                      |                | 1            | 2                   | 3            | 4 | 5 |  |
| Erosion - longitudinal        | 0                 | 1                     | 2                 | 3               | 4                  | 5                 |                      |                | 1            | 2                   | 3            | 4 | 5 |  |
| Corrugation                   | 0                 | 1                     | 2                 | 3               | 4                  | 5                 |                      |                | 1            | 2                   | 3            | 4 | 5 |  |
| Loose material                | 0                 | 1                     | 2                 | 3               | 4                  | 5                 |                      |                | 1            | 2                   | 3            | 4 | 5 |  |
| Stoniness - embedded          | 0                 | 1                     | 2                 | 3               | 4                  | 5                 |                      |                | 1            | 2                   | 3            | 4 | 5 |  |
| Stoniness - loose             | 0                 | 1                     | 2                 | 3               | 4                  | 5                 |                      |                | 1            | 2                   | 3            | 4 | 5 |  |
| Dustiness                     | 0                 | 1                     | 2                 | 3               | 4                  | 5                 |                      |                |              |                     |              |   |   |  |
| Slipperiness                  | Acceptable        |                       | Unacceptable      |                 |                    |                   |                      |                |              |                     |              |   |   |  |
| Skid resistance               | Acceptable        |                       | Unacceptable      |                 |                    |                   |                      |                |              |                     |              |   |   |  |
| Trafficability                | Acceptable        |                       | Unacceptable      |                 |                    |                   |                      |                |              |                     |              |   |   |  |
| Isolated problems             | Potholes          |                       | Subgrade exposure |                 | Transverse erosion |                   | Longitudinal erosion |                | Rough area   |                     | Slipperiness |   |   |  |
| Comments                      |                   |                       |                   |                 |                    |                   |                      |                |              |                     |              |   |   |  |
|                               |                   |                       |                   |                 |                    |                   |                      |                |              |                     |              |   |   |  |
| Inventory check               |                   |                       |                   |                 |                    |                   |                      |                |              |                     |              |   |   |  |
| Material                      | Basic crystalline |                       | Acid Crystalline  |                 | High Silica        |                   | Arenaceous           |                | Argillaceous |                     | Diamictite   |   |   |  |
|                               | Metaliferous      |                       | Carbonate         |                 | Pedocrete          |                   | Fer                  | Cal            | Gyp          | Sil                 | Transported  |   |   |  |
| Road width                    | <8m               | 8-10m                 | >10m              |                 | Road type          |                   | Gravel               |                | Earth        |                     | Treated      |   |   |  |

| UNSEALED ROAD ASSESSMENT FORM |     |         |     |        |         |           |    |                |          |          |   |   |   |
|-------------------------------|-----|---------|-----|--------|---------|-----------|----|----------------|----------|----------|---|---|---|
| Evaluator                     |     |         |     |        |         | Date/time |    |                |          |          |   |   |   |
| Project                       |     | Road No |     |        | Section |           |    | Position       |          |          |   |   |   |
| Material                      |     |         |     |        |         | Slope     |    |                | Moisture |          |   |   |   |
| Climate                       |     |         |     |        |         | Terrain   | F  | R              | M        | Traffic  | L | M | H |
| Map                           |     |         |     |        |         | Photo's   |    |                |          |          |   |   |   |
|                               |     |         |     |        |         |           |    |                |          |          |   |   |   |
|                               |     |         |     |        |         |           |    |                |          |          |   |   |   |
| Overall                       | 1   | 2       | 3   | 4      | 5       | Dust      | @  |                | QI/IRI   | @        |   |   |   |
| Gravel depth                  | 1   | 2       | 3   | 4      | 5       | mm        |    |                |          |          |   |   |   |
| Gravel quality                | 1   | 2       | 3   | 4      | 5       |           |    |                |          |          |   |   |   |
| Drainage (road)               | 1   | 2       | 3   | 4      | 5       |           |    |                |          |          |   |   |   |
| Drainage (side)               | 1   | 2       | 3   | 4      | 5       |           |    |                |          |          |   |   |   |
| Stoniness (loose)             | /   | 1       |     |        |         |           |    |                |          |          |   |   |   |
| Stoniness (fixed)             | /   | 1 ;     |     |        |         |           |    |                |          |          |   |   |   |
| Potholes                      | /   | 1 ;     |     |        |         |           |    |                |          | Max size |   |   |   |
| Rutting                       | /   | 88      | 99  | :      | :       |           |    |                |          | Max size |   |   |   |
| Loose material                | /   | 88      | 99  | :      | :       |           |    |                |          | Biggest  |   |   |   |
| Corrugations                  | /   | L       | F   | :      | :       |           |    |                |          |          |   |   |   |
| Erosion                       | /   | L       | T   | :      | :       |           |    |                |          |          |   |   |   |
| Cracking                      | /   |         |     |        |         |           |    |                |          |          |   |   |   |
| Slipperiness                  | Y   | N       |     |        |         |           |    |                |          |          |   |   |   |
| Skid resistance               | Y   | N       |     |        |         |           |    |                |          |          |   |   |   |
| Passability                   | Y   | N       |     |        |         |           |    |                |          |          |   |   |   |
| Maintenance                   |     |         |     |        |         |           |    |                |          |          |   |   |   |
| Road reserve                  |     |         |     |        |         |           |    |                |          |          |   |   |   |
| Notes                         |     |         |     |        |         |           |    |                |          |          |   |   |   |
|                               |     |         |     |        |         |           |    |                |          |          |   |   |   |
|                               |     |         |     |        |         |           |    |                |          |          |   |   |   |
|                               |     |         |     |        |         |           |    |                |          |          |   |   |   |
|                               |     |         |     |        |         |           |    |                |          |          |   |   |   |
|                               |     |         |     |        |         |           |    |                |          |          |   |   |   |
|                               |     |         |     |        |         |           |    |                |          |          |   |   |   |
|                               |     |         |     |        |         |           |    |                |          |          |   |   |   |
|                               |     |         |     |        |         |           |    |                |          |          |   |   |   |
|                               |     |         |     |        |         |           |    |                |          |          |   |   |   |
|                               |     |         |     |        |         |           |    |                |          |          |   |   |   |
| Density                       | Wet | Dry     | NMC | Tin No | GMC     | Pos       |    | Sample details |          |          |   |   |   |
| 150 mm                        |     |         |     |        |         | LO        | LI |                |          |          |   |   |   |
| 100 mm                        |     |         |     |        |         | C         |    |                |          |          |   |   |   |
| 50 mm                         |     |         |     |        |         | RI        | RO |                |          |          |   |   |   |

## **E. MATERIAL IDENTIFICATION**

---

In order to benefit from the use of gravel road assessments and management systems, it is essential that the materials used are correctly classified. This need not require a high degree of geological expertise.

This appendix contains a guide, modified after Weinert (1980), to the application of the 'rule of quartz' for rock identification. The guide is based on the assumption that the user is sufficiently familiar with the appearance of quartz and opal (amorphous silica) in rocks to recognize them macroscopically, i.e. with the naked eye or a hand lens (magnification 8 to 10 times). The inspection of the sample must always be done on a freshly crushed face and the following equipment should be available:

- Geological hammer
- Hand lens
- Pocket knife
- A bottle of diluted hydrochloric acid (HCl) is useful for the identification of carbonate materials.

To use the guide, begin with the left-hand column and proceed column by column to the right. Every item must be considered and the reader must keep within the same horizontal division proceeding to the right. This will lead to the group in which the inspected material belongs.

In the column to the right of that of the group names, individual rock names are shown. It is not essential that these rock types are individually identified but they are provided as an aid. Many of these names have been used in the past and will need to be assigned to the wider classification groups proposed.

| Quartz, Opal                                                                                                             | Texture & mineral composition                                                                                                                                | Colour and luster                                                                                                                      | Matrix                                                | Fracture face                                                                                            | Intermixed other components                                                  | Additional physical characteristics                                                                                              | Group                                                                                                              | Possible rock type                                                                 | Remarks                                                                                                                               |                                                                                 |
|--------------------------------------------------------------------------------------------------------------------------|--------------------------------------------------------------------------------------------------------------------------------------------------------------|----------------------------------------------------------------------------------------------------------------------------------------|-------------------------------------------------------|----------------------------------------------------------------------------------------------------------|------------------------------------------------------------------------------|----------------------------------------------------------------------------------------------------------------------------------|--------------------------------------------------------------------------------------------------------------------|------------------------------------------------------------------------------------|---------------------------------------------------------------------------------------------------------------------------------------|---------------------------------------------------------------------------------|
| All quartz or opal (amorphous silica)                                                                                    | Glassy to vitreous, very dense, uniform                                                                                                                      | Mostly white, but also many other colours, or colourless; shiny or glossy luster                                                       | None                                                  | Smooth, conchoidal                                                                                       | None                                                                         | Very hard, cannot be scratched with pocket knife                                                                                 | High-silica rock                                                                                                   | Vein quartz<br>Chert<br>Hornfels                                                   |                                                                                                                                       |                                                                                 |
|                                                                                                                          | Dense                                                                                                                                                        | Mostly dark shades of grey                                                                                                             |                                                       | Smooth to slightly rough                                                                                 |                                                                              |                                                                                                                                  |                                                                                                                    | Hornfels                                                                           |                                                                                                                                       |                                                                                 |
|                                                                                                                          | Granular with grains of varying sizes                                                                                                                        | Many but shades of grey predominant; luster shiny or glossy                                                                            | Siliceous                                             | Smooth, breaks equally through grains and matrix                                                         | Variable, depending on host material                                         | Cannot be scratched with pocket knife; voids (honeycomb)                                                                         | Pedogenic material                                                                                                 | Quartzite                                                                          | Occasionally contains sulphide minerals, e.g. pyrite                                                                                  |                                                                                 |
|                                                                                                                          |                                                                                                                                                              | Many but shades of grey predominant; luster dull but individual grains may flicker in sunlight                                         |                                                       | May be smooth or rough depending on strength of cementing matrix                                         |                                                                              |                                                                                                                                  |                                                                                                                    | (Quartzitic) sandstone, grit conglomerate                                          | Distinction from quartzite often very difficult; seek expert advice                                                                   |                                                                                 |
|                                                                                                                          |                                                                                                                                                              |                                                                                                                                        |                                                       | Breaks run through matrix and the unbroken (sand) grains protrude: fracture face feels rough (sandpaper) |                                                                              |                                                                                                                                  |                                                                                                                    |                                                                                    |                                                                                                                                       | Occasionally single minerals, especially feldspar, and rock fragments           |
| Mostly quartz or opal (>50%)                                                                                             | Granular, mostly sand grains                                                                                                                                 | Many colours, lustre dull                                                                                                              | Calcareous, ferruginous or clayey                     | Very rough, feels like sandpaper; grains can be removed with needle or pocket knife                      | Occasionally feldspar; very rarely other minerals                            | Matrix can be scratched with pocket knife; calcareous matrix 'boils' in hydrochloric acid (HCl)                                  | Diamicite                                                                                                          | Sandstone<br>Gritstone<br>Conglomerate<br>Arkose (if containing Feldspar)          | May contain mica or sulphide minerals, especially pyrite                                                                              |                                                                                 |
|                                                                                                                          | Granular; alternating thin sheets of quartz and mica                                                                                                         | Shades of grey, minerals flicker in sunlight                                                                                           | None                                                  | Smooth, parallel with bedding, and rough perpendicular to beds                                           | Occasionally minerals other than quartz and mica                             | Breaks into platy pieces. Scratched easily with pocket knife on bedding planes                                                   |                                                                                                                    | Sandstone Gritstone<br>Conglomerate Arkose (if containing Feldspar)                | May contain mica or sulphide minerals, especially pyrite                                                                              |                                                                                 |
|                                                                                                                          | Granular, grains of various sorts and sizes                                                                                                                  | Mostly shades of grey; lustre dull                                                                                                     | Clayey, rarely siliceous                              | Rough, feels like sandpaper, grains can be removed with needle or pocket knife                           | Contains angular to sub-angular fragments of all sorts of minerals and rocks | Strength may vary considerably. Resistance to scratching variable                                                                |                                                                                                                    | Greywacke Tillite<br>Volcanic breccia                                              | Recognition of these rocks often difficult, use should be made of expert advice                                                       |                                                                                 |
|                                                                                                                          | Dense to vitreous fine granular                                                                                                                              | Red to brown, generally dull but grains flicker in sunlight                                                                            | Ferruginous                                           | Smooth to rough: when rough it feels like fine sandpaper                                                 | None                                                                         | Very heavy                                                                                                                       | Metaliferous rock                                                                                                  | Ironstone                                                                          | Occasionally shades of colour vary in fine layers (banded ironstone)                                                                  |                                                                                 |
| Quart or opal prominent (>10%, <50%)                                                                                     | Vitreous, quartz as single crystals or as clusters may float in vitreous matrix; often signs of flow or turbulence                                           | Mostly shades of red from light to dark but other colours as well; lustre dull to slightly shiny                                       | Dense, rather uniform mass                            | Rather smooth, quartz grains may produce a degree of roughness                                           |                                                                              | If at all, can only be scratched with difficulty with pocket knife; may contain voids                                            | Acid crystalline rock                                                                                              | Felsite<br>Rhyolite<br>Quartz porphyry                                             | These rocks are not easily identified and expert advice may be required                                                               |                                                                                 |
|                                                                                                                          | Granular, crystalline                                                                                                                                        | Generally light coloured; crystals flicker in sunlight                                                                                 | None                                                  | Rough; there may be smooth faces of large crystals                                                       | Elongated crystals may be in parallel or sub-parallel arrangements           |                                                                                                                                  |                                                                                                                    | Granite<br>Gneiss (when parallel arrangement of crystals)<br>Pegmatite             |                                                                                                                                       |                                                                                 |
|                                                                                                                          |                                                                                                                                                              | Sand grains in very finely grained to dense material                                                                                   | Varying, lustre very dull                             | Clayey                                                                                                   | Rough                                                                        | Not significant                                                                                                                  | Scratched easily with pocket knife; feels like blotting paper on wet tongue; gritty feel between teeth when bitten | Argillaceous rock                                                                  | Mudstone<br>Shale<br>Slate                                                                                                            |                                                                                 |
| White, brown, yellowish-brown, reddish-brown to almost black; lustre generally dull, black parts may flicker in sunlight |                                                                                                                                                              |                                                                                                                                        | Carbonate, iron oxide (red) or iron hydroxide (brown) | Mostly rough, white (carbonate) materials may be rather smooth                                           | Any soil or weathered rock                                                   | Contains angular to sub-angular fragments of all sorts of minerals and rocks                                                     | Strength may vary considerably. Resistance to scratching variable                                                  | Diamictite                                                                         | Greywacke Tillite<br>Volcanic breccia                                                                                                 | Recognition of these rocks often difficult, use should be made of expert advice |
|                                                                                                                          |                                                                                                                                                              |                                                                                                                                        |                                                       |                                                                                                          |                                                                              | Scratched easily with pocket knife; white material (carbonate) 'boils' in hydrochloric acid (HCl)                                | Pedogenic material                                                                                                 | Calcrete (white)<br>Ferricrete (other colours)                                     |                                                                                                                                       |                                                                                 |
| Quartz or opal scarce or absent (<10%; can only be detected by looking carefully)                                        | Very finely 'bedded' with very thin bands of elongated lenses of quartz between often wavy layers of micaceous and other very fine-gained and dense material | Mostly shades of grey, brown or greenish: perpendicular to layers slightly flickering in sunlight; parallel to layers noticeably silky | None                                                  | Rough perpendicular to layers; smooth parallel to layers                                                 | None                                                                         | Feels soapy on layer planes which are also scratched easily with needle or pocket knife                                          | Argillaceous rock                                                                                                  | Phyllite<br>Sericite schist<br>Slate                                               |                                                                                                                                       |                                                                                 |
|                                                                                                                          | Granular, crystalline, appears to be composed of one type of mineral only                                                                                    | Mostly reddish or red but may also be white; often contains a few dark green to black minerals (hornblende)                            | None                                                  | Rough; there may be faces of large crystals                                                              | None                                                                         | Cannot be scratched with pocket knife but can be with a piece of quartz                                                          | Acid crystalline rock                                                                                              | Syenite                                                                            |                                                                                                                                       |                                                                                 |
|                                                                                                                          |                                                                                                                                                              | Mostly white but other colours also possible; general flicker in sunlight                                                              |                                                       |                                                                                                          |                                                                              | Scratched easily with pocket knife; 'boils' in hydrochloric acid (HCl)                                                           | Carbonate rock                                                                                                     | Marble                                                                             |                                                                                                                                       |                                                                                 |
|                                                                                                                          | Granular, crystalline                                                                                                                                        | Generally dark-coloured but a few types are light-coloured or even white. Crystals flicker in sunlight                                 | None                                                  | Rough                                                                                                    | None                                                                         | Individual minerals react different to scratching                                                                                | Basic crystalline rock                                                                                             | Amphibolite<br>Diabase<br>Diorite (light-coloured)<br>Dolerite<br>Gabbro<br>Norite | For identification of exact type of rock obtain expert advice                                                                         |                                                                                 |
|                                                                                                                          | Granular, crystalline                                                                                                                                        | Shades of green; lustre shiny; flicker in sunlight                                                                                     |                                                       |                                                                                                          |                                                                              | Can be scratched with pocket knife; surface may fee 'soapy'                                                                      | Serpentinite                                                                                                       |                                                                                    |                                                                                                                                       |                                                                                 |
|                                                                                                                          | Vitreous and dense. May contain empty or filled voids. There may be individual crystals (e.g. olivine) in dense material                                     | Dark shades of various colours; lustre shiny to dull                                                                                   |                                                       |                                                                                                          |                                                                              | Dense, uniform mass                                                                                                              |                                                                                                                    | Smooth to finely textured, rough                                                   | Voids may be filled with opal or even quartz besides other minerals (e.g. zeolites, calcite) which are mostly white to light-coloured | None                                                                            |
|                                                                                                                          | Very dense and sub-microscopically fine-grained                                                                                                              | Colour variable but mostly shades of grey or red; lustre dull                                                                          | None                                                  | Rough                                                                                                    | None                                                                         | Scratched easily with pocket knife; feels like blotting paper on wet tongue; silty or butter-like fell between teeth when bitten | Argillaceous rock                                                                                                  | Mudstone<br>Shale<br>Slate                                                         |                                                                                                                                       |                                                                                 |
|                                                                                                                          | Very dense and sub-microscopically fine-grained                                                                                                              | Colour often white but also shades of grey and others; lustre dull                                                                     | None                                                  | May be rough or smooth                                                                                   | Any weathered rock                                                           | Scratched easily with pocket knife; 'boils' in hydrochloric acid (HCl)                                                           | Carbonate rock                                                                                                     | Dolomite<br>Limestone                                                              | Limestone 'boils' much more vigorously than dolomite                                                                                  |                                                                                 |
|                                                                                                                          |                                                                                                                                                              |                                                                                                                                        |                                                       |                                                                                                          |                                                                              | Can be scratched with pocket knife; 'boils' in hydrochloric acid; may contain voids (honeycomb)                                  | Pedogenic material                                                                                                 | Calcrete Dolocrete                                                                 | Calcrete 'boils' much more vigorously than dolocrete                                                                                  |                                                                                 |
|                                                                                                                          |                                                                                                                                                              | Colour brown to reddish or yellowish brown, occasionally almost black; lustre generally dull but may flicker in sunlight when black    |                                                       |                                                                                                          |                                                                              | None                                                                                                                             | Rough                                                                                                              | None                                                                               | Nodular structure mostly clearly detectable; broken nodules may contain yellowish, soft, clayey material                              | Pedogenic material                                                              |
|                                                                                                                          | Dense to granular                                                                                                                                            | Black, may flicker in sunlight                                                                                                         | None                                                  |                                                                                                          |                                                                              | Very heavy, magnetic (affects needle of compass)                                                                                 | Metaliferous rock                                                                                                  | Magnetite                                                                          |                                                                                                                                       |                                                                                 |
|                                                                                                                          | Dense to fibrous                                                                                                                                             | White to light green                                                                                                                   |                                                       |                                                                                                          |                                                                              | Surface may feel slightly 'soapy'                                                                                                |                                                                                                                    | Magnesite                                                                          | Since confusion with other decomposition products of mafic minerals may occur, expert advice is recommended                           |                                                                                 |

**Definitions:**

Lustre – the character of light reflected by the minerals/rock

Vitreous – glass-like

Conchoidal – type of fracture with curved, ribbed surface

---

## F. REFERENCES

---

1. **Pavement management systems: standard visual assessment manual for flexible pavements.** 1992. Pretoria: Department of Transport. (Technical Methods for Highways (TMH); No 9).
2. **Manual for the visual assessment of pavement distress.** 1984. Pretoria: Department of Transport. (Manual M3-1).
3. **Nomenclature and methods for describing the condition of asphalt pavements.** 1985. Pretoria: Department of Transport. (Technical Recommendations for Highways (TRH), No 6).
4. WEINERT, H.H. 1980. **The natural road construction materials of southern Africa.** Cape Town: H and R Academia.
5. **Sampling methods for road construction materials.** 1981. Pretoria: Department of Transport. (Technical Methods for Highways (TMH), No 5).
6. **Pavement Management Systems.** 1994. Pretoria: Department of Transport. (Technical Methods for Highways (TRH); No 22)

### F.1. Other Relevant Documentation

1. **Pavement management systems: Gravel roads operations manual.** 1995. Cape Town: Provincial Administration of the Western Cape.
2. **Instandhoudingsbestuurstelsel: Riglyne en standarde vir distrik-inspeksies:** 1990. Pretoria: Gauteng Department of Transport and Public Works.
3. **Gravel road visual evaluation manual.** 1994. Republic of Venda Department of Works.

