


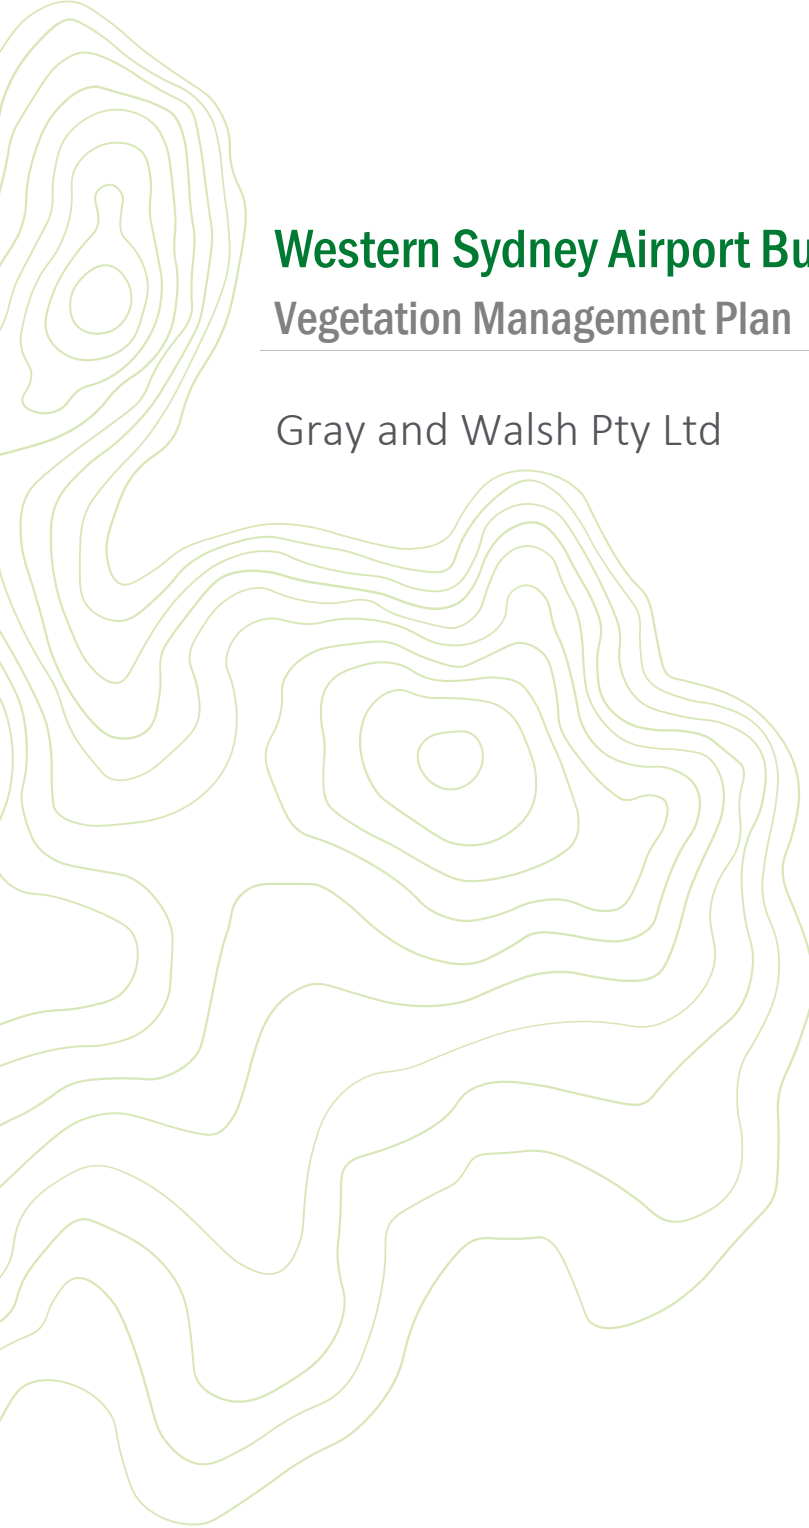

# **Western Sydney Airport Business Park**

## **Vegetation Management Plan**

---

Gray and Walsh Pty Ltd

Document Tracking

|                  |                                                                  |
|------------------|------------------------------------------------------------------|
| Project Name:    | Western Sydney Airport Business Park: Vegetation Management Plan |
| Project Number:  | 24SYD7568                                                        |
| Project Manager: | Courtney Blick                                                   |

| Version | Prepared by    | Reviewed by     | Approved by  | Status | Date       |
|---------|----------------|-----------------|--------------|--------|------------|
| 1       | Michael Gregor | Andrew Whitford | David Bonjer | Final  | 26/07/2024 |
| 2       | Courtney Blick | Andrew Whitford | David Bonjer | Final  | 21/08/2024 |
| 3       | Courtney Blick | Courtney Blick  | David Bonjer | Final  | 28/08/2024 |
| 4       | Courtney Blick | Andrew Norvill  | David Bonjer | Final  | 23/12/2025 |

This report should be cited as ‘Eco Logical Australia 2025, *Western Sydney Airport Business Park: Vegetation Management Plan*, Prepared for Gray and Walsh Pty Ltd.’

Acknowledgements

This document has been prepared by Eco Logical Australia Pty Ltd with support from Gray and Walsh Pty Ltd.

Disclaimer

*This document may only be used for the purpose for which it was commissioned and in accordance with the contract between Eco Logical Australia Pty Ltd and Gray and Walsh Pty Ltd. The scope of services was defined in consultation with Gray and Walsh Pty Ltd, by time and budgetary constraints imposed by the client, and the availability of reports and other data on the subject area. Changes to available information, legislation and schedules are made on an ongoing basis and readers should obtain up-to-date information. Eco Logical Australia Pty Ltd accepts no liability or responsibility whatsoever for or in respect of any use of or reliance upon this report and its supporting material by any third party. Information provided is not intended to be a substitute for site specific assessment or legal advice in relation to any matter. Unauthorised use of this report in any form is prohibited.*

## Abbreviations

| Abbreviation | Description                                                                       |
|--------------|-----------------------------------------------------------------------------------|
| AABR         | Australian Association of Bush Regenerators                                       |
| BA Act       | NSW <i>Biosecurity Act 2015</i>                                                   |
| BC Act       | NSW <i>Biodiversity Conservation Act 2016</i>                                     |
| CEEC         | Critically Endangered Ecological Community                                        |
| Council      | Liverpool City Council                                                            |
| DCP          | Development Control Plan                                                          |
| DPE          | Department of Planning and Environment (now NSW DCCEEW)                           |
| DCCEEW       | NSW Department of Climate Change, Energy, the Environment and Water               |
| DPI          | Department of Primary Industries                                                  |
| ELA          | Eco Logical Australia Pty Ltd                                                     |
| EPBC         | Commonwealth <i>Environment Protection and Biodiversity Conservation Act 1999</i> |
| LGA          | Local Government Area                                                             |
| LLS          | Local Land Services                                                               |
| PCT          | Plant Community Type                                                              |
| SEPP         | State Environmental Planning Policy                                               |
| VMP          | Vegetation Management Plan                                                        |
| WM Act       | NSW Water Management Act 2000                                                     |
| WoNS         | Weeds of National Significance                                                    |

# Contents

|                                                                                      |           |
|--------------------------------------------------------------------------------------|-----------|
| <b>1. Introduction</b>                                                               | <b>1</b>  |
| 1.1. Background and context .....                                                    | 1         |
| 1.2. Scope and objectives.....                                                       | 1         |
| 1.3. Preparation and implementation .....                                            | 2         |
| <b>2. Existing environment</b>                                                       | <b>4</b>  |
| 2.1. Location context.....                                                           | 4         |
| 2.2. Existing land use .....                                                         | 4         |
| 2.3. Topography and hydrology .....                                                  | 4         |
| 2.4. Vegetation communities .....                                                    | 4         |
| 2.4.1. PCT 3320: Cumberland Shale Plains Woodlands .....                             | 5         |
| 2.4.2. PCT 4023: Coastal Valleys Riparian .....                                      | 5         |
| 2.4.3. Other vegetation.....                                                         | 6         |
| 2.5. Weeds .....                                                                     | 6         |
| <b>3. Preliminary works</b>                                                          | <b>10</b> |
| 3.1. Fencing and interpretation signage.....                                         | 10        |
| 3.1.1. Temporary fencing.....                                                        | 10        |
| 3.1.2. Permanent fencing .....                                                       | 10        |
| 3.1.3. Signage and gates .....                                                       | 10        |
| 3.2. Soil and water management .....                                                 | 10        |
| 3.3. Preclearance and earthworks supervision and habitat enhancement .....           | 11        |
| 3.4. Pest control .....                                                              | 11        |
| 3.5. Soil preparation prior to revegetation .....                                    | 11        |
| <b>4. Vegetation management works</b>                                                | <b>14</b> |
| 4.1. VMP management zones .....                                                      | 14        |
| 4.1.1. Management Zone 1 – Swamp Oak Forest – Assisted Regeneration .....            | 14        |
| 4.1.2. Management Zone 2: Cumberland Plain Woodland – Assisted regeneration .....    | 14        |
| 4.1.3. Management Zone 3: Swamp Oak Forest – Revegetation .....                      | 15        |
| 4.1.4. Management Zone 4: Cumberland Plain Woodland – Revegetation .....             | 15        |
| 4.1.5. Management Zone 5: Cumberland Plain Woodland – Low Density Revegetation ..... | 15        |
| 4.2. Primary and secondary weed control .....                                        | 1         |
| 4.3. Maintenance .....                                                               | 1         |
| 4.4. Revegetation .....                                                              | 1         |
| <b>5. Implementation schedule</b>                                                    | <b>3</b>  |
| 5.1. Implementation schedule .....                                                   | 3         |
| 5.2. Adaptive management.....                                                        | 0         |
| 5.3. VMP management after maintenance period (in perpetuity) .....                   | 0         |
| 5.4. Training .....                                                                  | 0         |
| <b>6. Monitoring and reporting</b>                                                   | <b>1</b>  |
| 6.1. Photo monitoring .....                                                          | 1         |
| 6.2. Vegetation surveys.....                                                         | 1         |
| 6.3. Progress reports.....                                                           | 1         |
| 6.4. Performance criteria .....                                                      | 2         |
| <b>7. Costs</b>                                                                      | <b>5</b>  |
| 7.1. Preliminary works.....                                                          | 5         |

|                                                       |          |
|-------------------------------------------------------|----------|
| 7.1.1. Vegetation clearing and soil preparation ..... | 5        |
| 7.1.2. Seed collection .....                          | 5        |
| 7.2. Vegetation management works .....                | 5        |
| 7.2.1. Site preparation .....                         | 5        |
| 7.2.2. Weed control techniques .....                  | 5        |
| 7.2.3. Revegetation treatments .....                  | 5        |
| 7.2.4. Monitoring and reporting .....                 | 6        |
| 7.3. Pest Control.....                                | 6        |
| <b>8. References</b>                                  | <b>8</b> |

## List of Figures

|                                                                                         |   |
|-----------------------------------------------------------------------------------------|---|
| Figure 1: Location of the study area and VMP .....                                      | 3 |
| Figure 2: PCTs and other validated land types .....                                     | 8 |
| Figure 3: Parkland Priority Areas (Phase 2 DCP) and Riparian Corridor (ELA 2024b) ..... | 9 |
| Figure 4: VMP management zones .....                                                    | 0 |

## List of Tables

|                                                                                     |    |
|-------------------------------------------------------------------------------------|----|
| Table 1: VMP objectives.....                                                        | 2  |
| Table 2: Summary of PCTs and condition identified within the study area.....        | 5  |
| Table 3: A list of priority weeds and WoNS identified within the Project Site ..... | 7  |
| Table 4: Soil preparation works requirements.....                                   | 13 |
| Table 5: Planting assumptions .....                                                 | 2  |
| Table 6: Revegetation densities .....                                               | 2  |
| Table 7: Responsibility of works.....                                               | 3  |
| Table 8: Performance Criteria .....                                                 | 3  |
| Table 9: PCT benchmark conditions .....                                             | 4  |
| Table 10: Indicative costings .....                                                 | 7  |

## List of Appendices

|                                             |
|---------------------------------------------|
| Appendix A Existing Vegetation              |
| Appendix B Recommended Revegetation Species |
| Appendix C Techniques and specifications    |

# 1. Introduction

This Vegetation Management Plan (VMP) has been prepared by Eco Logical Australia (ELA) on behalf of Gray and Walsh Pty Ltd for the proposed State Significant Development Application (SSDA) at 2422-2430 The Northern Road, Luddenham NSW. The study area is legally defined as Lot 3 – 7 in Deposited Plan (DP) 1240511.

## 1.1. Background and context

The study area forms part of the Aerotropolis Core Precinct within the Western Sydney Aerotropolis and is zoned AGB (Agribusiness) and ENZ (Environment and Recreation) under the *State Environmental Planning Policy (Precincts – Western Parkland City) 2021*. The study area encompasses approximately 69 ha of exotic grassland, native vegetation and farm dams (ELA 2024a).

ELA has completed previous works associated with the proposed development of Western Sydney Airport Business Park (hereafter referred to as the “Project”). These works include but are not restricted to biodiversity, riparian, and wildlife risk assessments (ELA 2024a-d). This VMP is a component of the proposed Master Plan for the development and will be implemented in tandem with other management plans prepared for the Project. A Biodiversity Management Plan (ELA 2024a) has been prepared by ELA to guide the management of various biodiversity aspects include weeds, flora and fauna, and dam dewatering.

The study area contains three mapped 1<sup>st</sup> order watercourses, one 2<sup>nd</sup> order watercourse, two 3<sup>rd</sup> order watercourses, and one 4<sup>th</sup> order watercourse. As such the study area is comprised of waterfront land and must adhere to the *Controlled Activities – Guidelines for Vegetation Management Plans on Waterfront Land* (DPE 2022). The required extent of the VMP area under these guidelines has been determined and detailed in the Riparian Assessment (ELA 2024b).

## 1.2. Scope and objectives

The overarching objectives of the VMP is to improve ecological health and integrity, maintain and enhance habitat values within the VMP area. This document will address all issues related to the protection of existing vegetation from impacts associated with the undertaking of earthworks and any edge effects as well as undertaking bush regeneration and management actions to improve its extent, condition, and resilience.

This VMP will outline the areas to be revegetated as part of the works and recommend fully structured vegetated areas, where possible, as per *Controlled Activities – Guidelines for Vegetation Management Plans on Waterfront Land* (DPE 2022). The VMP strategy is to maintain and enhance native species cover and integrity in the riparian corridor by assisting natural regeneration through active restoration actions such as treating weed species and reintroducing native species (as plant or seed).

This VMP covers a five-year maintenance period plus the achievement of the performance criteria. This VMP may either be implemented all at once or staged by areas (e.g. to correspond with construction stages) as long as each stage follows the full VMP programme to meet the performance criteria.

The objectives for the VMP area are summarised in Table 1.

Table 1: VMP objectives

| Objective                                                                                                                                                     | Description                                                                                                                                                                                                                                                                                                                                                                                                                                |
|---------------------------------------------------------------------------------------------------------------------------------------------------------------|--------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| Reinstate native vegetation and maintain ecological health (species composition and structure) within the establishment period and 2-year maintenance period. | <ul style="list-style-type: none"> <li>● Protect existing native vegetation from development pressures.</li> <li>● Rehabilitate and revegetate riparian corridor using appropriate native species.</li> <li>● Control weeds and prevent new outbreaks.</li> <li>● Assist in the natural regeneration of native species.</li> <li>● Addition of logs, rocks etc. removed from the development footprint for habitat improvement.</li> </ul> |
| Improve ecological health and integrity.                                                                                                                      | <ul style="list-style-type: none"> <li>● Continue to assist natural regenerative processes.</li> <li>● Maintain weed control</li> <li>● Prevent outbreaks of priority weeds</li> <li>● Revegetate using appropriate native species.</li> </ul>                                                                                                                                                                                             |
| Maintain and enhance habitat values                                                                                                                           | <ul style="list-style-type: none"> <li>● Protect existing native vegetation.</li> <li>● Control of weeds of significance and environmental weeds and prevent new infestations.</li> <li>● Assist in the natural regeneration of species across the VMP areas.</li> </ul>                                                                                                                                                                   |
| Ensure stable bed and banks of creeks                                                                                                                         | Where practical a 'soft engineering' approach to the maintenance and management of the creek bed and banks (e.g. hand installed erosion controls such as jute mesh, eco-logs, etc.) with a focus on planting locally indigenous native species, slowing flows before they reach the creek and attenuating peak and high frequency flows.                                                                                                   |
| Control weeds of significance and environmental weeds, and prevent new infestations                                                                           | <ul style="list-style-type: none"> <li>● Primary weed control phase</li> <li>● Secondary / follow-up weed control phase</li> <li>● Maintenance</li> </ul>                                                                                                                                                                                                                                                                                  |
| Protect existing natural areas from the proposed works                                                                                                        | <ul style="list-style-type: none"> <li>● Provision of exclusion zone from the works area to the areas to be managed as part of the VMP (e.g. provision of protection fencing and signage).</li> </ul>                                                                                                                                                                                                                                      |

### 1.3. Preparation and implementation

This VMP has been prepared and reviewed by Restoration Ecologist(s) with over five years' experience in environmental consulting and management, and a relevant Bachelor of Science degree. The role of the project restoration ecologist, where noted, should be undertaken by a similarly qualified and experienced restoration ecologist or bush regenerator.

Maintenance of this areas is to be carried out by an accredited Bush Regenerator (AABR) or should possess the required qualifications and experience for membership. In addition to this, they should have as a minimum, a Certificate III in Conservation & Land Management or equivalent. The contractor will need to carry out best practice bush regeneration techniques as described by Buchanan (2009).



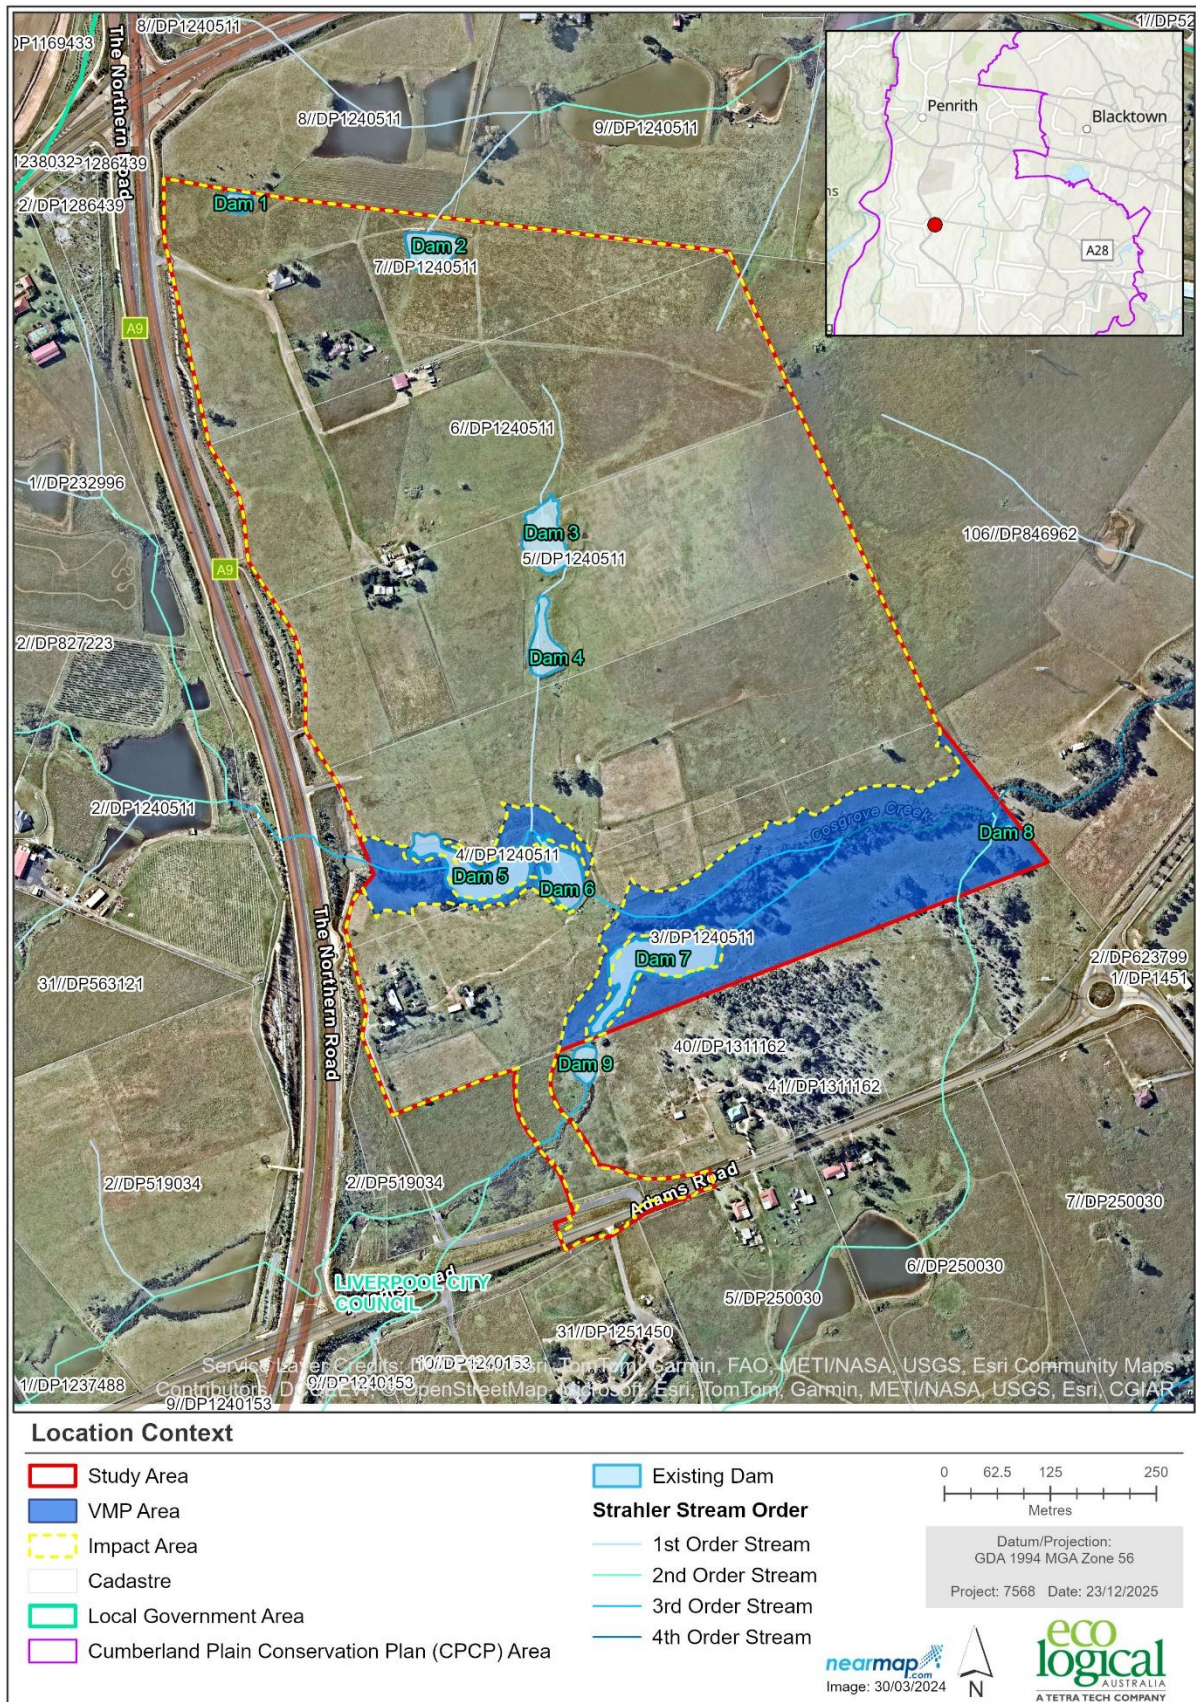


Figure 1: Location of the study area and VMP



## 2. Existing environment

### 2.1. Location context

The study area is located at 2422-2430 The Northern Road, Luddenham NSW, within the Liverpool City Council Local Government Area (LGA). The study area is within the Cumberland IBRA subregion. Conservation areas within a 10 km radius of the study area includes the Blue Mountains National Park (west), Burragorang State Conservation Area (southwest), Gulguer Nature Reserve (south), Kemps Creek Nature Reserve (east), and Mulgoa Nature Reserve (north).

### 2.2. Existing land use

The site has a historical land use for agricultural purposes and is currently used for cattle. The study area is largely cleared of native vegetation, it consists of pasture-improved exotic grassland, scattered paddock trees, riparian vegetation, farm dams and built form.

### 2.3. Topography and hydrology

The site is comprised of an undulating landscape sloping from north to south and west to east. The site contains 1<sup>st</sup> Order mapped Strahler streams that form and connect to the validated a 3rd order stream, Cosgroves Creek, within the study area which flows to the west of The Northern Road and flows to east across the study area.

### 2.4. Vegetation communities

Vegetation mapping provided within the Biodiversity Assessment Report (ELA 2024) identified two (2) Plant Community Types (PCT) in broad conditions within the study areas. The PCT identified are detailed below and shown in Figure 2.

PCT 3320 is listed as a threatened ecological community (TEC) under the BC Act and EPBC Act. Under the BC Act it is listed as critically endangered and named *Cumberland Plain Woodland in the Sydney Basin Bioregion*. Under the EPBC Act it can also be listed as the critically endangered ecological community, *Cumberland Plain Shale Woodlands and Shale-Gravel Transition Forest*. However, the patch sizes of PCT 3320 minimum condition thresholds for the TEC listing under the EPBC Act.

PCT 3975 can also correspond to a TEC under the BC Act, *Freshwater Wetlands on Coastal Floodplains of the New South Wales North Coast, Sydney Basin and South East Corner Bioregions*. However, the patch sizes of PCT 3975 within the study area.

Other vegetation types identified within the study area which do not conform to a native PCT include:

- Exotic planted
- Native planted
- Planted exotic/native
- Exotic grassland

Table 2: Summary of PCTs and condition identified within the study area

| Vegetation Community            | PCT ID and Name                                        | Condition    | Area (ha) | BC Act Status                           | EPBC Act Status                            |
|---------------------------------|--------------------------------------------------------|--------------|-----------|-----------------------------------------|--------------------------------------------|
| Coastal Valley Grassy Woodlands | PCT 3320: Cumberland Shale Plains Woodland             | Low          | 0.65      | CE                                      | CE – patch size does not meet requirements |
|                                 |                                                        | Regeneration | 0.55      |                                         |                                            |
| Coastal Freshwater Lagoons      | PCT 3975: Southern Lower Floodplain Freshwater Wetland | DNG          | 0.16      | E – patch size do not meet requirements | -                                          |
|                                 |                                                        | Low          | 1.77      |                                         |                                            |

#### 2.4.1. PCT 3320: Cumberland Shale Plains Woodlands

PCT 3320 (Low) was present as small patches throughout the Project Site. These patches were characterised by an intact canopy, exotic midstory and a mostly exotic ground layer with some natives present. The canopy was typically made up of one large tree with low canopy cover and was either the native *Eucalyptus tereticornis* (Forest Red Gum) or *Eucalyptus moluccana* (Grey Box). The midstorey was cleared with only a varying occurrence (5- 40% cover) of *Lycium ferocissimum* (African Boxthorn) present. The groundcover was dominated by weed species (> 75% cover) including *Axonopus fissifolius* (Carpet Grass), *Cenchrus clandestinus* (Kikuyu), *Cirsium vulgare* (Scotch Thistle), *Chloris gayana* (Rhodes Grass), *Cynodon dactylon* (Couch), *Ehrharta erecta* (Panic Veldtgrass), *Eragrostis curvula* (African Lovegrass), *Setaria parviflora* (Pidgeon Grass), *Paspalum dilatatum* (Paspalum), *Senecio madagascariensis* (Fireweed), *Sida rhombifolia* (Paddy's Lucerne), *Verbena bonariensis* (Purpletop) and *Plantago lanceolata* (Lamb's Tongues). The native species present (< 10% cover) included *Alternanthera denticulata* (Lesser Joyweed), *Dichondra repens* (Kidney Weed), *Einadia trigonos* (Fishweed), *Dysphania pumilio* (Small Crumbweed), *Microlaena stipoides* var. *stipoides* (Weeping Grass), *Sporobolus creber* (Slender Rat's Tail Grass) and *Portulaca oleracea* (Pigweed).

PCT 3320 (Regeneration) was present as four patches in the south-eastern area of the Project Site. These patches are characterised by a dense regenerating canopy or midstory ranging from 0.3 – 2 m in height, absent midstory and an exotic ground layer. The regenerating trees present included *Eucalyptus tereticornis* (Forest Red Gum) and *Eucalyptus moluccana* (Grey Box). The patches with midstorey regenerating included *Bursaria spinosa* (Blackthorn) at approximately 50% cover. The groundcover was dominated by weed species (> 80% cover) including *Axonopus fissifolius* (Carpet Grass), *Cenchrus clandestinus* (Kikuyu), *Cirsium vulgare* (Scotch Thistle), *Chloris gayana* (Rhodes Grass), *Cynodon dactylon* (Couch), *Setaria parviflora* (Pidgeon Grass), *Paspalum dilatatum* (Paspalum), *Sida rhombifolia* (Paddy's Lucerne), *Senecio madagascariensis* (Fireweed), *Trifolium repens* (White Clover), *Verbena bonariensis* (Purpletop) and *Plantago lanceolata* (Lamb's Tongues).

#### 2.4.2. PCT 4023: Coastal Valleys Riparian

PCT 4023 (Low) was present in the southern area of the Project Site along Cosgrove Creek. These patches are characterised by an intact canopy, exotic midstory and an exotic ground. The canopy was typically dense with high canopy cover (30 - 40%) and was dominated by *Casuarina glauca* (Swamp Oak) with *Eucalyptus tereticornis* (Forest Red Gum) and *Eucalyptus amplifolia* (Cabbage Gum) occurring less frequently. The midstory was sparse (~10% cover) and included *Lycium ferocissimum* (African Boxthorn), *Ligustrum lucidum* (Large-leaved Privet) and *Olea europaea* subsp. *cuspidata* (African Olive). The ground layer was made up of exotic grasses and forbs and included *Cenchrus clandestinus* (Kikuyu), *Chloris gayana* (Rhodes Grass), *Cyperus eragrostis* (Umbrella Sedge), *Juncus acutus* subsp. *acutus* (Sharp Rush), *Modiola caroliniana* (Red-flowered Mallow), *Setaria parviflora* (Pidgeon Grass) and *Sida rhombifolia* (Paddy's Lucerne).

PCT 4023 (DNG) was present as a floodplain patch connected to Cosgrove Creek within the Project Site. This patch is characterised by a absent canopy and midstory and a ground layer with native cover between 50-70%. The groundcover was mixed with native and exotic species. The patch was dominated by *Juncus usitatus* (Common Rush) with *Alternanthera denticulata* (Lesser Joyweed) and *Dysphania pumilio* (Small Crumbweed) occurring less frequently. The exotic species present included *Cenchrus clandestinus* (Kikuyu), *Chloris gayana* (Rhodes Grass), *Cyperus eragrostis* (Umbrella Sedge), *Hypochaeris radicata* (Catsear), *Setaria parviflora* (Pidgeon Grass) and *Sporobolus africanus* (Parramatta Grass).

#### 2.4.3. Other vegetation

Throughout the remaining area of the study area the vegetation was divided into four groupings, native planted vegetation, exotic planted, exotic shrubbery and exotic grasslands. These four areas did not conform to any PCT and are described below.

Planted native species consisting of *Callistemon salignus* (Willow Bottlebrush), *Callistemon viminalis* (Weeping Bottlebrush) and *Corymbia citriodora* (Lemon-scent Gum) surrounded the dwellings and structures within the study area. Mixed with the native planted species exotic vegetation consisting of *Photinia* spp., *Pinus* spp., *Erythrina x sykesii* (Coral tree), *Jacaranda mimosifolia* (Jacaranda) and other common garden species.

Further out from the structures and buildings, exotic vegetation in the form of open pasture and shrubbery persisted over much of the site. These areas consisted of exotic tree and shrub species ( *Ligustrum lucidum* (Large-leaved Privet), *Lycium ferocissimum* (African Boxthorn), *Olea europaea* subsp. *cuspidate* (African Olive) and exotic grasses, rushes and herbaceous weeds consisting of *Juncus acutus* subsp. *acutus* (Sharp Rush), *Axonopus fissifolius* (Narrow-leafed Carpet Grass), *Cenchrus clandestinus* (Kikuyu Grass), *Chloris gayana* (Rhodes Grass), *Eragrostis curvula* (African Lovegrass), *Paspalum dilatatum* (Paspalum), *Plantago lanceolata* (Lamb's Tongues), *Sida rhombifolia* (Paddy's Lucerne), *Senecio madagascariensis* (Fireweed), *Sporobolus africanus* (Parramatta Grass) and *Verbena rigida* var. *rigida* (Veined Verbena).

## 2.5. Weeds

The *Biosecurity Act 2015* (BA Act) and regulations provide specific legal requirements for the state level priority weeds (Table 3). Under the BA Act all plants are regulated with a general biosecurity duty to prevent, eliminate, or minimise any biosecurity risk they may pose. Any person who deals with any plant, who knows (or ought to know) of any biosecurity risk, has a duty to ensure the risk is prevented, eliminated, or minimised, so far as reasonably practicable.

Specific legal requirements apply to State determine priorities under the *Greater Sydney Regional Strategic Weed Management Plan 2023-2030*, while regional priorities include outcomes to demonstrate compliance with the general biosecurity duty and strategic responses in the region to achieve relevant management objectives (Greater Sydney LLS 2023). Weeds listed as 'other weeds of regional concern' under the plan warrant resources for local control or management programs and are a priority to keep out of the region. Inclusion in this list may assist Local Control Authorities and/or land managers to prioritise action in certain circumstances where it can be demonstrated the weed poses a threat to the environment, human health, agriculture etc.

Weed species identified during the field survey for this VMP includes six (6) of Weeds of National significance, and one (1) weed listed as Regional Level Priority. There were no weeds listed as other weeds of regional concern. The weeds present, their priority listing under the BA Act, the associated asset / value at risk and whether they are Weeds of National Significance (WoNS), area presented in Table 3. A

list of weeds recorded during field survey is provided in Table 3, with further detail in the Weed Eradication Management Plan (WEMP) (ELA 2024c).

**Table 3: A list of priority weeds and WoNS identified within the Project Site**

| Scientific Name                 | Common Name      | WoNS | Priority Weed Category                               |
|---------------------------------|------------------|------|------------------------------------------------------|
| <i>Lycium ferocissimum</i>      | African Boxthorn | Yes  | State priority – Containment and/or Asset Protection |
| <i>Senecio madagascariensis</i> | Fireweed         | Yes  | State priority - Containment and/or Asset Protection |



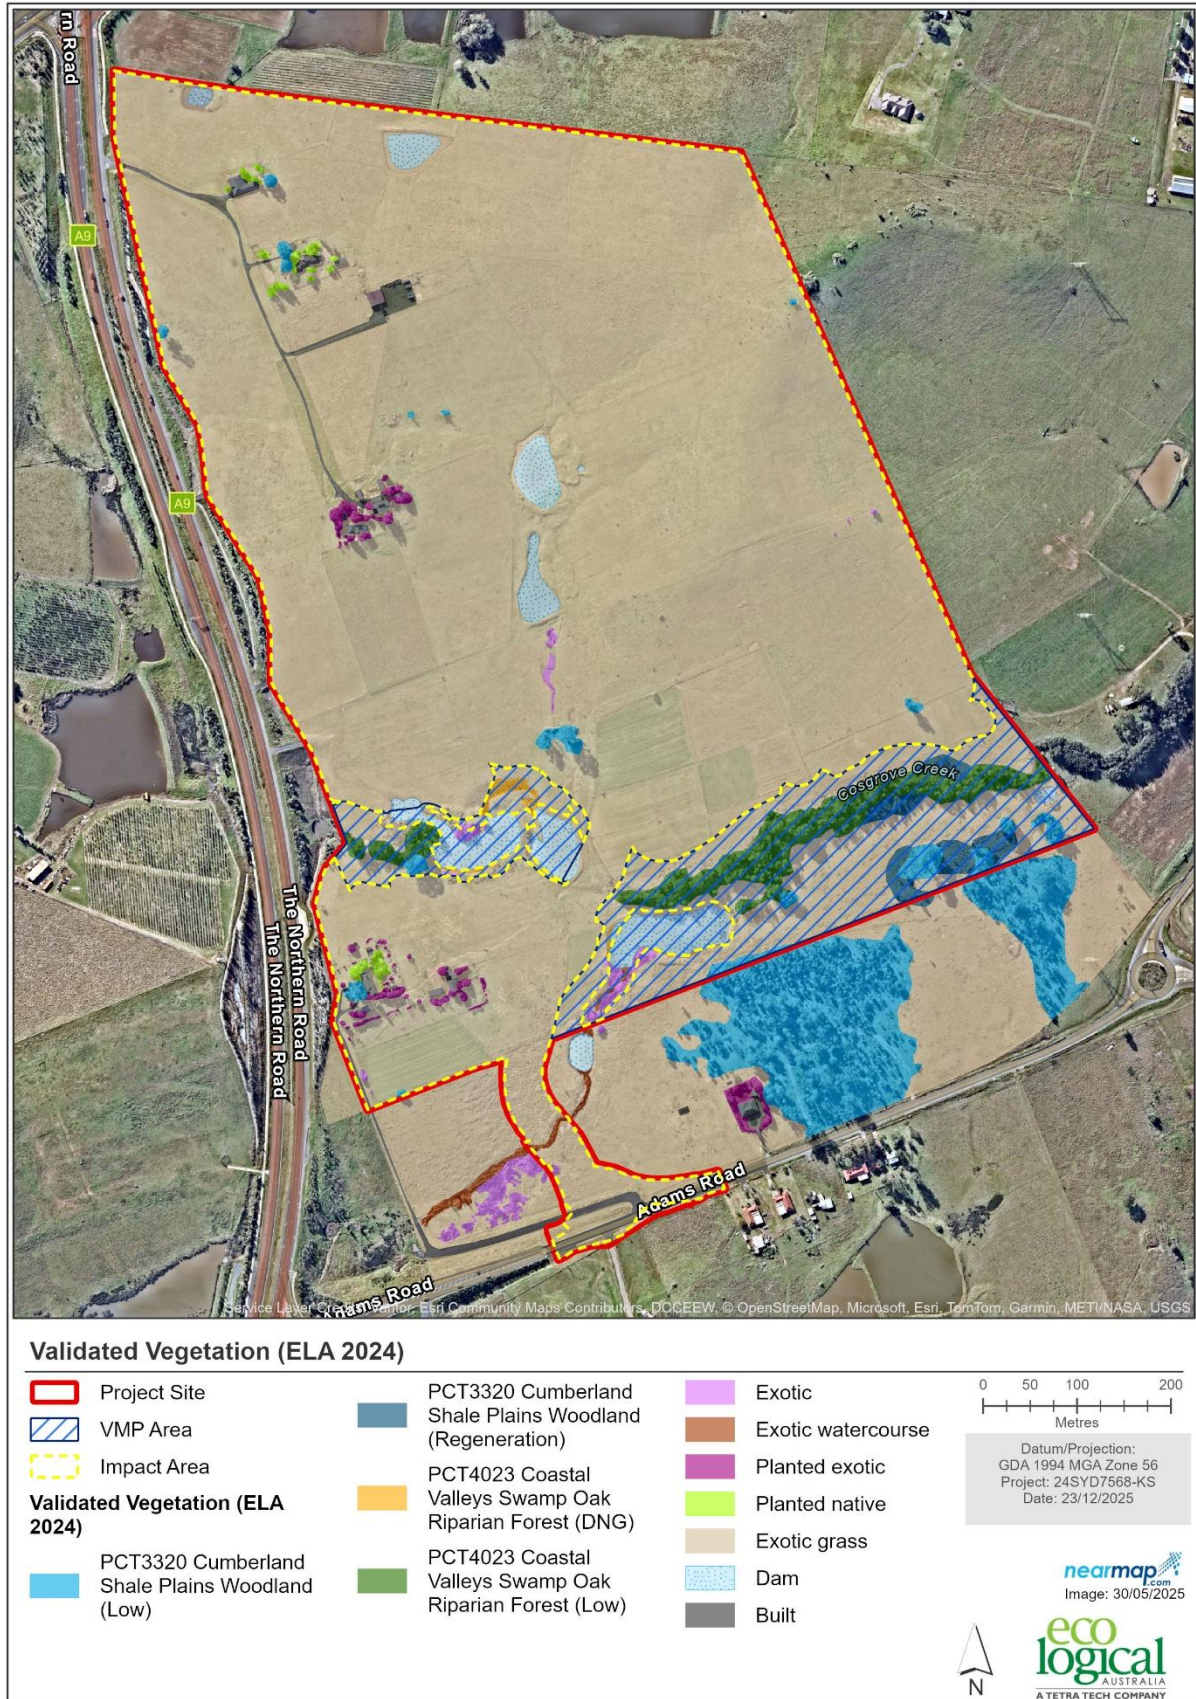


Figure 2: PCTs and other validated land types



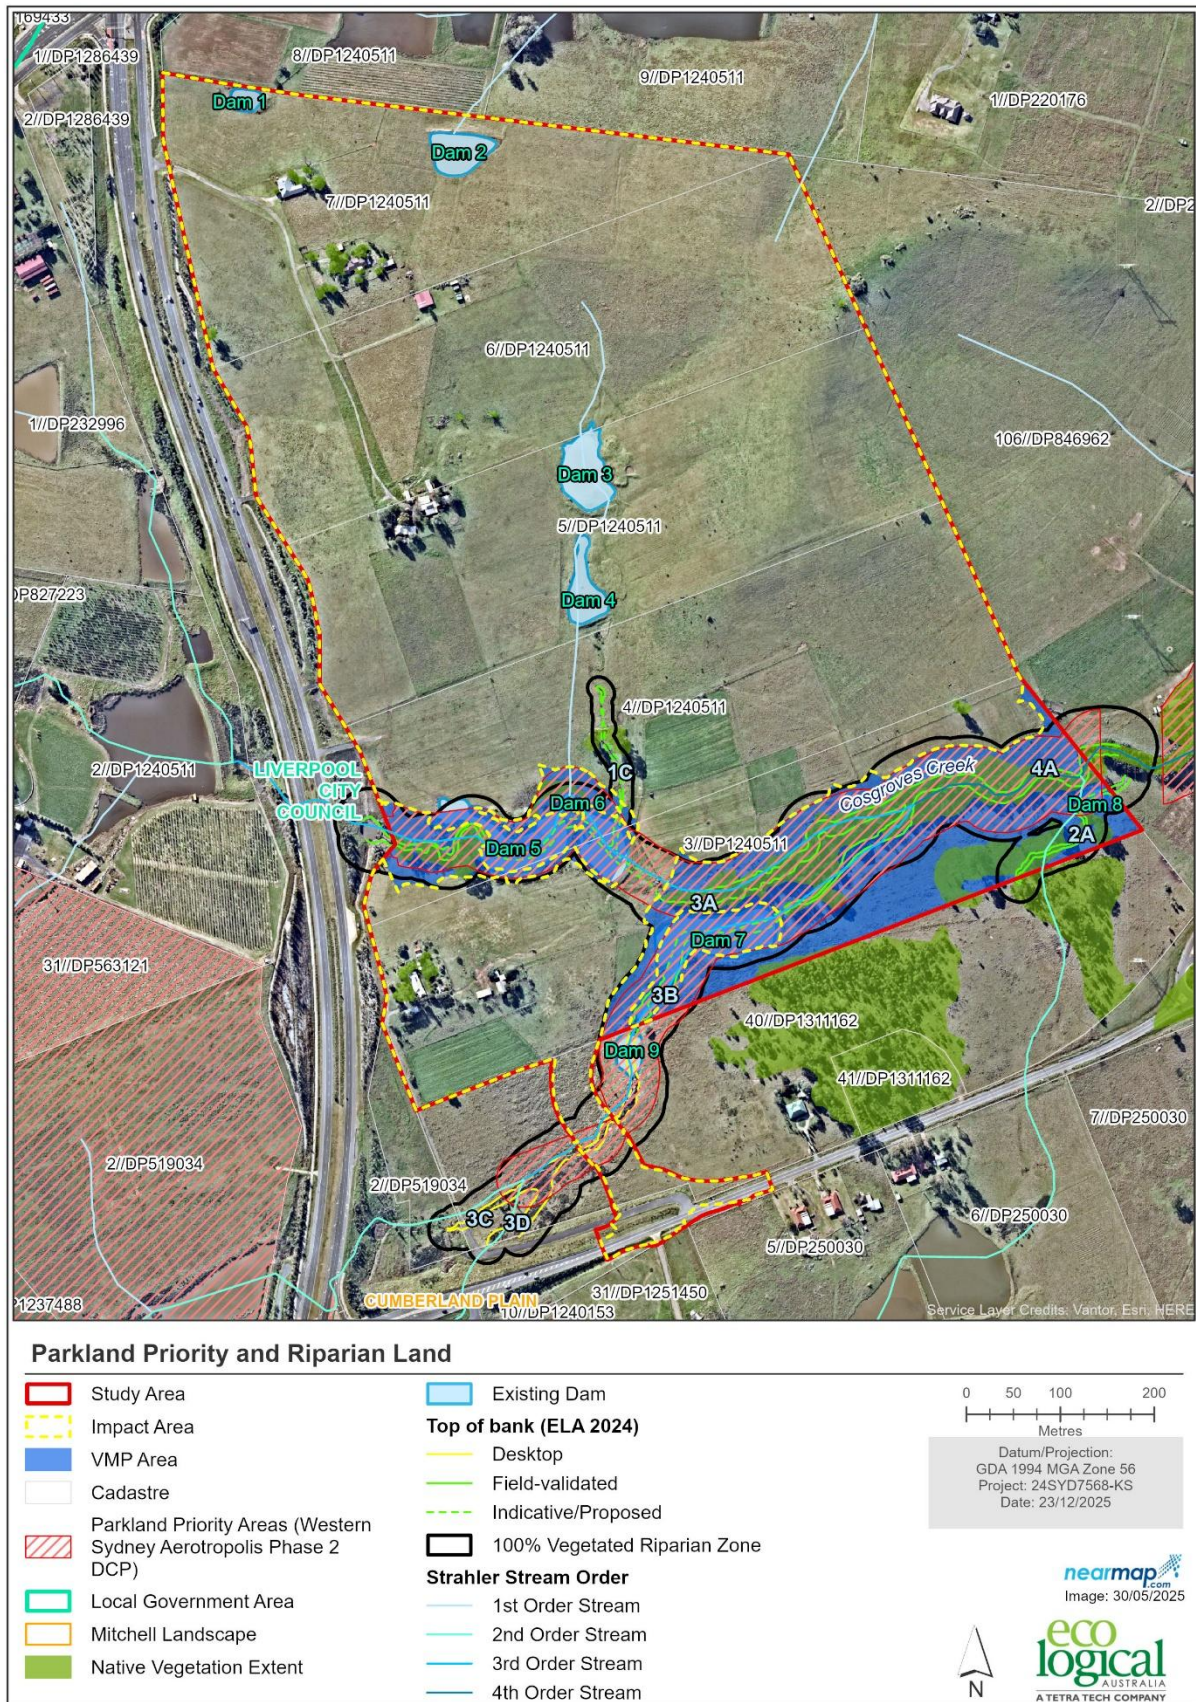


Figure 3: Parkland Priority Areas (Phase 2 DCP) and Riparian Corridor (ELA 2024b)

### 3. Preliminary works

The following works will be required prior to vegetation management works being undertaken.

#### 3.1. Fencing and interpretation signage

##### 3.1.1. Temporary fencing

The edge of the VMP area where it borders the development footprint is to be fenced with temporary construction fencing to prevent civil construction machinery from entering the VMP area unless under supervision from a suitably qualified ecologist or bush regenerator. The exception to this, is where earthworks must be completed to facilitate the realignment of Cosgrove Creek. Access must be maintained to the VMP area for implementation phase to facilitate revegetation works.

Informational signage must be installed on the construction fencing that identifies that there is to be no entry into the VMP area without an ecologist or bush regenerator present.

Tree protection zones (TPZ) are required to be installed and implemented prior to construction works commencing within the VMP area. Tree protection zones must be implemented within the VMP area around key mature and recruiting native species in accordance with AS 4970-2009.

##### 3.1.2. Permanent fencing

The VMP area should be fenced permanently or similarly protected following completion of implementation works to prevent any long-term impacts. Any fencing should incorporate suitable access for VMP and other works. A standard rural fence (1.2 m high star posts with a minimum four strands of plain wire) is recommended. Fencing must allow fauna movement but restrict motorised vehicles from accessing the VMP area.

##### 3.1.3. Signage and gates

Informational signage should be placed at minimum at each entry point into the VMP area. Informational signage should state *'The vegetation within bushland is protected. Activities such as firewood collection, bush rock removal, picking of native flowers and dumping of garden waste are prohibited'*.

#### 3.2. Soil and water management

An Erosion and Sediment Control Plan, preferably as part of a Construction Environmental Management Plan, must be developed and implemented prior to the commencement of any on-ground works. This plan must outline mitigation measures (e.g., silt fencing, drainage swale, etc.) to protect the natural creek line in the south of the VMP area from increased nutrient loads and weed seed incursion from site runoff.

Prior to construction commencing, sediment fencing is to be installed at the base of the construction fencing to prevent sediment running into the VMP area and limit the spread of weed propagules in soil sediments during the construction period.

Measures to prevent erosion may include:

- Implementing soft engineering measures and revegetation works assist in stabilising slopes.



- Install coir logs (Coir Log 300mm x 3m square shape), secured them with wooden stakes and high-quality slitted jute mats fastened using retaining pins parallel and across to the flowline or slopes as required.
- Ensure the coir log are joined with its head and tail by installing them directly next to each other, extending to cover the entire length of the flowline parallel or across. Install rows with an appropriate gap (e.g. 3-4 m) until bottom of slope on one slope, and/or both side slopes are present parallel to the flowline.
- Repurpose rock boulders of various types and sizes excavated during major construction earthworks for use in creek and dam embankment stabilisation.
- Cap all flowlines along their full length where they enter the creek from urban areas with rock-lined channels as outlined above.

### 3.3. Preclearance and earthworks supervision and habitat enhancement

Prior to vegetation removal a preclearance survey must be conducted to identify and mark all habitat features (i.e. hollow bearing trees, stags, rocky outcrops etc.) within the development footprint. During construction activities, when clearing areas of existing vegetation, earthworks and tree removal should be undertaken with a fauna ecologist or wildlife carer present to capture and release any displaced fauna in suitable habitat adjacent to the development footprint, with assistance provided by wildlife carers to attend to and care for injured fauna as needed. The removal of all habitat features must take place a minimum of 24 hours following the removal of all other vegetation. Prior to the removal of habitat features, under the guidance of a suitably qualified ecologist the habitat feature must be tapped several times to observe for any signs of fauna. Following no observation of fauna the habitat feature can then be removed. Following removal, the qualified ecologist must inspect the habitat feature to ensure no fauna were harmed during the removal.

During works, all-natural timber (i.e., fallen logs and branches), hollow stems, sections of trees / large woody material (>10 cm diameter) and suitable bush rock removed from within the development footprint/impact area must be used as habitat structures within the VMP area. This material provides microhabitat for fauna species, soil stability and nutrients cycling. Exotic vegetation is to be taken off-site and should not be used in habitat enhancement. The placement of all fauna habitat augmentation/relocation is to be carried out under the supervision of a qualified ecologist.

All viable seed and genetic material present at time of clearance will be collected for plant propagation uses.

### 3.4. Pest control

It is the responsibility of the landholder to remove and protect the VMP area from all livestock within the area. Pest control is the responsibility of the land holder, if pest control is required installation is to be undertaken by relevant contractors in consultation with Local Land Services (LLS) and Council.

### 3.5. Soil preparation prior to revegetation

Considerable chemical change can occur between soil A and B horizons, with some B horizons highly sodic and prone to deflocculation, erosion and water logging – which could significantly reduce revegetation works success. For this reason, excavation, shaping and re-leveling activities within the VMP area, if required, should take particular care with the removal, stockpiling and replacement of soil

horizons/strata to achieve final soil profiles that are appropriate for plant survival. Works should also have plans in place to minimise and remediate soil compaction where construction works are taking place in the VMP area. Furthermore, environmental hygiene is highly recommended to prevent the introduction or the transfer of pathogens or Noxious/WoNS seed. Safe Work Method Statements (SWMS) need to incorporate these measures for machinery and all pedestrians including work teams, reporters etc.

After all construction works, including haul roads and creek realignment works are complete and civil construction vehicle movements are excluded then surfaces should be treated with appropriate topsoils, compost and ameliorants to finished levels, ripped (where necessary) and cultivated to a light friable consistency. It is assumed that the Civil Contractor will undertake the soil preparation works but the exact requirements should be finalised in consultation with a suitably qualified and experienced Restoration Ecologist.

For this VMP, it is assumed that earthworks will be required for all areas impacted by the installation of stormwater drainage, rock riprap installation, vegetation removal and other development impacts. As such, it is assumed that management zones 3-5 within the VMP will require soil preparation works as identified in Table 4.



**Table 4: Soil preparation works requirements**

| Task                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                           |
|----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| Form and shape subgrade to 300mm below final levels                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                            |
| Install 225mm of suitable site topsoil consistent with the natural local soils                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                 |
| Install 75mm compost complying with AS4454-2012                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                |
| Undertake soil testing and install suitable ameliorants depending on the results. An indicative example of what might be required includes: <ul style="list-style-type: none"> <li>• 100g/m<sup>2</sup> Gypsum</li> <li>• 20g/m<sup>2</sup> microbial soil conditioner (e.g., Bactivate granular or equivalent)</li> <li>• 20g/m<sup>2</sup> quick-release multi-source 5:2:8 NPK organic granular fertiliser (e.g., Terralift TX10 + MYCORRHIZA or equivalent)</li> <li>• 120g/m<sup>2</sup> slow-release microbial native 14:1:4 NPK granular fertiliser (e.g., Troforte M Native, or equivalent)</li> </ul> |
| Work in topsoil, compost, and ameliorants together at 25% volume (3 parts soil plus 1 part compost)                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                            |
| Install to a depth of 300mm over subgrade                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                      |
| Rip and cultivate until light and friable                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                      |

## 4. Vegetation management works

### 4.1. VMP management zones

The following vegetation management zones are required to be implemented as part of this VMP. These five (5) management zones have been designed to incorporate natural regeneration and rehabilitation of the site to provide a sustainable natural area.

- Zone 1: Swamp Oak Forest – Assisted Regeneration
- Zone 2: Cumberland Plain Woodland – Assisted Regeneration
- Zone 3: Swamp Oak Forest – Revegetation
- Zone 4: Cumberland Plain Woodland – Revegetation
- Zone 5: Cumberland Plain Woodland – Low Density Revegetation

#### 4.1.1. Management Zone 1 – Swamp Oak Forest – Assisted Regeneration

Zone 1 (1.77 ha) encompasses areas of existing low condition Coastal Swamp Oak Riparian Forest within the riparian corridor. Throughout this management zone it is assumed that management of exotic species will allow the existing native seed bank to regenerate. No revegetation has been allocated within this zone, however this should be reviewed during management works.

The key management priorities throughout Zone 1 are:

- Install and maintain VMP boundary fencing prior to construction of the riparian corridor
- Management of exotic species
- Facilitation of natural regeneration through opportunistic direct seeding and brush matting
- Enhance habitat features (e.g. logs, rocks, etc.)
- Monitor native vegetation and weed densities.

#### 4.1.2. Management Zone 2: Cumberland Plain Woodland – Assisted regeneration

Zone 2 (0.96 ha) encompasses areas of existing low condition and regenerating Cumberland Shale Plain Woodland within the riparian corridor. Throughout this management zone it is assumed that management of exotic species will allow the existing native seed bank to regenerate. No revegetation has been allocated within this zone, however this should be reviewed during management works.

The key management priorities throughout Zone 2 are:

- Install and maintain VMP boundary fencing prior to construction of the riparian corridor
- Management of exotic species
- Facilitation of natural regeneration through opportunistic direct seeding and brush matting
- Enhance habitat features (e.g. logs, rocks, etc.)
- Monitor native vegetation and weed densities.

#### 4.1.3. Management Zone 3: Swamp Oak Forest – Revegetation

Zone 3 (1.60 ha) encompasses areas of existing exotic pasture, exotic riparian vegetation and the future riparian corridor to be constructed following the dewatering of three of the existing farm dams. This management zone aims to restore and connect the existing areas of low condition Coastal Swamp Oak Riparian Forest.

It is assumed that following the construction of the riparian corridor that this area will require 100% revegetation to achieve the performance criteria outlined in Table 8.

The key management goals throughout Zone 3 are:

- Install and maintain VMP boundary fencing following construction of the riparian corridor
- Removal exotic species
- Install jute matting as required.
- Establish native tubestock species as outlined in Table 5 and Table 6
- Irrigate until established and as needed ongoing.
- Enhance habitat features (e.g., rocks, logs etc.)
- Control exotic species
- Monitor native vegetation and weed densities.

#### 4.1.4. Management Zone 4: Cumberland Plain Woodland – Revegetation

Zone 4 (4.40 ha) encompasses areas of existing exotic pasture within the riparian corridor. This management zones aims to restore areas of CPW to support the regeneration of the riparian corridor. It is assumed that this management zone will require 100% revegetation following the construction of the riparian corridor to achieve the performance criteria outlined in Table 8.

The key management goals throughout Zone 4 are:

- Install and maintain VMP boundary fencing following construction of the riparian corridor
- Removal exotic species
- Install jute matting as required.
- Establish native tubestock species as outlined in Table 5 and Table 6
- Irrigate until established and as needed ongoing.
- Enhance habitat features (e.g., rocks, logs etc.)
- Control exotic species
- Monitor native vegetation and weed densities.

#### 4.1.5. Management Zone 5: Cumberland Plain Woodland – Low Density Revegetation

Zone 5 (1.20 ha) encompasses areas of existing exotic pasture, and is defined by areas of offsets which are (a) outside of the riparian corridor, (b) outside the Priority Parkland Area and (c) do not contain any existing native vegetation. These areas are required to be revegetated under the VMP to provide offsets to impacts on the outer 50% VRZ (ELA 2024b).

DCP controls relating to landscaping do not apply to Priority Parkland Areas. In areas outside of the Priority Parkland Areas, landscaping (and restoration under this VMP) must consider the requirements of the Aerotropolis DCP. There are several conflicting objectives set out by the Phase 2 DCP relating to canopy cover, Connecting with Country, urban heat reduction and restoration of natural waterways – with the important aim to support safe airport operations by reducing the attractiveness of wildlife habitat, thereby reducing the risk of bird and bat strike.

Under the VMP, outside the VRZ and Priority Parkland, revegetation is proposed to restore a modified groundcover layer with reduced density of tree and shrub species. The primary purpose of Zone 5 is to mitigate wildlife hazard assessment outcomes, while supporting the function of the riparian corridor along Cosgroves Creek and requirements for offsets under the Riparian Guidelines (DPE 2022). For example, the use of clumping grasses such as *Lomandra sp.* is not recommended throughout this management zone, as these species can provide habitat for small mammals increasing the likelihood of carnivorous avian fauna to occur on the site. The relationship between wildlife hazard and the VMP area is described in the separate Wildlife Hazard Assessment report (ELA 2024d).

The key management priorities and principles within Zone 5 are:

- Minimise the attractiveness of Zone 5 habitat for wildlife
- Installation and maintenance of VMP boundary fencing following construction activates where accessible
- Removal of exotic species
- Promote native species regeneration
- Installation of mulch/jute matting as required
- Establish native tubestock species as outlined in Table 5 and Table 6
- Irrigation of native tubestock until established and as needed ongoing.
- Enhance habitat features (e.g., rocks, logs etc.)
- Control of exotic grasses and other species
- Monitor native vegetation and weed densities.

It is noted that with regard to the wildlife objectives under the DCP, the VMP including MZ5 will be subject to ongoing monitoring and adaptive management measures will be implemented as required. This may result in changes to the management zone compositions or management techniques (e.g. removal of food sources, thinning of vegetation) based on monitoring outcomes. This monitoring is to be carried out in accordance with the Wildlife Hazard Management Plan (ELA 2024d).



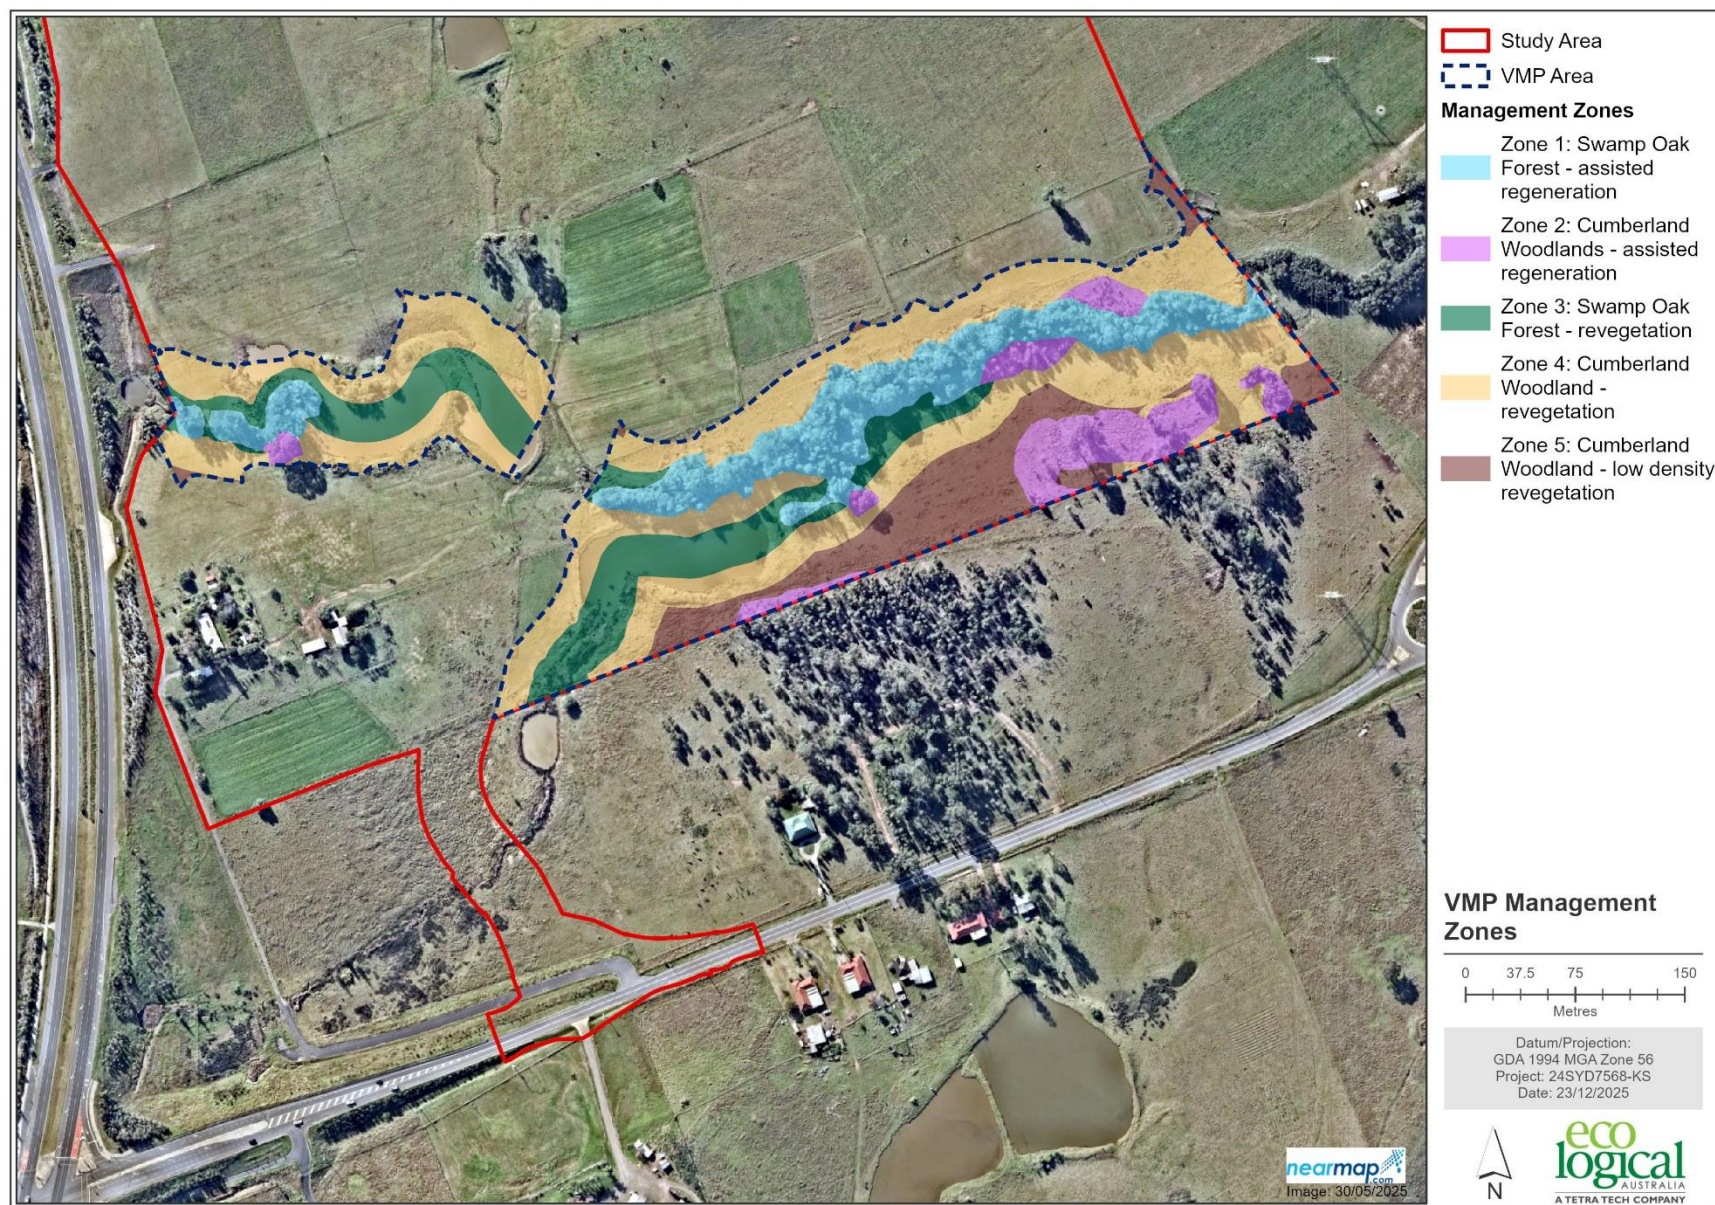


Figure 4: VMP management zones

## 4.2. Primary and secondary weed control

All weeds, including woody weeds will require treatment. Secondary and maintenance weed control will be required following revegetation. During these works, care must be taken to avoid any off-target damage to the natural regeneration of native species.

Primary weed control will include the removal of all woody and herbaceous exotic species outlined in Appendix A, specifically *Lycium ferocissimum* (African Boxthorn). Juvenile *L. ferocissimum* plants can be hand-pulled, provided the whole root is removed. Large *L. ferocissimum* plants can be treated using cut and paint method, removing the bulk of above ground biomass while retaining the root system to assist in erosion control. Chemical and mechanical control techniques will be required in follow up treatments. Follow up treatments of woody weeds including *L. ferocissimum* to control seedling growth will be required. For more information on specific weed control techniques, see Appendix C.

## 4.3. Maintenance

Following the completion of primary and secondary weed control works, all areas throughout the VMP will require ongoing maintenance to control weed regrowth from the existing soil seed bank. Maintenance work is to be undertaken by a qualified bush regeneration contractor(s) as per specifications provided in Appendix C.

Maintenance will be undertaken on a regular basis in the peak growing seasons (i.e., spring and summer), with less frequent visits necessary during cooler periods (i.e., autumn and winter). Maintenance work will include actions to encourage native regeneration in areas of lower resilience where it is not occurring naturally. These actions include techniques such as soil disturbance, niche seedling and transplanting, where appropriate.

## 4.4. Revegetation

This VMP requires the revegetation of Management Zones 3 - 5 to be undertaken as part of the rehabilitation of the site. It is assumed that Management Zones 1 – 2 have sufficient native resilience to naturally regenerate, however this should be further assessed during the management period. Revegetation, where undertaken, will consist of the installation of native tubestock (hiko/viro cells).

Propagation material for planting stock should be sourced from pre-clearance collections, nearby locations, or from within the catchment region following current Florabank Guidelines (Harrison et al. 2021). Appropriate planning and timelines for sourcing propagation and planting material should be allowed for. Suggested species in Appendix B should be used as a general guide but other suitable species may be used if required.

Mulch is required to be installed throughout Management Zone 4, where required mulch will should be laid to a depth of 100mm. Mulching is required to aid in the suppression of exotic species germination and increase soil organic matter content. Where possible it is preferred to use site obtained mulch from the clearance of native vegetation, although if this is not possible mulch can be externally sourced adhering to Australian Standards (i.e., AS4454 (2012): Compost soils conditioners and mulches). In addition, mulch should be comprised of un-composted wood preferably wood waste, with a particle size of about 15mm to 40mm with no fines and good air-filled porosity. Mulch should not contain and weed seeds, nor be derived from diseased trees or from any part of the tree lower than 1m above the ground. It is assumed site access will permit the delivery of mulch within 30 m of the VMP area and spread via bobcat.



Jute matting will be required in areas of higher inundation of the site during high rainfall periods, particularly within Management Zone 3. Jute matting must be comprised of 100% biodegradable jute fibres with a minimum weight of 680 g/m<sup>2</sup> (~6 mm thickness). Jute must be pegged with at least 3x150 mm pins per m<sup>2</sup> and each roll overlapped by 100 mm.

Planting densities for each management zone are provided in Table 6. A recommended planting list is provided in Appendix B. Revegetation will be done with species consistent with naturally occurring vegetation communities, being Coastal Swamp Oak Riparian Forest and Cumberland Shale Plains Woodland. All plantings are to be sourced from local provenance stock as per the Florabank guidelines (Mortlock 2000).

**Table 5: Planting assumptions**

| Zone | Description                                          | Area (m <sup>2</sup> ) | Reveg (%) | Reveg (m <sup>2</sup> ) | Jute Matt (%) | Jute Matt (m <sup>2</sup> ) | Mulch (%) | Mulch (m <sup>2</sup> ) |
|------|------------------------------------------------------|------------------------|-----------|-------------------------|---------------|-----------------------------|-----------|-------------------------|
| 1    | Swamp Oak Forest – Assisted Regeneration             | 17,691                 | 0         | 0                       | -             | -                           | -         | -                       |
| 2    | Cumberland Plain Woodland – assisted Regeneration    | 9,567                  | 0         | 0                       | -             | -                           | -         | -                       |
| 3    | Swamp Oak Forest – Revegetation                      | 16,027                 | 100%      | 16,027                  | 100%          | 16,027                      | -         | -                       |
| 4    | Cumberland Plain Woodland – Revegetation             | 44,046                 | 100%      | 44,046                  | -             | -                           | 100%      | 44,046                  |
| 5    | Cumberland Plain Woodland – Low density revegetation | 11,991                 | 100%      | 11,991                  | -             | -                           | 100%      | 11,991                  |
|      | <b>Totals</b>                                        | <b>99,322</b>          | <b>-</b>  | <b>72,065</b>           | <b>-</b>      | <b>16,027</b>               | <b>-</b>  | <b>56,037</b>           |

**Table 6: Revegetation densities**

| Zone | Description                                          | Reveg. Area (m <sup>2</sup> ) | Revegetation densities (m <sup>2</sup> )* |              |                    |                | Totals         |
|------|------------------------------------------------------|-------------------------------|-------------------------------------------|--------------|--------------------|----------------|----------------|
|      |                                                      |                               | Tree                                      | Shrub        | Herbs / Scramblers | Sedge / Grass  |                |
| 3    | Swamp Oak Forest – Revegetation                      | 16,027                        | 1/100                                     | 1/50         | 1                  | 4              | 80,617         |
| 4    | Cumberland Plain Woodland – Revegetation             | 44,046                        | 1/100                                     | 1/50         | 1                  | 4              | 221,551        |
| 5    | Cumberland Plain Woodland – Low density revegetation | 11,991                        | 1/200                                     | 1/100        | 2                  | 2              | 48,146         |
|      | <b>Totals</b>                                        | <b>72,065</b>                 | <b>661</b>                                | <b>1,321</b> | <b>84,056</b>      | <b>264,275</b> | <b>350,313</b> |

## 5. Implementation schedule

### 5.1. Implementation schedule

The VMP area will be managed with an establishment period expected to be 6-months and a five-year maintenance period. An indicative implementation schedule has been provided in Table 7 below.

Table 7: Responsibility of works

| Task                                      | Establishment | Year 1                        |   |   |   | Year 2 |   |   |   | Year 3 |   |   |   | Year 4 |   |   |   | Year 5 |   |   |   |
|-------------------------------------------|---------------|-------------------------------|---|---|---|--------|---|---|---|--------|---|---|---|--------|---|---|---|--------|---|---|---|
|                                           |               | 1                             | 2 | 3 | 4 | 1      | 2 | 3 | 4 | 1      | 2 | 3 | 4 | 1      | 2 | 3 | 4 | 1      | 2 | 3 | 4 |
| Preliminary works                         |               |                               |   |   |   |        |   |   |   |        |   |   |   |        |   |   |   |        |   |   |   |
| Site mark out/fencing                     |               |                               |   |   |   |        |   |   |   |        |   |   |   |        |   |   |   |        |   |   |   |
| Earthworks (riparian construction)        |               |                               |   |   |   |        |   |   |   |        |   |   |   |        |   |   |   |        |   |   |   |
| Revegetation                              |               |                               |   |   |   |        |   |   |   |        |   |   |   |        |   |   |   |        |   |   |   |
| Seed collection, cleaning, storage        |               |                               |   |   |   |        |   |   |   |        |   |   |   |        |   |   |   |        |   |   |   |
| Site preparation                          |               |                               |   |   |   |        |   |   |   |        |   |   |   |        |   |   |   |        |   |   |   |
| Jute matting / mulch                      |               |                               |   |   |   |        |   |   |   |        |   |   |   |        |   |   |   |        |   |   |   |
| Tubestock, supply and install             |               |                               |   |   |   |        |   |   |   |        |   |   |   |        |   |   |   |        |   |   |   |
| Replacement tubestock, supply and install |               |                               |   |   |   |        |   |   |   |        |   |   |   |        |   |   |   |        |   |   |   |
| Irrigation                                |               |                               |   |   |   |        |   |   |   |        |   |   |   |        |   |   |   |        |   |   |   |
| Weed control                              |               |                               |   |   |   |        |   |   |   |        |   |   |   |        |   |   |   |        |   |   |   |
| Establishment                             |               |                               |   |   |   |        |   |   |   |        |   |   |   |        |   |   |   |        |   |   |   |
| Maintenance Years 1-2                     |               |                               |   |   |   |        |   |   |   |        |   |   |   |        |   |   |   |        |   |   |   |
| Maintenance Years 3-5                     |               |                               |   |   |   |        |   |   |   |        |   |   |   |        |   |   |   |        |   |   |   |
| Associated works                          |               |                               |   |   |   |        |   |   |   |        |   |   |   |        |   |   |   |        |   |   |   |
| Monitoring and reporting                  |               |                               |   |   |   |        |   |   |   |        |   |   |   |        |   |   |   |        |   |   |   |
| Key                                       |               | Civil construction activities |   |   |   |        |   |   |   |        |   |   |   |        |   |   |   |        |   |   |   |
|                                           |               | Vegetation management works   |   |   |   |        |   |   |   |        |   |   |   |        |   |   |   |        |   |   |   |

## 5.2. Adaptive management

As this is a long-term project that will be implemented over five years an adaptive management approach will be implemented that enables the successful contractor to learn from and respond to successful and unsuccessful techniques used on the site. In its simplest form, this may include the substitution of species identified in the planting table or for undertaking advanced direct seeding techniques in place of manual planting techniques for revegetation works.

The success of the works will be determined by meeting the performance criteria identified in Table 8. Contractors have the flexibility to implement different techniques to those specified here providing that performance criteria are met. Any major departures from the VMP or proposed changes to performance criteria must be undertaken after the opportunity for inspection with LLC and approved in writing by Council.

## 5.3. VMP management after maintenance period (in perpetuity)

The VMP is to be re-evaluated upon completion of all works described within this VMP and at least every five years after that to ensure the site meets the performance criteria. Surveys at these inspections is to include both priority and environmental weed populations. Areas that do not conform to the performance criteria at the completion of works area required to be rehabilitated using the methods outlined within this VMP and may result in the extension of the VMP management period for a further five years.

## 5.4. Training

Construction staff will require training/inductions into the requirements of this VMP, including the location and requirements of tree/vegetation protection zones. Bush regeneration staff implementing this management plan must be a member of AABR or should possess the required qualifications and experience for membership. In addition to this, they should have, as a minimum, a Certificate III in Conservation & Land Management or equivalent. The contractor will need to conduct best practice bush regeneration techniques as described by Buchanan (2009).



## 6. Monitoring and reporting

### 6.1. Photo monitoring

Photo monitoring points should be set-up using a permanent reference point to provide a visual reference of changes in the vegetation. Photo monitoring to include:

- Set up a minimum of eight (8) photo monitoring points within the VMP area with a minimum of two (2) per zone photo monitoring points in each zone.
- Mark the photo point with a six-foot star picket and map the location and bearing of each photo point.
- Take a digital photo of each photo point with the whole length of the star picket visible in the photo to act as a reference point; and
- Organise the digital photos logically with each image labelled with a unique reference number indicating the location of the photo point, the direction of the photo and the date the photo is taken.

### 6.2. Vegetation surveys

Quadrat data points will be set up within the VMP area to monitor changes in the vegetation through time. The quadrat data forms the baseline for monitoring against the performance criteria for the duration of the VMP. Floristic plot data is to be collected including species richness, cover and abundance in a 5 x 5 m minimum sized quadrat.

### 6.3. Progress reports

completion of the project. This reporting includes the results of the monitoring actions specified in **Section 6.1** and **Section 6.2** and a description of the works that have been undertaken. These reports will be submitted to Council. Reports will include at a minimum:

- The time period the report relates to,
- Qualifications and experience of contractors,
- Certification of seed and local provenance stock,
- A summary of works carried out within the period including:
  - Date and time of site visits,
  - Works completed on the site at each visit,
  - A table detailing total person hours for each task carried out on-site,
  - Methods of weeding undertaken and details of herbicide use,
  - Numbers of tube stock planted if applicable,
  - Methods implemented for Assisted Natural Regeneration,
- Photo monitoring results to date,
- A description of any problems encountered in implementing the works outlined in this VMP and how they were overcome,

- Any observations made, including new plant species recorded (native and weed species), comments on rates of regeneration and any problems which impact on the implementation of the VMP,
- If applicable, the result of the implementation works in relation to the relevant performance criteria.

#### **6.4. Performance criteria**

The performance criteria are detailed in Table 8.

Failure to meet these performance criteria will mean that the maintenance period will be extended until they are achieved. Therefore, maintenance must continue until LCC agrees that the objectives and performance criteria have been met and the maintenance period has concluded. The author of this VMP, or an equally qualified and experience person, must prepare a statement certifying the compliance of the performance criteria at the end of the VMP period.

If monitoring indicates that the VMP tasks are not resulting in achievement of the performance criteria, the task program will be revised. The land owner and the bush regeneration contractor, in consultation with Council can adapt these criteria as required in response to the success of rehabilitation works.

The following performance criteria will need to be achieved in perpetuity:

- Across the VMP area, < 2% priority weeds cover and < 5% environmental weeds cover.
- No infiltration by exotic lawn species into the VMP area,
- No dumped garden waste within the VMP area,
- No patches of the VMP greater than 2m x 2m without any surviving natives or with significant erosion present.

Table 8: Performance Criteria

| Zones         | Establishment                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                      | Year 1                                                                                                | Year 2                                                                                                | Year 3                                                                                                | Year 4                                                                                                | Year 5                                                                                                |
|---------------|--------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------------------------------------------------------------------------------------------------|-------------------------------------------------------------------------------------------------------|-------------------------------------------------------------------------------------------------------|-------------------------------------------------------------------------------------------------------|-------------------------------------------------------------------------------------------------------|
| All Zones     | <p>Commencement of all tasks outlined in the VMP or evidence of planning for their implementation.</p> <p><b>Civil construction works:</b></p> <ul style="list-style-type: none"> <li>• All Construction and sediment fencing installed.</li> <li>• Information signage installed.</li> <li>• Removal and disposal of all exotic and native vegetation throughout the VMP, completed under the supervision of a qualified ecologist.</li> <li>• All earthworks within the VMP area completed under the supervision of an ecologist or bush regenerator.</li> <li>• All rubbish and debris and debris are removed.</li> <li>• All soil preparation works completed to provide suitable conditions for revegetation.</li> </ul> <p><b>Vegetation management works:</b></p> <ul style="list-style-type: none"> <li>• Revegetation, where required, is to be undertaken with a minimum of 40% of the benchmark levels for species diversity provided in Table 9</li> <li>• 85% survival of revegetation or equivalent regeneration across each zone</li> <li>• A minimum native ground cover density of 3.4 plants per m<sup>2</sup> in each management zone and no areas with more than 2 m x 2 m without surviving native plants</li> <li>• Maintenance replanting is to replace plants by the same species or where that species is unavailable with the same growth form (e.g., tree for tree) and must not decrease species diversity. Any new species must be from the community being emulated and of local provenance.</li> <li>• Treatment of any new weed infestations</li> <li>• No woody weeds present capable of producing seed.</li> <li>• No erosion or sedimentation beyond the boundary of the development lot</li> <li>• Monitoring and reporting undertaken in accordance with Section 6</li> </ul> |                                                                                                       |                                                                                                       |                                                                                                       |                                                                                                       |                                                                                                       |
| All Zones     | Treat 100% of Priority Weeds and WoNS<br>Treat 95% of all other weeds                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                              | No greater than 5% cover by priority weeds                                                            | No greater than 5% cover by priority weeds                                                            | No greater than 5% cover by priority weeds                                                            | No greater than 2% cover by priority weeds                                                            | No greater than 2% cover by priority weeds                                                            |
| Zones 1 and 2 | Native groundcover no less than 50% of non-rock areas<br>No greater than 40% groundcover by all weeds                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                              | Native groundcover no less than 55% of non-rock areas<br>No greater than 35% groundcover by all weeds | Native groundcover no less than 60% of non-rock areas<br>No greater than 30% groundcover by all weeds | Native groundcover no less than 70% of non-rock areas<br>No greater than 25% groundcover by all weeds | Native groundcover no less than 80% of non-rock areas<br>No greater than 15% groundcover by all weeds | Native groundcover no less than 90% of non-rock areas<br>No greater than 10% groundcover by all weeds |
| Zones 3 and 4 | Undertake all revegetation as per VMP                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                              | Native groundcover no less than 50% of non-rock areas<br>No greater than 40% groundcover by all weeds | Native groundcover no less than 60% of non-rock areas<br>No greater than 30% groundcover by all weeds | Native groundcover no less than 70% of non-rock areas<br>No greater than 20% groundcover by all weeds | Native groundcover no less than 80% of non-rock areas<br>No greater than 10% groundcover by all weeds | Native groundcover no less than 90% of non-rock areas<br>No greater than 5% groundcover by all weeds  |

| Zones  | Establishment                         | Year 1                                                                                                                                                                                                | Year 2                                                                                                                                                                                                | Year 3                                                                                                                                                                                                | Year 4                                                                                                                                                                                                | Year 5                                                                                                                                                                                               |
|--------|---------------------------------------|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| Zone 5 | Undertake all revegetation as per VMP | No greater than 40% groundcover by all weeds<br>Native vegetation cover no less than 40% of non-rock areas<br>Native canopy cover no more than 50% of BM<br>Native shrub cover no more than 50% of BM | No greater than 30% groundcover by all weeds<br>Native vegetation cover no less than 50% of non-rock areas<br>Native canopy cover no more than 50% of BM<br>Native shrub cover no more than 50% of BM | No greater than 20% groundcover by all weeds<br>Native vegetation cover no less than 60% of non-rock areas<br>Native canopy cover no more than 50% of BM<br>Native shrub cover no more than 50% of BM | No greater than 10% groundcover by all weeds<br>Native vegetation cover no less than 70% of non-rock areas<br>Native canopy cover no more than 50% of BM<br>Native shrub cover no more than 50% of BM | No greater than 5% groundcover by all weeds<br>Native vegetation cover no less than 80% of non-rock areas<br>Native canopy cover no more than 50% of BM<br>Native shrub cover no more than 50% of BM |

Table 9: PCT benchmark conditions

| PCT ID | PCT Common name (community) (BioNet 2022) | Species richness |       |              | Cover (%) |       |              |
|--------|-------------------------------------------|------------------|-------|--------------|-----------|-------|--------------|
|        |                                           | Canopy           | Shrub | Ground cover | Canopy    | Shrub | Ground cover |
| 3320   | Cumberland Shale Plain Woodland           | 5                | 8     | 32           | 52        | 15    | 73           |
| 4023   | Coastal Swamp Oak Forest                  | 4                | 8     | 22           | 21        | 21    | 74           |



## 7. Costs

The cost of implementation for the five-year maintenance period is approximately **\$2,724,885** exclusive of GST and CPI. An indicative annual costing timeline is provided in Table 10. Costs should be reassessed at the end of Year 2 based on the results of the management undertaken to that point. Rates and costs are based on typical commercial rates. Assumptions that have been made regarding the estimation of costs have been outlined below.

### 7.1. Preliminary works

#### 7.1.1. Vegetation clearing and soil preparation

It is assumed that all soil preparation works and vegetation clearing including primary weed removal will be undertaken by the civil contractor under the supervision of a qualified Ecologist or Bush Regenerator. No costs have been provided in this VMP for the soil preparation, vegetation clearing or supervision by a suitably qualified and experienced restoration ecologist.

Preliminary and construction phase activities are identified in Section 3 and have not been included in Table 10.

#### 7.1.2. Seed collection

Budget for the collection of seed has been included as a separate task. This is an indicative figure and does not consider seasonal and annual climatic variation which may increase or decrease the efficiency of seed collection. If further seed collection works are required, this may be an addition cost.

### 7.2. Vegetation management works

#### 7.2.1. Site preparation

Prior to mulching and revegetation, all exotic vegetation must be treated and controlled to an acceptable standard. It is assumed that all zones will require soil preparation and installation of mulch, which has been included in the VMP costs provided.

#### 7.2.2. Weed control techniques

Bush regeneration contractors will implement the weed control treatments identified in this VMP. These works have been estimated to cost \$2,850 for a team of four bush regenerators, including a supervisor, per day. The cost of bush regeneration works includes the costs of herbicide, vehicles and equipment which are required to implement the VMP.

Specific weed control techniques are available in Appendix C.

#### 7.2.3. Revegetation treatments

Bush regeneration contractors will implement the revegetation treatments identified in this VMP. Tube stock costs have been budgeted at an estimated \$5.50 per tree and shrub including planting and \$2.50 per herb, grass, sedge, and groundcover including planting.

A total of approximately 345,000 plants are assumed to be required to achieve the densities identified in the VMP, plus a 10% rate for replacement plantings to be installed throughout the remainder of the VMP period after initial revegetation works.

#### **7.2.4. Monitoring and reporting**

Monitoring and reporting can be undertaken either by the bush regeneration contractor or by the project ecologist. This includes:

- The initial set up of the photo points and conducting the baseline surveys at the beginning of the establishment period
- Preparing monitoring reports, including photo points and vegetation surveying at the end of the establishment period and annually until the end of Year 5

#### **7.3. Pest Control**

Costs for pest control works over the length of the maintenance period are difficult to predict and as such have not been included in the costings. The need and level of pest control works will be assessed in the monitoring reports and an approach will be determined in consultation with Council and LLS.

Table 10: Indicative costings

| Treatment                          | Establishment       | Year 1            | Year 2            | Year 3            | Year 4            | Year 5            | Total               |
|------------------------------------|---------------------|-------------------|-------------------|-------------------|-------------------|-------------------|---------------------|
| <b>Revegetation</b>                |                     |                   |                   |                   |                   |                   |                     |
| Seed collection, cleaning, storage | \$ 52,547           | \$ -              | \$ -              | \$ -              | \$ -              | \$ -              | <b>\$ 52,547</b>    |
| Site Preparation                   | \$ 72,065           | \$ -              | \$ -              | \$ -              | \$ -              | \$ -              | <b>\$ 72,065</b>    |
| Jute Matting / Mulch               | \$ 576,516          | \$ -              | \$ -              | \$ -              | \$ -              | \$ -              | <b>\$ 576,516</b>   |
| Tubestock                          | \$ 881,729          | \$ -              | \$ -              | \$ -              | \$ -              | \$ -              | <b>\$ 881,729</b>   |
| Replacement tubestock              | \$ -                | \$ 88,173         | \$ -              | \$ -              | \$ -              | \$ -              | <b>\$ 88,173</b>    |
| Irrigation                         | \$ 64,858           | \$ 7,206          | \$ -              | \$ -              | \$ -              | \$ -              | <b>\$ 72,065</b>    |
| <b>Weed control</b>                |                     |                   |                   |                   |                   |                   |                     |
| Establishment                      | \$ 93,871           | \$ -              | \$ -              | \$ -              | \$ -              | \$ -              | <b>\$ 93,871</b>    |
| Year 1                             | \$ -                | \$ 181,786        | \$ -              | \$ -              | \$ -              | \$ -              | <b>\$ 181,786</b>   |
| Year 2                             | \$ -                | \$ -              | \$ 167,802        | \$ -              | \$ -              | \$ -              | <b>\$ 167,802</b>   |
| Maintenance - Years 3-5            | \$ -                | \$ -              | \$ -              | \$ 146,970        | \$ 131,896        | \$ 97,980         | <b>\$ 376,845</b>   |
| <b>Associated costs</b>            |                     |                   |                   |                   |                   |                   |                     |
| Disbursements                      | \$ 9,387            | \$ 18,179         | \$ 16,780         | \$ 14,697         | \$ 13,190         | \$ 9,798          | <b>\$ 82,030</b>    |
| Monitoring & Reporting             | \$ 9,932            | \$ 19,864         | \$ 19,864         | \$ 9,932          | \$ 9,932          | \$ 9,932          | <b>\$ 79,458</b>    |
| <b>Totals</b>                      | <b>\$ 1,760,904</b> | <b>\$ 315,208</b> | <b>\$ 204,447</b> | <b>\$ 171,599</b> | <b>\$ 155,018</b> | <b>\$ 117,710</b> | <b>\$ 2,724,885</b> |

## 8. References

- Buchanan, R.A. 2009. *Bush regeneration: recovering Australian landscapes*. 2nd ed., TAFE NSW, Sydney.
- Eco Logical Australia (ELA) 2025b. *Western Sydney Airport Business Park– Biodiversity Assessment*. Prepared for Gray & Walsh Pty Ltd.
- Eco Logical Australia (ELA) 2025b. *Western Sydney Airport Business Park – Riparian Assessment*. Prepared for WSABP Management Pty Ltd.
- Eco Logical Australia (ELA) 2025c. *Western Sydney Airport Business Park – Biodiversity Management Plan*. Prepared for Gray and Walsh Pty Ltd.
- Eco Logical Australia (ELA) 2025d. *Western Sydney Airport Business Park – Wildlife Hazard Assessment Report*. Prepared for Gray and Walsh Pty Ltd.
- Department of Planning and Environment – Water (DPE) 2022. *Guidelines for controlled activities on waterfront land – Riparian corridors*. Available online at [https://water.dpie.nsw.gov.au/data/assets/pdf\\_file/0008/386207/licensing\\_approvals\\_controlled\\_activities\\_riparian\\_corridors.pdf](https://water.dpie.nsw.gov.au/data/assets/pdf_file/0008/386207/licensing_approvals_controlled_activities_riparian_corridors.pdf)
- Local Land Services (LLS) 2023. *Greater Sydney Regional Strategic Management Plan 2023-2030*.

## Appendix A Existing Vegetation

### Native species

| Botanical Name                                        | Common Name              |
|-------------------------------------------------------|--------------------------|
| <i>Alternanthera denticulata</i>                      | Lesser Joyweed           |
| <i>Bothriochloa macra</i>                             | Red Grass                |
| <i>Bursaria spinosa</i> subsp. <i>spinosa</i>         | Native Blackthorn        |
| <i>Callistemon</i> spp.                               |                          |
| <i>Carex inversa</i>                                  | Knob Sedge               |
| <i>Casuarina glauca</i>                               | Swamp Oak                |
| <i>Chloris truncata</i>                               | Windmill Grass           |
| <i>Corymbia</i> spp.                                  |                          |
| <i>Cynodon dactylon</i>                               | Common Couch             |
| <i>Dichondra repens</i>                               | Kidney Weed              |
| <i>Dysphania pumilio</i>                              | Small Crumb weed         |
| <i>Einadia trigonos</i> subsp. <i>stellulata</i>      |                          |
| <i>Eragrostis leptostachya</i>                        | Paddock Lovegrass        |
| <i>Eucalyptus moluccana</i>                           | Grey Box                 |
| <i>Eucalyptus tereticornis</i>                        | Forest Red Gum           |
| <i>Glycine clandestina</i>                            | Twining glycine          |
| <i>Grevillea robusta</i>                              | Silky Oak                |
| <i>Hypericum gramineum</i>                            | Small St John's Wort     |
| <i>Juncus usitatus</i>                                |                          |
| <i>Lachnagrostis filiformis</i>                       |                          |
| <i>Ludwigia peploides</i> subsp. <i>montevidensis</i> | Water Primrose           |
| <i>Microlaena stipoides</i> var. <i>stipoides</i>     | Weeping Grass            |
| <i>Oxalis perennans</i>                               |                          |
| <i>Paspalum distichum</i>                             | Water Couch              |
| <i>Portulaca oleracea</i>                             | Pigweed                  |
| <i>Rumex</i> spp.                                     | Dock                     |
| <i>Solanum americanum</i>                             | Glossy Nightshade        |
| <i>Sporobolus creber</i>                              | Slender Rat's Tail Grass |
| <i>Typha orientalis</i>                               | Broad-leaved Cumbungi    |

### Exotic species

| Botanical Name               | Common Name                |
|------------------------------|----------------------------|
| <i>Alternanthera pungens</i> | Khaki Weed                 |
| <i>Araujia sericifera</i>    | Moth Vine                  |
| <i>Aster subulatus</i>       | Wild Aster                 |
| <i>Axonopus fissifolius</i>  | Narrow-leaved Carpet Grass |
| <i>Briza subaristata</i>     | Chilean quacking grass     |
| <i>Cenchrus clandestinum</i> | Kikuyu Grass               |
| <i>Cestrum parqui</i>        | Green Cestrum              |
| <i>Chloris gayana</i>        | Rhodes Grass               |



| Botanical Name                                 | Common Name                |
|------------------------------------------------|----------------------------|
| <i>Cirsium vulgare</i>                         | Spear Thistle              |
| <i>Conyza bonariensis</i>                      | Flax leaf Fleabane         |
| <i>Cyperus brevifolius</i>                     |                            |
| <i>Cyperus eragrostis</i>                      | Umbrella Sedge             |
| <i>Ehrharta erecta</i>                         | Panic Veldt grass          |
| <i>Eleusine indica</i>                         | Crows foot Grass           |
| <i>Eragrostis curvula</i>                      | African Lovegrass          |
| <i>Erythrina x sykesii</i>                     | Coral tree                 |
| <i>Hypochaeris radicata</i>                    | Catsear                    |
| <i>Jacaranda mimosifolia</i>                   | Jacaranda                  |
| <i>Juncus acutus</i> subsp. <i>acutus</i>      | Sharp Rush                 |
| <i>Lagerstroemia</i> spp.                      |                            |
| <i>Ligustrum lucidum</i>                       | Large-leaved Privet        |
| <i>Lolium perenne</i>                          | Perennial Ryegrass         |
| <i>Lotus angustissimus</i>                     | Slender Birds-foot Trefoil |
| <i>Lycium ferocissimum</i>                     | African Boxthorn           |
| <i>Megathyrsus maximus</i> var. <i>maximus</i> |                            |
| <i>Modiola caroliniana</i>                     | Red-flowered Mallow        |
| <i>Olea europaea</i> subsp. <i>cuspidata</i>   | African Olive              |
| <i>Opuntia stricta</i> var. <i>stricta</i>     | Common Prickly Pear        |
| <i>Paspalum dilatatum</i>                      | Paspalum                   |
| <i>Phytolacca octandra</i>                     | Inkweed                    |
| <i>Pinus</i> spp.                              |                            |
| <i>Plantago lanceolata</i>                     | Lamb's Tongues             |
| <i>Schinus</i> spp.                            |                            |
| <i>Senecio madagascariensis</i>                | Fireweed                   |
| <i>Setaria parviflora</i>                      |                            |
| <i>Sida rhombifolia</i>                        | Paddy's Lucerne            |
| <i>Solanum nigrum</i>                          | Black-berry Nightshade     |
| <i>Solanum sisymbriifolium</i>                 |                            |
| <i>Sonchus oleraceus</i>                       | Common Sow thistle         |
| <i>Sporobolus africanus</i>                    | Parramatta Grass           |
| <i>Verbena bonariensis</i>                     | Purpletop                  |
| <i>Verbena rigida</i> var. <i>rigida</i>       | Veined Verbena             |

## Appendix B Recommended Revegetation Species

| Strata | Botanical Name                  | Common name              | Western Sydney Aerotropolis Landscape Species List | Zone 3 | Zone 4 | Zone 5 |
|--------|---------------------------------|--------------------------|----------------------------------------------------|--------|--------|--------|
| Trees  | <i>Acacia decurrens</i>         | Black wattle             | Y                                                  | *      | *      | *      |
|        | <i>Acacia implexa</i>           | Hickory wattle           | Y*                                                 | *      | *      | *      |
|        | <i>Acacia parramattensis</i>    | Sydney Green Wattle      | Y                                                  | *      | *      | *      |
|        | <i>Allocasuarina littoralis</i> | Black she-oak            | Y                                                  | *      | *      | *      |
|        | <i>Angophora floribunda</i>     | Rough-barked Apple       | Y*                                                 | *      | *      | *      |
|        | <i>Brachychiton populensis</i>  | Kurrajong                | Y                                                  | *      | *      | *      |
|        | <i>Casuarina cunninghamia</i>   | River oak                | Y                                                  | *      | *      | *      |
|        | <i>Casuarina glauca</i>         | Swamp Oak                | Y                                                  | *      | *      | *      |
|        | <i>Clerodendrum tomentosum</i>  | Lolly bush               | Y                                                  | *      | *      | *      |
|        | <i>Corymbia maculata</i>        | Spotted Gum              | Y*                                                 | *      | *      | *      |
|        | <i>Eucalyptus amplifolia</i>    | Cabbage Gum              | Y*                                                 | *      | *      | *      |
|        | <i>Eucalyptus crebra</i>        | Narrow-Leaved Ironbark   | Y*                                                 | *      | *      | *      |
|        | <i>Eucalyptus elata</i>         | River White Gum          | Y*                                                 | *      |        |        |
|        | <i>Eucalyptus eugenioides</i>   | White Stringybark        | Y*                                                 | *      | *      | *      |
|        | <i>Eucalyptus fibrosa</i>       | Red Ironbark             | Y*                                                 | *      | *      | *      |
|        | <i>Eucalyptus moluccana</i>     | Grey Box                 | Y*                                                 | *      | *      | *      |
|        | <i>Eucalyptus tereticornis</i>  | Forest Redgum            | Y*                                                 | *      | *      | *      |
|        | <i>Melaleuca linariifolia</i>   | Snow in Summer           | Y*                                                 | *      | *      | *      |
|        | <i>Melaleuca styphelioides</i>  | Prickly-Leaved Paperbark | Y*                                                 | *      | *      | *      |
|        | <i>Melia azedarach</i>          | White Cedar              | Y*                                                 | *      | *      | *      |
| Shrubs | <i>Acacia falcata</i>           | Sickle Wattle            | N                                                  | *      | *      | *      |
|        | <i>Breynia oblongifolia</i>     | Coffee Bush              | Y                                                  | *      | *      | *      |
|        | <i>Bursaria spinosa</i>         | Blackthorn               | Y                                                  | *      | *      | *      |

| Strata                   | Botanical Name                    | Common name                | Western Sydney Aerotropolis Landscape Species List | Zone 3 | Zone 4 | Zone 5 |
|--------------------------|-----------------------------------|----------------------------|----------------------------------------------------|--------|--------|--------|
|                          | <i>Daviesia ulicifolia</i>        | Gorse Bitter Pea           | Y                                                  | *      | *      | *      |
|                          | <i>Dillwynia sieberi</i>          | Prickly-Parrot Pea         | N                                                  | *      | *      | *      |
|                          | <i>Dodonaea viscosa</i>           | Giant hop bush             | Y                                                  | *      | *      | *      |
|                          | <i>Indigofera australis</i>       | Australian Indigo          | Y                                                  | *      | *      | *      |
|                          | <i>Kunzea ambigua</i>             | Tick Bush                  | Y                                                  | *      | *      | *      |
|                          | <i>Ozothamnus diosmifolius</i>    | Rice Flower                | N                                                  | *      | *      | *      |
|                          | <i>Melaleuca decora</i>           | White Feather Honey Myrtle | Y*                                                 | *      | *      | *      |
|                          | <i>Trema tomentosa</i>            | peach bush                 | Y                                                  | *      | *      | *      |
| Grasses and groundcovers | <i>Carex appressa</i> *           | Tall Sedge                 | Y+                                                 | *      | *      |        |
|                          | <i>Aristida ramosa</i>            | Purple Wiregrass           | Y+                                                 | *      | *      | *      |
|                          | <i>Aristida vagans</i>            | Three awn Spear grass      | N                                                  | *      | *      | *      |
|                          | <i>Arthropodium milleflorum</i> * | Vanilla Lily               | Y                                                  | *      | *      |        |
|                          | <i>Austrostipa ramosissima</i>    | Stout Bamboo Grass         | N                                                  | *      | *      | *      |
|                          | <i>Brunoniella australis</i>      | Blue Trumpet               | Y                                                  | *      | *      | *      |
|                          | <i>Centella asiatica</i>          | Centella                   | N                                                  | *      | *      | *      |
|                          | <i>Chloris truncata</i>           | Windmill Grass             | Y+                                                 | *      | *      | *      |
|                          | <i>Chloris ventricosa</i>         | Plump Windmill Grass       | N                                                  |        | *      | *      |
|                          | <i>Clematis glycinoides</i> var.  |                            | Y                                                  | *      | *      | *      |
|                          | <i>Commelina cyanea</i>           | Scurvy Weed                | Y                                                  | *      | *      | *      |
|                          | <i>Cymbopogon refractus</i> *     | Barbed Wiregrass           | Y+                                                 | *      | *      |        |
|                          | <i>Desmodium varians</i>          | Slender Tick-trefoil       | Y+                                                 | *      | *      | *      |
|                          | <i>Dianella longifolia</i> *      | Smooth Flax Lily           | Y+                                                 | *      | *      |        |
|                          | <i>Dichelachne micrantha</i>      | Short-hair Plume Grass     | Y+                                                 | *      | *      | *      |
|                          | <i>Dichondra repens</i>           | Kidney Weed                | Y                                                  | *      | *      | *      |
|                          | <i>Echinopogon ovatus</i>         | Forest Hedgehog Grass      | Y                                                  | *      | *      | *      |
|                          | <i>Einadia hastata</i>            | Berry Saltbush             | Y                                                  | *      | *      | *      |

| Strata | Botanical Name                                    | Common name            | Western Sydney Aerotropolis Landscape Species List | Zone 3 | Zone 4 | Zone 5 |
|--------|---------------------------------------------------|------------------------|----------------------------------------------------|--------|--------|--------|
|        | <i>Einadia trigonos</i> subsp.                    | Fish weed              | N                                                  | *      | *      | *      |
|        | <i>Entolasia marginata</i>                        | Boarded Panic          | Y                                                  | *      | *      | *      |
|        | <i>Eragrostis brownii</i>                         | Browns lovegrass       | N                                                  | *      | *      | *      |
|        | <i>Eremophila debilis</i>                         | Winter Apple           | Y                                                  | *      | *      | *      |
|        | <i>Euchiton sphaericus</i>                        | Cudweed                | N                                                  | *      | *      | *      |
|        | <i>Ficinia nodosa</i>                             | Knobby Club Rush       | Y+                                                 | *      | *      | *      |
|        | <i>Geranium solanderi</i>                         | Native Geranium        | N                                                  | *      | *      | *      |
|        | <i>Glycine clandestine</i>                        | Twining Glycine        | N                                                  | *      | *      | *      |
|        | <i>Glycine tabacina</i>                           | Love Creeper           | N                                                  | *      | *      | *      |
|        | <i>Goodenia hederacea</i>                         | Forest Goodenia        | Y                                                  | *      | *      | *      |
|        | <i>Hardenbergia violacea</i>                      | Purple Coral Pea       | Y                                                  | *      | *      | *      |
|        | <i>Hibbertia diffusa</i>                          | Wedge Guinea Flower    | N                                                  | *      | *      | *      |
|        | <i>Imperata cylindrica</i> *                      | Blady Grass            | N                                                  | *      | *      |        |
|        | <i>Juncus usitatus</i>                            | Common Rush            | Y+                                                 | *      | *      | *      |
|        | <i>Lepidosperma laterale</i> *                    | Variable Sword Sedge   | N                                                  | *      | *      |        |
|        | <i>Lomandra filiformis</i> *                      | Wattle Mat-rush        | Y+                                                 | *      | *      |        |
|        | <i>Microlaena stipoides</i> var. <i>stipoides</i> | Weeping Meadow Grass   | Y+                                                 | *      | *      | *      |
|        | <i>Oplismenus aemulus</i>                         | Creeping Beard Grass   | Y+                                                 | *      | *      | *      |
|        | <i>Oxalis perennans</i>                           | Grassland Wood-Sorrel  | N                                                  | *      | *      | *      |
|        | <i>Panicum simile</i>                             | Two Colour Panic Grass | N                                                  | *      | *      | *      |
|        | <i>Paspalidium distans</i>                        | Shot Grass             | N                                                  | *      | *      | *      |
|        | <i>Poa labillardieri</i> *                        | Tussock Grass          | Y+                                                 | *      | *      |        |
|        | <i>Pratia purpurascens</i>                        | Whiteroot              | Y                                                  | *      | *      | *      |
|        | <i>Solanum prinophyllum</i>                       | Forest Nightshade      | Y                                                  | *      | *      | *      |
|        | <i>Themeda australis</i> *                        | Kangaroo Grass         | Y+                                                 | *      | *      |        |
|        | <i>Veronica cinerea</i>                           | Speedwell              | N                                                  | *      | *      | *      |

| Strata | Botanical Name               | Common name     | Western Sydney Aerotropolis Landscape Species List | Zone 3 | Zone 4 | Zone 5 |
|--------|------------------------------|-----------------|----------------------------------------------------|--------|--------|--------|
|        | <i>Viola hederacea</i>       | Native Violet   | Y                                                  | *      | *      | *      |
|        | <i>Wahlenbergia gracilis</i> | Native Bluebell | N                                                  | *      | *      | *      |
|        | <i>Wahlenbergia stricta</i>  | Tall bluebell   | Y                                                  | *      | *      | *      |

Y\* = ONLY WITHIN 3KM WILDLIFE BUFFER, WHERE SUPPORTED BY ECOLOGIST REPORT, CONFIRMING LANDSCAPE DESIGN MINIMISES WILDLIFE ATTRACTION. REFER TO ELA 2024D.

Y+ = SUBJECT TO MONITORING AND/OR MAINTENANCE PLAN TO ENSURE POTENTIAL FOR WILDLIFE ATTRACTION IS MANAGED.

\*= CLUMPING GRASS



## Appendix C Techniques and specifications

### WEED CONTROL

Weed control involves a combination of mechanical, physical, and chemical techniques to remove the weeds and prevent regrowth. Weed control will be undertaken across the entire zone. A selection of the best suited weed control method within the site depends on a number of factors, including:

- The species or combination of weeds being targeted,
- The density of weeds present,
- Resources available (time, labour, equipment, and finances), weather condition on the day.

### WEED CONTROL TECHNIQUES

Details of specific weed control techniques to be used such as cut-and-paint, scrape-and-paint, herbicide-spraying, and hand weeding are provided in Brodie (1999). The principles of bush regeneration and techniques to trigger natural regeneration are to be in accordance with the Bradley Method and other techniques described in Buchanan (2009). Management techniques for different types of weeds are provided below.

#### ***Annual grasses***

Annual grasses should be hand removed or spot sprayed where isolated or in low concentrations. Larger patches of annual grasses may be slashed/brush cut in late spring to early summer, after flowering, but prior to seed set. For most species, slashing/brush cutting prior to late spring through to early summer will promote vigorous growth and should not occur. However, some annual grasses can grow and produce seed at any time of the year dependent on climatic conditions such as high rainfall and warm temperatures. Monitoring of annual species should be undertaken and if new growth occurs, the same treatment will be applied to the new growth to prevent seed production. Individual plants should be hand removed, bagged, and disposed of appropriately offsite.

#### ***Perennial grasses***

Perennial grasses will be hand removed where isolated or in low concentrations. Larger patches may be slashed prior to seed production in spring or summer (depending on the growth cycle of the species) and the regrowth spot-sprayed 2-3 weeks later when it is actively growing and approximately 10 cm in length. Monitoring of these species will occur and if new seed production occurs, the same treatment will be applied again as required. However, slashing will not reduce the presence of exotic grasses on its own and must always be combined with targeted removal to reduce densities and allow for native regeneration. Individual plants should be hand removed, bagged, and disposed of at a registered green waste facility.

#### ***Woody weeds***

Primary control of trees such as *Olea europaea subs. cuspidata* following vegetation removal, should be implemented by using the cut and paint or drill and fill method using a non-selective herbicide. The most appropriate method to be used depends on the size of the individual to be removed and will be determined by the bush regeneration contractor. Primary weed control should use techniques that will not encourage flushes of secondary weed growth. All seedlings of woody weeds will be hand pulled or spot-sprayed with a non-selective herbicide.

Follow up treatment of woody weeds, including *O.europaea subs. cuspidata* will be controlled by the cut and paint or drill and fill method using a non-selective herbicide.

The most appropriate method to be used depends on the size of the individual to be removed and will be determined by the bush regeneration contractor. Primary weed control should use techniques that will not encourage flushes of secondary weed growth. All seedlings of woody weeds will be hand pulled or spot-sprayed with a non-selective herbicide.

### ***Creepers and climbers***

The control of exotic vines should be managed by skirting at chest height then spraying the target once it is on the ground. This should be done with a dicot specific herbicide such as Grazon®. Follow up treatments will be necessary and should be done as the germinating vines are still saplings.

The control of creepers varies depending on the species. For the most part, seedlings will be hand pulled, while mature plants can be controlled by the stem-scrape method or spot spraying using a non-selective herbicide. The precise method to be used will be determined by the bush regeneration contractor depending on the species, size, and reproductive status of the individual. All vegetative material removed should be bagged, removed from site, and disposed of appropriately.

### ***Herbaceous weeds***

Herbaceous weeds will be hand pulled prior to flowering. Where large swaths of these species occur, they will be sprayed using a non-selective herbicide. If high densities of mature stands occur, weeds may be slashed first using a brush cutter and any subsequent regrowth sprayed. Regular monitoring of these species will be required to prevent seed production. All vegetative material that is pulled out and has the potential to regrow if deposited on ground will be bagged and removed from site.

### ***Management of weed waste***

All weed propagules, especially priority weeds, will be bagged and disposed of as directed by legislation at facility licensed to receive green waste. All weed waste without propagules will be composted onsite in small unobtrusive piles.

### ***Herbicide use***

The use of herbicide to control weeds should be carefully considered. Herbicide must only be used for the purpose described on the product label, as per the NSW *Pesticides Act 1999*. Herbicide use should assess potential long-term impacts of the technique, including whether the proposed works address the source of the weed infestation. However, herbicide application forms an important and useful component of an integrated weed management approach and can be the most appropriate method for the control and eventual eradications of some weed species.

Herbicide use should occur during the active growing season for plants to encourage the chemical uptake into the plant. The selection of herbicides should also consider the type of weed and the location. Where non-selective herbicides are required for use, glyphosate is the most suitable. A glyphosate-based herbicide, formulated for use near waterways, will be used if works require herbicide application near waterways, a (e.g., Roundup Biactive®).

Broad-leaf selective herbicide may be used as per the NSW Weed Control Handbook (DPI 2018). However, this type of herbicide is extremely toxic to aquatic life and must not be used in, or adjacent to, waterways.

Registration and records must be kept in accordance with the NSW *Pesticides Regulation 2017*.

## REVEGETATION WORKS

Revegetation has the dual aim of both re-establishing the original native vegetation community at the site and reducing erosion along the length of the riparian corridor, which will carry greatly increased peak flows due to the increased run-off from the hard surfaces created by the associated residential development. Any plantings should consist of local provenance stock. Planting of Hiko for trees and shrub species and Hiko or Viro cells for grasses and other groundcover species is the preferred method. Planting should be done via a low impact method such as hand digging or hand auger. The holes dug for each plant should be at least 1.5x the width and 2x the depth of the root ball. Fertiliser should be added to each hole dug as per the label specifications. Water crystals or wetting agents should be added to each plant hole. This will increase the water holding capacity of the soil and reduce watering schedules. Initial irrigation of the plantings is essential to ensure that the soil forms around the root ball and air pockets are removed. This will be required unless sufficient rainfall (approx. 10mm) occurs on the day of planting.

Tree guards should be installed on each tree or shrub to protect seedlings from extreme weather (frosts and heat), herbivorous grazing and herbicide drift during maintenance works. Bio-degradable tree guards are recommended to protect the seedlings. Following the revegetation works, irrigation needs to be undertaken for at least 8 weeks following planting to ensure the establishment of the plants. The level of irrigation will be determined by rainfall and temperature experienced at the planting site.

A temporary irrigation system should be installed to assist in the establishment of vegetation. Timing of the planting of these areas will need to take into consideration surrounding civil works and erosion/sediment control requirements, these areas will not be planted until earthworks have been completed. A minimum rate of attrition of 10% is to be expected and should be allowed for.

Mulch can be derived from vegetation removed from the development area, if available. Alternately, mulch should be comprised of un-composted wood (preferably wood waste), with a particle size of 15 mm to 40 mm, with no fines, and good air-filled porosity. Mulch should not contain any weed seeds, nor be derived from diseased trees or from any part of the tree lower than 1 m above the ground. Mulch, where required, should be installed to a depth of 100 mm.

Jute matting, where required, must be comprised of 100% biodegradable jute fibres with a minimum weight of 680g/m<sup>2</sup> (~6 mm thickness). Jute must be pegged with at least 3 x 150 mm pins per m<sup>2</sup>, and each roll overlapped by 100 mm.

### ***Seed collection***

For the growth of the plants used in the revegetation works, seed must be collected from local provenance species. Groundcovers, shrubs and trees should be collected as within close proximity (i.e., <20km) to the site. However, soil type, climate and aspect of the collection site(s) should also be considered. Native grasses typically have much larger dispersal mechanisms and are to be collected from within the Sydney basin.

Where species identified in this VMP cannot be sourced, they may be substituted for other species as identified by Tozer (2003). Species must be substituted with species of a similar form, e.g., trees for tree, grasses for grasses, etc. Only wild native species are to be used. Plants are not to be substituted with horticultural varieties under any circumstances.

Record keeping of seed collection and planting locations are to follow the Florabank guidelines (Mortlock, 2000). A Section 132C licence under the NSW *National Parks and Wildlife Act 1974* will be required to undertake seed collection works.

## BUSH REGENERATION CONTRACTORS

The rehabilitation and revegetation requirements detailed in this VMP must be implemented under the supervision of the supervising Ecologist or Bush Regenerator.

The supervising Bush Regenerator should be a member of AABR or should possess the required qualifications and experience for membership. In addition to this, they should have, as a minimum, a Certificate III in Conservation & Land Management or equivalent. The contractor will need to conduct best practice bush regeneration techniques as described by Buchanan (2009).

A flexible approach to this site is recommended since techniques may need to be changed or modified to suit site conditions. This approach is consistent with adaptive management and allows the contractor to develop and build on site knowledge whilst implementing this VMP. Monitoring will assist in the development of the VMP actions in subsequent years.


## HYGIENE PROTOCOLS

To avoid introducing soil pathogens / diseases, in particular *Phytophthora cinnamomi* (Root rot disease), onto site a hygiene protocol should be undertaken as per the guidelines developed by the Royal Botanic Gardens in 'Best Practice Management Guidelines for *Phytophthora cinnamomi* with the Sydney Metropolitan Catchment Management Authority.' Management actions should be outlined within the Biodiversity management plan (ELA 2024).

For Bush Regenerators all tools and boots should be washed down and thoroughly cleaned of soil / mud using a solution of water and disinfectants prior to undertaking works onsite. All machinery should be thoroughly cleaned of all soil / mud / debris prior to working within the VMP area.

## RABBIT EXCLUSION FENCING

Rabbit proof fencing may be required to be installed to the guidelines in the Commonwealth Department of the Environment Catalogue of fence designs. The fencing will need to be a minimum of 90mm high, with a 180 mm skirt as per the figure below.

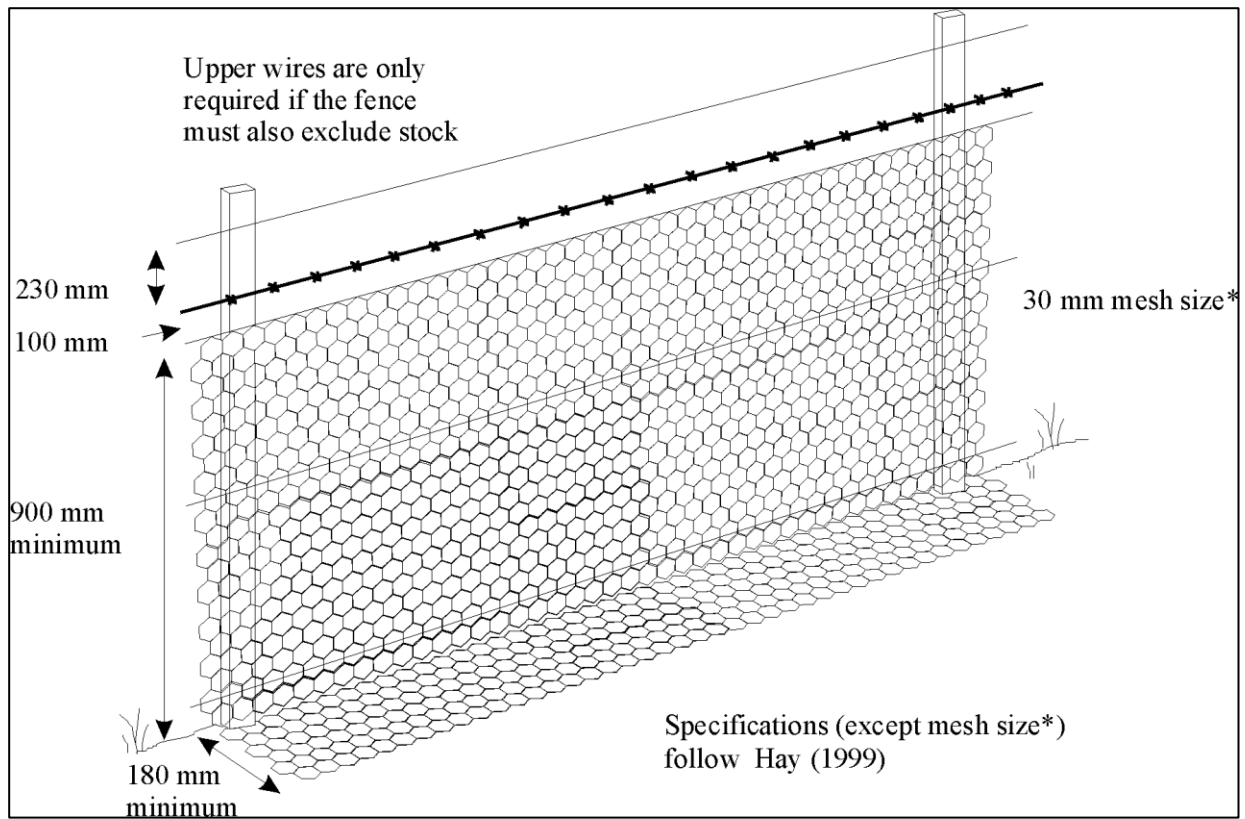

Recommended fencing for rabbit exclusion (DoEE 2004)

