




	Component	Weight (t)	Distance (m)	Crane Capacity (t)	Percentage (%)
1	Tower	4.3	59	8.7	49.43
2	Tower head + Slew table + Mechanism	10.5	-	-	-
2.1	Tower head + Top Slew*	7	59	8.7	80.46
2.2	Bottom Slew*	3.5	59	8.7	40.23
3	Cabin	1.2	59	8.7	13.79
4	Complete Counterjib	9.36	50	10.72	87.31
5	Counterweight	3	46.2	11.81	25.40
6	Complete Jib	14.8	-	-	-
6.1	Jib Section 01 + Hook	9.32	48.9	11.02	84.57
6.2	Jib Section 02	5.52	32.3	17.97	30.72
7	Static Base	7.5	59	8.7	86.21
8	Climbing Frame	7.8	59	8.7	89.66
9	Grillage (Individual Beam)	3.3	63.1	7.9	41.77



TITAN Cranes & Rigging
7 Curtis Rd, Mulgrave NSW 2765
+61 1300 30 40 52

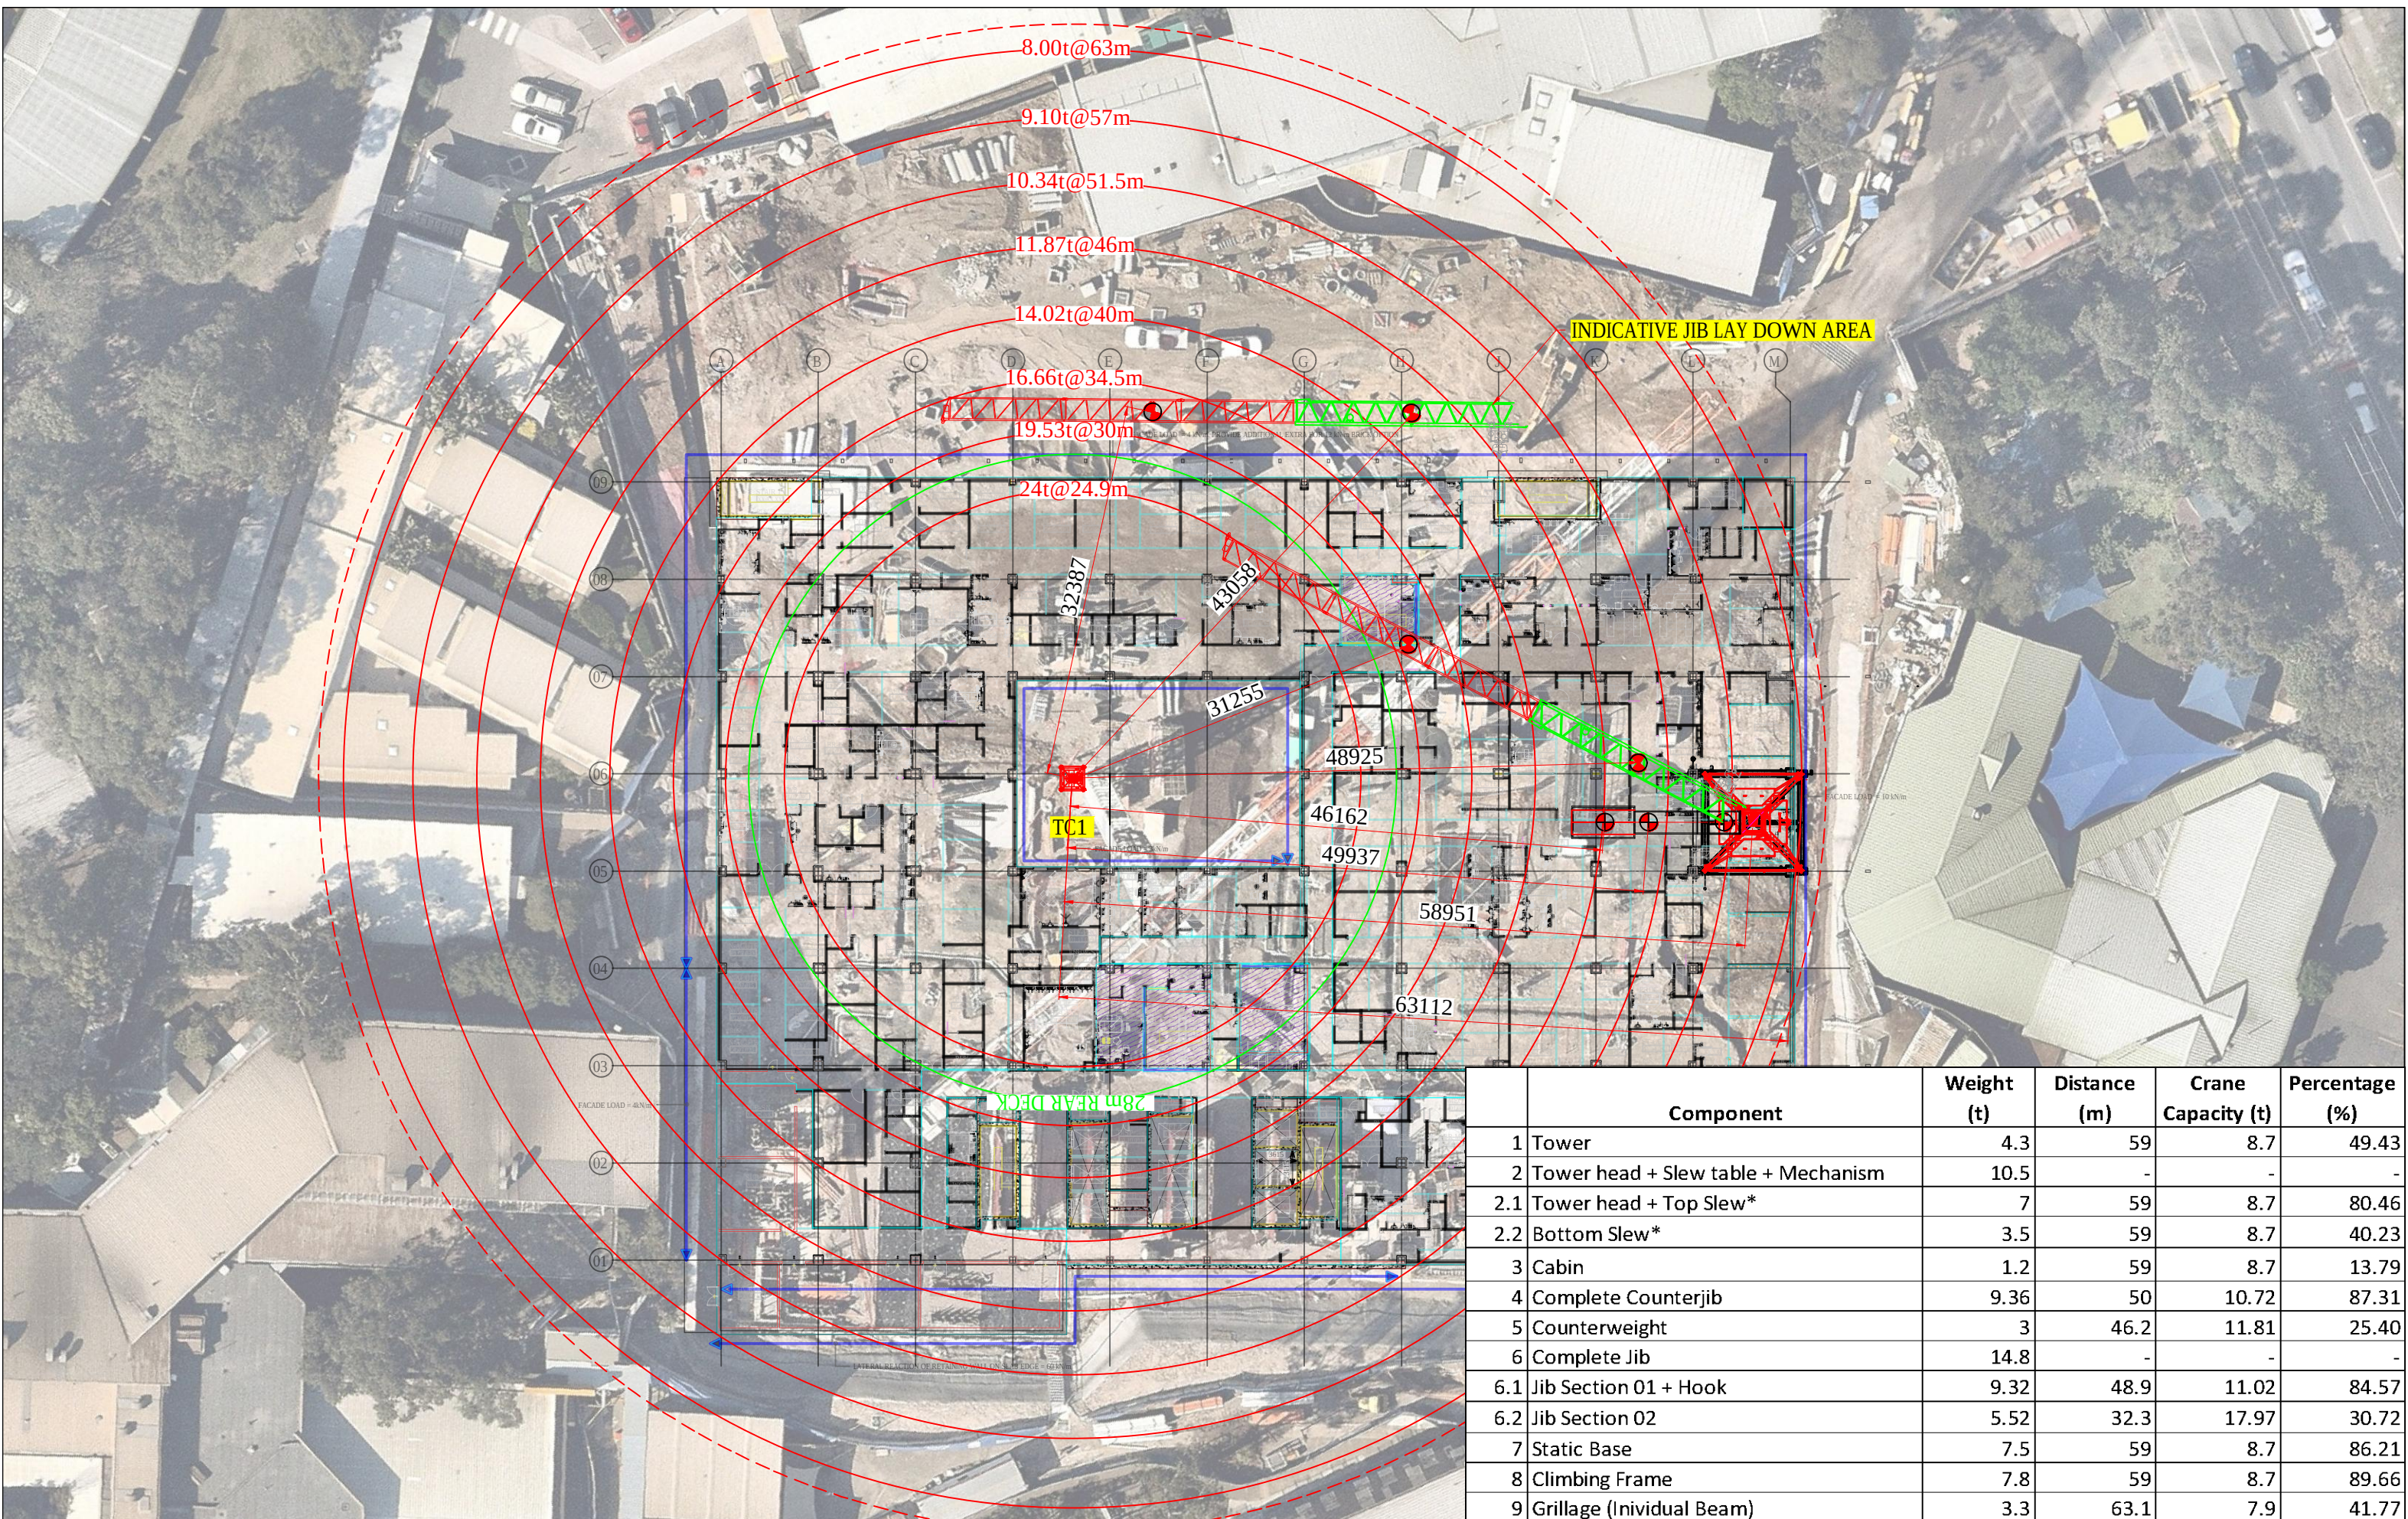

Client
CPB CONTRACTORS

Project
Nepean Hospital - Stage 02

Drawing
LEVEL 00

CRANE	MODEL	JIB	MAX CAPACITY	TOWERS	HUH
TC1	Jaso J600	63m	24t	16	x
TC2	Jaso J360	50m	18t	11	x

NOT FOR CONSTRUCTION

Rev	Description	Drn.	Chk.	Date
P1	Information	AK	-	18.07.19
P2	Information	AK	-	02.12.19
P3	Information	AK	-	05.12.19
P4	Information	AK	-	09.12.19

Current Revision P4

Dwg No. 3328-01-03
Sheet No. T101
Scale 1:500 @ A3
Drawn By AK

These drawings remain the property of Titan Cranes, any modification/reproduction of them in any form is prohibited without written consent from Titan Cranes. Please make sure you have the latest revision of this drawing, it is not Titan Cranes responsibility. Do not scale off this drawing - If you need dimensions please contact Titan Cranes.

Quote: 3328
