

4.4.3 VEHICLE ACCESS

The proposed access to the site during construction will be located along Warringah Road. Bantry Bay Road will initially be used during bulk excavation and while the southern entry (Gate 1) to Hospital Road is being constructed (shown in Figure 4.4).

The southern entry is consistent with the construction access from the Stage 1 works. It is noted that in the Stage 1 consultation with community stakeholders, this entry was identified as the preferred option.

Access gates will be set back from Warringah Road to allow construction vehicles to queue within the site and minimise impact on through traffic on Warringah Road. Full time ticketed traffic controllers will manage pedestrians at the site access locations for vehicles entering or leaving the site.

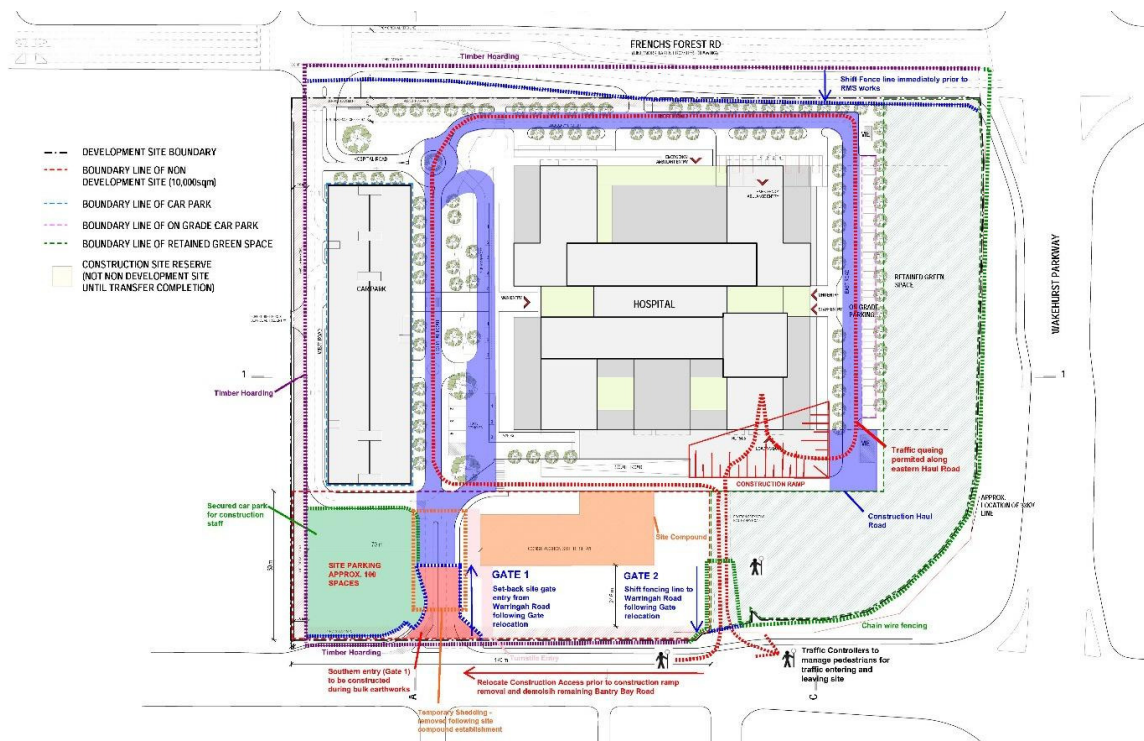


Figure 4-4 Site layout, parking and accommodation during Hospital Road entry construction

Following the construction of the main access onto Hospital Road the Bantry Bay Road access will be made obsolete and the site fence will be relocated to the site boundary along Warringah Road (shown in Figure 4-5)

On site construction access routes have been established, within the construction boundary, along the western, northern and eastern boundary of the site and mainly according to the proposed layout of the internal road network to facilitate materials handling for tower/crawler cranes and forklifts. Hoists will transport personnel and lighter materials within each building structure.
