REFER TO SHEET C006 FOR CONTINUATION

SEDIMENT AND EROSION CONTROL NOTES

1. IT HAS BEEN ASSUMED THAT HOARDINGS/SILT FENCING WILL BE PROVIDED TO THE STAGE BOUNDARY SUFFICIENT TO PREVENT SEDIMENT RUNOFF FROM LEAVING SITE (EXCEPT IN THE CASE OF ENTRY/EXIT LOCATIONS WHERE TEMPORARY CONSTRUCTION ENTRY/EXIT SEDIMENT TRAP ARE PROVIDED). IF THIS IS NOT THE CASE, PROVIDE SEDIMENT FENCE TO STANDARD DETAIL BELOW AS REQUIRED TO PREVENT SEDIMENT FROM LEAVING SITE, DIRECT RUNOFF TO SEDIMENT BASIN.
2. ALL SEDIMENT CONTROL MEASURES TO BE INSTALLED IN ACCORDANCE WITH LANDCOM MANAGING URBAN STORMWATER "BLUE BOOK".
3. MINIMISE CLEARING IN ACCORDANCE WITH THE ARBORIST REPORT: "ARBORIST IMPACT ASSESMENT AND SPOIL PROFILE" PREPARED BY MCARDLE ARBORICULTURAL CONSULTANCY, DATED 22ND OCTOBER 2019
4. SEDIMENT CONTROL FOR LANDSCAPED WORKS DOWNSTREAM OF THE BUILDING TO INCLUDE A SILTFENCE AND SANDBAGS AS REQUIRED. INSTALL BUND TO DIVERT UPSTREAM CATCHMENT AWAY FROM DISTURBED SOIL AREA.

SEDIMENT CONTROL CONDITIONS

1. SEDIMENT FENCES WILL BE INSTALLED AS SHOWN AND ELSEWHERE AT THE DISCRETION OF THE SITE MANAGER TO CONTAIN COARSER SEDIMENT FRACTIONS INCLUDING AGGREGATED FINES) AS NEAR AS POSSIBLE TO THEIR SOURCE.
2. SEDIMENT REMOVED FROM ANY TRAPPING DEVICE WILL BE RELOCATED WHERE FURTHER POLLUTION TO DOWNSLOPE LANDS & WATERWAYS CANNOT OCCUR.
3. STOCKPILES WILL BE PLACED WHERE SHOWN ON DRAWING OR ELSEWHERE AT THE DISCRETION OF THE SITE MANAGER AND NOT WITHIN 5m OF HAZARD AREAS INCLUDING LIKELY AREAS OF HIGH VELOCITY FLOWS SUCH AS WATERWAYS, PAVED AREAS & DRIVEWAYS.
4. WATER WILL BE PREVENTED FROM DIRECTLY ENTERING THE PERMANENT DRAINAGE SYSTEM WITH INLET FILTERS (SEE DETAILS) UNLESS IT IS SEDIMENT FREE.
5. TEMPORARY SEDIMENT TRAPS WILL BE RETAINED UNTIL AFTER THE LANDS THEY ARE PROTECTING ARE COMPLETELY REHABILITATED.
6. CONTRACTOR TO DESIGN/SIZE/CONSTRUCT TEMPORARY SEDIMENT BASIN, WATER SHOULD BE ALLOWED TO SETTLE BEFORE DISCHARGE. CONTRACTOR MUST VERIFY THAT WATER QUALITY MEETS AUTHORITIES REQUIREMENTS PRIOR TO DISCHARGE . ACCUMULATED SEDIMENT SHOULD THEN BE REMOVED & DISPOSED OF IN ACCORDANCE WITH ENVIRONMENTAL MANAGEMENT PROCEDURES.

SITE INSPECTION & MAINTENANCE CONDITIONS

THE SITE MANAGER WILL INSPECT THE SITE AT LEAST WEEKLY AND WILL:

1. ENSURE THAT DRAINS OPERATE PROPERLY & TO EFFECT ANY NECESSARY REPAIRS
2. REMOVE SPILLED SAND OR OTHER MATERIALS FROM HAZARD AREAS, INCLUDING LANDS CLOSER THAN 5m FROM AREAS OF LIKELY CONCENTRATED OR HIGH VELOCITY FLOWS ESPECIALLY WATERWAYS & PAVED AREAS.
3. REMOVE TRAPPED SEDIMENT WHENEVER LESS THAN DESIGN CAPACITY REMAINS WITHIN THE STRUCTURE
4. ENSURE REHABILITATED LANDS HAVE EFFECTIVELY REDUCED THE EROSION HAZARD AND TO INITIATE UPGRADING OR REPAIR AS APPROPRIATE.
5. CONSTRUCT ADDITIONAL EROSION AND/OR SEDIMENT CONTROL WORKS AS MIGHT BECOME NECESSARY TO ENSURE THE DESIRED PROTECTION IS GIVEN TO DOWNSLOPE LANDS AND WATERWAYS.
6. MAINTAIN EROSION & SEDIMENT CONTROL MEASURES IN A FULLY FUNCTIONING CONDITION UNTIL ALL EARTHWORK ACTIVITIES ARE COMPLETED AND THE SITE IS REHABILITATED.
7. REMOVE TEMPORARY SOIL CONSERVATION STRUCTURES AS THE LAST ACTIVITY IN THE REHABILITATION PROGRAM.

AS PART OF THE STATUTORY 'DILIGENCE OF CARE' RESPONSIBILITIES, THE SITE MANAGER WILL KEEP A LOGBOOK MAKING ENTRIES AT LEAST WEEKLY, IMMEDIATELY BEFORE FORECAST RAIN AND AFTER RAINFALL.
ENTRIES WILL INCLUDE:

1. THE VOLUME & INTENSITY OF ANY RAINFALL EVENTS
2. THE CONDITION OF ANY SOIL & WATER MANAGEMENT WORKS
3. THE CONDITION OF VEGETATION & ANY NEED TO IRRIGATE
4. THE NEED FOR DUST PREVENTION STRATEGIES
5. ANY REMEDIAL WORKS TO BE UNDERTAKEN

THE BOOK WILL BE KEPT ONSITE & MADE AVAILABLE TO ANY AUTHORISED PERSON ON REQUEST. IT WILL BE GIVEN TO THE PROJECT MANAGER AT THE CONCLUSION OF WORKS.

TREE PROTECTION

REFER TO "ARBORIST IMPACT ASSESSMENT AND SPOIL PROFILE" BY MCARDLE ARBORICULTURAL CONSULTANCY DATED 22ND OCTOBER 2019 FOR THE EXTENT OF TREES PROTECTION ZONE AND THE PROTECTION MEASURES REQUIRED.

LEGEND

- SITE BOUNDARY
- SITE FENCE
- SEDIMENT FENCE
- TEMPORARY CATCH DRAIN
- TEMPORARY SHAKER RAMP FOR ENTRY/EXIT
- TEMPORARY STOCKPILE (LOCATION TBC ON-SITE)
- SEDIMENT BASIN (LOCATION TBC ON-SITE)
- GEOTEXTILE PIT FILTER / FILTER SURROUND INSTALLED ON EXISTING PIT
- OVERLAND FLOW
- EXISTING BUILDING TO BE DEMOLISHED

THIS DRAWING MAY BE PREPARED IN COLOUR AND MAY BE INCOMPLETE IF COPIED

COPYRIGHT
All rights reserved.
These drawings, plans and specifications and the copyright therein are the property of the Bonacci Group and must not be used, reproduced or copied wholly or in part without the written permission of the Bonacci Group.

Rev	Description	Date	By	App
P2	ISSUED FOR SSDA	06.10.20	JF	–
P1	ISSUED FOR SCHEMATIC DESIGN	07.02.20	SY	–

ST JOHN OF GOD Health Care

BONACCI
Bonacci Group (NSW) Pty Ltd
ABN 29 102 716 352
Consulting Engineers. Structural - Civil - Infrastructure
Level 6, 37 York Street, Sydney, NSW 2000 Australia
Tel: +61 2 8247 8400 Fax: +61 2 8247 8444
sydney@bonaccigroup.com
www.bonaccigroup.com

Project Name: ST JOHN OF GOD HOSPITAL REDEVELOPMENT
177 GROSE VALE RD NORTH RICHMOND NSW 2753

Drawing Title: SOIL AND WATER MANAGEMENT PLAN SHEET 1

PRELIMINARY

Designed	EW	Approved	Date
Drawn	JF		
Scale	1:200		
Date	DEC 2019	Project Ref	Drawing No / Rev
Sheet	A0	12056 01	C005 P2

North

File: G:\12056\12056\02 WORKS\Civil\01 CAD\01 Autocad\St John Of God Richmond Hospital\Issued\Dwg\12056\1C-C005-C4(SP2).dwg Plotted: 06.10.20 at 11:45 AM By: Jonathan Fragoo

REFER TO SHEET C005 FOR CONTINUATION

SEDIMENT AND EROSION CONTROL NOTES

1. IT HAS BEEN ASSUMED THAT HOARDINGS/SILT FENCING WILL BE PROVIDED TO THE STAGE BOUNDARY SUFFICIENT TO PREVENT SEDIMENT RUNOFF FROM LEAVING SITE (EXCEPT IN THE CASE OF ENTRY/EXIT LOCATIONS WHERE TEMPORARY CONSTRUCTION ENTRY/EXIT SEDIMENT TRAP ARE PROVIDED). IF THIS IS NOT THE CASE, PROVIDE SEDIMENT FENCE TO STANDARD DETAIL BELOW AS REQUIRED TO PREVENT SEDIMENT FROM LEAVING SITE, DIRECT RUNOFF TO SEDIMENT BASIN.
2. ALL SEDIMENT CONTROL MEASURES TO BE INSTALLED IN ACCORDANCE WITH LANDCOM MANAGING URBAN STORMWATER "BLUE BOOK".
3. MINIMISE CLEARING IN ACCORDANCE WITH THE ARBORIST REPORT: "ARBORIST IMPACT ASSESMENT AND SPOIL PROFILE" PREPARED BY MCARDLE ARBORICULTURAL CONSULTANCY, DATED 22ND OCTOBER 2019
4. SEDIMENT CONTROL FOR LANDSCAPED WORKS DOWNSTREAM OF THE BUILDING TO INCLUDE A SILTFENCE AND SANDBAGS AS REQUIRED. INSTALL BUND TO DIVERT UPSTREAM CATCHMENT AWAY FROM DISTURBED SOIL AREA.

SEDIMENT CONTROL CONDITIONS

1. SEDIMENT FENCES WILL BE INSTALLED AS SHOWN AND ELSEWHERE AT THE DISCRETION OF THE SITE MANAGER TO CONTAIN COARSER SEDIMENT FRACTIONS (INCLUDING AGGREGATED FINES) AS NEAR AS POSSIBLE TO THEIR SOURCE.
2. SEDIMENT REMOVED FROM ANY TRAPPING DEVICE WILL BE RELOCATED WHERE FURTHER POLLUTION TO DOWNSLOPE LANDS & WATERWAYS CANNOT OCCUR.
3. STOCKPILES WILL BE PLACED WHERE SHOWN ON DRAWING OR ELSEWHERE AT THE DISCRETION OF THE SITE MANAGER AND NOT WITHIN 5m OF HAZARD AREAS INCLUDING LIKELY AREAS OF HIGH VELOCITY FLOWS SUCH AS WATERWAYS, PAVED AREAS & DRIVEWAYS.
4. WATER WILL BE PREVENTED FROM DIRECTLY ENTERING THE PERMANENT DRAINAGE SYSTEM WITH INLET FILTERS (SEE DETAILS) UNLESS IT IS SEDIMENT FREE.
5. TEMPORARY SEDIMENT TRAPS WILL BE RETAINED UNTIL AFTER THE LANDS THEY ARE PROTECTING ARE COMPLETELY REHABILITATED.
6. CONTRACTOR TO DESIGN/SIZE/CONSTRUCT TEMPORARY SEDIMENT BASIN, WATER SHOULD BE ALLOWED TO SETTLE BEFORE DISCHARGE. CONTRACTOR MUST VERIFY THAT WATER QUALITY MEETS AUTHORITIES REQUIREMENTS PRIOR TO DISCHARGE. ACCUMULATED SEDIMENT SHOULD THEN BE REMOVED & DISPOSED OF IN ACCORDANCE WITH ENVIRONMENTAL MANAGEMENT PROCEDURES.

SITE INSPECTION & MAINTENANCE CONDITIONS

THE SITE MANAGER WILL INSPECT THE SITE AT LEAST WEEKLY AND WILL:

1. ENSURE THAT DRAINS OPERATE PROPERLY & TO EFFECT ANY NECESSARY REPAIRS
2. REMOVE SPILLED SAND OR OTHER MATERIALS FROM HAZARD AREAS, INCLUDING LANDS CLOSER THAN 5m FROM AREAS OF LIKELY CONCENTRATED OR HIGH VELOCITY FLOWS ESPECIALLY WATERWAYS & PAVED AREAS.
3. REMOVE TRAPPED SEDIMENT WHENEVER LESS THAN DESIGN CAPACITY REMAINS WITHIN THE STRUCTURE
4. ENSURE REHABILITATED LANDS HAVE EFFECTIVELY REDUCED THE EROSION HAZARD AND TO INITIATE UPGRADING OR REPAIR AS APPROPRIATE.
5. CONSTRUCT ADDITIONAL EROSION AND/OR SEDIMENT CONTROL WORKS AS MIGHT BECOME NECESSARY TO ENSURE THE DESIRED PROTECTION IS GIVEN TO DOWNSLOPE LANDS AND WATERWAYS.
6. MAINTAIN EROSION & SEDIMENT CONTROL MEASURES IN A FULLY FUNCTIONING CONDITION UNTIL ALL EARTHWORK ACTIVITIES ARE COMPLETED AND THE SITE IS REHABILITATED.
7. REMOVE TEMPORARY SOIL CONSERVATION STRUCTURES AS THE LAST ACTIVITY IN THE REHABILITATION PROGRAM.

AS PART OF THE STATUTORY 'DILIGENCE OF CARE' RESPONSIBILITIES, THE SITE MANAGER WILL KEEP A LOGBOOK MAKING ENTRIES AT LEAST WEEKLY, IMMEDIATELY BEFORE FORECAST RAIN AND AFTER RAINFALL.
ENTRIES WILL INCLUDE:

1. THE VOLUME & INTENSITY OF ANY RAINFALL EVENTS
2. THE CONDITION OF ANY SOIL & WATER MANAGEMENT WORKS
3. THE CONDITION OF VEGETATION & ANY NEED TO IRRIGATE
4. THE NEED FOR DUST PREVENTION STRATEGIES
5. ANY REMEDIAL WORKS TO BE UNDERTAKEN

THE BOOK WILL BE KEPT ONSITE & MADE AVAILABLE TO ANY AUTHORISED PERSON ON REQUEST. IT WILL BE GIVEN TO THE PROJECT MANAGER AT THE CONCLUSION OF WORKS.

TREE PROTECTION

REFER TO "ARBORIST IMPACT ASSESSMENT AND SPOIL PROFILE" BY MCARDLE ARBORICULTURAL CONSULTANCY DATED 22ND OCTOBER 2019 FOR THE EXTENT OF TREES PROTECTION ZONE AND THE PROTECTION MEASURES REQUIRED.

LEGEND

- SITE BOUNDARY
- SITE FENCE
- SEDIMENT FENCE
- TEMPORARY CATCH DRAIN
- TEMPORARY SHAKER RAMP FOR ENTRY/EXIT
- TEMPORARY STOCKPILE (LOCATION TBC ON-SITE)
- SEDIMENT BASIN (LOCATION TBC ON-SITE)
- GEOTEXTILE PIT FILTER / FILTER SURROUND INSTALLED ON EXISTING PIT
- OVERLAND FLOW
- EXISTING BUILDING/GAMES COURT TO BE DEMOLISHED

THIS DRAWING MAY BE PREPARED IN COLOUR AND MAY BE INCOMPLETE IF COPIED

COPYRIGHT
All rights reserved.
These drawings, plans and specifications and the copyright therein are the property of the Bonacci Group and must not be used, reproduced or copied wholly or in part without the written permission of the Bonacci Group.

Rev	Description	Date	By	App
P2	ISSUED FOR SSDA	06.10.20	JF	-
P1	ISSUED FOR SCHEMATIC DESIGN	07.02.20	SY	-

Rev	Description	Date	By	App

ST JOHN OF GOD Health Care

BONACCI
Bonacci Group (NSW) Pty Ltd
ABN 29 102 778 362
Consulting Engineers - Structural - Civil - Infrastructure
Level 6, 37 York Street, Sydney, NSW 2000 Australia
Tel: +61 2 8247 8400 Fax: +61 2 8247 8444
sydney@bonaccigroup.com
www.bonaccigroup.com

Project Name: ST JOHN OF GOD HOSPITAL REDEVELOPMENT
177 GROSE VALE RD NORTH RICHMOND NSW 2753

Drawing Title: SOIL AND WATER MANAGEMENT PLAN SHEET 2

PRELIMINARY

Designed	EW	Approved	Date
Drawn	JF		
Scale	1:200		
Date	DEC 2019		
Sheet	A0		

North

Project Ref	Drawing No	Rev
12056 01	C006	P2

File: P:\12056\12056\01 WP\02 CIVIL\01 CAD\01 Autocad\St John Of God Richmond Hospital\Issued\Dwg\12056\01-C-C006-CAD(P2).dwg Plotted: 06.10.20 at 11:47 AM By: Jonathan Fragoo





TEMPORARY CONSTRUCTION VEHICLE ENTRY/EXIT SEDIMENT TRAP

NOT TO SCALE



KERB INLET SEDIMENT TRAP

NOT TO SCALE



SEDIMENT FENCE

NOT TO SCALE



SANDBAG KERB INLET SEDIMENT TRAP

NOT TO SCALE



GEOTEXTILE PIT FILTER 1

NOT TO SCALE



ON GRADE KERB INLET SEDIMENT TRAP

NOT TO SCALE



ALTERNATIVE SEDIMENT FENCE

NOT TO SCALE

ALTERNATIVE SEDIMENT FENCE NOTES

1. INSTALL THIS TYPE OF SEDIMENT FENCE WHEN USE OF SUPPORT POSTS IS NOT DESIRABLE OR NOT POSSIBLE. SUCH CONDITIONS MIGHT APPLY, FOR EXAMPLE, WHERE APPROVAL IS GRANTED FROM THE APPROPRIATE AUTHORITIES TO PLACE THESE FENCES IN HIGHLY SENSITIVE ESTUARINE AREAS.
2. USE BENT TRENCH MESH TO SUPPORT THE F82 WELDED MESH FACING AS SHOWN ON THE DRAWING ABOVE. ATTACH THE JUTE MESH TO THE WELDED MESH FACING USING UV-RESISTANT CABLE TIES.
3. STABILISE THE WHOLE STRUCTURE WITH SANDBAG OR ROCK ANCHORING OVER THE TRENCH MESH AND THE LEADING EDGE OF THE JUTE MESH. THE ANCHORING SHOULD BE SUFFICIENTLY LARGE TO ENSURE STABILITY OF THE STRUCTURE IN THE DESIGN STORM EVENT, USUALLY THE 10 YEAR EVENT.



GEOTEXTILE PIT FILTER 2

NOT TO SCALE



CATCH DRAIN

NOT TO SCALE





FIELD INLET SEDIMENT TRAP

NOT TO SCALE

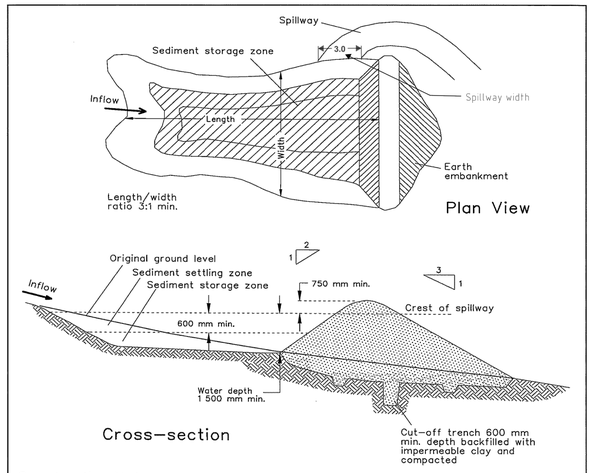

Construction Notes

1. Remove all vegetation and topsoil from under the dam wall and from within the storage area.
2. Construct a cut-off trench 500 mm deep and 1,200 mm wide along the centreline of the embankment extending to a point on the gully wall level with the riser crest.
3. Maintain the trench free of water and recompact the materials with equipment as specified in the SWMP to 95 per cent Standard Proctor Density.
4. Select fill following the SWMP that is free of roots, wood, rock, large stone or foreign material.
5. Prepare the site under the embankment by ripping to at least 100 mm to help bond compacted fill to the existing substrate.
6. Spread the fill in 100 mm to 150 mm layers and compact it at optimum moisture content following the SWMP.
7. Construct the emergency spillway.
8. Rehabilitate the structure following the SWMP.

EARTH BASIN - WET

(APPLIES TO 'TYPE D' AND 'TYPE F' SOILS ONLY)

SD 6-4

COPYRIGHT
All rights reserved.
These drawings, plans and specifications and the copyright therein are the property of the Bonacci Group and must not be used, reproduced or copied wholly or in part without the written permission of the Bonacci Group.

Rev	Description	Date	By	App
P2	ISSUED FOR SSDA	06.10.20	JF	-
P1	ISSUED FOR SCHEMATIC DESIGN	07.02.20	JF	-

ST JOHN OF GOD Health Care

BONACCI
Bonacci Group (NSW) Pty Ltd
ABN 29 102 716 352
Consulting Engineers, Structural - Civil - Infrastructure
Level 6, 37 York Street, Sydney, NSW 2000 Australia
Tel: +61 2 8247 8400 Fax: +61 2 8247 8444
sydney@bonaccigroup.com
www.bonaccigroup.com

Project Name: ST JOHN OF GOD HOSPITAL REDEVELOPMENT
177 GROSE VALE RD NORTH RICHMOND NSW 2753

Drawing Title: SOIL AND WATER MANAGEMENT DETAILS

PRELIMINARY

Designed	EW	Approved	Date
Drawn	JF		
Scale	1:200		
Date	DEC 2019		
Sheet	A0		

North

Project Ref	Drawing No	Rev
12056 01	C007	P1

File: \\jarvis\ref\Data\jobs\12056\01 WPK2 Cutoff CAD\01 Autocad\St John Of God Richmond Hospital\Issued\Dwg\12056\01-C-C007-CAD(P1).dwg
Plotted: Jul 10 2020 11:47 AM By: Jonathan Franco
