D. Design & Construction Program

THE RIBBON

MASTER PROGRAMME

09-Aug-13

Activity ID	Activity Name	Original Durat...	Start	Finish
THE RIBBON - CMP Programme August 20 13		817	12-Aug-13	30-Nov-16
DA100	DA Approval Process	146	12-Aug-13	18-Mar-14
Design		270	02-Sep-13	29-Sep-14
A1030	Concept Design	65	02-Sep-13*	29-Nov-13
A1040	Design Development	75	02-Dec-13	31-Mar-14
A1050	IFT Documentation for Early Trades	65	01-Apr-14	30-Jun-14
A1080	IFC Documentation	65	01-Jul-14	29-Sep-14
Construction		670	01-Apr-14	30-Nov-16
Demolition		107	01-Apr-14	16-Sep-14
A1000	Commence On Site Works	0	01-Apr-14*	
A1005	Site Establishment and Mobilisation	30	01-Apr-14	10-May-14
A1020	Demolition of Exisitng IMAX Theatre	113	01-May-14	16-Sep-14
A1060	Demolition Complete	0	16-Sep-14	
Inground Works		119	17-Sep-14	27-Feb-15
A1070	Bulk Excavation	25	17-Sep-14	20-Oct-14
A1230	Inground Works incl. Piling/ Services	72	21-Oct-14	31-Jan-15
A1250	Raft Slabs	85	31-Oct-14	27-Feb-15
A1270	FRP Lift Core Bases	54	07-Nov-14	28-Jan-15
Above Ground Structure		252	08-Jan-15	21-Nov-15
A1280	Set Up Jump Form & Construct Cores	204	08-Jan-15	22-Sep-15
A1300	FRP Slabs - Tower	238	28-Jan-15	21-Nov-15
A1310	Construct Imax Structure	48	01-Aug-15	28-Sep-15
Facade / Finishes / Commissioning		438	30-Mar-15	30-Nov-16
A1320	External Facade - Curtain Wall	229	26-Jun-15	22-Apr-16
A1330	Podium Floor Finishes	145	30-Mar-15	28-Sep-15
A1340	Office Floor Finishes / Commissioning	310	07-Jul-15	15-Aug-16
A1350	Delay Allowance - 12 %	84	16-Aug-16	30-Nov-16*
A2000	Project Completion	0		30-Nov-16

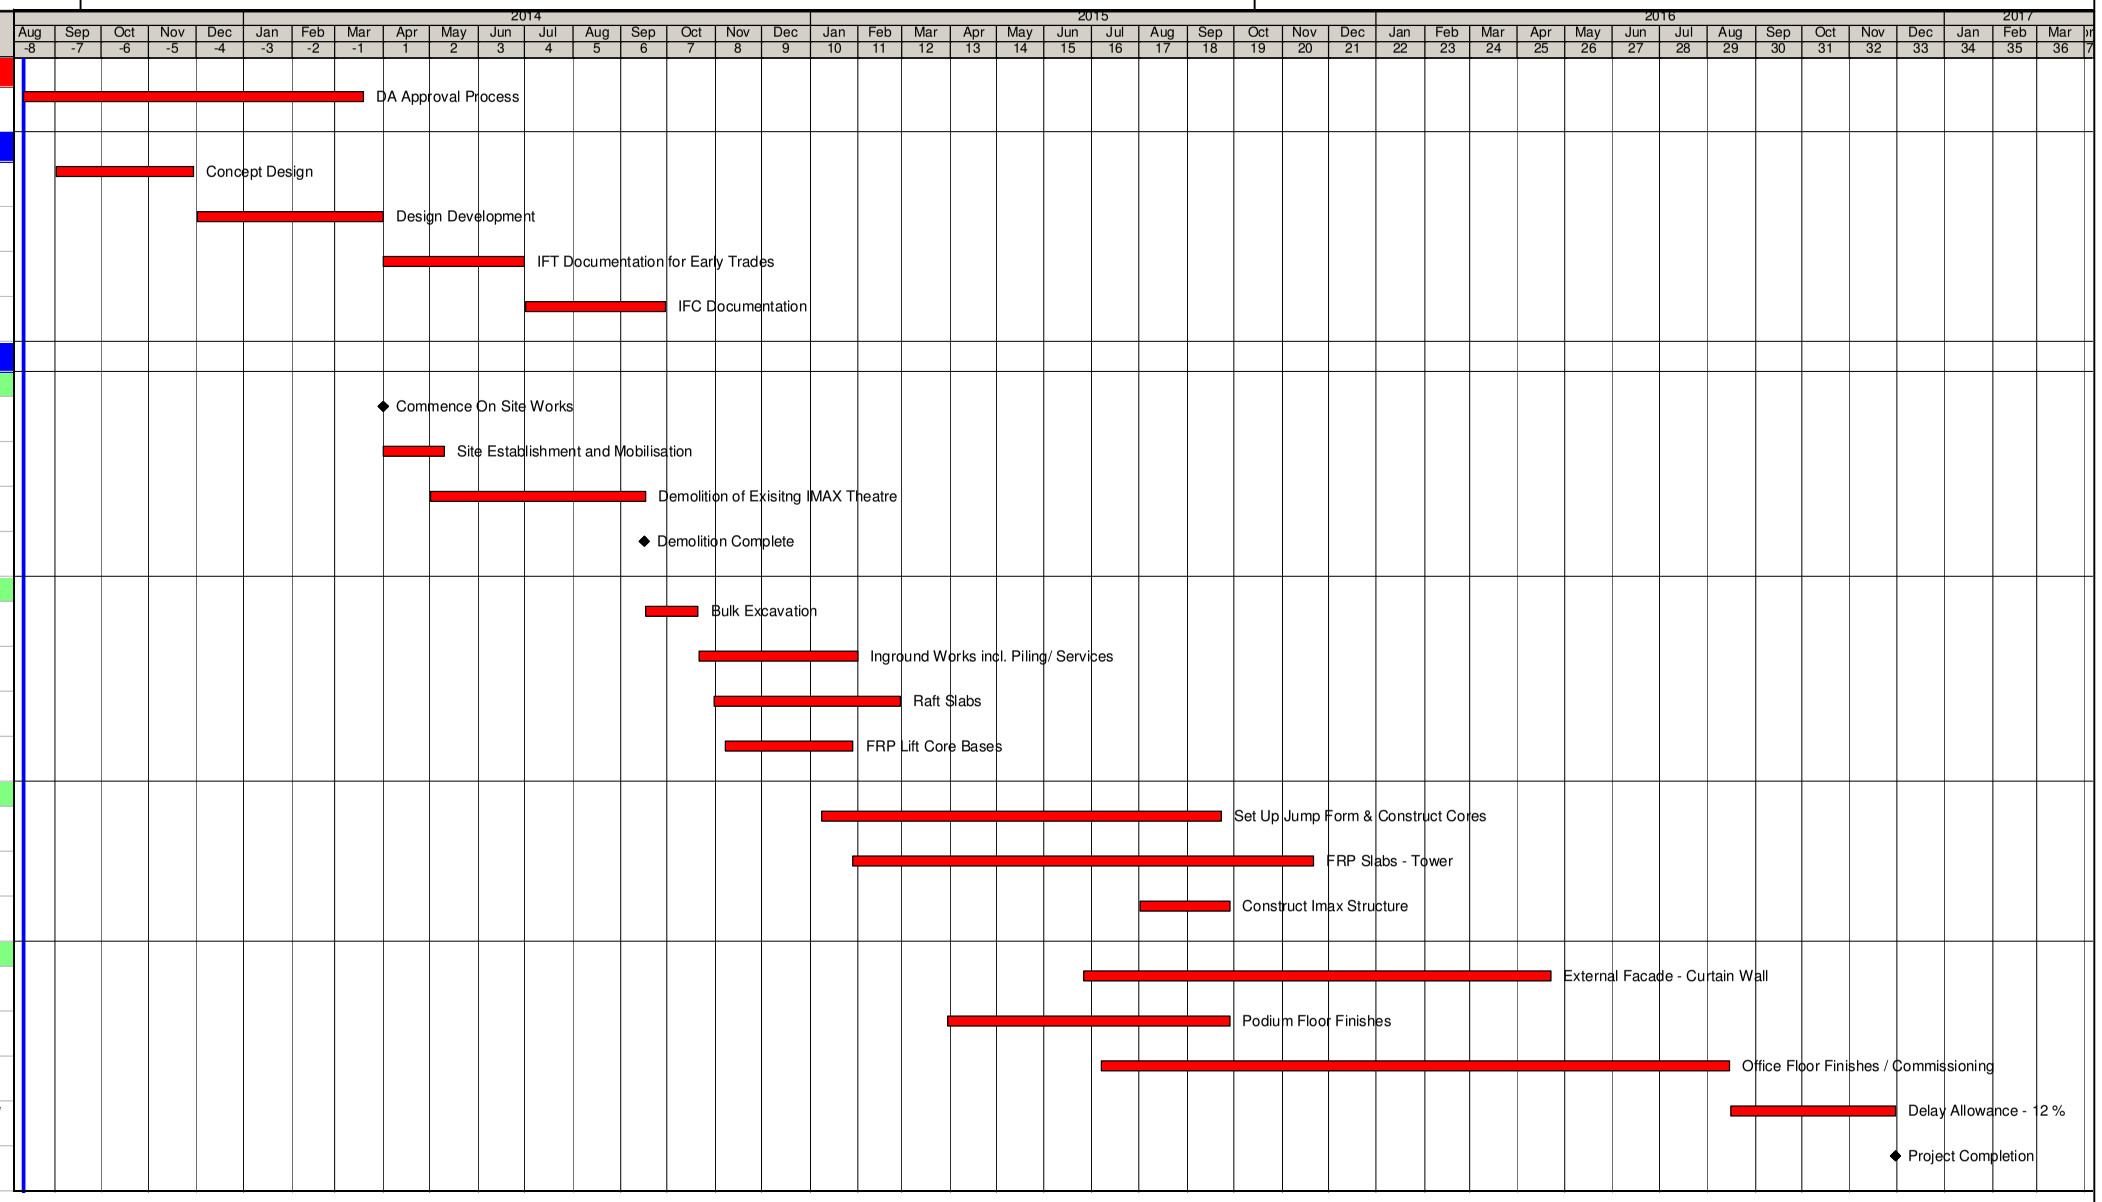

Remaining Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
◆ Milestone

Date	Revision	Checked	Approved
09-Aug-13	CMP Issue		
